

ANNEXURE-A

Quarterly Progress Report for quarter ending December 2022 (Year)

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP93535-1/821/R-382/2019	Name of Project/Phase of Registered Project	PANCHHI ENCLAVE
Name of Promoter	ANUP KUMAR	Project Address	MAUZA-BEUR, P.S.-PHULWARISHARIF, DIST-PATNA
Name of Co-promoter	NA		
Project Registration is valid up to	30/06/2022		
Starting date of Project or Phase of the Project	30/01/2019		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	Residential	
Period of validity of map by the Competent Authority			

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS				
Building/Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments –
1. Avinash Kumar	8. 1 BHK	- 2 BHK 633 Sqft	32	1. Booked/ Allotted-17 2. Sold - 5
2. Sudha Kumari	9. 2 BHK,	- 2 BHK 710Sqft		
3. Rajeev Kumar Verma	10. BHK	3 2 BHK 633 Sqft		
4. Avinash Kumar	8.Shop	- 2 BHK 633 Sqft		
5. Rudrabhan Yadav	5.Bungalow	- 3 BHK 985 Sqft		
6. Ved Prakesh	6. Plot etc.	- 2 BHK 633 Sqft		
7. Nitu Choudhary				

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted-17	-
		2. Sold-5	-
1. Avinash Kumar	1		
2. Sudha Kumari	1		
3. Rajeev Kumar Verma	1		
4. Avinash Kumar	1		
5. Rudrabhan Yadav	1		
6. Ved Prakesh	1		
7. Nitu Choudhary	1		

IV. Construction Progress of the Project		
1. Building / Wing / Layout Number _____ (To be added for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	N/A
2.	Basements (if any)	N/A


ARCADIA HOMES

Anup Kumar

PARTNER

3.	Podiums (if any)	COMPLETED
4.	Plinth	COMPLETED
5.	Stilt Floor	COMPLETED
6.	Slabs of Super Structure	COMPLETED
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	COMPLETED
8.	Sanitary Fittings within the Flat/Premises. Electrical Fittings within the Flat/Premises	COMPLETED
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	COMPLETED
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	COMPLETED
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities	NOT COMPLETED


V. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	NO		
2.	Water Supply	YES	Own Drain Tube well	

ARCADIA HOMES

 PARTNER

3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES		
4./+ 4	Storm Water Drains	YES		
5.	Landscaping & Tree Planting	NO		
6.	Street Lighting	NO		
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	YES		
9.	Solid Waste Management & Disposal	NO		
10.	Water Conservation / Rain Water Harvesting	NO		
11.	Energy Management	YES		
12.	Fire Protection and Fire Safety Requirements	YES		
13.	Closed Parking	NO		
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	N/A		
16.	Others (Option to Add More)			

VI. PHOTOGRAPH OF THE BLOCKS (EACH BLOCK) OF THE BUILDING		
S. No.	Particulars	
1.	Front Elevation.	(ATTACH)
2.	Rear Elevation	(ATTACH)
3.	Side Elevation	(ATTACH)

VII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)

ARCADIA HOMES

 PARTNER

(1)	(2)	(3)
1.	Project Account No.	40180200000296
2.	Estimated Cost of the Project including land cost at the start of the Quarter	
3.	Amount received during the Quarter	1616600=00
4.	Actual Cost Incurred during the Quarter	3322299=00
5.	Net amount at end of the Quarter	217180=00
6.	Total expenditure on Project till date	
7.	Details of Mortgage or Charge, if any, created on the Land and the projects	

VIII. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	
2.	Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

ARCADIA HOMES

Anup Kumar

PARTNER

Signature of Promoter

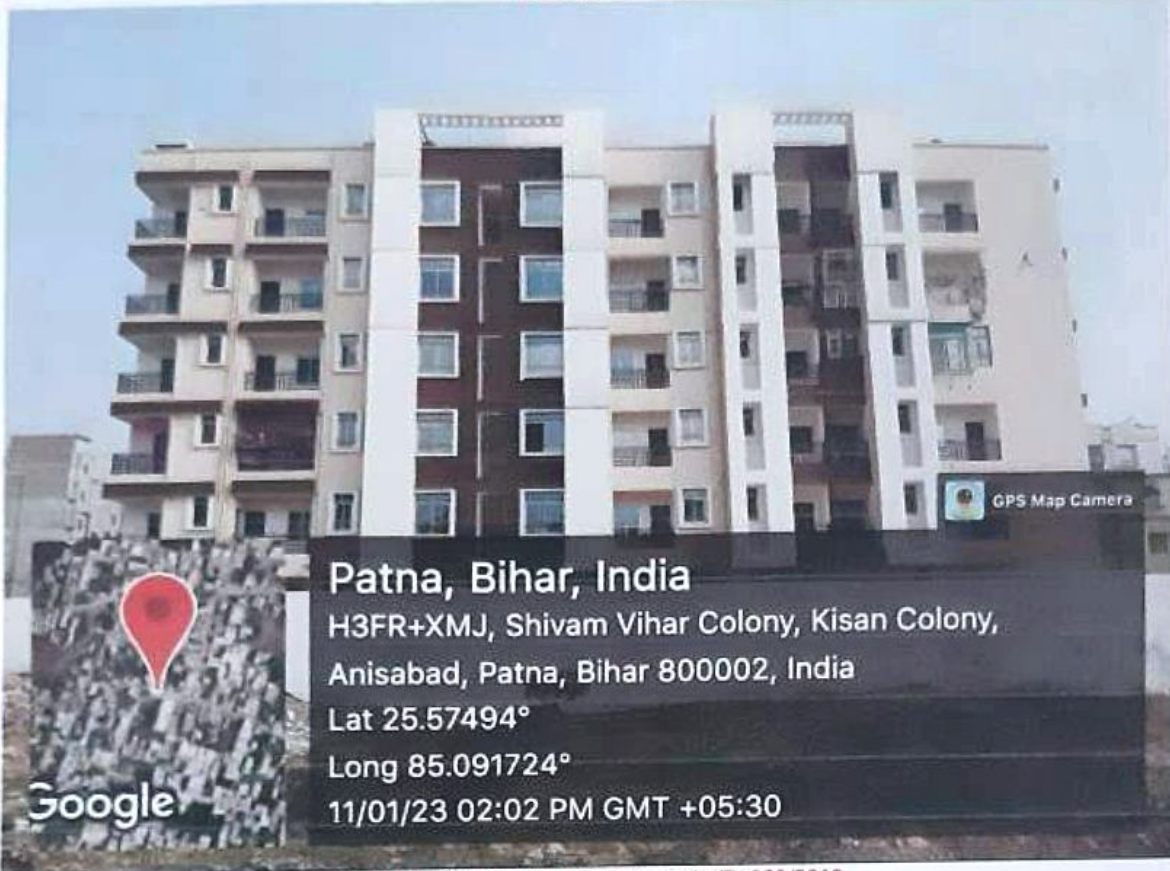
Name: *Anup Kumar*

Date

Promoter:- ARCADIA HOMES

Project:- PANCHHI ENCLAVE

FRONT SIDE



BRERA NO:-BRERAP93535-1/821/R-382/2019

SIDE PHOTO



ARCADIA HOMES

Anup Kumar

PARTNER

Promoter:- ARCADIA HOMES

Project:- PANCHHI ENCLAVE

REAR SIDE



Patna, Bihar, India

H3FR+XRP, Kisan Colony, Beur, Patna, Bihar 800002, India

Lat 25.574942°

Long 85.091995°

11/01/23 02:04 PM GMT +05:30

BRERA NO:-BRERAP93535-1/821/R-382/2019

SIDE PHOTO



Patna, Bihar, India

H3FR+RF4, Mitra Mandal Colony, Kisan Colony, Anisabad, Patna, Bihar 800002, India

Lat 25.574573°

Long 85.091224°

11/01/23 02:03 PM GMT +05:30

ARCADIA HOMES

Anup Kumar
PARTNER
