

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending March of 2025

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Registration no. of the Partnership firm/LLP Identification number/Any other	F000115/2018	Name of the Promoter's Entity ARCADIA HOMES	Remarks
Address of the Promoter's Entity :	HOUSE NO. -422, SAKET VIHAR, MITRA MANDAL COLONY, ANISABAD, PATNA-800002		
Total Experience of the promoter in Real Estate sector (In Completed years)			
Total Experience in Real Estate Sector after Commencement of RERA (In Completed years)			
No of Projects done before Commencement of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Commencement of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP93535-002/160/R-1632/2024	Name of Project	J B ENCLAVE
Name of Promoter	ARCADIA HOMES	Project Address	SAKET VIHAR, M.M COLONY, PATNA
Project Registration is valid up to	22/06/2028		
Starting date of Project	05/01/2024		
Type of Project	Residential		
Name of the Competent Authority which sanctioned the project map			

ARCADIA HOMES

 PARTNER

Period of validity of map as granted by the Competent Authority concerned	5 YEARS		
---	---------	--	--

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/ Block Number	Apartment/ Unit Type	Carpet Area	Total Number of sanctioned apartments/ unit-wise	Total Numbers of apartments in Promoter's share- Booked	Total Numbers of apartments in Promoter's share- Agreement for sale Executed	Total Numbers of apartments in Landowner's share Booked	Total Numbers of apartments in Landowner's share Agreement for sale Executed
	1-BHK						
	2-BHK		11	03			
	3-BHK		09	04			
	4-BHK and over						
	shop						
	Office Space						
	Bungalow						
	Plots (in case of plots specific area of plot must be mentioned)						
		Total Carpet Area		% of total Units	% of total Units	% of total Units	% of total Units

IV. DETAILS OF ASSOCIATION OF ALLOTTEES :

Mandatory in case the booking percentage exceeds 50% of the total sanctioned flats/plots/buildings/commercial space

The details of the Association of Allottees need to be provided in the proforma of Association of Allottees attached with this Form.

V. CANCELLATION OF FLAT ALLOTMENT, IF ANY WITH FLAT NUMBER/BUNGALOW/PLOT NO./OFFICE SPACE/SHOP/ETC.

(A) Cancelled by Allottees	(B) Cancelled by Promoters
Flat No./Plot no./Shop No./Etc. :	Flat No./Plot no./Shop No./Etc. :
*whether notice and reminder of cancellation was Served to the promoters by Allottee/s	*whether notice and reminder of cancellation has been Served to the Allottees by serving

ARCADIA HOMES

Amr Kumar
PARTNER

Yes/No	Yes/No	
VI. DISCLOSURE OF BOOKED INVENTORY OF GARAGES/PARKING SPACE		
Building Wise / Block Number	Total Number of Sanctioned Garages/Parking Space	Total Number of Garages/Parking Space: 1. Booked/Allotted
	20	07

VII. DETAILS OF BUILDING APPROVALS				
(If already filed along with Registration Application, then there is no need of further filing)				
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Validity up to	Attach Copy
1.	Environment Clearance			
2.	Fire N.O.C.			
3.	Airport Authority of India N.O.C.			
4.	Water Supply Permission			
5.	Other Approval(s), if any, required for the Project.			

VIII. PROGRESS OF THE PROJECT-INTERNAL INFRASTRUCTURE DEVELOPMENT			
In case of more than one Block/Building/Apartment/Plots/Bungalow, the details have to be filled for each Block separately			
S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) . Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	0%	
6.	Slabs of Super Structure	100%	

7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	80% 50% 0% 0%	31-06-2026 31-08-2026 01-03-2027 31-05-2027
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 40%	31-09-2027 30-03-2028
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 0% 80%	 3-10-2025 10-11-2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	03-03-2027 28-02-2027 31-10-2025 25-10-2025
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per prescribed norms	0% 100% 0%	31-03-2028 10-12-2027
12.	N.O.C, Electrical fittings, Mechanical Equipment, compliance to conditions of environment as per prescribed norms	0%	31-01-2028
13.	Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 0% 0%	10-11-2027 03-03-2028 05-04-2028
14.	Overall Percentage of Actual work Done and Final Completion date		

**IX. EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS –
PROGRESS RELATED TO AMENITIES AND COMMON AREA**

ARCADIA HOMES
Anup Kumar
PARTNER

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	31-03-2028
2.	Water Supply	YES	0%	31-10-2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31-12-2027
4.	Storm Water Drains	YES	0%	06-01-2028
5.	Landscaping & Tree Planting	YES	0%	30-04-2028
6.	Street Lighting	YES	0%	01-04-2028
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	28-02-2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	04-04-2028
11.	Energy Management	YES	0%	02-03-2028
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			
17.	Overall Percentage of Actual Work Done and final Completion date			

X. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT				
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

XI. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	327102000000224
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	
5.	Amount received during the Quarter	60,27,757=00

ARCADIA HOMES

Amr Kumar
PARTNER

6.	Actual Cost Incurred during the Quarter	51,63,696=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project till date	1,92,88,827=00
9.	Cumulative fund collected till the end of Quarter in question	2,12,16,757=00
10.	Cumulative expenditure done till the end of Quarter in question	1,92,88,827=00
11.	Percentage of Expenditure incurred of the total Estimated development cost of the project	

XIII. GEO TAGGED AND DATE PHOTOGRAPH (EACH BLOCK/BUILDING/APARTMENT/PLOTS/BUNGLOW) OF THE PROJECT

The photograph must have date.

(A)	Sr. No.		
	1.	Photographs showing Front Elevation	Attach
	2.	Photographs showing Rear Elevation	Attach
	3.	Photographs showing Side Elevation (Both Sides)	Attach
	4.	Photograph of each floor showing the progress of interior works	
	5.	Photographs of Common Areas (Staircase, Lift Area, Terrace, parking, etc.)	
(B)	Sr. No.		
	1.	Photograph of the display board set up at the project site providing requisite information along with the QR code of the project allotted by the Authority	

XIV. MISCELLANEOUS

A	List of Legal Cases (if any) – Against Project / Promoter
1.	(a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO
2.	No of Execution Cases against this project (a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO
3.	No of Suo - Moto cases against this project (a) Case No. (b) Name of Parties

	Order passed, if Yes, Whether complied (Yes/No) NO
4.	No of Certificate cases /PDR cases against this project (a) Case No. (b) Name of Parties Order passed, if Yes, Whether complied (Yes/No) NO

XV. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

- Weather the project in progress as per time schedule or lagging behind? Yes/No
- If yes, whether it would be completed on the completion date fixed as per RC. Yes/No.
- If No, then Reason for delay:

XVI. BROCHURE /Prospectus : Copy of the brochure/prospectus to be uploaded with Form-7

XVII Name of Grievance Redressal Officer nominated by the promoter whom allottee can contact in case of any query or grievance

Name : ANUP KUMAR

Contact No : 9430906829

Email id : arcadiahomes0612@gmail.com

Address : HOUSE NO-22,SAKET VIHAR MITRA MANDAL COLONY,PHULWARI PATNA

Undertaking:


I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

ARCADIA HOMES
Anup Kumar
PARTNER

Signature of Promoter

Name: ANUP KUMAR

Date: 14/04/2025

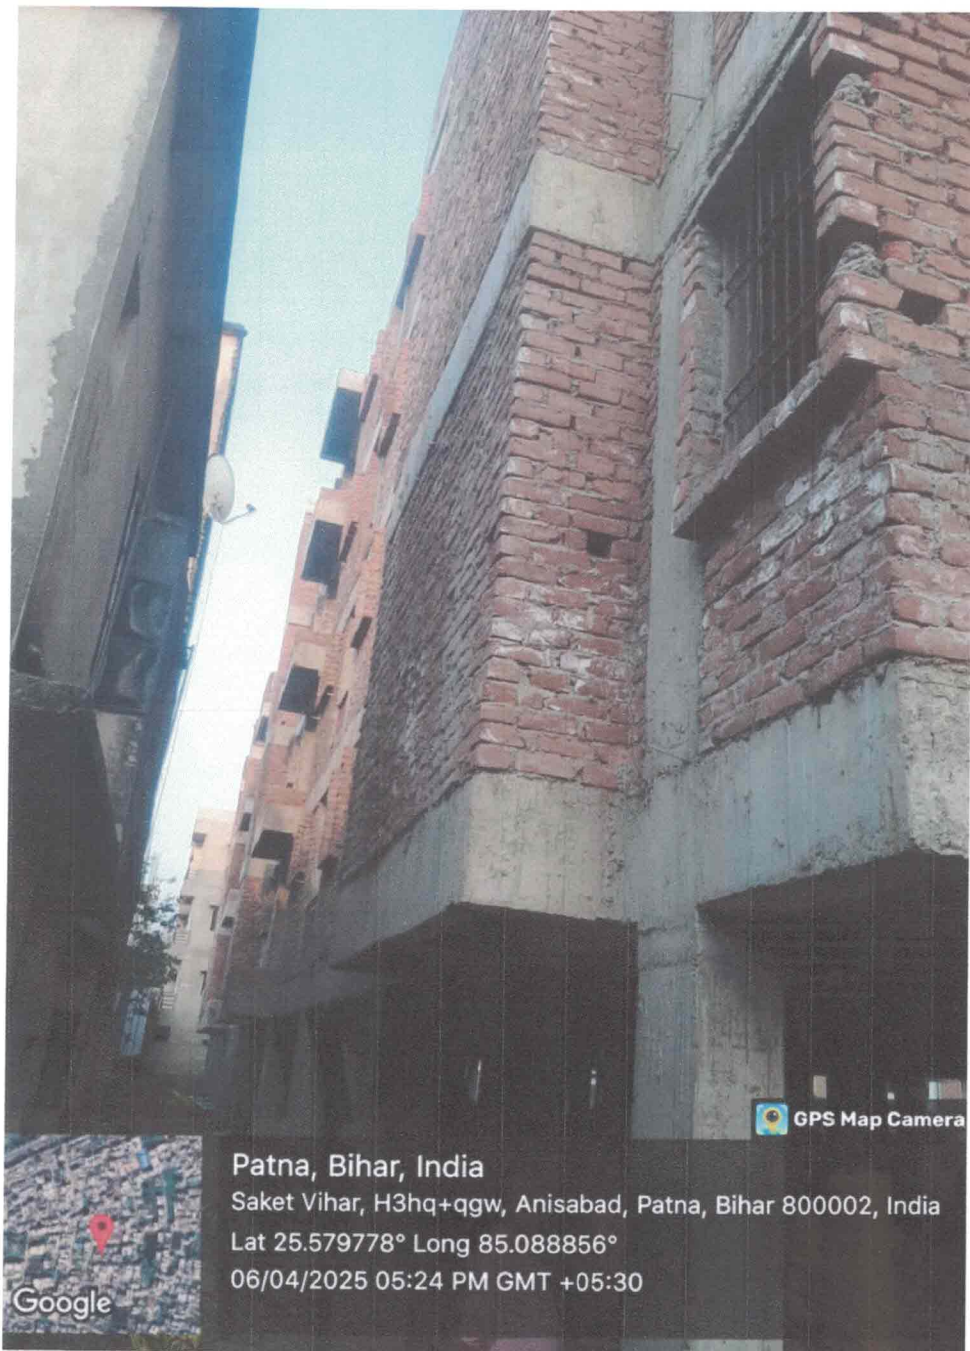



ARCADIA HOMES
Amfcland
PARTNER
