

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	F000115/2018	Name of Firm	ARCADIA HOMES
Firm Address :	HOUSE NO. -422, SAKET VIHAR, MITRA MANDAL COLONY, ANISABAD, PATNA-800002		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP93535-002/160/R-1632/2024	Name of Project/Phase of Registered Project	J B ENCLAVE
Name of Promoter	ARCADIA HOMES	Project Address	SAKET VIHAR, M.M COLONY, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	22/06/2028		
Starting date of Project or Phase of the Project	05/01/2024		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	5 YEARS		

Amib Kumar

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-11	Total Number of Apartments in Landowner's share - FALT-09
	1. 1 BHK	11 09		20	1. Booked / Allotted -NIL	3. Booked/ Allotted-NIL
	2. 2 BHK, -				2. Sold-NIL	Sold -NIL
	3. 3 BHK					
	4. Shop					
	5. Bungalow					
	6. Plot etc.				Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- NIL
	20	2. Sold	- NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)


S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

Anup Kumar

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____ (To be filled for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	0%	
6.	Slabs of Super Structure	70%	30-07-2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	31-06-2026 31-08-2026 01-03-2027 31-05-2027
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	31-09-2027 30-03-2028
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	31-05-2025 3-10-2025 10-11-2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	03-03-2027 28-02-2027 31-10-2025 25-10-2025



11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	31-03-2028
		100%	
		0%	10-12-2027
		0%	31-01-2028
		0%	10-11-2027
		0%	03-03-2028
	Any other activities	0%	05-04-2028

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	31-03-2028
2.	Water Supply	YES	0%	31-10-2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31-12-2027
4.	Storm Water Drains	YES	0%	06-01-2028
5.	Landscaping & Tree Planting	YES	0%	30-04-2028
6.	Street Lighting	YES	0%	01-04-2028
7.	Community Buildings	NO		

Amr Kumar

8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	28-02-2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	04-04-2028
11.	Energy Management	YES	0%	02-03-2028
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

Anup Kumar

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	327102000000224
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project.	
5.	Amount received during the Quarter	41,10,000=00
6.	Actual Cost Incurred during the Quarter	47,10,269=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project till date	75,48,428=00
9.	Cumulative fund collected till the end of Quarter in question	76,95,000=00
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED	



Anup Kumar

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		



XIV UNITS ALLOCATION DETAILS			
Total Number of sanctioned apartments 1 BHK- 2 BHK -11 3 BHK-09 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc N/A
	FLAT NO.	FLAT TYPE	
	305	3 BHK	
	105	3 BHK	
	201	3 BHK	
	202	2 BHK	
	306	3 BHK	
XV. BROCHURE /Prospectus			
XVI Grievance Redressal Officer			
Name : ANUP KUMAR			
Contact No : 9430906829			
Email id : arcadiahomes0612@gmail.com			
Address : HOUSE NO-22,SAKET VIHAR MITRA MANDAL COLONY,PHULWARI PATNA			

Anup Kumar

J-B Enclave

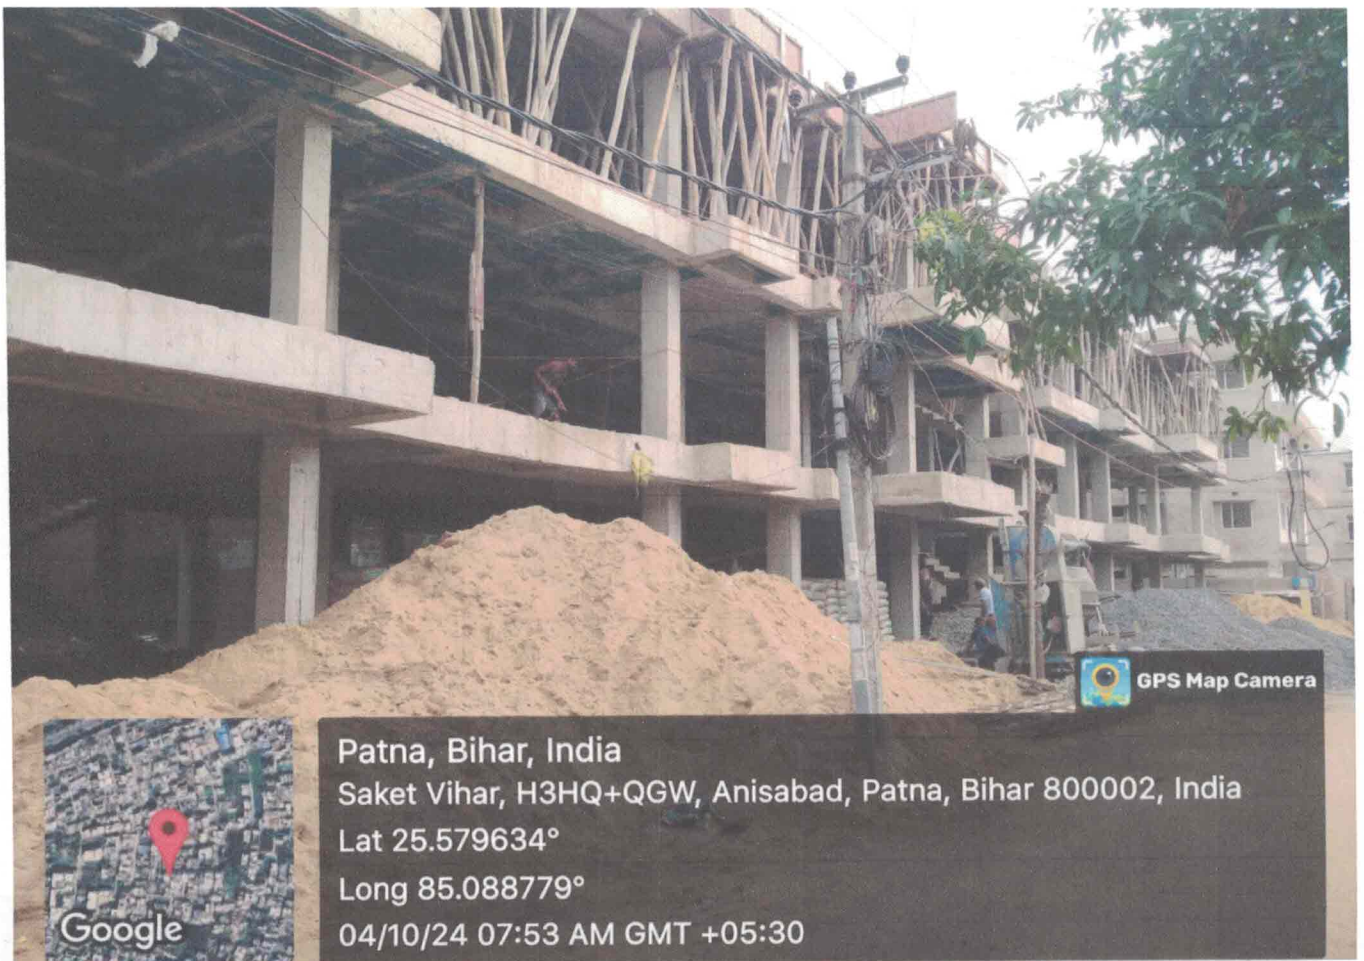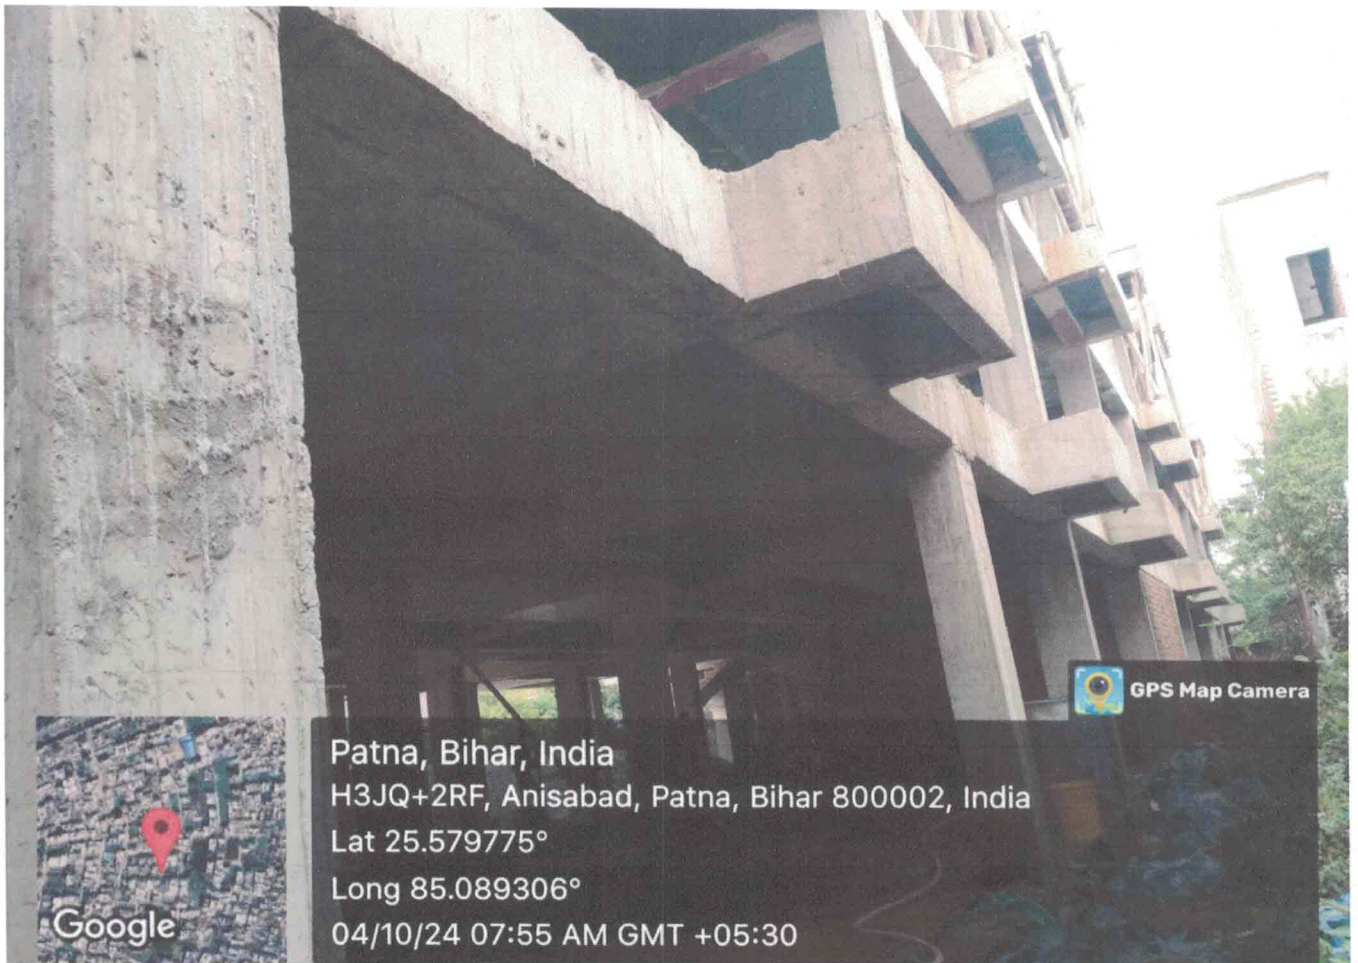

Anup Kumar

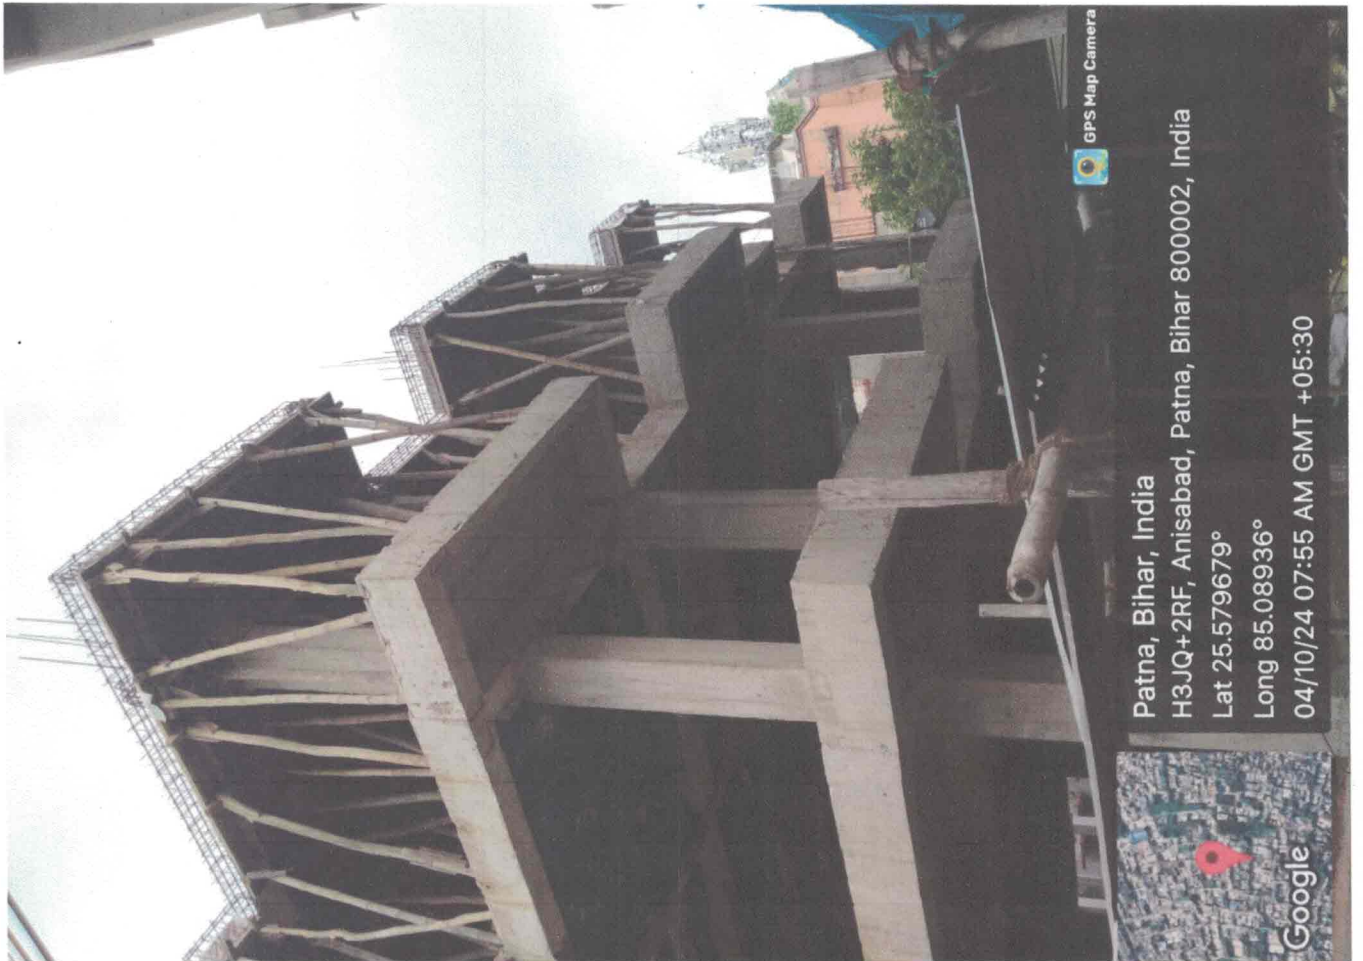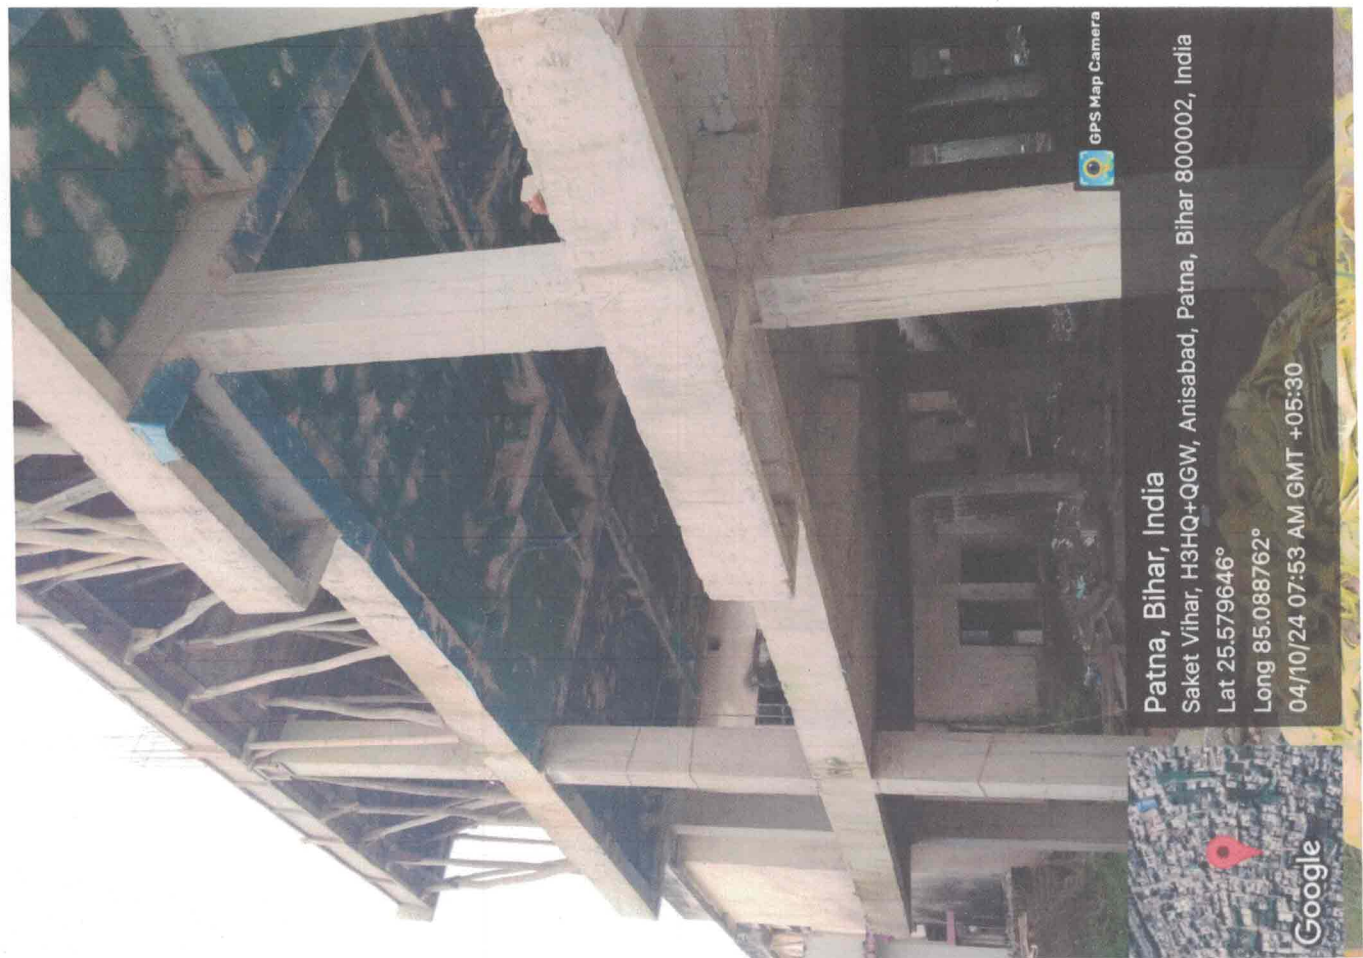

Anup Kumar
