

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies		Name of Firm	SHARDE CONSTRUCTION
Firm Address :	SHRI RAMCHANDRA NIWAS, ASHIYANA, FRIENDS COLONY, PATNA		
Total Experience of promoter in Real Estate sector	03 YEARS		
Total Experience in Real Estate after Implementation of RERA	03 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	N/A	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	N/A	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP01527-1/17/R-1540/2023	Name of Project/Phase of Registered Project	CHANDA ENCLAVE
Name of Promoter	SHARDE CONSTRUCTION	Project Address	KHAT ANO.- 214, 221, PLOT NO.- 972, 973, MAUZA-DANAPUR SHAHJADPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/12/2027		
Starting date of Project or Phase of the Project	10/03/2023		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	5 YEARS		



III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	1. 1 BHK			23	1. Booked / Allotted -04	3. Booked/ Allotted-NIL
	2. 2 BHK, -				2. Sold-NIL	Sold -NIL
	3. 3 BHK				Percentage of booking 33%	Percentage of booking 0%
	4. Shop					
	5. Bungalow					
	6. Plot etc.					

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 04
	23	2. Sold	- NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____ (To beaded for each Building / Wing)

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	N/A

Abhinav

2.	Basements (if any)	NO	N/A
3.	Podiums (if any)	NO	N/A
4.	Plinth	100%	31-12-2024
5.	Stilt Floor	90%	31-12-2024
6.	Slabs of Super Structure	100%	31-12-2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	70%	31-12-2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	30%	31-12-2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	55%	31-12-2024
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	25%	31-12-2024
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	10%	31-12-2024

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

Abhinav

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	50%	31-12-2024
2.	Water Supply	YES	50%	31-12-2024
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	25%	31-12-2024
4.	Storm Water Drains	YES	10%	31-12-2024
5.	Landscaping & Tree Planting	YES	0%	31-12-2024
6.	Street Lighting	YES	0%	31-12-2024
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	31-12-2024
13.	Closed Parking	YES	90%	31-12-2024
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	10%	31-12-2024
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

Abhinav

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT

Abhim

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	439005000694
2.	Estimated Cost of the Project including land cost at the start of the Project	3,00,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	16,00,000=00
6.	Actual Cost Incurred during the Quarter	35,00,000=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project till date	1,55,00,000=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	

Abhinav

1.	Sale Deed	NIL
2.	Agreement for Sale	04
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



Signature of Promoter

Name: Abhinav Pr.

Date:



GPS Map Camera

Check In


Patna, Bihar, India

J3F6+X9X, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur,
Bihar 801503, India

Lat 25.62494°

Long 85.060925°

08/07/24 10:14 AM GMT +05:30

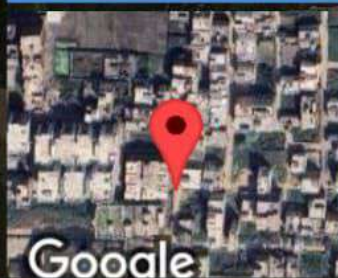

Goole



GPS Map Camera

Check In


Patna, Bihar, India

J3F6+V5F, Chankyapuri Gali, near PRACHIN HANUMAN MANDIR, Danapur
Nizammat, Vivek Vihar Colony, SAINIK COLONY, Patna, Danapur, Bihar 801503,
India

Lat 25.624706°

Long 85.0605°


08/07/24 10:16 AM GMT +05:30

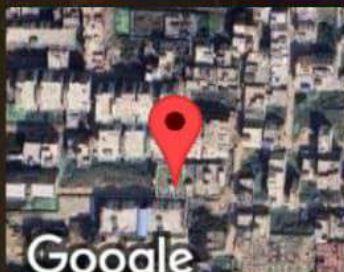



GPS Map Camera

Check In

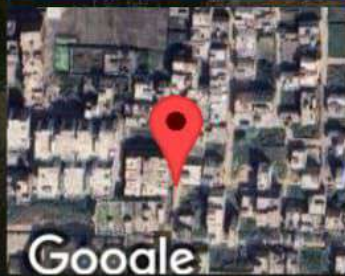

Goole

Patna, Bihar, India

J3F6+X9X, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur,
Bihar 801503, India

Lat 25.62494°

Long 85.060925°

08/07/24 10:14 AM GMT +05:30



GPS Map Camera

Check In


Patna, Bihar, India

J3F6+X9X, Vivek Vihar Colony, Danapur Nizamat, Patna, Danapur,
Bihar 801503, India

Lat 25.624934°

Long 85.060922°

08/07/24 10:13 AM GMT +05:30

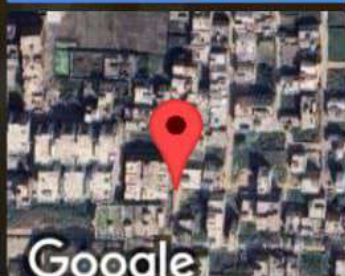

Goole
