



SHREE OM SAI & SATYARISHI

Ref.....

Date..14/10/2024.....

Quarterly Progress Report for quarter ending September of 2024.

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	Partnership Deed No. : 22	Name of Firm	SHREE OM SAI AND SATYARISHI
Firm Address:	Flat No. 101/102, Sai R. J. Kutir, R. K. Puram, Danapur-Khagaul Road, Patna-801503.		
Total Experience of promoter in Real Estate sector	10 + Years of Experience in Real Estate Sector		
Total Experience in Real Estate After Implementation of RERA	7 Years		
No of Project done Before Implementation of RERA	1. Residential	3 Nos.	
No of Project done After Implementation of RERA	1. Residential 2. Residential-cum Commercial	2 Nos. 1 No.	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP84615-1/51/R-1165/2021	Name of Project/Phase of Registered Project	SAI CREATIVE ENCLAVE
Name of Promoter	SHREE OM SAI AND SATYARISHI	Project Address	Near School Of Creative Learning, Nargadda, Danapur-Shivala Main Road, Danapur, Patna.
Name of Co-promoter			
Project Registration is valid up to	05.03.2026		
Starting date of Project or Phase of the Project	05.04.2021		
Type of Project or Phase of the Project	Mixed Development (Residential And Commercial)		
Period of validity of map by the Competent Authority	3 Years		

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER

AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments 391 Nos.	Total Number of Apartments in Promoter's Share - 233 Nos.	Total Number of Apartments in Landowner Share - 158 Nos.
					1. Booked/ Allotted - 82 Nos.	2. Booked/ Allotted - N/A.
4	1. 1 BHK -	110 Nos.	43,339.20		2. Sold - NIL	2. Sold - NIL
	2. 2 BHK -	154 Nos.	1,14,488.00			
	3. 3 BHK -	120 Nos.	1,17,619.50			
	4. SHOP -	07 Nos.	25,308.50			
					Percentage of Booking - 35%	Percentage of Booking - N/A

IV. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES

Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	69 Nos.
4	281	2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport				
5.	Other Approval (s), if any, required for the Project.				

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER



AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

VI. (A) Construction Progress of the Project for Block 'A'Plan Case No. PMAA/PCRN/^{IAMSAUT}SHAHNUPUR /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	90%	31.12.2025
3.	Podiums (if any)	70%	31.12.2025
4.	Plinth	100%	Completed
5.	Stilt Floor	100%	Completed
6.	Slabs of Super Structure	95%	31.10.2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	75%	30.06.2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	27%	30.06.2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	20%	30.06.2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	31.12.2025
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.	0%	31.12.2025
	Any other activities.		

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER



Amit Kumar
AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDHD, GOVERNMENT OF BIHAR

VI. (B) Construction Progress of the Project for Block 'B'

1. Plan Case No. PMAA/PCRN/^{JAMSAIT}_{SHAHIPUR} /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	90%	31.03.2026
3.	Podiums (if any)	70%	31.03.2026
4.	Plinth	100%	Completed
5.	Stilt Floor	100%	31.03.2026
6.	Slabs of Super Structure	15%	30.04.2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	0%	31.03.2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	31.03.2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	31.03.2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	31.03.2026
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%	31.03.2026

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER



Amir
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

VI. (C) Construction Progress of the Project for Block 'C'

2. Plan Case No. PMAA/PCRN/ JAMSAIT
SHAHIPUR /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	100%	Completed
3.	Podiums (if any)	90%	31.03.2025
4.	Plinth	100%	Completed
5.	Stilt Floor	100%	Completed
6.	Slabs of Super Structure	98%	31.10.2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	80%	31.10.2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	30%	30.06.2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	25%	30.06.2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	30.06.2025
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.	0%	30.06.2025
	Any other activities.		

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER



Auth
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

VI. (D) Construction Progress of the Project for Block 'D'

 3. Plan Case No. PMAA/PCRN/ JAMSAUIT
SHAHNUPUR /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	60%	31.03.2026
2.	Basements (if any)	10%	31.03.2026
3.	Podiums (if any)	0%	31.03.2026
4.	Plinth	0%	31.03.2026
5.	Stilt Floor	0%	31.03.2026
6.	Slabs of Super Structure	0%	31.03.2026
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	0%	31.03.2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	31.03.2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	31.03.2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	31.03.2026
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%	31.03.2026

 SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER


 AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514

UDHD, GOVERNMENT OF BIHAR

VII. Amenities and Common Area and External Infrastructure Development Works

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	85%	30.06.2025
2.	Water Supply	NO	N/A	N/A
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31.03.2026
4.	Storm Water Drains	YES	0%	31.03.2026
5.	Landscaping & Tree Planting	YES	10%	31.03.2026
6.	Street Lighting	YES	0%	31.03.2026
7.	Community Buildings	YES	0%	31.03.2026
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	31.03.2026
9.	Solid Waste Management & Disposal	YES	0%	31.03.2026
10.	Water Conservation/RainWater Harvesting	YES	0%	31.03.2026
11.	Energy Management	NO	N/A	31.03.2026
12.	Fire Protection and Fire Safety Requirements	YES	0%	31.03.2026
13.	Closed Parking	YES	0%	31.03.2026
14.	Open Parking	NO	N/A	31.03.2026
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	31.03.2026
16.	Others (Option to AddMore)			

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

[Signature]
PARTNER



[Signature]
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

	PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As On date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths		
2.	Water Supply		
3.	Sewerage Chambers Septic Tank		
4.	Drains		
5.	Parks, Land Scaping and Tree Planting		
6.	Street Lighting		
7.	Disposal of sewage & Sullage water		
8.	Water conservation/Rain Water Harvesting		
9.	Energy Management		

IX. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT.

(A)	S. No.	Particulars	
	1.	Front Elevation.	Attached
	2.	Rear Elevation	Attached
	3.	Side Elevation	Attached
(B)		Photograph of each floor	Attached

X. Financial Progress of the Project

S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	41957771403
2.	Estimated Cost of the Project including land cost at the start of the Quarter	5848.00 LAKH
3.	Estimated Development Cost the Project at the start of the Project. (Excluding Land Cost)	4900.00 LAKH
4.	Any Variation in Development Cost which is declared at the start of the Project.	0.00
5.	Amount received during the Quarter	3,07,26,751.80
6.	Actual Cost Incurred during the Quarter	3,05,20,700.88
7.	Net amount at end of the Quarter	1,73,200.92
8.	Total expenditure on Project till date	28,11,62,345.87
9.	Cumulative fund collected till the end of Quarter in question	35,40,08,734.96
10.	Cumulative expenditure done till the end of Quarter in question	28,11,62,345.87

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER



Amit Kumar
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

Registered Mortgage-Khata No.- 332, 263, 390, 322, 342, Survey Plot No.- 1253, 1533, 1548, 1549, 1550, 1551, 1553, 1554, 1555, 1556 (P), Tauzi No. 5468, Plot Area - 93.34 decimal from SBI, SME Dakbunglow Branch.

Total Sanction Amount 5 Cr., in which 0.00 Cr. disbursed within qtr.

XII. MISCELLANEOUS

A	List of Legal Cases (if any) - On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases / PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NOT YET
2.	Agreement for Sale	4

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE


[Signature]
PARTNER



[Signature]
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

XII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

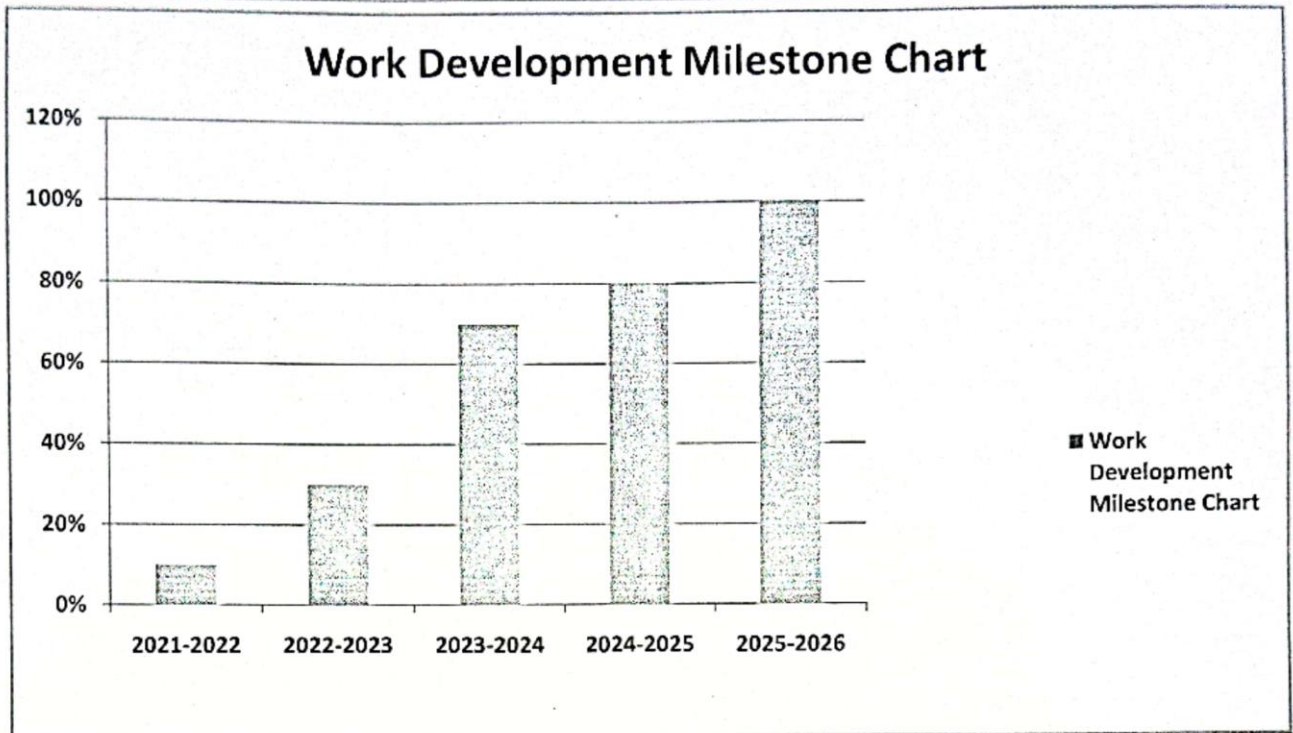

Project is in progress as per time schedule.

The registration is valid for a period of 5 years commencing from 05.04.2021 and ending with 05.03.2026.

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

PARTNER




Signature of Promoter

Name : Amitesh Arun

Date : 14.10.2024



Amit
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR



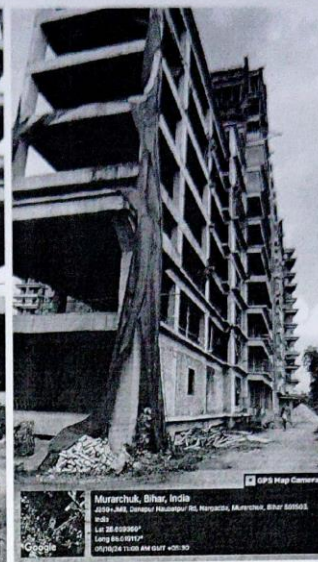
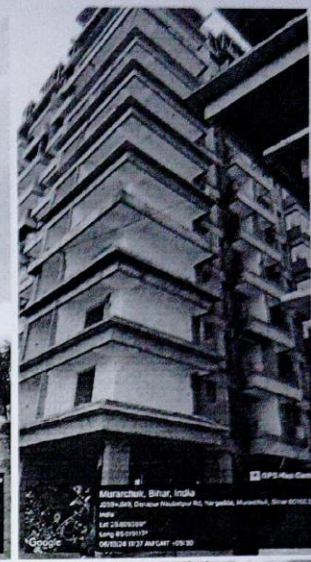



SHREE OM SAT & SATYAKISHI
SAI CREATIVE ENCLAVE

PARTNER



AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

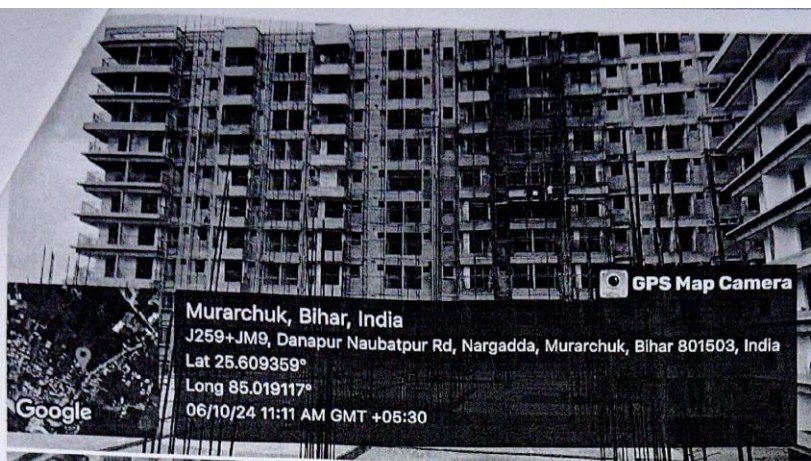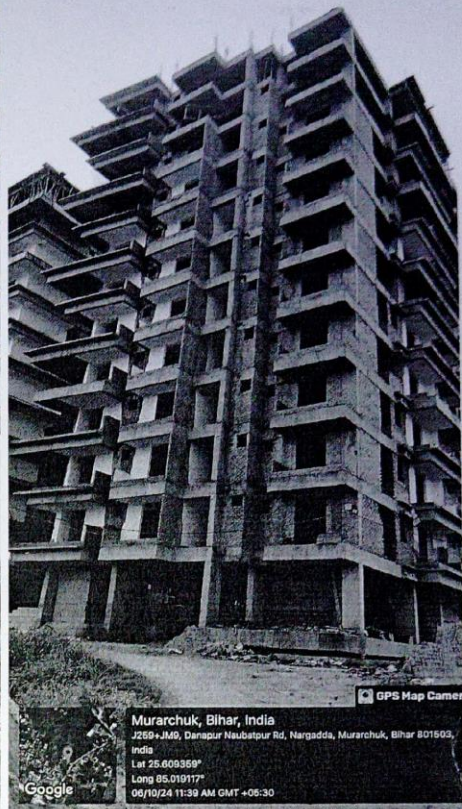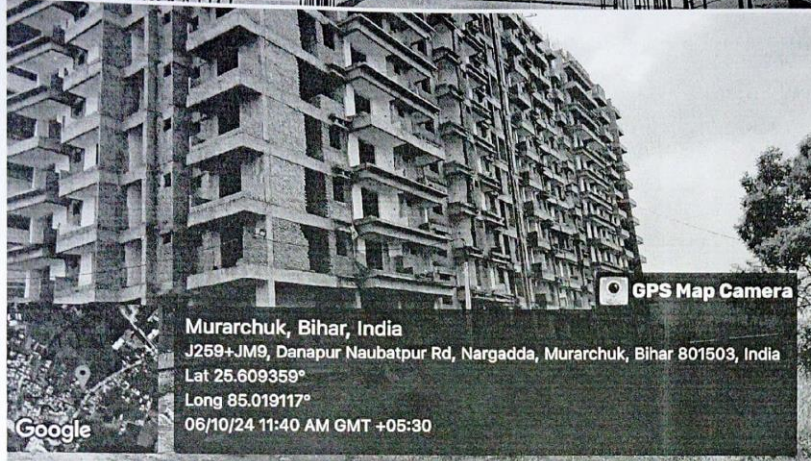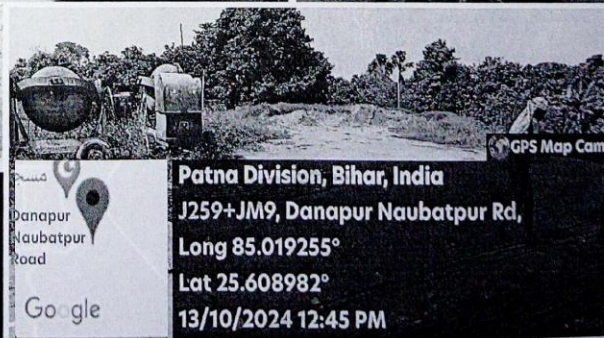

SHREE OM SAI & SATYARISHI-
SAI CREATIVE ENCLAVE

Amit
PARTNER



Amit
AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

FORM NO. 1
[See Regulation 3]

ARCHITECT'S CERTIFICATE
(To be submitted at the time of Registration of Ongoing Project and for withdrawal of
Money from Designated Account)

Date: 14/10/2024

To,
M/s Shree Om Sai And Satyarishi,
R. J. Sai Kurir, R. K. Puram, Khagaul –Danapur Road,
Saguna More, Patna-801503.

Subject: Certificate of Percentage of Work executed in the project

Having project, Sai Creative Enclave, No. of Building(s) 4 Wing(s) of the Phase-1, bearing the Bihar RERA registration No. BRERAP84615-1/51/R-1165/2021 and being developed on the plot bearing CS No.____ Khata No.- 332, 263, 390, 322, 342, Survey Plot No.- 1253, 1533, 1548, 1549, 1550, 1551, 1553, 1554, 1555, 1556 (P) demarcated by its boundaries (latitude and longitude of the end points) of the land 25.612677 & 85.158875 situated in Nargada, Usri, Village-Jamsaut, Block- Danapur, Division- Danapur, District- Patna, PIN -801503. Admeasuring - 9637.70 sq.mts. area being developed by the promoter Shree Om Sai And Satyarishi.

Sir,

I, We Ar. Amit Kumar have undertaken assignment as Architect / Licensed Surveyor of certifying Percentage of execution of Work of the Project, Sai Creative Enclave Building(s) 4 Wing(s) of the 1 Phase of the Project, Situated on the plot bearing C.S. No. / Survey Plot No. 1253, 1533, 1548, 1549, 1550, 1551, 1553, 1554, 1555, 1556 (P) of Village- Jamsaut, Block- Danapur, Division-Danapur, District- Patna, PIN- 801503, admeasuring 9637.70 sq.mts. area being developed by the promoter Shree Om Sai And Satyarishi.

1. Following technical professionals are appointed by Owner / Promoter :-

- (i) M/s /Shri/Smt. Amit Kumar as L.S. / Architect;
- (ii) M/s /Shri/Smt Brajesh Kumar as Structural Consultant
- (iii) M/s /Shri/Smt. Amit Kumar as Mechanical/Electrical/Plumbing Consultant (MEP)
- (iv) M/s/Shri/Smt. Er. Santosh Kumar as Site Supervisor

Based on site Inspection, with respect to reach of the Building/ Wing of the aforesaid Real Estate Project, I certify that as on the date of this certificate, the Percentage of Work done for each of the building/Wing of the Real Estate Project as registered vide number BRERAP84615-1/51/R-1165/2021 Under Bihar RERA is as per table A herein below. The percentage of the work executed with respect to each of the activity of the entire phase is detailed in Table B.


AMIT KUMAR
ARCHITECT
EMPANELMENT NO.
CA/1999/25514
UDHD, GOVERNMENT OF BIHAR

Table A

Building / Wing Number 4 (to be prepared separately for each Building/Wing of the Project)

I. (A) Construction Progress of the Project for Block 'A'		
1. Plan Case No. PMAA/PCRN/ <small>JAMSAUT SHAHPUR</small> /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	90%
3.	Podiums (if any)	70%
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	95%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	75%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	27%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	20%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	10%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%


AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDHD, GOVERNMENT OF BIHAR

V. (B) Construction Progress of the Project for Block 'B'		
1. Plan Case No. PMAA/PCRN/ <small>JAMSAUT SHAHPUR</small> /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	90%
3.	Podiums (if any)	70%
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	15%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	0%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%
11.	<p>Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.</p> <p>Any other activities.</p>	0%


AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDDH. GOVERNMENT OF BIHAR

V. (C) Construction Progress of the Project for Block 'C'		
1. Plan Case No. PMAA/PCRN/ <small>JAMSAUT SHAHPUR</small> /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	90%
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	98%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	80%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	30%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	25%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%


AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDHO, GOVERNMENT OF BIHAR

V. (D) Construction Progress of the Project for Block 'D'		
1. Plan Case No. PMAA/PCRN/ <small>JAMSAUT SHAHPUR</small> /BLOCK-A, B, C- B+G+11, BLOCK-D- G+04/50/2020 (To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	60%
2.	Basements (if any)	10%
3.	Podiums (if any)	0%
4.	Plinth	0%
5.	Stilt Floor	0%
6.	Slabs of Super Structure	0%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	0%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%


AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDHD, GOVERNMENT OF BIHAR

TABLE-B**Internal and External Development Work in respect of the entire Registered Phase.**

VI. Amenities and Common Area and External Infrastructure Development Works				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy)
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	85%	30.06.2025
2.	Water Supply	NO	N/A	N/A
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	31.03.2026
4.	Storm Water Drains	YES	0%	31.03.2026
5.	Landscaping & Tree Planting	YES	10%	31.03.2026
6.	Street Lighting	YES	0%	31.03.2026
7.	Community Buildings	YES	0%	31.03.2026
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	31.03.2026
9.	Solid Waste Management & Disposal	YES	0%	31.03.2026
10.	Water Conservation/Rain Water Harvesting	YES	0%	31.03.2026
11.	Energy Management	NO	N/A	31.03.2026
12.	Fire Protection and Fire Safety Requirements	YES	0%	31.03.2026
13.	Closed Parking	YES	0%	31.03.2026
14.	Open Parking	NO	N/A	31.03.2026
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	31.03.2026
16.	Others (Option to Add More)			

Yours Faithfully,


AMIT KUMAR
 ARCHITECT
 EMPANELMENT NO.
 CA/1999/25514
 UDHD, GOVERNMENT OF BIHAR

Signature & Name (IN BLOCK LETTERS) of L.S./Architect

(Registration No./license No.....)
