



30/09/2024

To,

The Chairman,

Real Estate Regulatory Authority,

6th Floor Bihar State Building Construction Corporation Campus.

Hospital Road, Shastri Nagar Patna – 800023

Sub :- QPR 2ND Qtr JULY-24 TO SEPT-24 (PARAM ANAND RESIDENCY)

Sir,

In the light of Bihar Rera Regulations (Amendment) 2022 notification. QPR for the 2ND quarter of F.Y 2024-25 IN RESPECT OF OUR PROJECT PARAM ANAND RESIDENCY located at Sona Goplapur Patna, Khesra / Plot No.-552,553,Khata No.-392,477, Thana No.-124,Mauza-Sona Gopalpur Patna is enclosed in the prescribed format as following annexure.

1	QPR QUARTER 2 ND F/Y 2024-25	ANNEXURE –A
2	Architect's Certificate	ANNEXURE –B
3	Engineer's Certificate	ANNEXURE -C
4	Chartered Accountant Certificate	ANNEXURE -D
5	FIRE N.O.C	ANNEXURE -E
6	Patna Metropolitan Area Authority Map Approval Letter.	ANNEXURE -F

For VIBHAS BUILDTECH INDIA PVT LTD.

DIRECTOR



FORM-7[REGULATION-9]

Quarterly progress report for quarter ending Sept of 2024(year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45201JH2018PTC011799	Name of Firm	VIBHAS BUILDTECH INDIA PVT.LTD.
Firm Address:	4 TH FLOOR, HIRA ENCLAVE, NEW DAKBANGLOW ROAD,PATNA-800001		
Total Experience of promoter in Real Estate sector	10 YEARS		
Total Experience in Real Estate After Implementation of RERA	5 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP33236- 3/207/R-1507/2022	Name of Project/Phase of Registered Project	PARAM ANAND RESIDENCY
Name of Promoter	VIBHAS BUILDTECH INDIA PVT. LTD.	Project Address	Sona Goplapur Patna,Khesra / Plot No.-552,553, Khata No.-392,477, Thana No.-124, Mauza-Sona Gopalpur
Name of Co-promoter			
Project Registration Is valid upto	15-07-2027		
Starting date of Project or Phase Of the Project	27-12-2022		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential- cum-Commercial 4.Plottedproject	RESIDENTIAL	
Period of validity of map by the Competent Authority	18-10-2027		

For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS						
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 12	Total Number of Apartments in Landowner's share -12
BLOCK-A	1. 1BHK 2. 2BHK,- 3. 3BHK 4. Shop 5. Bungalow - 6. Plot etc.	24	22824	24	1. Booked-3 /Allotted-1 2. Sold-0 Percentage of booking- 33%	3. Booked-0/ Allotted-0 Sold - Percentage of booking

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS						
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 18	Total Number of Apartments in Landowner's share -17
BLOCK-B	1. 1BHK 2. 2BHK,- 3. 3BHK 4. Shop 5. Bungalow - 6. Plot etc.	35	24094		1. Booked-3 /Allotted-1 2. Sold-0 Percentage of booking- 22%	3. Booked-0/ Allotted-0 Sold -0 Percentage of booking

IV. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES				
Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:		
		1. Booked/Allotted	-	3 / 1
BLOCK-A	25	2. Sold	-	

IV. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES				
Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:		
		1. Booked/Allotted	-	3 / 1
BLOCK-B	35	2. Sold	-	

V. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	Office of the state fire officer-cum-director, Patna	--	27/06/2022	ANNEXURE-E
3.	Water Supply Permission	Will Apply			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	PMAA, Patna (Map Approval)	--	25/10/2022	ANNEXURE-F

For VIBHAS BUILDTech INDIA PVT. LTD.

DIRECTOR

**VI. CONSTRUCTION PROGRESS OF THE PROJECT
BLOCK-B**

1. Plan Case No. _____ (To be added for each Building/Wing)

S.No. (1)	Tasks/Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation(if any)	100%	
2.	Basements(if any)	60% (Work stopped due to water lodging and inconvenience in material supply)	15/11/2024
3.	Podiums(if any)	-----	
4.	Plinth	Not Started	25/11/2024
5.	Stilt Floor	Not Started	25/01/2025
6.	Slabs of Super Structure	Not Started	16/04/2026
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	Not Started	30/06/2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Not Started	30/10/2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	Not Started	30/12/2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	Not Started	30/12/2026
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas Appurtenant to Building/Wing, Compound Wall and all other	Not Started	30/04/2027

For VIBHAS BUILDTech INDIA PVT. LTD.

 **DIRECTOR**

	requirements as me be required to complete project as per Specifications in Agreement of Sale.		
	Any other activities.		

VII. CONSTRUCTION PROGRESS OF THE PROJECT **BLOCK-A**

1. Plan Case No. _____ (To be added for each Building/Wing)

S.No. (1)	Tasks/Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation(ifany)	Not Started	16/01/2025
2.	Basements(ifany)	Not Started	16/03/2025
3.	Podiums(ifany)	-----	
4.	Plinth	Not Started	16/04/2025
5.	StiltFloor	Not Started	30/04/2025
6.	Slabs of Super Structure	Not Started	16/04/2026
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	Not Started	16/06/2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Not Started	16/08/2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	Not Started	30/10/2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	Not Started	30/11/2026

For VIBHAS BUILDTECH INDIA PVT LTD.

 **DIRECTOR**

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas Appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	Not Started	30/04/2027
	Any other activities.		

VIII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed(Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Foot paths	YES	0%	30/04/2027
2.	Water Supply	YES	0%	30/04/2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30/04/2027
4.	Storm Water Drains	YES	0%	30/04/2027
5.	Landscaping & Tree Planting	YES	0%	30/04/2027
6.	Street Lighting	YES	0%	30/04/2027

For VIBHAS BUILDTECH INDIA PVT LTD.


 DIRECTOR

7.	Community Buildings	NO	0%	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	0%	
9.	Solid Waste Management & Disposal	NO	0%	
10.	Water Conservation/Rain Water Harvesting	YES	0%	30/04/2027
11.	Energy Management	NO	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	30/04/2027
13.	Closed Parking	YES	0%	30/04/2027
14.	Open Parking	NO	0%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	30/04/2027
16.	Others(Option to Add More)	NO	0%	

IX. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As On date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			

For VIBHAS BUILDTECH INDIA PVT. LTD.



DIRECTOR

5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR

X. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr.No.		
	1.	Front Elevation	
	2.	Rear Elevation	
	3.	Side Elevation	
(B)		Photograph of each floor	

XI. FINANCIAL PROGRESS OF THE PROJECT		
S.No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	41417290770
2.	Estimated Cost of the Project including land cost at the start of the Project	9,27,50,000/-
3.	Estimated Development Cost of the Project at the Start of the Project.(Excluding Land Cost)	9,00,00,000/-
4.	Any Variation in Development Cost which is declared at the start of the Project.	NO
5.	Amount received during the Quarter	5,01,000/-
6.	Actual Cost Incurred during the Quarter	2,20,173/-
7.	Net amount at end of the Quarter	2,93,702.42/-
8.	Total expenditure on Project till date (INCLUDING LAND COST -RS.27,50,000/-)	1,67,64,955/-
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XII. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED	

For VIBHAS BUILDTECH INDIA PVT LTD.

 **DIRECTOR**

XIII.MISCELLANEOUS

A	List of Legal Cases(if any)-On Project/Promoter	
1.	Case No.	N/A
2.	Name of Parties	N/A
3.	No of Execution Cases against this project Case No. Name of Parties	
4.	No of Suo-Moto cases against this project Case No. Name of Parties	
5.	No of Certificate cases/PDR cases against this project Case No. Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	N/A
2.	Agreement for Sale	N/A
3.	No. of possessions given to allottees	

XIII.PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

For VIBHAS BUILDTECH INDIA PVT LT

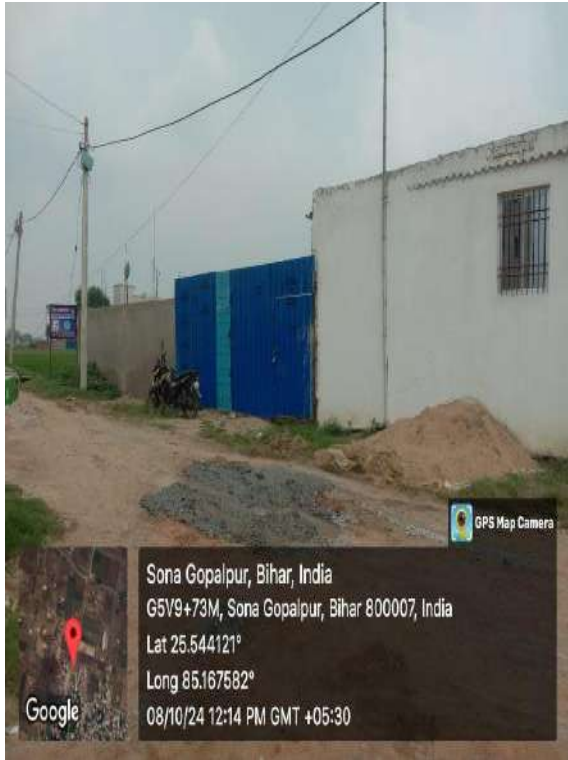
 DIRECTOR

Signature of Promoter

Name:

Date:

PARAM ANAND RESIDENCY
PHOTO 2ND QTR SEP_2024



For VIBHAS BUILDTech INDIA PVT. LTD.


DIRECTOR



For VIBHAS BUILDTech INDIA PVT. LTD.

DIRECTOR

ARCHITECT'S CERTIFICATE

Date -30.09.2024

To,

Vibhas Buildtech India Pvt. Ltd.

Office Address – 403 Heera Enclave,

New Dakbanglow Road, Patna - 800001

Subject: Certificate of Percentage of Construction work of the project **PARAM ANAND RESIDENCY** having (Bihar RERA Registration Number **BRERAP33236-3/207/R-1507/2022** situated on the plot No.- 552, 553, Khata No – 392, 477, Thana No. 124, Mauza – Sona Gopalpur, demarcated by its boundaries (latitude and longitude of the end points), District – Patna, Admeasuring **2145sq.mts.** Area being developed by **Vibhas Buildtech India Pvt. Ltd.**

Sir,

I **Uma Shankar Kumr** have undertaken assignments Architect/Licensed of certifying percentage of completion of construction work of the project situated on the plot No.- 552, 553, Khata No – 392, 477, Thana No. 124, Mauza – Sona Gopalpur, demarcated by its boundaries (latitude and longitude of the end points), District – Patna, Admeasuring **2145 sq.mts.** Area being developed by **Vibhas Buildtech India Pvt. Ltd.**

Following technical professionals are appointed by Owner/Promoter:- **Vibhas Buildtech India Pvt. Ltd.**

- (i) Shri Uma Shankar Kumar as L.S./Architect;
- (ii) Shri Sushil Kumar as Structural Consultant
- (iii) Shri Jitendra Kumar as a Mechanical /
/Electrical/Plumbing Consultant(MEP)
- (iv) Shri Ravi Kumar as Site Supervisor

Based on Site Inspection, with respect to each of the Building/Wing of the aforesaid Real Estate Project, I certify that as on the date of this certificate, the Percentage of Work done for each of the building/Wing of the Real Estate Project as registered vide number **BRERAP33236-3/207/R-1507/2022** under Bihar RERA is as per table A herein below. The percentage of the work executed with respect to each of the activity of the entire project is detailed in Table A & B.


For VIBHAS BUILDTECH INDIA PVT LTD.
DIRECTOR
Yours Faithfully,
AR. Umashankar Kumar
Registered Architect
Reg. No.-CA/2011/54023

**TABLE-A
BLOCK-A**

Sr.No.	Tasks/Activity	Percentage of work done
1	Excavation	0%
2	Number of Basement(s) and Plinth	0%
3	Number of Podiums	0%
4	Stilt Floor	0%
5	Number of Slabs of Super Structure	0%
6	Internal Walls, Internal Plaster, Floorings with in Flats/Premises, Door and Windows To each of the Flat/Premises.	0%
7	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises.	0%
8	Staircases, Lifts Wells and Lobbies at each Floor level connecting Staircases and Lifts, Over head and Underground Water Tanks.	0%
9	The external plumbing and external plaster, elevation, completion of terraces with Water proofing of the Building/Wing.	0%
10	Installation of lifts, water pumps, Fire Fighting Fittings and Equipment as per NOC from the concerned department, Electrical fittings to common Areas, electro, mechanical equipment, Compliance to conditions of environment/CRZNOC, finishing to entrance lobby/s, plinth protection, paving fares appurtenant to Building/Wing, Compound Wall and all other requirement may be required to Obtain Occupation/Completion Certificate.	0%

For VIBHAS BUILDTech INDIA PVT LTD.



DIRECTOR


Yours Faithfully, 
AR. Umashankar Kumar
Registered Architect
Reg. No.-CA/2011/54023


**TABLE-A
BLOCK -B**

Sr.No.	Tasks/Activity	Percentage of work done
1	Excavation	100%
2	Number of Basement(s) and Plinth	60%
3	Number of Podiums	0%
4	Stilt Floor	0%
5	Number of Slabs of Super Structure	0%
6	Internal Walls, Internal Plaster, Floorings with in Flats/Premises, Door and Windows To each of the Flat/Premises.	0%
7	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises.	0%
8	Staircases, Lifts Wells and Lobbies at each Floor level connecting Staircases and Lifts, Over head and Underground Water Tanks.	0%
9	The external plumbing and external plaster, elevation, completion of terraces with Water proofing of the Building/Wing.	0%
10	Installation of lifts, water pumps, Fire Fighting Fittings and Equipment as per NOC from the concerned department, Electrical fittings to common Areas, electro, mechanical equipment, Compliance to conditions of environment/CRZ NOC, finishing to entrance lobby/s, plinth protection, paving areas appurtenant to Building/Wing, Compound Wall and all other requirement may be required to Obtain Occupation/Completion Certificate.	0%

For VIBHAS BUILDTECH INDIA PVT LTD.




DIRECTOR


Yours Faithfully,

A.R. Umashankar Kumar
Registered Architect
Reg. No. -CA/2011/54023

TABLE-B

Sr.No.	Common areas and Facilities ,Amenities	Proposed (Yes/No)	Percentageof Workdone	Details
1	Internal Roads &Foot-Paths.	YES	0 %	
2	Water Supply	YES	0%	
3	Sewerage(chamber,lines, Septic Tank, STP)	YES	0 %	
4	Storm Water Drains	YES	0 %	
5	Landscaping & Tree Planting.	YES	0 %	
6	Street Lighting	YES	0 %	
7	Community Buildings	NO	0 %	
8	Treatment and disposal Of sewage and selvage water	NO	0 %	
9	Solid Waste Management & disposal.	YES	0 %	
10	Water conservation,Rain water have sting.	YES	0 %	
11	Energy management	YES	0 %	
12	Fire protection and fire Safety requirements	YES	0%	
13	Electrical meter room, Sub-Station, receiving station.	YES	0 %	
14	Others (Option to Add more).			


 Yours Faithfully, Aft. Umashankar Kumar
 Registered Architect
 Reg. No.-CA/2011/54023

For VIBHAS BUILDTECH INDIA PVT LTD.


 DIRECTOR

ENGINEER'S CERTIFICATE

Date -30.09.2024

To,

Vibhas Buildtech India Pvt. Ltd.

Office Address – 403 Heera Enclave,

New Dakbanglow Road, Patna - 800001

Subject: Certificate of Cost Incurred for Development of **Project PARAM ANAND RESIDENCY** (Bihar RERA Registration Number **BRERAP33236-3/207/R-1507/2022** situated on the plot No.- 552, 553, Khata No – 392, 477, Thana No. 124, Mauza – Sona Gopalpur, demarcated by its boundaries (latitude and longitude of the end points), District- Patna, Admeasuring **2145sq.mts.** Area being developed by **Vibhas Buildtech India Pvt. Ltd.**

Ref: Bihar RERA Registration Number **BRERAP33236-3/207/R-1507/2022**

Sir,

I, **Sushil Kumar**, undertaken assignment of certifying Cost for the Subject Real Estate Project **PARAM ANAND RESIDENCY** registered under RERA, Bihar situated on the plot No.- 552, 553, Khata No- 392, 477, Thana No. 124, Mauza- Sona Gopalpur, demarcated by its boundaries (latitude and longitude of the end points), District- Patna, Admeasuring **2145 sq.mts.** Area being developed by **Vibhas Buildtech India Pvt. Ltd.**


Following technical professionals are appointed by Owner / Promoter :-

- (i) **Shri Uma Shankar Kumar** as L.S. / Architect;
- (ii) **Shri Sushil Kumar** as Structural Consultant
- (iii) **Shri Jitendra Kumar** as MEP Consultant
- (iv) M/s /Shri/Smt. **Ansrul Hasnain** as Quantity Surveyor

2. We have estimated the cost of the completion to obtain Occupation Certificate/ Completion Certificate, of the Civil, MEP and Allied works, of the building(s) of the project. Our estimated cost calculations are based on drawings/plans made available to us for the project under reference by the Developer and Consultants and the assumption of the cost of material, labor and other inputs made by developer, and the site inspection carried out by us.

For VIBHAS BUILDTECH INDIA PVT LTD.

 **DIRECTOR**


SUSHIL KUMAR
Registration No.
BR/UDHD/SE/23-0111
UDHD, Govt. of Bihar

3. We estimate Total Estimated Cost of completion of the building(s) of the aforesaid project under reference as **Rs. 9,00,00,000/-** (Total of Table A and B) . The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for the purpose of obtaining occupation certificate / completion certificate for the building(s) from the PMAA being the planning Authority under whose jurisdiction the aforesaid project is being implemented.
4. The Estimated Cost Incurred till date is calculated at **Rs. 1,40,14,955/-** (Total of Table A and B). the amount of Estimated Cost incurred is calculated on the base of amount of Total Estimated Cost.
5. The Balance cost of Completion of the Civil, MEP and Allied works of the building(s) of the subject project to obtain Occupation Certificate/ Completion Certificate from PMAA (planning Authority) is estimated at **Rs. 7,59,85,045/-** (Total of Table A and B)
6. I certify that the Cost of the Civil, MEP and allied work for the aforesaid Project as completed on the date of this certificate is as given in Table A and B below:

TABLE-A

Sr.No.	Particulars	Amounts
1.	Total Estimated cost of the building/wing as on date of Registration is	Rs. 8,79,00,000/-
2.	Cost incurred as on (Based on the Estimated cost)	Rs. 1,35,14,955/-
3.	Work done in Percentage (As Percentage of the estimated cost)	15.38 % (Material Purchases + Supplier Adv.)
4.	Balance Cost to be Incurred (Based on Estimated Cost)	Rs. 7,43,85,045/-
5.	Cost Incurred on Additional/Extra Items as on _____ not included in the Estimated Cost (Annexure A)	Rs. - 0

TABLE-B

Sr.No.	Particulars	Amounts
1.	Total Estimated cost of the Internal and External Development Works including amenities and Facilities in the layout as on date of Registration is	Rs 21,00,000/-


For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR

2.	Cost incurred as on (Based on the Estimated cost).	Rs. 5,00,000/-
3.	Work done in Percentage (As Percentage of the estimated cost).	23.80 %
4.	Balance Cost to be Incurred (Based on Estimated Cost).	Rs 16,00,000/-
5.	Cost Incurred on Additional/Extra Items as on _____ not included in the Estimated Cost (Annexure A).	N/A

Yours Faithfully,


SUDHAKAR KUMAR
 Registration No.
 BR/UDHD/SE/23-0111
 UDHD, Govt. of Bihar

For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR



Sanjeev Kiran & Associates

Chartered Accountants

FORM- C

(See Regulation 3)

(CHARTERED ACCOUNTANTS CERTIFICATE)

(FOR SUBSEQUENT WITHDRAWAL OF MONEY FOR THE QUARTER ENDED 30Th Sept 2024)

Cost of Real Estate Project Bihar RERA Reg. Number :- BRERAP33236-3/207/R-1507/2022.

PROJECT NAME : PARAM ANAND RESIDENCY

Company Name : Vibhas Buildtech India Pvt. Ltd.

Reg Office: - Bijay Singh, S/o – Baidnath Singh, Gurudwara Road, Jumritilliya Koderma, Jharkhand, India – 825410.

Sr. No.	Particulars		Amount (Rs.)	
			Estimated	Incurred
1(i)	Land Cost :			
	A	Acquisition Cost of Land or Development Rights, lease Premium, lease rent, interest cost incurred or payable on Land Cost and legal cost	27,50,000	27,50,000
	B	Amount of Premium payable to obtain development rights, FSI, additional FSI, fungible area, and any other incentive under DCR from Local Authority or State Government or any Statutory Authority	-	-
	C	Acquisition cost of TDR (if any)		
	D	Amounts payable to State Government or competent authority or any other statutory authority of the State or Central Government, towards stamp duty, transfer charges, registration fees etc; and	-	-
	E	Land Premium payable as per annual statement of rates (ASR) for redevelopment of land owned by public authorities.	(Included in point no. 1(i)(a)	(Included in point no. 1(i)(a)
	F	Under Rehabilitation scheme:		
	(i)	Estimated construction cost of rehab building including site development and infrastructure for the same as certified by Engineer	-	-
	(ii)	Actual Cost of construction of rehab building incurred as per the books of accounts as verified by the CA	-	-
Note : (for total cost of construction incurred, Minimum of (i) or (ii) is to be considered)				



Ground Floor, Shyam Bhawan, S P sinha Path, East Boaring Canal Road, Patna 800 001

e-mail: kirandubey4@gmail.com,

Office : Patna & Delhi



Sanjeev Kiran & Associates

Chartered Accountants

	(iii)	Cost towards clearance of land of all or any encumbrances including cost of removal of legal/illegal occupants, cost for providing temporary transit accommodation or rent in lieu of Transit Accommodation, overhead cost,	-	-
	(iv)	Cost of ASR linked premium, fees, charges and security deposits or maintenance deposit, or any amount whatsoever payable to any authorities towards and in project of rehabilitation.	-	-
		Sub-Total of Land Cost	27,50,000	27,50,000

Note:- Payment of Amount of Rs. 27,50,000/- For Acquisition Cost of Land or Development Rights from Management A/C No-7968559635 (S.B.I)

Sr. No.	Particulars		Amount (Rs.)	
			Estimated	Incurred
1(ii)	Development Cost/ Cost of Construction :			
	A	(i) Estimated Cost of Construction as certified by Engineer. (As per Table- A Rs.8,79,00,000+Table-B Rs.21,00,000)	9,00,00,000/-	NA
		(ii) Actual Cost of construction incurred as per the books of accounts as verified by the CA(Till Date-cumulative)	-	98,63,648/-

Note :(for adding to total cost of construction incurred, Minimum of (i) or (ii) is to be considered)

			Estimated	Incurred
	(iii)	On-site expenditure for development of entire project excluding cost of construction as per (i) or (ii) above, i.e. salaries, consultants fees, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance costs, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered.	--	41,51,307/-



Ground Floor, Shyam Bhawan, S P sinha Path, East Boaring Canal Road, Patna 800 001

e-mail: kirandubey4@gmail.com,

Office : Patna & Delhi



Sanjeev Kiran & Associates

Chartered Accountants

	B	Payment of Taxes, cess, fees, charges, premiums, interest etc to any statutory Authority.	--	--
	C	Principal sum and interest payable to financial institutions, scheduled banks, non-banking financial institution (NBFC) or money lenders on construction funding or money borrowed for construction ;	-	-
		Sub-Total of Development Cost	9,00,00,000/-	1,40,14,955/-
Sr. No.	Particulars		Amount (Rs.)	
2	Total Estimated Cost of the Real Estate Project [1(i) +1(ii)] of Estimated Column -A		9,27,50,000/-	
3	Total Cost Incurred of the Real Estate Project [1(i) +1(ii)] of Incurred Column-B		1,67,64,955/-	
4	Percentage of completion of Construction Work (as per Project Architect's Certificate Table-A) = 15.38% (as per Project Architect's Certificate Table-B) = 23.80%		As per form I Attached	
5	Proportion of the Cost incurred on Land Cost and Construction Cost to the Total Estimated Cost.(3/2%)		18.075%	
6	Amount Which can be withdrawn from the Designated Account Total Estimated Cost * Proportion of cost incurred (Sr. number 2* Sr. number 5)		1,67,64,955/-	
7	Less: Amount withdrawn till date of this certificate as per the Books of Accounts and Bank Statement		1,40,14,955/-	
8	Net Amount which can be withdrawn from the Designated Bank Account under this certificate		27,50,000/-	

This certificate is being issued for RERA compliance for the **Vibhas Buildtech India Pvt. Ltd** (CIN : U45201JH2018PTC011799) and is based on the records and documents produced before us and explanation provided before us by the management of the company.

Yours Faithfully

Sanjeev Kiran and Associates
Chartered Accountants FRN : 023011N

(CA Kiran Dubey)
Partner (M No : 066974)
UDIN : **24066974BKFIXY1962**



Place : Patna
Date : 13th October 2024

Ground Floor, Shyam Bhawan, S P sinha Path, East Boaring Canal Road, Patna 800 001
e-mail: kirandubey4@gmail.com,
Office : Patna & Delhi



Sanjeev Kiran & Associates

Chartered Accountants

(ADDITIONAL INFORMATION FOR ONGOING PROJECTS)

RERA Reg. Number :- BRERAP33236-3/207/R-1507/2022

S No	Particulars	Amount (Rs)
1	Estimated Balance Cost to Complete the Real Estate Project (Difference of Total Estimated Project cost less Cost incurred)(Including Land Cost)	7,59,85,045/-
2	Balance amount of receivables from sold apartments / Commercial as per Annexure-A to this certificate (as certified by management)	2,74,01,812/-
3	i Balance Unsold area (certified by Management and to be verified by CA from the records and books of accounts)	13781Sq. Ft
	ii Estimated amount of sales proceeds in respect of unsold apartment (calculated as per ASR multiplied to unsold area as on date of certificate) as per Annexure-A	7,99,29,800/-
4	Estimated receivables of ongoing project. Sum of 2 +3 (ii)	10,73,31,612/-
5	Amount to be deposited in Designated Account- 70% or 100% IF 4 is greater than 1, then 70 % of the balance receivables of ongoing project will be deposited in designated Account. IF 4 is lesser than 1, then 100% of the of the balance receivables of ongoing project will be deposited in designated Account.	7,51,32,128/-

This certificate is being issued for RERA compliance for the **Vibhas Buildtech India Pvt. Ltd** (CIN : U45201JH2018PTC011799) and is based on the records and documents produced before us and explanation provided before us by the management of the company.

Yours Faithfully

Sanjeev Kiran and Associates
Chartered Accountants FRN : 023011N

(CA Kiran Dubey)
Partner (M No : 066974)
UDIN : **24066974BKFIXY1962**



Place : Patna
Date : 13th October 2024

प्रपत्र-इ

File No. - 233/2022

औपबंधिक अग्नि निवारण एवं अग्नि सुरक्षा अनापत्ति प्रमाण पत्र
 बिहार अग्निशमन सेवा अधिनियम, 2014 की धारा-02 की उपधारा-(छ) के अधीन
 बिहार अग्निशमन सेवा नियमावली, 2021 के नियम 15(च)(iii) के अन्तर्गत
निदेशक, राज्य अग्निशमन सेवा, बिहार, पटना का कार्यालय।

प्रेषक,

सेवा में,

निदेशक,
 राज्य अग्निशमन सेवा,
 बिहार, पटना ।

संजय कुमार,
 पिता-श्री शिवदयाल सिंह,
 सोना गोपालपुर, पटना।

संदर्भ :- क्रमांक.....3102..... दिनांक.27/06/2022.....

आवेदनकर्ता मे० वास्तुविद, उमाशंकर कुमार (विशिष्ट आई.डी.नं० CA/2011/54023)

विषय :- भवन निर्माण के लिए औपबंधिक अनापत्ति प्रमाण पत्र निर्गत ।
 महाशय,

राज्य अग्निशमन सेवा, बिहार, पटना के द्वारा गठित अग्नि सुरक्षा एवं निवारण स्कंध (FSPW) की संतुष्टि के उपरान्त व उक्त समिति में शामिल विशेषज्ञों की अनुशंसा के आलोक में भवन निर्माणकर्ता मे० संजय कुमार के द्वारा प्रस्तावित भवन/ब्लॉक का निर्माण हेतु बिहार अग्निशमन सेवा नियमावली, 2021 के नियम 15(च)(iii) के अंतर्गत औपबंधिक अनापत्ति प्रमाण पत्र निर्गत किया जाता है।

प्रस्तावित भवन योजना से संबंधित भवन का नाम Vibhas Buildtech India Pvt. Ltd., निदेशक-श्री संजय कुमार, पिता-श्री शिवदयाल सिंह, प्लॉट नं०-552,553, खाता नं०-392,477, थाना नं०-124, थाना-गोपालपुर, मौजा-सोना गोपालपुर, जिला-पटना, अधिभोग आवासीय, उप श्रेणी आवासीय, भवन की ऊँचाई 23.95 (मीटर में) फर्श क्षेत्र 7179.33 वर्गमीटर, भवन के तलों की संख्या 6,7, तलघर की संख्या 1, स्लिट/भूतल की संख्या 1, भवन के ब्लॉक की संख्या 2, प्रत्येक मंजिल का औसत अधिभोग भार 24, लिफ्ट की संख्या 2, फायर लिफ्ट की संख्या 1, रैम्प की संख्या 2, आपातकालीन शरण स्थल (रिफ्यूजी एरिया) की संख्या शून्य, फायर टावर की संख्या शून्य है। राष्ट्रीय भवन संहिता के दिशा-निर्देश, स्थानीय भवन नियमावली एवं स्थानीय परिस्थिति के आधार पर निम्नलिखित सलाह/अनुशंसा के साथ भवन निर्माण योजना की स्वीकृति दी जाती है, जिसका अनुपालन संबंधित वास्तुविद/भवन निर्माणकर्ता/भू-स्वामी के द्वारा किया जाएगा।

भवन योजना पर प्रतिहस्ताक्षर के बाद आपके अनुमोदन हेतु अग्रसारित किया जाता है :-

(1) भवन निर्माणकर्ता द्वारा भवन के लिए खुली जगह (मीटर) (उत्तर 5.0 मी०, दक्षिण 5.0 मी०, पूर्व 5.0 मी०, पश्चिम 8.0 मी०) एवं पलायन के साधन (आंतरिक सीढ़ियों की संख्या 3, चौड़ाई 2.44,0.90 (मीटर)/बाह्य सीढ़ियों की संख्या 1, चौड़ाई 2.44 (मीटर) प्रस्तावित किया गया है।

(2) खुला स्थान एवं पहुँच-

(क) भवन के चारों तरफ तत्समय प्रवृत्त भवन उपविधि एवं अन्य तत्संबंधी अधिनियम/नियम/विनियमन/स्थानीय आवश्यकता के अनुसार खुला स्थान होगा एवं अग्निशमन दस्ते के पहुँच एवं घुमाने के लिए न्यूनतम 3.60 मीटर जगह (भवन श्रेणी एवं निर्माण के अनुसार परिवर्तनीय) छोड़ा जाना चाहिए।

(ख) भवन का पहुँच पथ मजबूत एवं चौड़ी हो जो 20 मिट्रिक टन अग्निशामक वाहन का भार आसानी से सहन कर सके।

(ग) भवन के प्रवेश द्वार की चौड़ाई 4.5 मीटर एवं ऊँचाई 5 मीटर से कम नहीं होना चाहिए।

(3) बनावट :-

(क) प्रस्तावित भवन का पूरा निर्माण अनुमोदित योजना के अनुसार बिहार भवन उपविधि, 2014 समय-समय पर यथा संशोधित तथा स्थानीय नगर निकाय के भवन संबंधी नियमों को ध्यान में रखकर किया जाएगा।

For VIBHAS BUILDTECH INDIA PVT LTD.

DIRECTOR

(ख) भवन का फर्श क्षेत्र 750 वर्गमीटर से अधिक होने की स्थिति में अलग-अलग दिवारों से उचित रूप से छत तक बॉटा जाएगा, जिसमें कम से कम दो घंटे तक अग्नि प्रतिरोधक क्षमता होगा।

(ग) भवन की आंतरिक सजावट अग्नि फैलाव निरोधक सामग्री से बना हुआ आईओएसओ गुण स्तर का होगा।

(घ) भवन के केन्द्रीय कोर डक्ट का crown के पास वेन्टीलेशन का प्रावधान होगा। सभी उर्ध्व डक्ट का सीढ़ी पर्याप्त अग्नि निरोधक क्षमता के सामग्री से करने का व्यवस्था करना होगा।

(4) सीढ़ी :-

(क) भवन का सीढ़ी बंद प्रकार का होगा। पूरे भवन निर्माण कार्य ईट/आर.सी.सी. से न्यूनतम 04 घंटे के अग्नि प्रतिरोधक क्षमता का होगा।

(ख) भवन का सीढ़ी के उपरी भाग में स्थायी भेंट होगा जो सीढ़ी के क्रॉस सेक्शन एरिया का 05 प्रतिशत होगा। साथ ही सीढ़ी के क्रॉस सेक्शन क्षेत्र का 15 प्रतिशत क्षेत्र के बराबर प्रत्येक मंजिल के स्तर पर खुलने योग्य Sashes होगा। यह भवन के बाहरी दीवार पर प्रदान किया जाएगा।

(ग) भवन के सभी सीढ़ियों का निर्माण कमरे से अलग होगा एवं किसी भी कमरे में प्रवेश किये बिना हर मंजिल पर एक दूसरे से परगम्य होगा, जिसे संबंधित छत के लेवल तक बढ़ाया जाएगा। सीढ़ी वाली दीवाल की छत आस-पास की छत के क्षेत्र से 1 मीटर ऊपर होगी।

(घ) विभिन्न श्रेणी के भवनों में सीढ़ी की चौड़ाई तथा कोरिडोर एवं यात्रा दूरी संबंधित भवन नियमों के अनुसार होगा।

(ङ) दो सीढ़ी के मामले में एक सीढ़ी बाहरी दीवाल से होनी चाहिए।

(च) तलघर तक पहुँच के लिए दोनों सीढ़ी तलघर मंजिल तक नहीं जाना चाहिए। पहुँच के लिए एक अलग सीढ़ी होगा।

(5) अग्नि सुरक्षा प्रणाली :- राष्ट्रीय भवन संहिता, 2016 समय-समय पर यथा संशोधित के प्रावधानों के आलोक में निम्नलिखित अग्नि सुरक्षा उपायों के प्रावधान के साथ अनुमोदित भवन योजना अग्रसारित किया जाता है:-

- (क) डोज रील
- (ख) वेट राईजर-सह-डाउन कमर सिस्टम (02 अदद)
- (ग) यार्ड हाईड्रेन्ट सिस्टम
- (घ) हस्तचालित विद्युत अग्नि एलार्म सिस्टम
- (ङ) पूरे भवन में ऑटोमेटिक डिटेक्शन एण्ड अलार्म सिस्टम
- (च) स्प्रिंकलर सिस्टम (आवश्यकतानुसार)
- (छ) भूतल स्टैटिक, टैंक की क्षमता 100000 लीटर
- (ज) ओवर हेड वाटर टैंक 25000, 25000 लीटर क्षमता प्रति ब्लॉक
- (झ) एक पम्प हाउस 2850 एल.पी.एम. इलेक्ट्रीक एवं डीजल, 180 एल.पी.एम. जॉकी पम्प, 900 एल.पी.एम. बूस्टर पम्प
- (ञ) फायर एक्सटींग्यूअर

(6) संबंधित अधिनियम/नियम/विनियमन जैसे- बिहार भवन उपविधि, 2014, समय-समय पर यथा संशोधित राष्ट्रीय भवन संहिता, 2016, समय-समय पर यथा संशोधित बहुमंजिली भवन निर्माण विनियम, 1981, बिहार अग्निशमन सेवा अधिनियम, 2014, बिहार अग्निशमन सेवा नियमावली, 2021 में संबंधित अधिभाग के लिए वांछित अन्य शर्तों का पालन किया जाएगा। कुछ शर्तें निम्न प्रकार हैं :-

(क) लिफ्ट :-

(i) भवन का लिफ्ट की दीवार न्यूनतम 02 घंटे का अग्नि निरोधक क्षमता का होगा।

(ii) भवन का लिफ्ट उच्च गति "फायर लिफ्ट" पर डिजाइन की जाएगी और योजना में स्पष्ट रूप से चिन्हित होगा।

For VIBHAS BUILDTECH INDIA PVT LTD.

DIRECTOR

(iii) सामान्य विद्युत आपूर्ति की विफलता के मामले में, स्वचालित वैकल्पिक व्यवस्था होना चाहिए। अपार्टमेंट भवनों के लिए विद्युत आपूर्ति में परिवर्तन हेतु हस्ताचालित परिवर्तनीय स्वीच के माध्यम से यह व्यवस्था किया जा सकता है। वैकल्पिक रूप से लिफ्ट इस तरह से वायर्ड होगा कि बिजली की विफलता की स्थिति में भी यह जमीन स्तर तक आयेगा एवं दरवाजा आसानी से खुल सकेगा।

(iv) आग लगने की स्थिति में प्रति घंटा 30 बार हवा परिवर्तन करने हेतु स्मोक वेंटिंग सिस्टम का समावेश सभी लिफ्ट सॉफ्ट में कर धुँआ निकासी हेतु व्यवस्था की जाएगी। यह इस प्रकार का डिजाइन किया जाएगा कि स्पीक्लर एवं फायर एलार्म क्रियाशील हो सके। सामान्य विद्युत आपूर्ति की विफलता के मामले में यह स्वचालित रूप से वैकल्पिक आपूर्ति के लिए कार्य करेगा।

(v) अग्नि नियंत्रण कक्ष के साथ लिफ्ट का संचार व्यवस्था बनाये रखने सहित अन्य सभी आवश्यकताएँ आई0 एस0 गुण स्तर के अनुरूप करना होगा, जिसमें भवन के लिफ्ट कार, अग्नि नियंत्रण कक्ष के साथ जुड़ी होनी चाहिए, जिससे संचार व्यवस्था बनी रहे।

(vi) राष्ट्रीय भवन संहिता, 2016 समय-समय पर यथा संशोधित से संबंधित प्रावधानों का पालन करते हुए फायर लिफ्ट होना चाहिए जैसे 1200 वर्गमीटर के फर्श क्षेत्र के लिए एक फायर लिफ्ट होना चाहिए।

(ख) भवन में सक्रिय अग्नि सुरक्षा प्रणाली जैसे प्रत्येक मंजिल पर लैण्डिंग भत्व के साथ डाउन कमर सिस्टम एवं होज रील, छत स्तर पर 900 एल0पी0एम0 पम्प के साथ होगा। आई0 एस0 2190/1992 तथा संबंधित विशिष्टियों का आई0एस0आई0 मार्कड अग्निशामन यंत्र, फायर चेक, दरवाजा, हस्ताचालित कॉल अलार्म प्वाइन्ट, अग्नि सुरक्षा चमकीला संकेत एवं भवन निर्माण संहिता के अनुसार अन्य अग्नि निरोध उपाय किये जायेंगे।

(ग) तलघर में स्वचालित स्पीक्लर सिस्टम होना चाहिए एवं दो अलग-अलग निकास द्वार होना चाहिए।

(घ) भूतल जल स्टैटिक टैंक (20,000 लीटर से कम क्षमता) का नहीं स्वचालित रिफिलिंग की व्यवस्था के साथ हो, जहाँ अग्निशामक वाहन आसानी से पहुँच सके। आभर हेड वाटर स्टैटिक टैंक (10,000 लीटर क्षमता से कम नहीं) अधिवास के पूर्व हो जाना चाहिए।

(ङ) भवन के प्रत्येक मंजिल पर विद्युत केबुल सील होनी चाहिए।

(च) भवन का कम्पार्टमेंटेशन इस प्रकार होगा कि आग एवं धुँआ उसी क्षेत्र में सीमित रहेगा जहाँ अग्निकांड हुआ है तथा भवन के अन्य भागों में नहीं फैले।

(छ) भवन के अलगाव दीवार एवं फ्लोर में खुला स्थान - ऐसे सभी प्रकार के तथ्यों पर ध्यान देना होगा जो आग एवं धुँआ के फैलाव को इन खुला स्थानों में प्रवेश को सीमित कर सके और बनावट का फायर रेटिंग बरकरार रह सके। सभी दीवार में खुला स्थान न्यूनतम दो घंटे की फायर रेटिंग के अग्नि निरोधक दरवाजा से सुरक्षित रहेगा। मंजिलों में सभी खुला स्थान vertical enclosure से सुरक्षित रहेगा एवं ऐसे enclosure का दीवार न्यूनतम दो घंटे की फायर रेटिंग का होगा।

(ज) मंजिलों के प्रत्येक vertical openings यथोचित रूप से बंद एवं सुरक्षित रहेगा तथा निम्नलिखित व्यवस्थाएँ की जाएगी :-

(i) पलायन के रास्ता का प्रयोग करते वक्त अधिवासियों को मंजिल दर मंजिल खुले स्थान से आग एवं धुँआ के फैलाव को रोकने के लिए प्रर्याप्त सुरक्षा प्रदान करना होगा। यह सुनिश्चित करना होगा कि अधिवासियों के निकासी मार्ग में कम से कम 21 मिली मीटर का उपरी भाग खुला हो।

(ii) दो घंटे की फायर रेटिंग का अग्नि दरवाजा बाहर भागने/निकलने के रास्ते एवं लिफ्ट में प्रवेश के रास्ते तथा सीढ़ी पर एवं अन्य उपयुक्त स्थानों पर आग एवं धुँआ के फैलाव को रोकने के लिए दिया जाएगा।

(iii) निकासी मार्ग का सुरक्षित प्रयोग हेतु स्मोक वेंटिंग सुविधा प्रदान किया जाएगा।

(iv) आंतरिक सजावट से जहरीला धुँआ के उत्पन्न होने से बचाने हेतु धुँआ निरोधी सामग्रियों का प्रयोग किया जाएगा।

(v) भवन के निकासी मार्ग (सीढ़ी एवं कोरिडोर) का रौशनीकरण/सीढ़ियों का प्रेसराइजेशन/ तलघर का वेंटिलेशन राष्ट्रीय भवन संहिता, 2016 समय-समय पर यथा संशोधित के अनुसार करना होगा।

(vi) एयर कंडिशनिंग एवं वेंटिलेशन सिस्टम को इस प्रकार अधिष्ठापित किया जाएगा, जिससे आग एवं धुँआ एक फ्लोर से दूसरे फ्लोर और भवन से बाहर नहीं फैल सके। एयर फिल्टर में आग लगने पर धुँआ

For VIBHAS BUILDTECH INDIA PVT LTD.

DIRECTOR

को फैलने से बचाने के लिए स्मोक सेंसिटीव डिवाइस भवन में होना चाहिए। प्रत्येक तल पर आग और धुँए के हजार्ड से बचाने के लिए प्रत्येक तल पर अलग-अलग एयर हैंडलिंग यूनिट होना चाहिए। फायर डंपर्स को ए0सी0 सिस्टम में प्रदान किया जाएगा, ताकि आग की स्थिति में स्वचालित रूप से बंद हो सके और इस तरह अग्नि/धुँआ का फैलाव रोका जा सके।

(vii) विद्युत अधिष्ठापन- विद्युत सुरक्षा भारतीय विद्युत नियमावली एवं संबंधित आई0एस0/संहिता के प्रावधान के आलोक में होगा। लाईसेंस विद्युत टेकेदार के द्वारा विद्युत अधिष्ठापन किया जाएगा। मुख्य रूप से अलग नली में वायरिंग, अलग सर्किट, स्वचालित सर्किट ब्रेकर, मास्टर स्वीच, इंसपेक्शन पैनल दरवाजा, आपातकालीन/वैकल्पिक विद्युत आपूर्ति का आवश्यक सत्यापन आदि पर ध्यान दिया जाएगा।

(viii) भवन का अधिवास प्राप्त करने के बाद प्रत्येक वर्ष कम से कम दो बार नियमित रूप से फायर एक्जीट ड्रिल किया जाना चाहिए।

(ix) अग्नि सुरक्षा अधिकारी-एन0बी0सी0 2016 और बिहार अग्निशमन सेवा अधिनियम, 2014 के अनुसार।

(x) भवन में अधिष्ठापित अग्निशमन उपकरणों आदि का ए0एम0सी0 योग्य फर्म या व्यक्ति को दिया जाना चाहिए।

(xi) स्थापित नियम के आलोक में भवन के सेट बैक का चेकिंग वास्तुविद/पारित करने वाले द्वारा किया जाएगा।

(xii) यह स्पष्ट किया जाता है कि उपरोक्त सिफारिशों का पालन नहीं करने की स्थिति में भविष्य में होने वाली किसी भी कानूनी विवाद के मामले में, जिम्मेवारी डेवलपर्स/वास्तुविद/जमीन मालिक पर होगी एवं किसी भी सरकारी प्राधिकार (जैसे कि राज्य अग्निशमन पदाधिकारी, बिहार, पटना) की नहीं होगी।

(xiii) इसके द्वारा यह भी स्पष्ट किया जाता है कि इस कार्यालय (अर्थात राज्य अग्निशमन पदाधिकारी-सह-निदेशक, बिहार, पटना/प्राधिकृत पदाधिकारी) का कार्यालय उस भूमि के किसी भी कानूनी विवाद के लिए जिम्मेवार नहीं है, जिसपर प्रस्तावित भवन का निर्माण होगा।

(7) अनिवार्यतः अन्डरटेकिंग्स के सभी प्रावधानों का पालन करना होगा।

(8) इसे औपबंधिक अनापत्ति प्रमाण पत्र माना जाएगा। उपरोक्त सभी अग्नि एवं जीवन सुरक्षा अनुशंसाओं के अनुपालन के बाद आवश्यक निरीक्षण एवं अधिष्ठापन के जाँच हेतु राज्य अग्निशमन कार्यालय को सूचित करना होगा। सभी बिन्दुओं की जाँच से संतुष्टि के बाद अंतिम अग्नि निवारण एवं अग्नि सुरक्षा अनापत्ति प्रमाण पत्र निर्गत किया जाएगा।

(9) अनुमोदित भवन योजना में बिना पूर्व स्वीकृति के किसी भी प्रकार का विचलन या परिवर्तन किये जाने की स्थिति में इस औपबंधिक अनापत्ति प्रमाण पत्र को रद्द कर दिया जाएगा।

(10) हस्ताक्षर एवं मुहर के साथ नक्शा वापस किया जाता है।

अनुलग्नक:-

1) मे0 वास्तुविद, उमाशंकर कुमार

2) अध्यक्ष, नगर निगम, पटना

निदेशक-सह-राज्य अग्निशमन पदाधिकारी,

बिहार, पटना।

For VIBHAS BUILDTech INDIA PVT LTD.

DIRECTOR

पटना महानगर क्षेत्र प्राधिकार

(बिहार सरकार का उपक्रम)

पाँचवां तल्ला, बिहार राज्य भवन निर्माण निगम लिमिटेड

शास्त्री नगर, पटना - 800023

सं०सं०:-PMAA/PRN/^{SONA GOPALPUR}_{PHULWARI SHARIF}/Block-A(B+G+06)& Block-B(B+G+07)/49/2022

पटना, दिनांक- 25/10/2022

- 708 -

प्रेषक,

प्रमारी निदेशक,
पटना महानगर क्षेत्र प्राधिकार,
बिहार पटना।

सेवा में,

श्री संजय कुमार,
पिता-शिव दयाल सिंह,
निदेशक-मेसर्स विभास बिल्डटेक इंडिया प्रा०लि०,
403, हीरा इन्कलेव, न्यू डाकबंगला रोड,
जिला-पटना-800001

विषय:- प्लान केस संख्या:- PMAA/PRN/^{SONA GOPALPUR}_{PHULWARI SHARIF}/Block-A(B+G+06)& Block-B (B+G+07)/49/2022 की स्वीकृति के संबंध में।

महाशय,

आपके आवेदन सं०:- PMAA/PRN/^{SONA GOPALPUR}_{PHULWARI SHARIF}/Block-A(B+G+06)& Block-B (B+G+07)/49/2022 दिनांक-01.07.2022 के संदर्भ में श्री संजय कुमार, पिता-शिव दयाल सिंह, निदेशक-मेसर्स विभास बिल्डटेक इंडिया प्रा०लि०, 403, हीरा इन्कलेव, न्यू डाकबंगला रोड, जिला-पटना-800001, बिहार के भवन निर्माण के लिए पटना महानगर क्षेत्र प्राधिकार में बिहार शहरी आयोजना तथा विकास अधिनियम, 2012 के अधीन अधिसूचित विकास योजना/पटना महानगर क्षेत्र प्राधिकार/आयोजना स्कीम/पटना मास्टर प्लान-2031 के आलोक में मौजा-सोना गोपालपुर, सर्वे थाना-फुलवारीशरीफ, थाना सं०-124, सर्वे प्लॉट सं०-552, 553, खाता सं०-392, 477, में आवासीय भवन, (Block A - (B + G + 06) & Block B - (B + G + 07), दिनांक-19.10.2022 को स्वीकृतार्थ नक्शा के बाबत निम्नलिखित शर्तों/निर्बंधनों के अध्याधीन एतद् द्वारा अनुमति प्रदान की जाती है।

1. भूमि/भवन का उपयोग अन्य रूप से आवासीय भवन प्रयोजन, के लिए किया जाएगा और इस प्राधिकार के पूर्व अनुमोदन के बिना उपयोगों को किसी अन्य उपयोग के लिए परिवर्तित नहीं किया जाएगा।
2. विकास पूर्ण रूप से आवश्यक अनुमति के पृष्ठांकन के साथ संलग्न योजनाओं के अनुसार किया जाएगा।
3. अनुमोदन योजना में दर्शाया गया 1816.69 वर्गमीटर का पार्किंग स्थान खुला रखा जाएगा और इसके किसी भाग पर निर्माण नहीं किया जाएगा। बेसमेंट में Ventilation हेतु समुचित व्यवस्था बिहार भवन उपविधि के आलोक में प्रावधान करना होगा।
4. प्रश्नगत भूमि आवेदक के विधिपूर्ण स्वामित्व एवं शांतिपूर्ण कब्जा में अवश्य हो।
5. अमीन के स्थल निरीक्षण एवं सहायक अभियंता की टिपणी के अनुसार भुखंड के पश्चिम में 16.76मी० से 16.91मी० चौड़ी वर्तमान सर्वे सड़क है।
6. अनुमति (अनुज्ञा) जारी किये जाने की तारीख से पाँच वर्षों की अवधि के लिए विधि मान्य होगी।


For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR

7. इस उपबन्ध के अधीन दी गयी अनुमति को उस भूखण्ड जिसके लिए योजना अनुमोदित की गयी है के अधिकार हक, हित की बाबत साक्ष्य नहीं मानी जाएगी।
8. योजना के अनुमोदन के पश्चात् भू-अभिलेख के कारण या अधिकार/हक/हित की बाबत कोई विवाद होने पर विवाद की अवधि के दौरान योजना का अनुमोदन स्वतः रद्द समझी जायेगी।
9. भू-स्वामित्व एवं नक्शा से संबंधित समस्त दस्तावेजों/कागजात के सत्यता की जिम्मेदारी आवेदक की है। भविष्य में इसमें किसी प्रकार की त्रुटि/हेर-फेर/कपटपूर्ण रचना पाये जाने पर नक्शा अस्वीकृत किये जाने के साथ आवेदक के विरुद्ध विधि सम्मत कार्रवाई की जायेगी।
10. निर्माणकर्ता को प्राधिकार के विनिर्देशों के अनुसार मल जल, निकास सड़क, एवं अन्य आधारभूत संरचनाओं का विकास बिहार भवन उपविधि-2014 में प्रावधानित उपविधि 8(5) के आलोक में करना होगा।
11. बिहार भू-सम्पदा (विनियामक और विकास) नियमावली-2017 की शर्तों के अधीन राज्य में गठित भू-सम्पदा विनियामक प्राधिकरण से इस परियोजना का निबंधन अनिवार्य होगा।
12. श्रम सेस के संबंध में नगर विकास एवं आवास विभाग/श्रम संसाधन विभाग द्वारा निर्गत अनुदेशों का अनुपालन निर्माणकर्ता द्वारा सुनिश्चित किया जाएगा।
13. समय-समय पर सरकार द्वारा निर्गत आदेशों एवं नीतियों का विस्तृत रूप में पालन करना अनिवार्य होगा।
14. स्थल पर Rainwater Harvesting का प्रावधान निश्चित रूप से करना होगा।
15. बिहार भवन उपविधि-2014, एवं संशोधित भवन उपविधि (2022) तथा पटना मास्टर प्लान-2031 के साथ DCR में प्रावधानित के अनुसार निर्माण कार्य सम्पन्न कराना होगा।
16. बिहार भवन उपविधि-2014, एवं संशोधित भवन उपविधि (2022) तथा पटना मास्टर प्लान-2031 के आलोक में स्वीकृत नक्शा में प्रावधानित ग्रीन एरिया एवं अन्य प्रावधानों का प्रावधान किया जाए।
17. बिहार भवन उपविधि-2014 (संशोधित उपविधि-2022) के अनुसार नगर विकास एवं आवास विभाग, बिहार, पटना से बिल्डर रजिस्ट्रेशन कराना होगा।

विश्वासभाजन,


प्रमारी निदेशक, 25/10/2022
पटना महानगर क्षेत्र प्राधिकार।

For VIBHAS BUILDTECH INDIA PVT LTD.



DIRECTOR
