


## FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending Sept of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	U70109BR2018PTC037373	Name of Firm	NANDISH DEVELOPER AND CONSTRUCTION PVT LTD
Firm Address :	C/O SURENDRA PRASAD, GOAL BAGICHA, GAYA . GAYA, Bihar, India - 823002		
Total Experience of promoter in Real Estate sector	05 YEARS		
Total Experience in Real Estate after Implementation of RERA	02 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	NIL	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP92310-1/221/R-1515/2023	Name of Project/Phase of Registered Project	AARTI KUNJ
Name of Promoter	NANDISH DEVELOPER AND CONSTRUCTION PVT LTD	Project Address	DHANAWAN, NEAR TRIRAJ COLD STORAGE, BODH GAYA, GAYA
Name of Co-promoter	N/A		
Project Registration is valid up to	15-09-2027		
Starting date of Project or Phase of the Project	12-01-2023		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	5 years date of Passing		

## III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

  
DIRECTOR

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	
					FLAT-	FLAT-
	1. 1 BHK			16	1. Booked / Allotted -04	3. Booked/ Allotted-NIL
	2. 2 BHK, -	04	2310.92		2. Sold-NIL	Sold -NIL
	3. 3 BHK	12	9253.16			
	4. Shop					
	5. Bungalow					
	6. Plot etc.					
					Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of Association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any )
------	---------	----------------	--------------------

#### IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	-
	48	2. Sold	-

#### V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

#### VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 01/07/2022

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR

	Any other activities		
--	----------------------	--	--

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	15.06.2027
2.	Water Supply	YES	0%	20.03.2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	15.07.2027
4.	Storm Water Drains	NO	N/A	
5.	Landscaping & Tree Planting	YES	0%	10.04.2027
6.	Street Lighting	YES	0%	15.06.2027
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	20.06.2027
10.	Water Conservation / Rain Water Harvesting	YES	0%	15.06.2027
11.	Energy Management	YES	0%	16.04.2027
12.	Fire Protection and Fire Safety Requirements	YES	0%	20.07.2027
13.	Closed Parking	YES	0%	15.7.2027

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR



14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			

**VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT**

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

**IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT**

(A)	Sr. No.		
	1.	Front Elevation	Attach Below
	2.	Rear Elevation	Attach Below

8 CONSTRUCTION PVT. LTD.



*Rahul Kumar*  
DIRECTOR

3.	Side Elevation	Attach Below
(B)	Photograph of each floor	Attach Below



NANDISH DEVELOPERS  
 & CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
 DIRECTOR

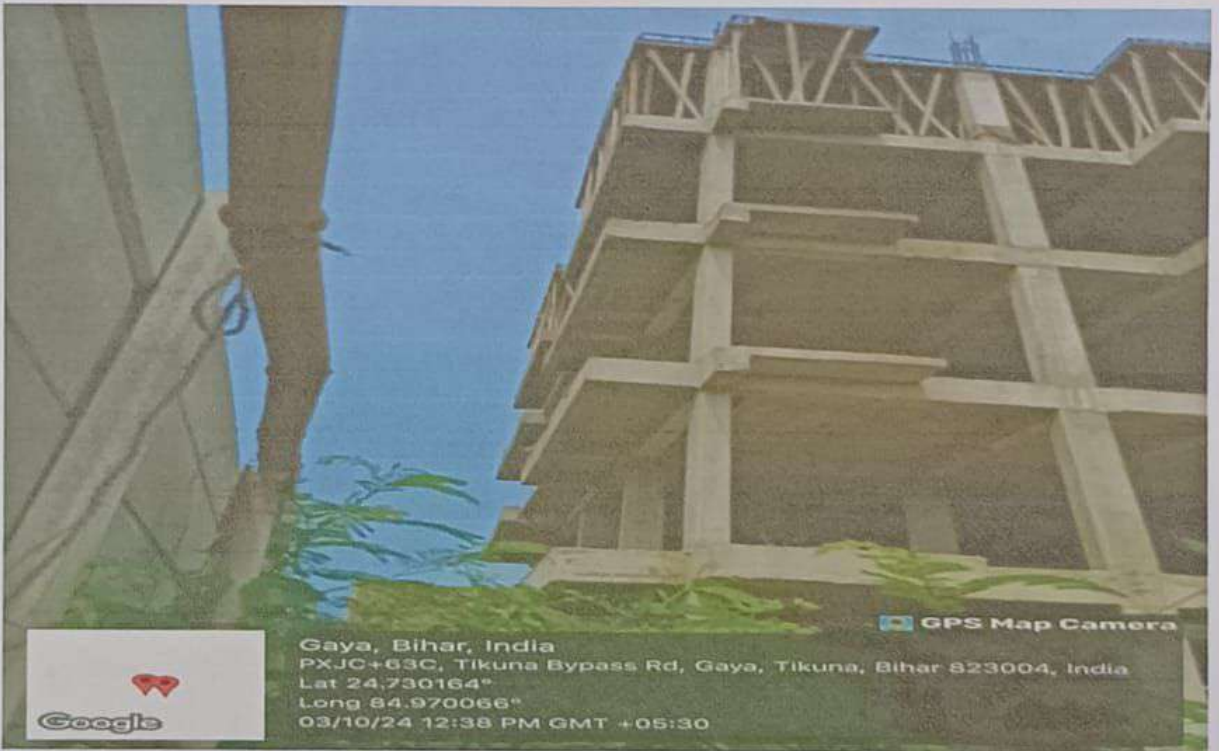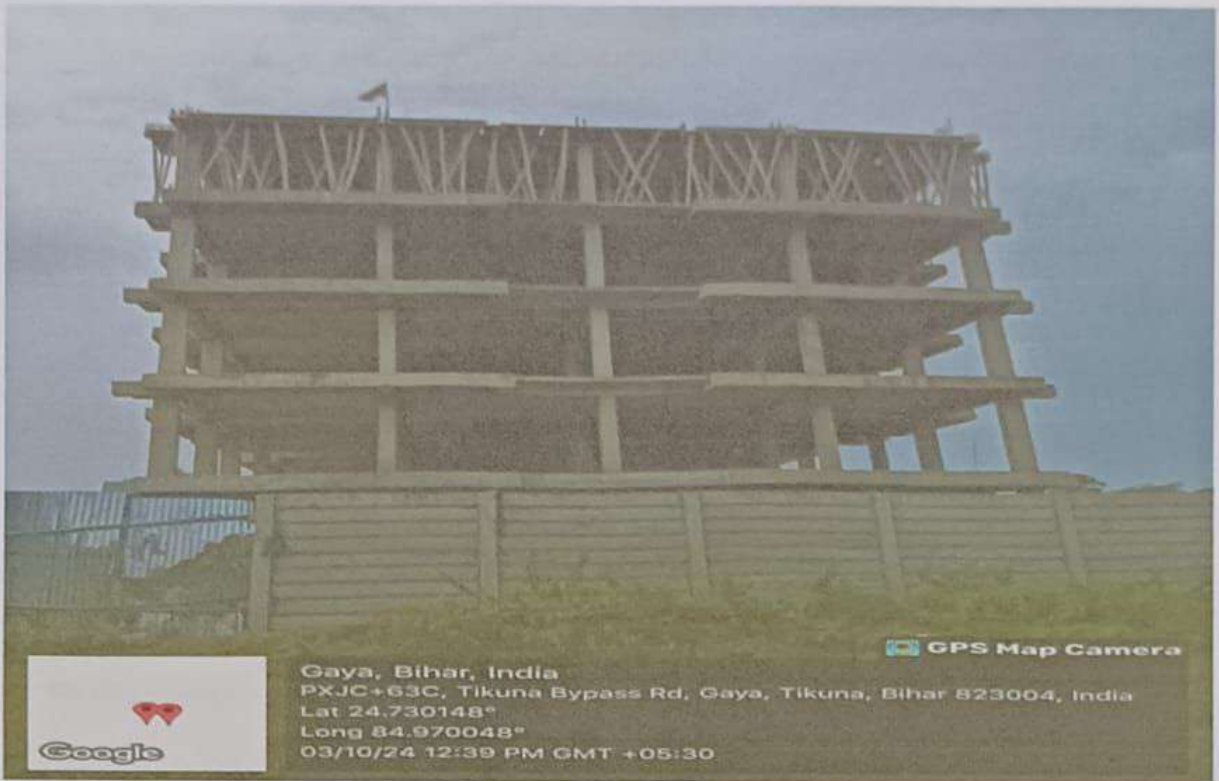

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR






**X. FINANCIAL PROGRESS OF THE PROJECT**

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	5251676779
2.	Estimated Cost of the Project including land cost at the start of the Project	0
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	2,57,00,000.00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	18,96,000.00
6.	Actual Cost Incurred during the Quarter	12,14,208.00
7.	Net amount at end of the Quarter	769932.59
8.	Total expenditure on Project till date	51,69,566.00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

**XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED**

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.  
  
 DIRECTOR

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)		
4.	Plinth	100%	
5.	Stilt Floor		
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	10.03.2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	15.03.2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	10.08.2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	20.05.2027
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	15.04.2027

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR



--

XII. MISCELLANEOUS		
<b>A</b> List of Legal Cases (if any) - On Project / Promoter		
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
<b>B</b> Sale/Agreement for Sale during the Quarter		
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		
XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK -04 3 BHK- 12 4 BHK- Shop- 19 Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc  Flat Booking 1A 2A 2B	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc  N/A
XV. BROCHURE /Prospectus		

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR

**XVI Grievance Redressal Officer**

**Name :** RAHUL KUMAR

**Contact No :** 9504695501

**Email id :** nandishdevelopers@gmail.com

**Address :** LATE AYODHYA PRASAD, GOAL BAGAICHA, GAYA

**Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

NANDISH DEVELOPERS  
& CONSTRUCTIONS PVT. LTD.

*Rahul Kumar*  
DIRECTOR

Signature of Promoter

Name:

Date:
