

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending December of 2024

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	FORM REGISTRATION NO. F000025/2021	Name of Firm	DEO JYOTI BUILDCON
Firm Address :	APARNA BANK COLONY, BEHIND DELHI PUBLIC SCHOOL, RAM JAIPAL ROAD, BAILEY ROAD, PATNA		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	04 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP75942- 1/143/R- 1315/2022	Name of Project/Phase of Registered Project	DEO ENCLAVE
Name of Promoter	DEO JYOTI BUILDCON	Project Address	LEKHA NAGAR, ASHOPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/10/2024		
Starting date of Project or Phase of the Project	29/03/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	14-04-2024		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS						
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-27	Total Number of Apartments in Landowner's share - FLAT-27
BLOCK-A & B	1. 1 BHK			FLAT-54	1. Booked / Allotted - BLOCK-A-06 BLOCK-B-04	3. Booked/ Allotted-NIL
	2. 2 BHK, -	10	7044.90		2. Sold-NIL	Sold -NIL
	3. 3 BHK	44	40560.08		Percentage of booking 37.03%	Percentage of booking 0%
	4. Shop					
	5. Bungalow					
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.			
Association of allottees name			
Details of allottees - Name, Address, Email id (if any), contact number.			
These details may not be available to common people			
Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-A & B	54	1. Booked/Allotted	10
		2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIG HG & FS CUM STATE FIRE OFFICER, BIHAR, PATNA		09-10-2020	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

DEO JYOTI BUILDCON

M. K. Mishra,

PARTNER

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 05/21-22

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	NO	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	95%	30-02-2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	15% 0% 0% 0%	30-05-2025 30-07-2025 30-08-2025 30-09-2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	30-09-2025 30-06-2025
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	95% 95% 0%	30-02-2025 30-02-2025 30-10-2025
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	30-07-2025 30-07-2025 30-10-2025 30-08-2025

DEO JYOTI BUILDCON

M. K. Mishra

DIRECTOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	30-10-2025
		0%	30-10-2025
		0%	30-10-2025
		0%	30-10-2025
	Any other activities	0%	30-10-2025
		0%	30-10-2025

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	12-10-2025
2.	Water Supply	YES	10%	12-10-2025
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	10-07-2025
4.	Storm Water Drains	YES	0%	10-07-2025
5.	Landscaping & Tree Planting	YES	0%	13-08-2025
6.	Street Lighting	YES	0%	13-08-2025
7.	Community Buildings	NO	N/A	

DEO JYOTI BUILDCON

M. U. Mishra/
PARTNER

8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	13-08-2025
9.	Solid Waste Management & Disposal	YES	0%	13-08-2025
10.	Water Conservation / Rain Water Harvesting	YES	0%	10-08-2025
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	10-12-2025
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

DEO JYOTI BUILDCON

M. K. Mishra


8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	



DEO JYOTI BUILDCON
M. K. Mishra
PARTNER

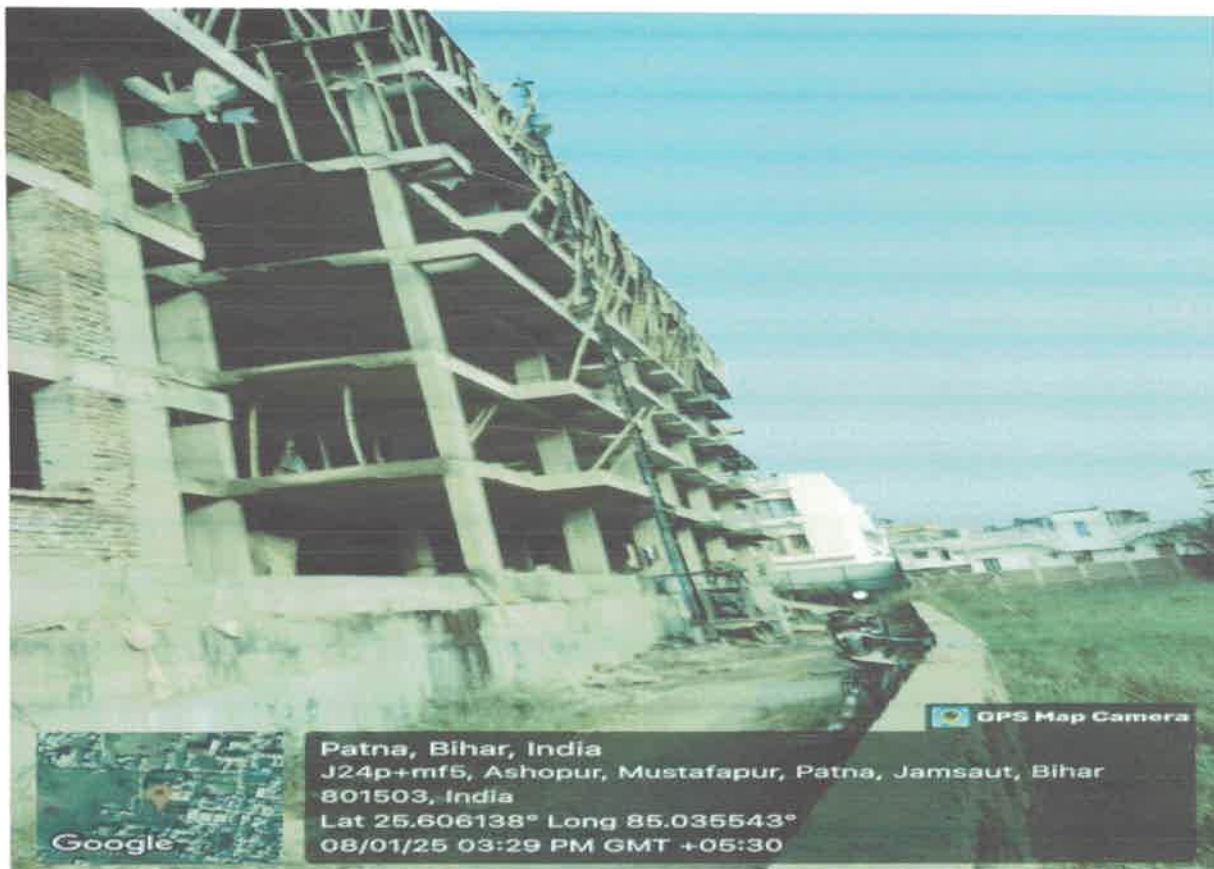

DEO JYOTI BUILDCON
 M.K. Mishra
 PARTNER



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	83970200001253
2.	Estimated Cost of the Project including land cost at the start of the Project	11,44,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	9,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	32,21,337=00
6.	Actual Cost Incurred during the Quarter	29,82,923=00
7.	Net amount at end of the Quarter	2,38,414=00
8.	Total expenditure on Project till date	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED
--

DEO JYOTI BUILDCON

M. V. Mishra
PARTNER

XII. MISCELLANEOUS

A List of Legal Cases (if any) – On Project / Promoter

1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

B Sale/Agreement for Sale during the Quarter

1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK -10 3 BHK-44 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc			Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
	BLOCK	FLAT NO.	TYPE OF FLAT	
	BLOCK-A	G-02	3BHK	
	BLOCK-A	201	3BHK	
	BLOCK-A	203	3BHK	
	BLOCK-A	204	2BHK	
	BLOCK-A	301	3BHK	
	BLOCK-A	303	3BHK	
	BLOCK-B	102	3BHK	
	BLOCK-B	103	3BHK	
	BLOCK-B	401	3BHK	
	BLOCK-B	404	3BHK	

DEO JYOTI BUILDCON

M. K. Mishra

PARTNER

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : MITHILESH KUMAR MISHRA

Contact No : 9973144647

Email id : prakashchandra55@gmail.com

Address : APARNA BANK COLONY, BEHIND DELHI PUBLIC SCHOOL, RAM JAIPAL ROAD, BAILEY ROAD, PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

DEO JYOTI BUILDCON

M. K. Mishra

PARTNER

Signature of Promoter

Name:

Date:
