

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	PARTNERSHIP DEED NO. 432/2009	Name of Firm	KALAKRITI CONSTRUCTION
Firm Address :	HOUSE NO. 79,GANDHIPATH NEHRU NAGAR NORTH S K PURI PATNA 13		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	06 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00359-1/371/R-175/2018	Name of Project/Phase of Registered Project	KALAKRITI'S LALBAGH
Name of Promoter	KALAKRITI CONSTRUCTION	Project Address	MAHULI TOLA, HARNICHAK, ANISABAD, PATNA-2
Name of Co-promoter	N/A		
Project Registration is valid up to	03/07/2021		
Starting date of Project or Phase of the Project	19/09/2018		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

For Kalakriti Construction

Partner

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
	1. 1 BHK			38	1. Booked / Allotted -15	3. Booked/ Allotted-NIL
	2. 2 BHK, -	22			2. Sold-NIL	Sold -NIL
	3. 3 BHK	16				
	4. Shop					
	5. Bungalow					
	6. Plot etc.				Percentage of booking	Percentage of booking

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 15
	39	2. Sold	- NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

For Kalakriti Construction

Shyam
Partner

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/HARNICHAK-PRN-B+G+3/48/20217

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project	100%	

For Kalakriti Construction



Partner

	as per Specifications in Agreement of Sale.		
	Any other activities		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	85%	
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	85%	
4.	Storm Water Drains	YES	90%	
5.	Landscaping & Tree Planting	YES	70%	
6.	Street Lighting	YES	70%	
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	75%	
11.	Energy Management	YES	85%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	85%	

For Kalakriti Construction

[Signature]

Partner

14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT


		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			


IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach

For Kalakruti Construction

	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

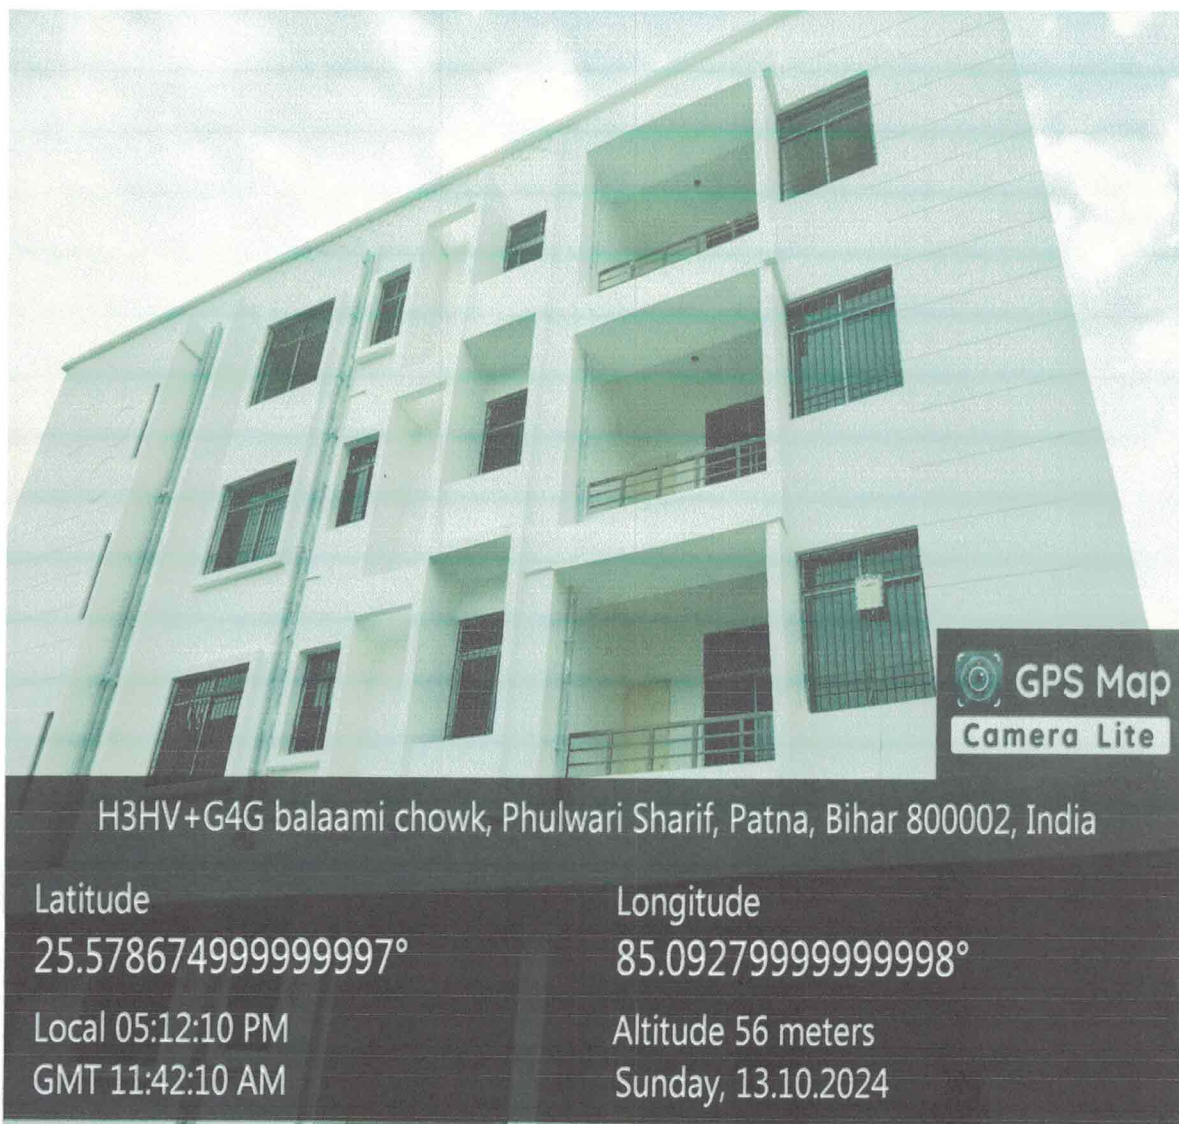

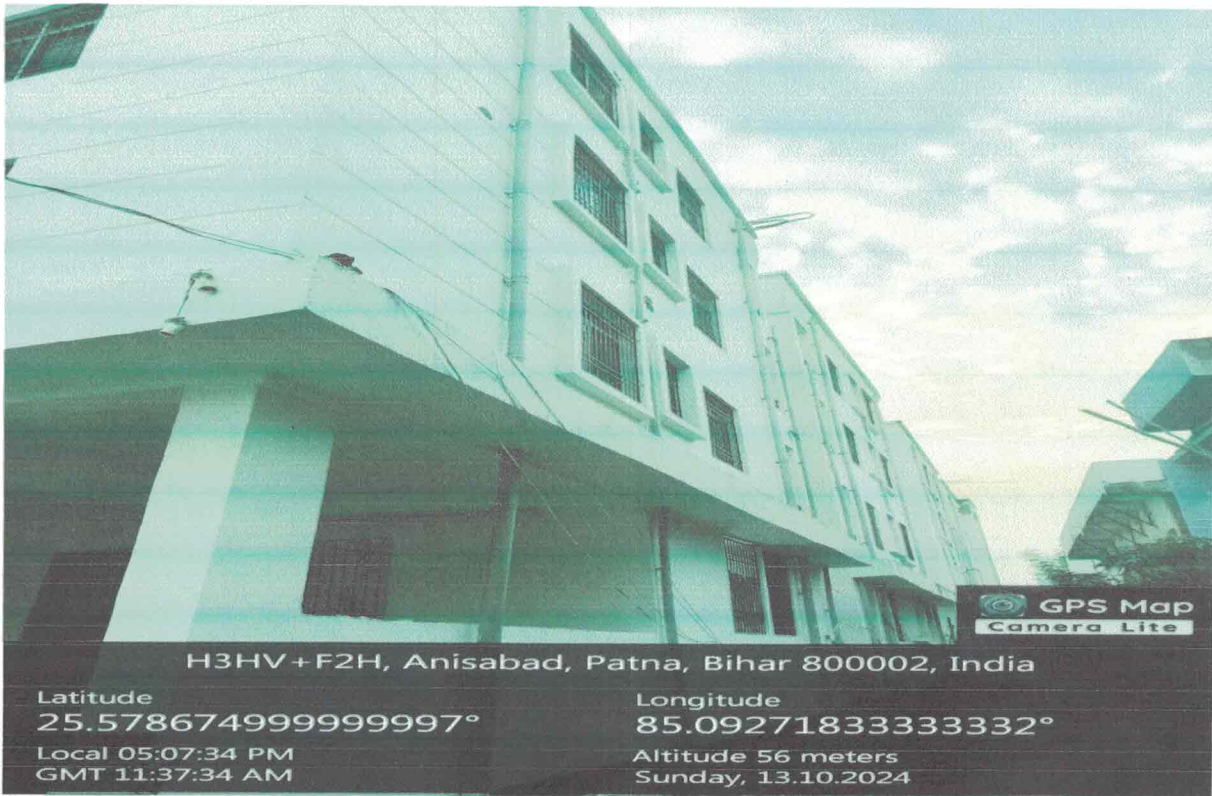

H3HV+F2H, Anisabad, Patna, Bihar 800002, India

Latitude
25.578674999999997°

Local 05:07:34 PM
GMT 11:37:34 AM

Longitude
85.09271833333332°

Altitude 56 meters
Sunday, 13.10.2024



H3HV+F2H, Anisabad, Patna, Bihar 800002, India

Latitude
25.578691666666668°

Local 05:08:18 PM
GMT 11:38:18 AM

Longitude
85.09250333333333°

Altitude 56 meters
Sunday, 13.10.2024

For Kalakriti Construction

Syau

Partner

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	32219487385
2.	Estimated Cost of the Project including land cost at the start of the Project	11,65,51,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,98,04,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	NO
5.	Amount received during the Quarter	52,98,000=00
6.	Actual Cost Incurred during the Quarter	48,87,195=32
7.	Net amount at end of the Quarter	5,60,181=10
8.	Total expenditure on Project till date	5,22,65,126=32
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	
XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED		

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

For Kalakriti Construction

 Partner

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS			
Total Number of sanctioned apartments 1 BHK- 2 BHK -22 3 BHK-16 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
	FLAT NO.	FLAT TYPE	
	B-202 B-BLOCK	2 BHK	
	B-301 B-BLOCK	2 BHK	
XV. BROCHURE /Prospectus			
XVI Grievance Redressal Officer Name : SHYAM NANDAN PRASAD Contact No : 8340786442 Email id : shyam2308@rediffmail.com Address : HOUSE NO. 79,GANDHIPATH NEHRU NAGAR NORTH S K PURI PATNA 13			


For Kalakriti Construction

 Partner

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

JFKalekroli Construction

 P. P. P.

Signature of Promoter

Name:

Date:
