


FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45200BR2010PTC016275	Name of Firm	N S A CONSTRUCTION PRIVATE LIMITED
Firm Address :	Sidhu Bhawan, Road No. -9, Patel Nagar, Patna-800023		
Total Experience of promoter in Real Estate sector	14 Years		
Total Experience in Real Estate after Implementation of RERA	4 Years		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	03	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	0	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP12362-001/102/R-1595/2023	Name of Project/Phase of Registered Project	NITYA HOMES
Name of Promoter	N S A CONSTRUCTION PRIVATE LIMITED	Project Address	OPPOSITE PETROL PUMP, MAINPURA, PATEL NAGAR, PATNA-800023
Name of Co-promoter	N/A		
Project Registration is valid up to	05/07/2028		
Starting date of Project or Phase of the Project	17/08/2023		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	05/07/2028		

N.S.A. Construction Pvt. Ltd.


 Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - Flat-08	Total Number of Apartments in Landowner's share - Flat-08
	1. 1 BHK	10		Flat - 16	1. Booked / Allotted -04	3. Booked/ Allotted-NIL
	2. 2 BHK, -	06			2. Sold-00	Sold -NIL
	3. 3 BHK				Percentage of booking 50%	Percentage of booking 0%
	4. Shop					
	5. Bungalow					
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
	16	1. Booked/Allotted	04
		2. Sold	00

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	AAI		21-01-2022	PATN/EAST/B/01 0822/647521
5.	Other Approval(s), if any, required for the Project.	N/A			

N.S.A. Construction Pvt. Ltd.


Niraj Kumar Dubey
Director

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/MAINPURA/PRN-G+3/466/2021

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 0% 0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	50% 50%	15.03.2027 10.06.2027
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	50% 50% 50%	01.12.2027 05.12.2027 01.12.2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 60% 0% 0%	05.03.2027 15.06.2027 10.03.2028 17.04.2028

N.S.A. Construction Pvt. Ltd.


Director

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	20.04.2028
		100%	
		0%	03.03.2028

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	15.04.2028
2.	Water Supply	YES	0%	15.03.2028
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	15.04.2028
4.	Storm Water Drains	NO	N/A	
5.	Landscaping & Tree Planting	NO	N/A	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	10.04.2028

N.S.A. Construction Pvt. Ltd.

Narain Kumar Dubey
Director

9.	Solid Waste Management & Disposal	YES	0%	10.05.2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	15.02.2028
11.	Energy Management	YES	0%	10.04.2028
12.	Fire Protection and Fire Safety Requirements	NO	N/A	04.04.2028
13.	Closed Parking	YES	0%	15.03-2028
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			


N.S.A. Construction Pvt. Ltd.

Naveen Kumar Bhatnagar
Director

9.	Energy Management			
----	-------------------	--	--	--


IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

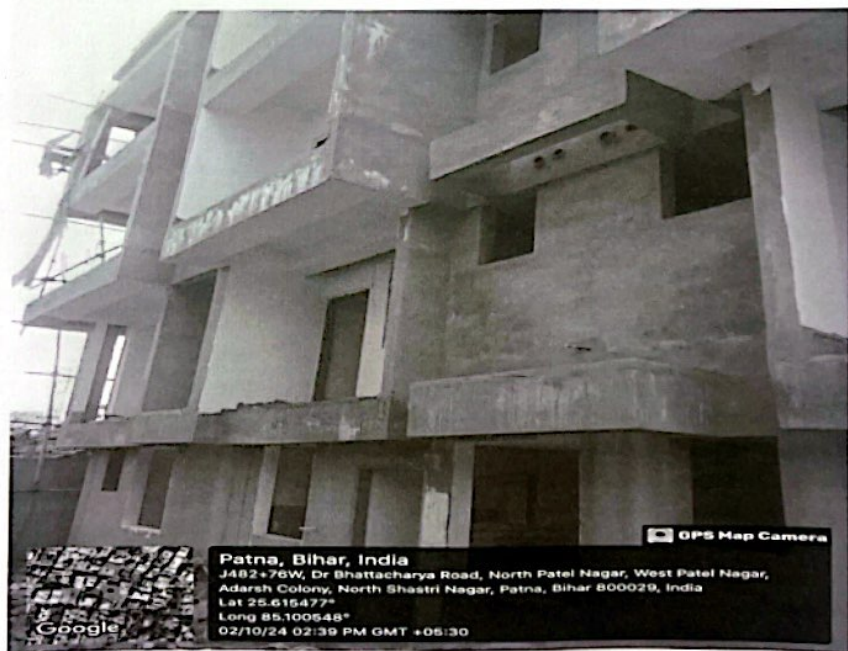


N.S.A. Construction Pvt. Ltd.

Niraj Kumar Baskin
 Director

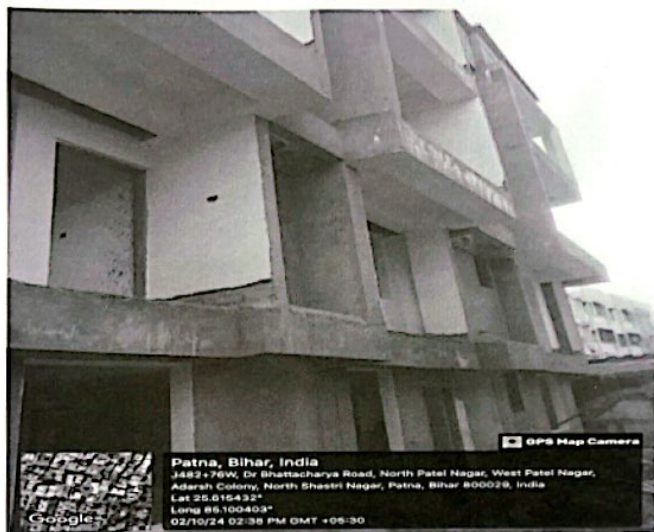

N.S.A. Construction Pvt. Ltd.

Niraj Kumar Dickey
 Director

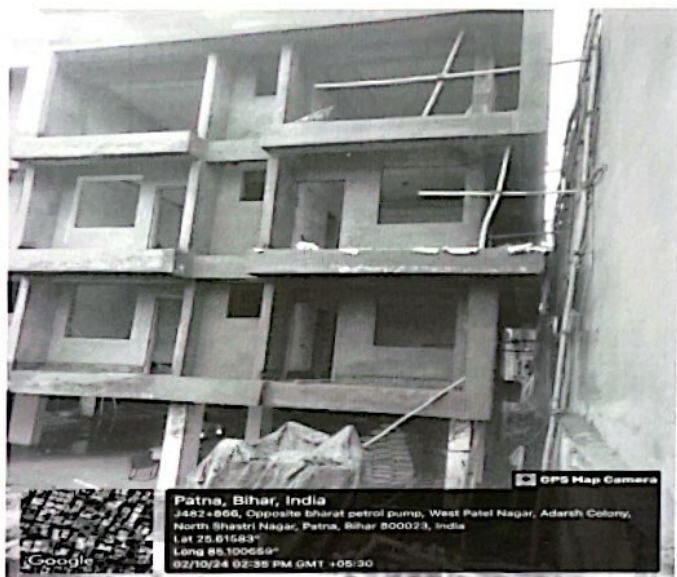

X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	401505000657
2.	Estimated Cost of the Project including land cost at the start of the Project	6,56,90,000-00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	3,00,00,000-00
4.	Any Variation in Development Cost which is declared at the start of the Project .	N/A
5.	Amount received during the Quarter	58,21,803-00
6.	Actual Cost Incurred during the Quarter	38,98,672-00
7.	Net amount at end of the Quarter	20,97,514-00
8.	Total expenditure on Project till date	1,93,59,244-00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	1,93,59,244-00

N.S.A. Construction Pvt. Ltd.

Niraj Kumar Dubey
Director

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A List of Legal Cases (if any) – On Project / Promoter		
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B Sale/Agreement for Sale during the Quarter		
1.	Sale Deed	NIL
2.	Agreement for Sale	
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK, -10 3 BHK-06 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	
	FLAT NO.	FLAT TYPE
	205	3BHK
	305	3BHK
	202	3BHK
	304	2BHK
	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc N/A	

N.S.A. Construction Pvt Ltd.

Narain Kumar Desai
Director

XV. BROCHURE /Prospectus

XVI Grievance Redressal Officer

Name : NEERAJ KUMAR DUBEY

Contact No : 9818712890


Email id : neeraj_infopark@yahoo.com

Address : Sidhu Bhawan, Road No. -9, Patel Nagar, Patna-800023

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

N.S.A. Construction Pvt. Ltd.


Director

Signature of Promoter

Name: NEERAJ KUMAR DUBEY

Date: 8/10/24
