

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending 31st March of 2025 (Year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No.	U45309BR2016PTC031689
Name of the Promoter's Entity	HAUSLINE DEVELOPERS PRIVATE LIMITED
Address of the Promoter's Entity :	FLAT NO 208,OLD PATLIPUTRA COLONY ROAD NO 2 PATNA Patna BR 800013 IN
Total Experience of promoter in Real Estate Sector	1
Total Experience in Real Estate After commencement of RERA	1
No of Project done Before commencement of RERA	0
No of Project done After commencement of RERA	1. Hausline city (Ongoing)

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP12460-001/153/R-1628/2023
Name of Project	HAUSLINE CITY
Name of Promoter	HAUSLINE DEVELOPERS PRIVATE LIMITED
Project Address	GODHNA, BIHTA, DANAPUR, PATNA
Project Registration is valid up to	01/08/2028
Starting date of Project	01/11/2023
Type of Project	Mixed
Name of the Competent Authority which sanctioned the project map	Patna Metropolitan area authority (PMAA)
Period of validity of map by the Competent Authority	5 Years from the date of passing of MAP

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share– 57		Total Number of Apartments in Landowner's share–44	
				Booked	AFS Executed	Booked	AFS Executed
Hausline City Block A	3 BHK	890.73	24				
Hausline City Block A	3 BHK	912.43	6	1	1		
Hausline City Block A	3 BHK	912.40	6	3	2		
Hausline City Block A	3 BHK	892.55	6	2	1		
Hausline City Block A	3 BHK	874.88	6				
Hausline City Block A	2 BHK	757.02	6				
Hausline city Block A	Shop	365.6	1				
Hausline city Block A	Shop	340.62	1				
Hausline city Block A	Shop	286.12	2				
Hausline city Block A	Shop	717.58	1				
Hausline city Block A	Shop	502.52	1				
Hausline city Block A	Shop	200.37	2	1			
Hausline city Block A	Shop	238.54	1	1	1		
Hausline city Block A	Shop	256.03	1	1	1		
Hausline city Block A	Shop	351.06	1	1	1		
Hausline city Block A	Shop	327.08	2				
Hausline city Block A	Shop	351.06	1				
Hausline city Block A	Shop	174.41	1				
Hausline city Block A	Shop	125.76	1				
Hausline city Block A	Shop	189	2				
Hausline city Block A	Shop	225	1				
Hausline city Block A	Shop	241.5	1				

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share- 57		Total Number of Apartments in Landowner's share-44	
				Booked	AFS Executed	Booked	AFS Executed
Hausline city Block A	Shop	755.12	1				
Hausline city Block A	Shop	274.74	1	2	2		
Hausline city Block A	Shop	274.75	1				
Hausline City Block B	3 BHK	854.72	14	8	7		
Hausline City Block B	3 BHK	851.63	7	1	1		
Hausline City Block B	3 BHK	793.38	7				
Total no.			101	21	17	0	0
Percentage of total Units				36.84 % of total units	29.82 % of total units	00% of total units	00% of total units

IV. DETAILS OF ASSOCIATION OF ALLOTTEES :

Mandatory in case the booking percentage exceeds 50% of the total sanctioned flats/plots/buildings/commercial space

- Association of Allottee not be made because, booking percentage not exceeds 50% yet.

V. CANCELLATION OF FLAT ALLOTMENT, IF ANY WITH FLAT NUMBER/BUNGALOW /PLOT NO. /OFFICE SPACE/SHOP/ETC.

(A) Cancelled by Allotees No Any	(B) Cancelled by Promoters No Any
--	---

VI. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES/ PARKING SPACE

Building Wise/ Block Number	Total Number of Sanctioned Garages/ Parking Space	Total Number of Garages/Parking Space: 1. Booked/Allotted -
Hausline City	101	<u>21</u>

VII. DETAILS OF BUILDING APPROVALS

Already filed along with Registration Application

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Validity Upto		Attach Copy
1.	Environment Clearance				
2.	Fire N.O.C.				
4.	Airport Authority of India NOC				
5.	Water Supply Permission				
6.	Other Approval(s), if any, required for the Project.				

VIII. PROGRESS OF THE PROJECT – INTERNAL INFRASTRUCTURE DEVELOPMENT

In case of more than one Block/Building/Apartments/Plots/Bungalow, the details have to be filled for each Block separately

1. Plan Case No.- PMAA/PCRN/GODHNA/BIHTA/BLOCK -A (B+G+07)/24/2020 (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	0%	14-05-2025
2.	Piling	0%	14-05-2025
3.	Basements (if any)	0%	20-06-2025
4.	Podiums (if any)	NA	
5.	Plinth	0%	14-09-2025
6.	Stilt Floor	0%	25-07-2025
7.	Slabs of Super Structure	0%	30-05-2026
8.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	30-06-2027
9.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	30-10-2027
10.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	30-06-2027

11.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	30-12-2027
12.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per prescribed norms.	0%	30-07-2027
13.	N.O.C, Electrical fittings, Mechanical Equipment, compliance to conditions of environment as per prescribed norms	0%	30-07-2027
14.	Finishing to entrance lobby/s plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities.	0%	30-07-2027
15.	Overall Percentage of Actual Work Done and final completion date	0%	30-07-2028

VIII. PROGRESS OF THE PROJECT – INTERNAL INFRASTRUCTURE DEVELOPMENT

In case of more than one Block/Building/Apartments/Plots/Bungalow, the details have to be filled for each Block separately

1. Plan Case No.- PMAA/PCRN/GODHNA/BIHTA/BLOCK -B (B+G+07)/24/2020 (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	0%	14-03-2025
2.	Piling	85%	14-02-2025
3.	Basements (if any)	0%	20-06-2025
4.	Podiums (if any)	NA	
5.	Plinth	0%	14-05-2025

6.	Stilt Floor	0%	25-07-2025
7.	Slabs of Super Structure	0%	30-05-2026
8.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	30-06-2027
9.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	30-10-2027
10.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	30-06-2027
11.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	30-12-2027
12.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per prescribed norms.	0%	30-07-2028
13.	N.O.C, Electrical fittings, Mechanical Equipment, compliance to conditions of environment as per prescribed norms	0%	30-07-2028
14.	Finishing to entrance lobby/s plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per Specifications in Agreement of Sale. Any other activities.	0%	30-07-2028
15.	Overall Percentage of Actual Work Done and final completion date	6.53 %	30-07-2028

IX. EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS - PROGRESS RELATED TO AMENITIES AND COMMON AREA

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format

(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	0%	30-06-2027
2.	Water Supply	Yes	0%	30-06-2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0%	30-06-2027
4.	Storm Water Drains	No	NA	
5.	Landscaping & Tree Planting	Yes	0%	30-06-2027
6.	Street Lighting	No	NA	
7.	Community Hall and GYM	Yes	0%	30-06-2027
8.	Treatment and Disposal of Sewage and Sullage Water	No	NA	
9.	Solid Waste Management & Disposal	No	NA	
10.	Water Conservation / RainWater Harvesting	Yes	0%	30-06-2027
11.	Energy Management	No	NA	
12.	Fire Protection and FireSafety Requirements	Yes	0%	30-06-2027
13.	Closed Parking	Yes	0%	30-06-2027
14.	Open Parking	No	NA	
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	0%	30-06-2027
16.	Others (Option to AddMore)	No	NA	
17.	Overall Percentage of Actual Work Done and final completion date	Yes	1	30-07-2027

X. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

Our Project is residential hence not applicable.

XI. Financial Progress of the Project

S.No. (1)	Particulars (2)	Amount (in Rs.) (3)
--------------	--------------------	------------------------

1	Project Account No.	923020023063387
2	Estimated Cost of the Project including land cost at the start of the Project	8,74,34,392.00/-
3	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost)	51639392.00/-
4	Any Variation in Development Cost which is declared at the start of the Project.	No Any
5	Amount received during the Quarter	13,48,000.00/-
6	Actual Cost Incurred during the Quarter	13,11,711.00/-
7	Net amount at end of the Quarter	36,000.00/-
8	Total expenditure on Project till date	37,53,411.00/-
9	Cumulative fund collected till the end of Quarter in question	50,03,615.00/-
10	Cumulative expenditure done till the end of Quarter in question	37,53,411.00/-
11	Percentage of Expenditure incurred of the total Estimated development cost of the project.	7.26 %

XII. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED/DETAILS OF LOAN TAKEN BY PROMOTERS AGAINST THE PROJECT, If any

NO Any

XIII. GEO TAGGED PHOTOGRAPHS (EACH BLOCK/BUILDING/APARTMENTS/PLOTS/BUNGALOW) OF THE PROJECT The photograph must have date.

(A)	S. No.	Particulars
	1.	Photographs showing Front Elevation.- Attached Below
	2.	Photographs showing Rear Elevation.- Attached Below
	3.	Photographs showing Side Elevation (Both sides) Attached Below
	4.	Photograph of each floor showing the progress of interior works
	5.	Photograph of Common Areas (Staircase, Lift Area, Terrace, Parking, etc.)
(B)		Photograph of the display board set up at the project site providing requisite information along with the QR code of the project allotted by the Authority

XIV. MISCELLANEOUS


A	List of Legal Cases (if any) On Project / Promoter
---	--

1.	(a)Case No. (b)Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
2.	No. of Execution Cases against this project (a) Case No. (b) Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
3.	No. of Suo - Moto cases against this project (a) Case No. (b) Name of Parties Order Passed, if Yes , Whether complied (Yes/No)	NA
4.	No. of Certificate cases /PDR cases against this project (a) Case No. (b) Name of Parties Order Passed, if Yes, Whether complied (Yes/No)	NA


XV. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

- a. Whether the project is in progress as per time schedule or lagging behind? Yes
- b. If yes, whether it would be completed on the completion date fixed as per RC.
Yes
- c. If No, then Reason for delay:

PROGRESS CHART BLOCK A



PROGRESS CHART BLOCK B

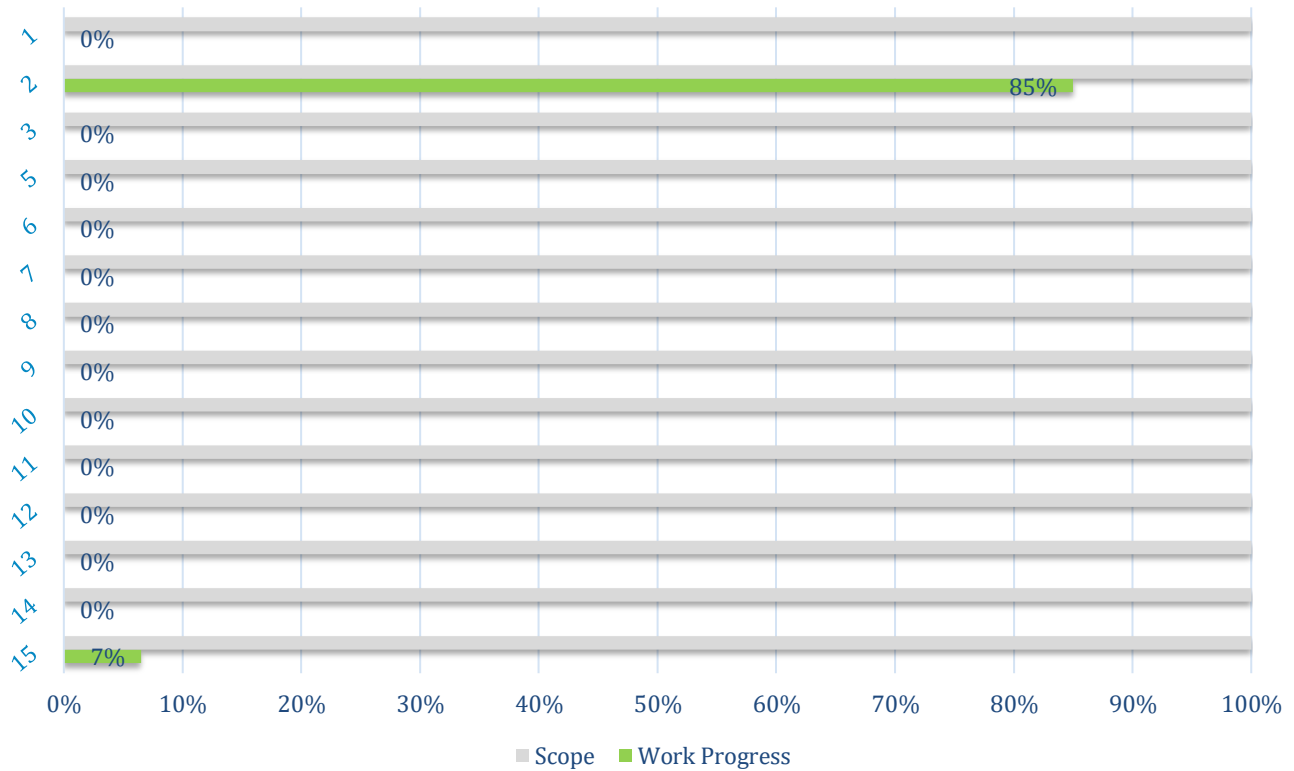

XVI. BROCHURE /Prospectus - Attached Below

XVII Grievance Redressal Officer

Name: Prem Kumar
 Contact No: 9931643931
 Email id: hauslinedevelopers@gmail.com
 Address: GODHNA, BIHTA, DANAPUR, PATNA

Project Site Photographs





Neora, Bihar, India

Hxjg+x4q, Neora, Bihar 801113, India

Lat 25.582964° Long 84.974906°

12/04/2025 12:51 PM GMT +05:30

GPS Map Camera



GPS Map Camera

Chaura Gopalpur, Bihar, India

Hxmf+2m7, Chaura Gopalpur, Bihar 801113, India

Lat 25.583018° Long 84.974734°

12/04/2025 02:58 PM GMT +05:30



GPS Map Camera

Chaura Gopalpur, Bihar, India

Hxmf+2m7, Chaura Gopalpur, Bihar 801113, India

Lat 25.582952° Long 84.974687°

12/04/2025 02:57 PM GMT +05:30

Google



Neora, Bihar, India

Hxjg+x4q, Neora, Bihar 801113, India

Lat 25.583031° Long 84.974985°

12/04/2025 12:52 PM GMT +05:30

GPS Map Camera



GPS Map Camera



Neora, Bihar, India

Hxjg+x4q, Neora, Bihar 801113, India

Lat 25.583057° Long 84.974768°

12/04/2025 02:59 PM GMT +05:30

BROCHURE:

HAUSLINE
DEVELOPERS PVT. LTD.
Smart Move To Smart Home...

RERA BIHAR WEBSITE:
Rera.bihar.gov.in

QR CODE

RERA NO:- BRERAP12460-001/153/R-1628/2023

HAUSLINE CITY
COMMERCIAL / RESIDENTIAL
AT SHIWALA GORHANA

Happy Home Hausline Home

APPROVED

The brochure features a 3D architectural rendering of a modern, multi-story apartment building with a blue and white facade, balconies, and a ground-floor commercial area. The building is set against a light blue sky with stylized clouds. A large, stylized red and orange graphic element, resembling a rising sun or a stylized 'H', is positioned behind the building. The text 'HAUSLINE CITY' is prominently displayed in large, bold, red and orange letters. Below it, 'COMMERCIAL / RESIDENTIAL' and 'AT SHIWALA GORHANA' are written in smaller, bold, black letters. At the bottom, the slogan 'Happy Home Hausline Home' is written in a playful, red font with yellow smiley faces. The top left corner contains the Hausline Developers Pvt. Ltd. logo and tagline. The top center features a QR code and the RERA Bihar website address. The top right corner displays the RERA registration number and a red circular 'APPROVED' stamp.



Available Flat 2BHK & 3BHK

Block - A
2D Floor Plan (2nd to 7th)

AREA STATEMENT

SL.NO.	B.V.U AREA	CARPET AREA	BLOOM AREA	B.V.U AREA	FLOOR
01	1076.15 sqft	886.55 sqft	189.57 sqft	1461.28 sqft	2BHK
02	886.75 sqft	787.08 sqft	98.90 sqft	1163.17 sqft	2BHK
03	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK
04	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK
05	1180.89 sqft	918.48 sqft	176.89 sqft	1476.26 sqft	2BHK
06	1180.89 sqft	918.48 sqft	176.89 sqft	1476.26 sqft	2BHK
07	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK
08	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK
09	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK
10	1083.77 sqft	886.73 sqft	98.90 sqft	1289.50 sqft	2BHK



Block - B

2D Floor Plan (1st to 7th)

AREA STATEMENT

SL.NO.	B/U AREA	CARPET AREA	BALCONY AREA	S. B/U AREA	PLAT
01	968.54 sqft.	854.72 sqft	93.00 sqft	1255.84 sqft	3BHK
02	968.54 sqft.	854.72 sqft	93.00 sqft	1255.84 sqft	3BHK
03	968.54 sqft	801.63 sqft	93.00 sqft	1255.84 sqft	3BHK
04	908.57 sqft	793.38 sqft	93.00 sqft	1181.14 sqft	3BHK



Block - A, First Floor
2D Floor Plan (Commercial)

AREA STATEMENT:-

S.N.	SQ. AREA	CARPET AREA	SQ. AREA
01	294.53 sqft.	265.80 sqft.	559.59 sqft.
02	298.74 sqft.	240.89 sqft.	489.69 sqft.
03	312.42 sqft.	288.12 sqft.	421.78 sqft.
04	312.42 sqft.	288.12 sqft.	421.78 sqft.
05	757.07 sqft.	717.58 sqft.	1088.04 sqft.
06	691.80 sqft.	608.52 sqft.	717.85 sqft.
07	219.25 sqft.	200.37 sqft.	295.98 sqft.
08	219.25 sqft.	200.37 sqft.	295.98 sqft.
09	254.54 sqft.	239.24 sqft.	348.85 sqft.
10	276.79 sqft.	258.03 sqft.	378.58 sqft.
11	276.19 sqft.	251.08 sqft.	307.86 sqft.
12	246.05 sqft.	227.08 sqft.	427.16 sqft.
13	298.05 sqft.	274.74 sqft.	402.36 sqft.
14	298.05 sqft.	274.75 sqft.	402.36 sqft.
15	246.05 sqft.	227.08 sqft.	427.16 sqft.
16	276.19 sqft.	251.06 sqft.	307.86 sqft.
17	197.12 sqft.	176.41 sqft.	266.11 sqft.
18	148.55 sqft.	125.76 sqft.	198.52 sqft.
19	202.54 sqft.	182.00 sqft.	282.85 sqft.
20	207.80 sqft.	182.00 sqft.	279.79 sqft.
21	290.57 sqft.	235.00 sqft.	394.76 sqft.
22	281.52 sqft.	241.50 sqft.	353.05 sqft.
23	795.28 sqft.	755.18 sqft.	1079.54 sqft.





Specifications

STRUCTURE

- Foundation Reinforced Cement Concrete.
- Super Structure Reinforced Cement Concrete.
- Steel: Standard Quality & ISI Marked.

KITCHEN

- Granite Platform Slab
- Dado Glazed Tiles
- Vitrified Tiles / Marble / Equivalent
- Stainless Steel Sink
- Fitting/Fixtures
- External Wall: Wall Putty & Apex Paint
- Internal Walls: Plaster of Paris

TOILET

- Floor: Tiles / Equivalent
- Wall: Tiles / Ceramics Tile upto 7ft. height

LIFT

- 2 Lift of 8 Passengers Capacity in each block

BEDROOMS/LIVING/DINNING/LOBBY/PASSAGES

- Floor: Vitrified Tiles/Equivalent
- Walls: Plaster of Paris
- Doors: Internal Doors Chowkhats Wood with Beading PVC Door Shutter & Frame
- WINDOWS: uPVC Frame with Glass Fitting & Steel Grill Brass Fitting
- INTERCOM: Facility in each Flat

GENERATOR

- Silent Generator of Adequate Capacity.

FIRE SECURITY

- Fire safety Equipment



Superior Location

Use only premium Material

More amenities

Better utility of space and ventilation

Kids and senior citizens friendly

Common Amenities



Common Amenities

- | | | | |
|-------------------------|------------------|-------------------|---------------|
| CCTV | Power Back up | Intercom facility | Tennis Court |
| Lift | Reserved Parking | Security | Temple |
| Water supply & Drainage | Swimming Pool | Play Ground | Jogging Track |



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

HAUSLINE DEVELOPERS PVT. LTD
 Bern K.
 DIRECTOR

Name: HAUSLINE DEVELOPERS PRIVATE LIMITED

Date: 13-04-2025
