


FORM-7[REGULATION-9]

Quarterly progress report for quarter ending March-2025

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number CIN/No/Partnership deed no LLP Details/Any other registration with MSME Or Govt. Bodies	DEED NO.-13961 GSTIN-10AETFS4075E1ZZ	Name of Firm	SANKALP GREEN HOMES
Firm Address:	Ground Floor, Das Enclave, East Lohanipur, Kadamkuan, Patna-800003.		
Total Experience of promoter in Real Estate sector	Experience of promoter in Real Estate Sector Since 30/06/2022.		
Total Experience in Real Estate After Implementation of RERA	Since-30/06/2022.		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project	NIL NIL NIL NIL	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential-cum Commercial 4. Plotted project	NIL NIL NIL NIL	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP12714-002/64/R-1712/2024	Name of Project/Phase of Registered Project	Ghosh Enclave
Name of Promoter	SANKALP GREEN HOMES	Project Address	Jakkanpur (Khesra/Plot No-20(P), 23 (P) Khata N.-26, 27, Thana No-29, Mauza-Jakkanpura, Dist-Patna
Name of Co-promoter	NIL		
Project Registration is valid upto	14/12/2026		
Starting date of Project or Phase Of the Project	27/02/2024		
Type of Project or Phase of the Project	1 Residential 2 Commercial 3 Residential-cum-Commercial 4 Plotted project	Residential	
Period of validity of map by the Competent Authority	15/12/2023 TO 14/12/2028		

For
SANKALP GREEN HOMES
Rajesh Kumar Singh
PARTNER


PANKAJ KR. KARN
EMPANELLED ENGINEER)
EMP. No.-BR/UDHD/CE/23-0012
UDHD, Bihar



III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building /Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share- 1. Booked /Allotted-3 Up to Last - 2. Sold- Nil	Total Number of Apartments in Landowner's share- 3. Booked/ Allotted- Nil Sold - Nil
	1. 1BHK 2. 2BHK,- 3. 3BHK 4. Shop 5. Bungalow 6. Plot etc.	2+2 6+6	1650 5275 (Promoter's Share) 2+6=8 Land owner's Share 2+6=8		
				Percentage of booking- 37.5%	Percentage of booking- Nil

IV. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES			
Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 3
I	16	2. Sold	- Nil

V. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S.No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.	State fire officer cum Director, Bihar - Patna	05/06/2023		
3.	Water Supply Permission				
4.	NOC from Airport Authority of India	Générale manager airport authority of India / N.S.C.B.I. AIRPORT KOLKATTA	20/07/2023		
5.	Other Approval(s), if any, required for the Project.				

For **SANKALP GREEN HOMES**
Rajesh Kumar Singh
 PARTNER

Pankaj Kr. Karn

ER. PANKAJ KR. KARN
 EMPANELLED ENGINEER)
 EMP. No.-BR/UDHD/CE/23-0012
 UDHD, Bihar



VI. CONSTRUCTION PROGRESS OF THE PROJECT			
1. Plan Case No. _____ (To be added for each Building/Wing)			
S.No. (1)	Tasks/Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	No	
2.	Basements (if any)	No	
3.	Podiums (if any)	No	
4.	Plinth	No	
5.	Stilt Floor	No	
6.	Slabs of Super Structure	3 rd floor slab work completed	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats / Premises.	Yes Internal wall Work Started	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	Yes Work Not Started	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	Yes Work Not Started	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	Yes Work Not Started	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas Appurtenant to Building/Wing, Compound Wall and all other	Yes Work Not Started	

For
SANKALP GREEN HOMES
Rajesh Kumar Singh
PARTNER

Pankaj Kr. Karn
ER. PANKAJ KR. KARN
 EMPANELLED ENGINEER)
 EMP. No.-BR/UDHD/CE/23-0012
 UDHD, Bihar



	requirements as may be required to complete project as per Specifications in Agreement of Sale.		
	Any other activities.		

VILAMENITIESAND COMMONAREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed(Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	Work Not Started	Yes
2.	Water Supply	Yes	Work Not Started	Yes
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	Work Not Started	Yes
4.	Storm Water Drains	No	-	No
5.	Landscaping & Tree Planting	Yes	Work Not Started	Yes
6.	Street Lighting	Yes	Work Not Started	Yes
7.	Community Buildings	No	-	No
8.	Treatment and Disposal of Sewage and Sullage Water	No	-	No
9.	Solid Waste Management & Di sposal	No	-	No
10.	Water Conservation/Rain Water Harvesting	Yes	Work Not Started	Yes
11.	Energy Management	No	-	No

For
SANKALP GREEN HOMES
Rajesh Kumar Singh
PARTNER

Pankaj Kr. Karn
PANKAJ KR. KARN
EMPANELLED ENGINEER)
EMP. No.-BR/UDHD/CE/23-0012
UDHD, Bihar

12.	FireProtectionandFire Safety Requirements	Yes	Work Not Started	Yes
13.	ClosedParking	Yes	Work Not Started	Yes
14.	OpenParking	No	-	No
15.	ElectricalMeterRoom.Sub-Station, Receiving Station	Yes	Work Not Started	Yes
16.	Others(OptiontoAdd More)	-	-	-

VIII. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSE D YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As On date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths	Yes	Work Not Started	Yes
2.	Water Supply	Yes	Work Not Started	Yes
3.	Sewerage Chambers Septic Tank	Yes	Work Not Started	Yes
4.	Drains	Yes	Work Not Started	Yes
5.	Parks, Land Scaping and Tree Planting	Yes	Work Not Started	Yes
6.	Street Lighting	Yes	Work Not Started	Yes
7.	Disposal of sewage & sullage water	No	-	No
8.	Water conservation/Rain Water Harvesting	Yes	Work Not Started	Yes
9.	Energy Management	No	-	No

For
SANKALP GREEN HOMES
Rajesh Kumar Singh
PARTNER

Pankaj Kr. Karn
ER. PANKAJ KR. KARN
 (EMPANELLED ENGINEER)
 EMP. No. - BR/UDHD/CE/23-0012
 UDHD, Bihar



IX. GEOTAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr.No.		
	1.	Front Elevation	✓
	2.	Rear Elevation	✓
	3.	Side Elevation	✓
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT		
S.No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	ICICI BANK A/C NO.- 030705009887
2.	Estimated Cost of the Project including land cost at the start of the Project	Development cost 26904000, Land owner cost 22715000
3.	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost)	Development cost 26904000
4.	Any Variation in Development Cost which is declared at the start of the Project.	NA
5.	Amount received during the Quarter (Own Fund)	2300000.00
6.	Actual Cost Incurred during the Quarter (Money Spent)	2397825.00
7.	Net amount at end of the Quarter	108171.00
8.	Total expenditure on Project till date	10186523.00
9.	Cumulative fund collected till the end of Quarter in Question (Including Own Fund)	9432106.00
10.	Cumulative expenditure done till the end of Quarter in question	10186522.00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED	

For
SANKALP GREEN HOMES
Rajesh Kumar Singh
PARTNER

Pankaj Kr. Karn
ER. PANKAJ KR. KARN
 (EMPANELLED ENGINEER)
 EMP. No.-BR/UDHD/CE/23-0012
 UDHD, Bihar

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project/Promoter	
1.	Case No.	
2.	Name of Parties	
3.	No. of Execution Cases against this project Case No. Name of Parties	
4.	No. of Suit-Motocases against this project Case No. Name of Parties	
5.	No. of Certificate cases/PDR cases against this project Case No. Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	Nil
2.	Agreement for Sale	1
3.	No. of possessions given to allottees	
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Whether the project in progress is as per times schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes


For this undertaking
SANKALP GREEN HOMES
Rajesh Kumar Singh
 PARTNER

Pankaj Kr. Karn

Signature of Promoter
 Name:
 PARTNER
 Date: 09/04/2025.

ER. PANKAJ KR. KARN
 EMPANELLED ENGINEER)
 EMP. No.-BR/UDHD/CE/23-0012
 UDHD, Bihar



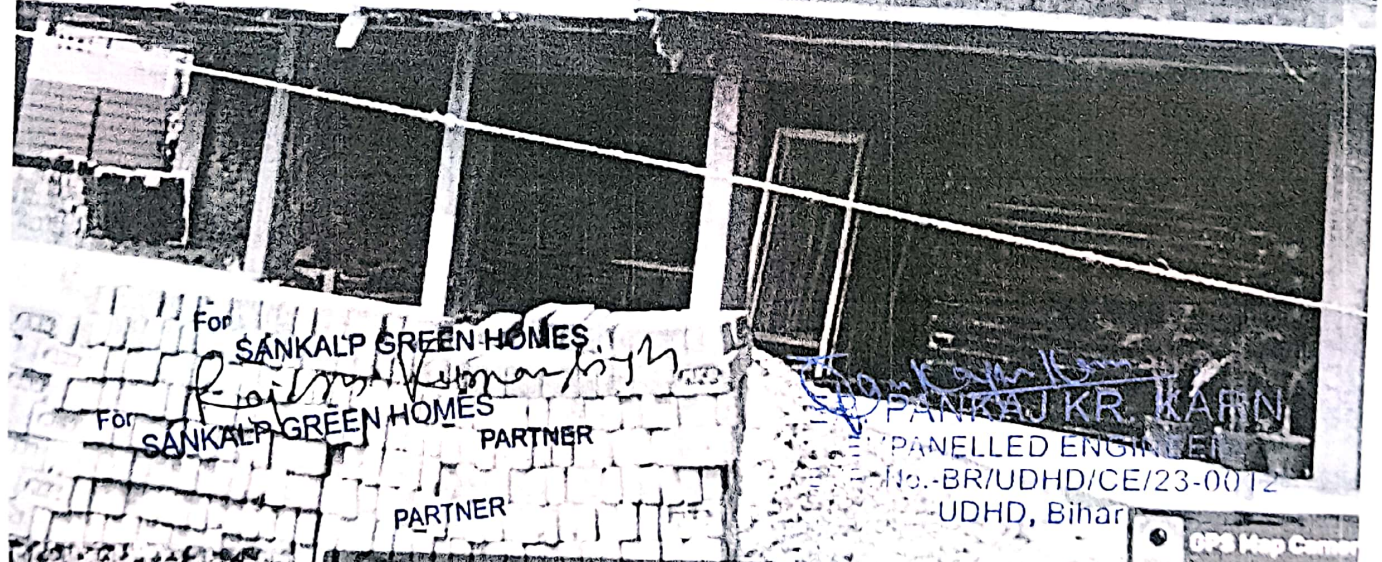

For
SANKALP GREEN HOMES
For
SANKALP GREEN HOMES
PARTNER
PARTNER

PANKAJ KR. KARN
PANELLED ENGINEER
No.-BR/UDHD/CE/23-0012
UDHD, Bihar

GPS Map Camera

Patna, Bihar, India
Dr, Nc Ghosh Ln, New Jakkampur, Gardaniabagh, Patna,
Bihar 800001, India
Lat 25.593774° Long 85.125805°
11/04/25 10:11 AM GMT +05:30

Google

ER PANKAJ KR. KARNI
EMPANELLED ENGINEER
EMP. No. BR/UDHD/CE/23-0012
UDHD, Bihar

For SANKALP GREEN HOMES

GPS Map Camera

Patna, Bihar, India
H4vg+f2w, Nc Ghosh Ln, New Jakkanpur, Gardanibagh,
Patna, Bihar 800001, India
Lat 25.593764° Long 85.125198°
11/04/25 10:49 AM GMT +05:30

Google



Scanned with OKEN Scanner

For SANKALP GREEN HOMES

PARTNER

ER. PANKAJ KR. KARN
(EMPANELLED ENGINEER)

EMP. No. B-50470, Bihar
HEAD, Bih

Patna, Bihar, India
H4vg+h5g Laxmi Market, Gandhi Path, Jakkanpur,
Gardanibagh, Patna, Bihar 800001, India
Lat 25.593814° Long 85.125463°
11/04/25 10:50 AM GMT +05:30

Google

