

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	233/2024	Name of Firm	APNA GHAR ASSOCIATES
Firm Address :	Holding – 5, Ward No – 14, Nandan Park, Nandan Park Chowk, Deoghar, Jharkhand – 814112 and Kali Bari, 103, Gulmohar Apartment, Manik Sarkar Ghat Road, Manik Sarkar, Bhagalpur, Bihar - 812002		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA			
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP12593-001/11/R-1717/2024	Name of Project/Phase of Registered Project	NEELAM HEIGHTS
Name of Promoter	APNA GHAR ASSOCIATES	Project Address	KHARMANCHAK, D.N ROAD, KHALIPHABAGH, BHAGALPUR
Name of Co-promoter	N/A		
Project Registration is valid up to	13/12/2028		
Starting date of Project or Phase of the Project	24/06/2024		
Type of Project or Phase of the Project	Residential- cum- Commercial		
Period of validity of map by the Competent Authority	13/12/2028		

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - 11	Total Number of Apartments in Landowner's share - 11
	1. 1 BHK			FLAT-20 HALL-02	1. Booked / Allotted -NIL	3. Booked/ Allotted-NIL
	2. 2 BHK, -	05			2. Sold-NIL	Sold -NIL
	3. 3 BHK	15				
	4. Shop	02				
	5. Bungalow					
	6. Plot etc.				Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	NIL
	20	2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR CUM STATE FIRE OFFICER, BIHAR, PATNA		16-08-2023	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No.

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	80%	15-01-2025
2.	Basements (if any)	40%	10-07-2025
3.	Podiums (if any)	N/A	
4.	Plinth	40%	12-04-2025
5.	Stilt Floor		
6.	Slabs of Super Structure	10%	18-12-2027
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	22-02-2028 18-06-2028 21-07-2028 28-05-2028
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	21-08-2028 16-07-2028
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	10% 10% 0%	14-02-2028 11-07-2028 26-06-2028
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	05-02-2028 05-02-2028 16-08-2028 12-07-2028

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	10-08-2028
		100%	
		0%	06-09-2028
		0%	31-07-2028
		0%	28-08-2028
		0%	30-09-2028
	Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	20-10-2028
2.	Water Supply	YES	15%	25-02-2028
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30-01-2028
4.	Storm Water Drains	NO	N/A	
5.	Landscaping & Tree Planting	YES	0%	25-09-2028
6.	Street Lighting	YES	0%	30-08-2028
7.	Community Buildings	NO	N/A	

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	15-04-2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	10-05-2028
11.	Energy Management	YES	0%	20-03-2028
12.	Fire Protection and Fire Safety Requirements	YES	50%	05-06-2028
13.	Closed Parking	YES	80%	01-07-2028
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO	N/A	
16.	Others (Option to Add More)	NO	N/A	


VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT


		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	Attach

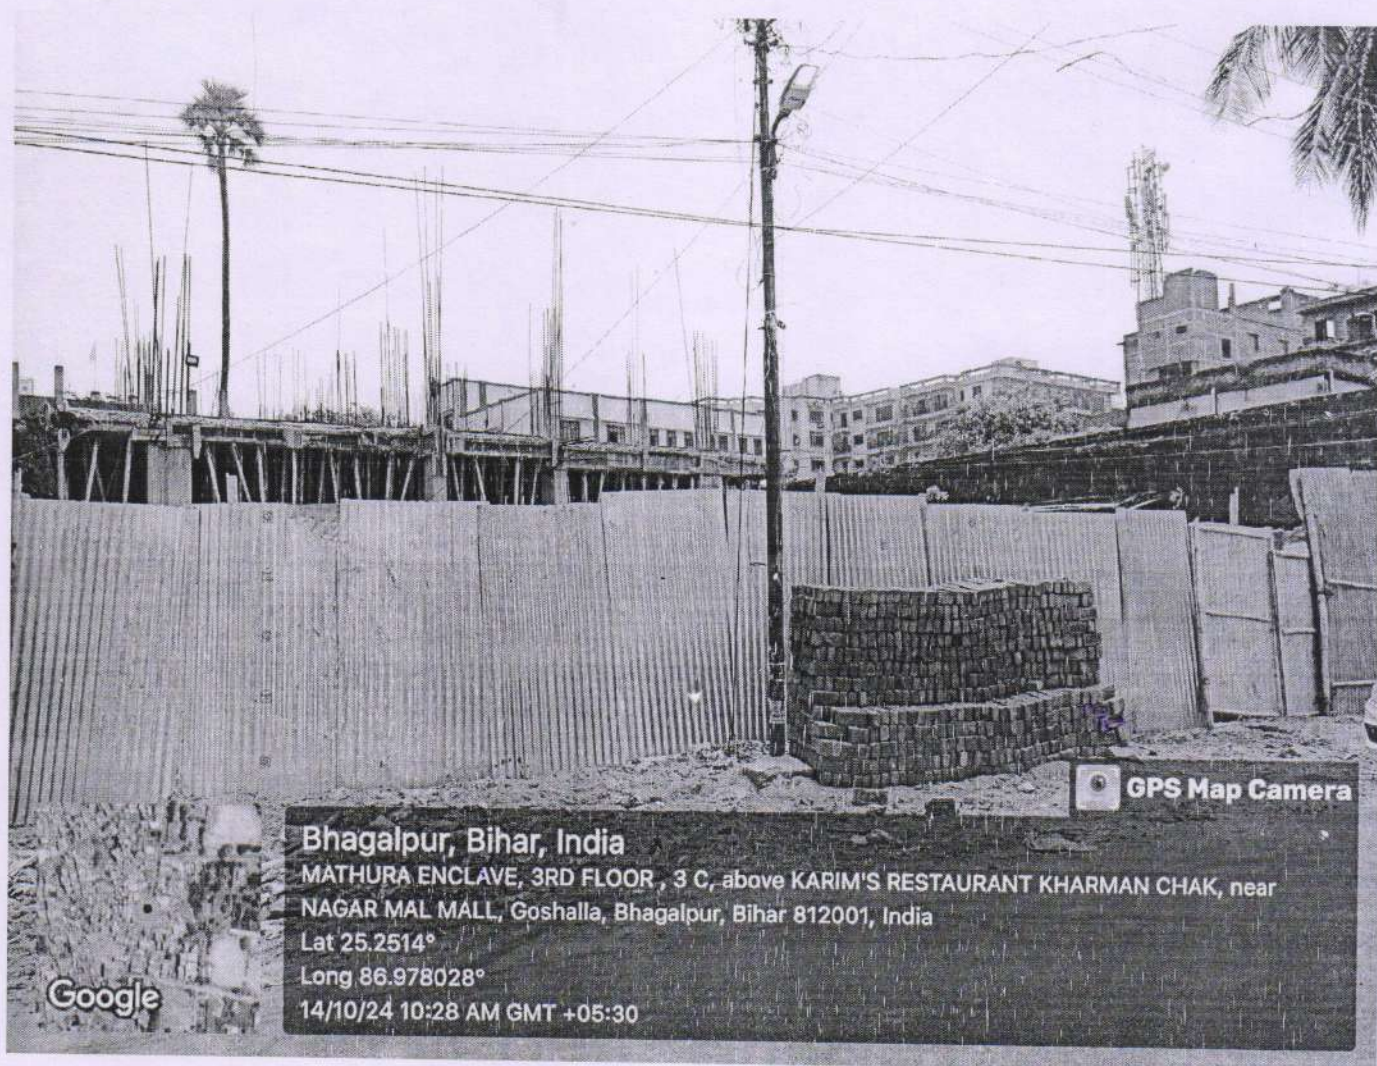

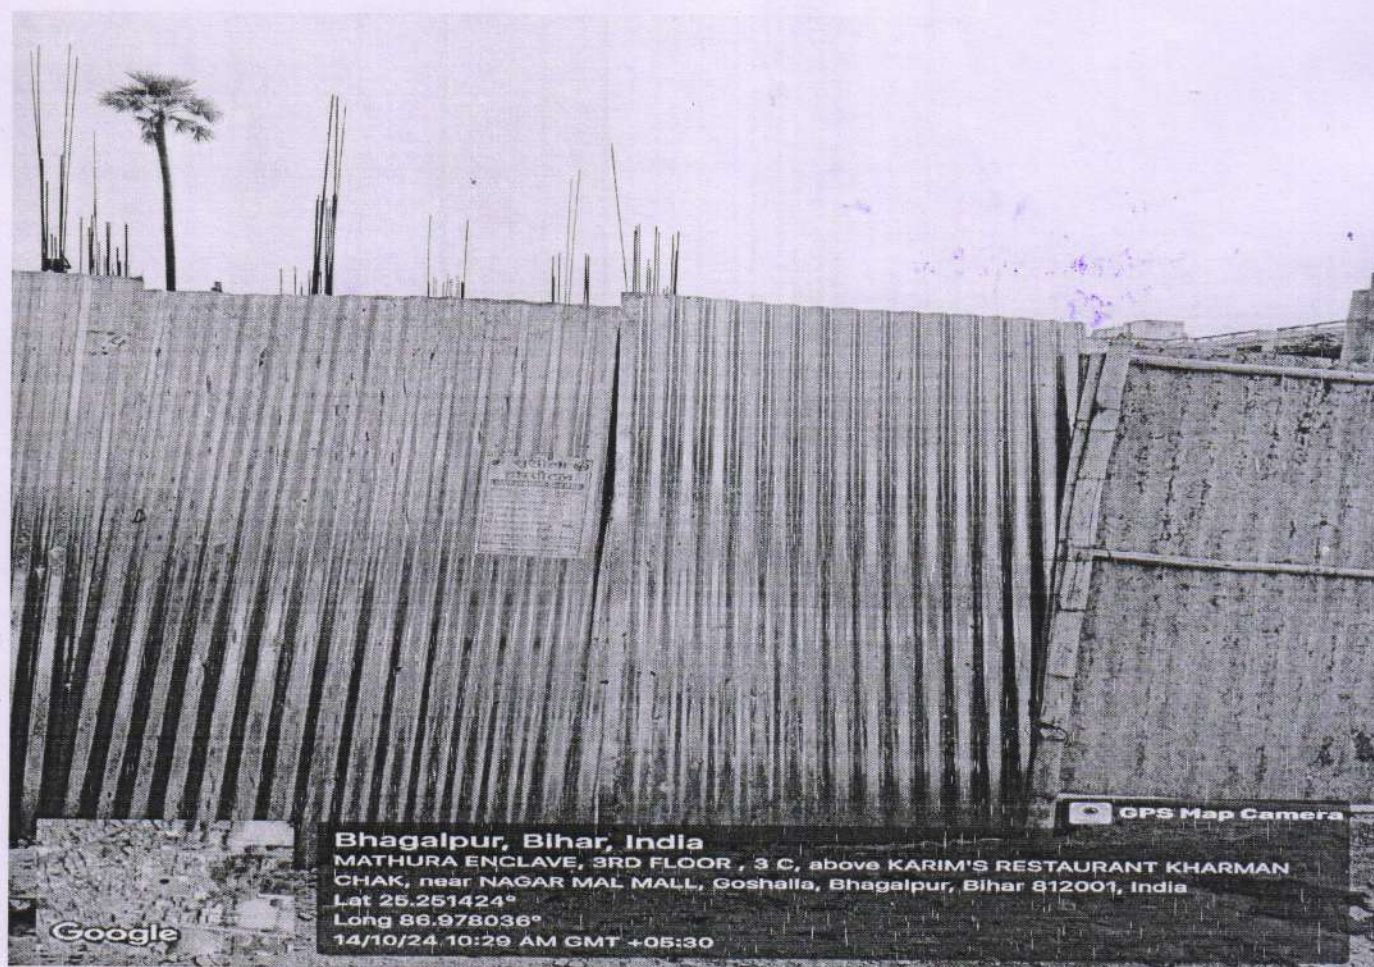

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	120026303196
2.	Estimated Cost of the Project including land cost at the start of the Project	6,18,36,384=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	2,53,76,384=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	N/A
5.	Amount received during the Quarter	0
6.	Actual Cost Incurred during the Quarter	49,04,275=00
7.	Net amount at end of the Quarter	4,09,370=00
8.	Total expenditure on Project till date	2,00,96,377=00
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK, -05 3 BHK-15 4 BHK- Shop- 02 Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc NO BOOKING	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
XV. BROCHURE /Prospectus		

XVI Grievance Redressal Officer

Name : KUMAR ABHIJEET

Contact No : 7004918677

Email id : apnaghardgr20@gmail.com

Address : NANDAN PAHAR CHOWK, DEOGHAR

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

APNA GHAR ASSOCIATES

Kumar Abhijeet
PARTNER

Signature of Promoter

Name: KUMAR ABHIJEET

Date: 14-10-2024
