

QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Jul - Sep, 2019

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

INDRALOK GARDEN

PROMOTER NAME

INDRALOK CONSTRUCTIONS

RERA REGISTRATION NO.

BRERAP00506-3/977/R-669/2019



PROJECT QUARTERLY PROGRESS STATUS

Quarter: Jul-Sep, 2019

Project Description: A mixed use Real Estate project consisting of LB+UB+G+4 Floors. The project has 12 flats premium 3 BHK flats and shops and offices.


Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	90%	Excavation works are being carried out partially at a time to avoid caving of soil.
2	Foundation Works	Yes	85%	Partial PCC has been done on which raft reinforcement works is being carried out.
3	Lower Basement	Yes	22%	Retaining wall is 60% complete.
4	Slabs of structure	Yes	7%	Columns from lower basement to upper basement is complete. Shuttering and reinforcement work is under progress.
5	Walls	Yes	0%	Brickwork and subsequent finishing activities yet to start.
6	Internal Plaster& Putty	Yes	0%	
7	Flooring inside units and common areas	Yes	0%	
8	Doors and Window to each of unit and common areas	Yes	0%	
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	0%	
10	Electrical fitting within the unit	Yes	0%	
11	Staircase, lift walls and lobbies at each floor	Yes	0%	
12	Water tank	Yes	0%	

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	0%	
14	External Plaster	Yes	0%	
15	External Paint	Yes	0%	
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	11%	Submersible pump has been installed.

PROGRESS CHART

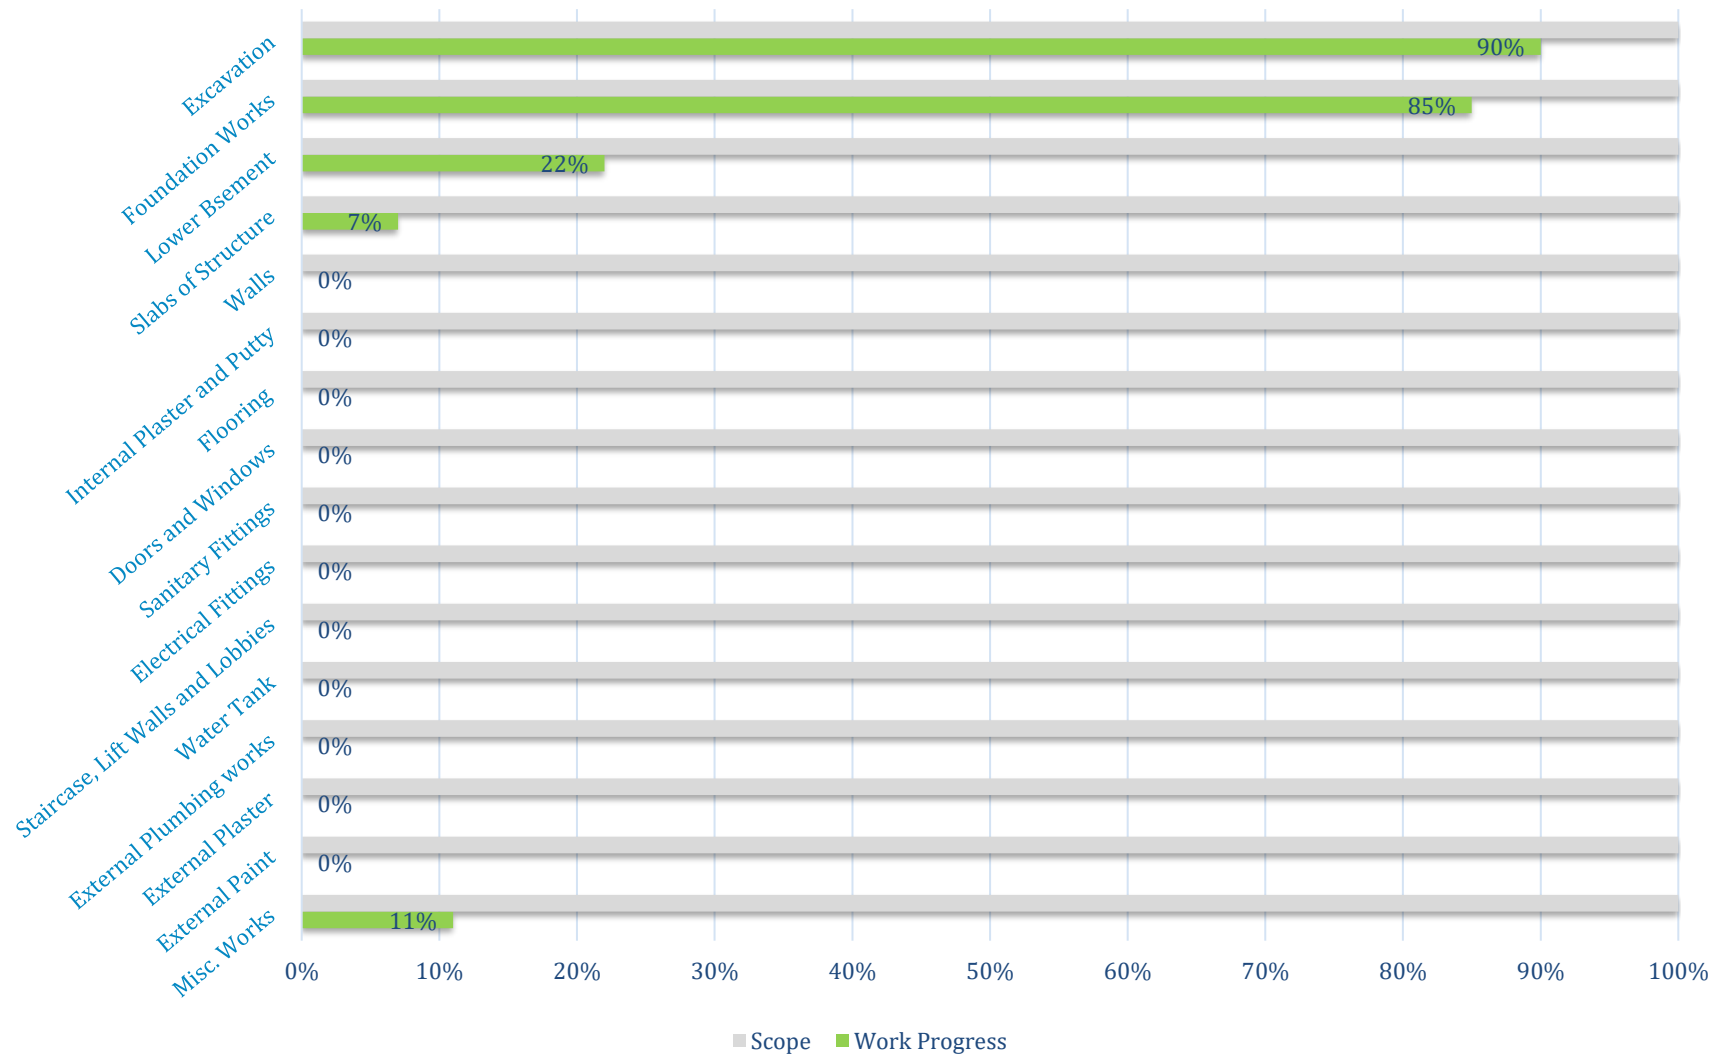

Progress Update for Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	50%	Compound wall brickwork erection has already been done. Finishing works yet to start.
2	Water supply	Yes	40%	Boring works complete and supply pipes installation balance.

Update on number and types of flats/units booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Units Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	3 BHK	7	0	2	0	2	0	2	0	2
2	Shop	1	0	0	0	0	0	0	0	0
3	Office	1	0	0	0	0	0	0	0	0

Status of financials in the project up to 30thSeptember, 2019

S.No.	Description	Amount (in Rs.)
1	Amounts received from allottees against booking of units(for builder's share) (Incl GST)	16,00,000.00 /-
2	Expenditure done towards completion of project	1,02,18,058.65 /-

Status of Approvals**A. Approval Received**

S. No.	Description	Date of Receipt
1	Provisional fire clearance	28.12.18
2	Sanctioning of Building Plan	25.04.19
3	RERA Registration	19.06.19

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs

