
# FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

Promoter's Registration		PT-76514	Name of Firm	KANTYAN
Number/CIN No/Partnership deed				DEVELOPERS
no/LLP Details/Any other				
registration with MSME Or Govt. Bodies				
Firm Address :	Kantyan	Bhawan, Link Road,I	Budha Colony,Patna	
Total Experience of promoter in Real Estate sector	08 YEAF	RS		
Total Experience in Real Estate after Implementation of RERA	06 YEAF	RS		
No of Project done Before Implementation of RERA	1. 2. 3. 4.	Residential Commercial Residential- cum Commercial Plotted project	01	RESIDENTIAL
No of Project done After	1.	Residential	02	RESIDENTIAL
Implementation of RERA	2. 3.	Commercial Residential- cum		,
	4.	Commercial Plotted project		

II. PARTICULARS OF PROJEC	<b>T</b>		
Project Registration Number	BRERAP00407-	Name of Project/Phase	RAMA HERITAGE,
	2/184/R-	of Registered Project	BLOCK B
	1479/2022		
Name of Promoter	KANTYAN	Project Address	MOHALLA-
	DEVELOPERS		KARORICHAK, MAUZA-PHULWAR
		T .	SHARIF, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	10/10/2027	ě.	
Starting date of Project or Phase			
of the Project	21/10/2022		
Type of Project or Phase of the	Residential		
Project			
Period of validity of map by the Competent Authority	05-04-2025		



Building /Block Number	Apartment	Туре	Carpet Area	Total Number of sanctioned	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
RAMA	1. 1 BHK			apartments	Flat-08	Flat-08
HERITAGE	2. 2 BHK, -	04		El-t-16	1. Booked	3. Booked/
BLOCK-B	3. 3 BHK	12		Flat-16	/ Allotted -06	Allotted-NIL
	4. Shop				2. Sold-NIL	Sold -NIL
	5. Bungalow				Percentage of	
	6. Plot etc.				booking 75%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name


Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name Address contact number Email id (If any )

IV. DISCLOSURE OF	SOLD / BOOKED INVE	ENTORY OF GARAGES		
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:  1. Booked/Allotted	_	06
RAMA HERITAGE BLOCK-B	16	2. Sold	-	NIL

	ETAILS OF BUILDING APP				
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR-CUM- STATE FIRE OFFICER, BIHAR, PATNA		02-08-2016	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			



Plar	1 Case No. 22/2021-22		
5. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	80%	25-11-2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	12-05-2025 20-11-2026 05-04-2025 15-12-2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	02-07-2026 03-05-2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground	70% 0%	20-02-2025 06-05-2026 04-06-2026
10.	Water Tanks.  External plumbing and	0%	20-06-2025
10.	external planting and external plaster, elevation, completion of terraces with	0% 0% 0%	20-06-2025 20-08-2025

For Kantyan Developers

Nil/h. Partner

11.	Installation of Lifts,	0%	10-06-2026
	water pumps,	100%	
	Fire Fighting Fittings and	0%	01-12-2026
	Equipment as per CFO NOC,	0%	04-10-2026
	Electrical fittings, Mechanical		
	Equipment, compliance to		
	conditions of environment/CRZ		
	NOC,		
	Finishing to entrance lobby/s,		
	plinth protection,	0%	12-12-2026
	paving of areas	0,0	12-12-2020
	appurtenant to Building/Wing,	0%	
	Compound Wall and all other	070	
	requirements as me be		
	required to complete project		
	as per Specifications in		
	1 1	8	
	Agreement of Sale.		4
	Any other activities		
	This other activities	·	

VII.	AMENITIES AND COMMON INFRASTRUCTURE DEVELO			
C	Common Areas and Facilities		Percentage of actual Work	Expected Completion
S. No.		Proposed (Yes/No)	Done (As on date of the Certificate)	date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	03-04-2025
4.	Storm Water Drains	YES	0%	04-06-2025
5.	Landscaping & Tree Planting	YES	0%	12-12-2026
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	10-06-2025



10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	10-12-2026
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub- Station, Receiving Station	NO		
16.	Others (Option to Add More)			
VIII	. A EXTERNAL AND INTERN PLOTTED DEVELOPMENT		PMENT WORKS IN	CASE OF
		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank	,		
4	Drains		ē	
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			



9.	Energy Management		

IX. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT				
(A)	Sr. No.			
	1.	Front Elevation	Attach	
	2.	Rear Elevation	Attach	
	3.	Side Elevation	Attach	
(B)		Photograph of each floor		

X. F					
S. No.	Particulars	Amount (In Rs.)			
(1)	(2)	(3)			
1.	Project Account No.	922020009106690			
2.	Estimated Cost of the Project including land cost at the start of the Project	2,73,47,000=00			
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	2,25,00,000=00			
4.	Any Variation in Development Cost which is declared at the start of the Project.	N/A			
5.	Amount received during the Quarter	53,48,000=00			
6.	Actual Cost Incurred during the Quarter	25,00,007=00			
7.	Net amount at end of the Quarter	28,85,247=40			
8.	Total expenditure on Project till date				
9.	Cumulative fund collected till the end of Quarter in question				
10.	Cumulative expenditure done till the end of Quarter in question				

XI.	DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED			
16. 12.001				

## XII. MISCELLANEOUS

A List of Legal Cases (if any) - On Project / Promoter



4	a N				
1.	Case No.	NO			
2.	Name of Parties	NO			
3.	No of Execution Cases against this project Case No. Name of Parties	NO			
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO			
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO			
В	Sale/Agreement for Sale during the Quarter				
1.	Sale Deed	NIL			
2.	Agreement for Sale	NIL			
3.	No. of possessions given to allottees	NIL			
XII	I. PERCENTAGE OF WORK ALONG W	ITH MILESTONE CHART			
Weather the project in progress is as per time schedule or lagging behind?					

XIV UNITS ALLOCATION DETAILS					
Total Number of sanctioned apartments 1 BHK- 2 BHK -04 3 BHK-12 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/Bungalow-Plot etc  Flat No.  103 — 3 BHK  202 — 3 BHK  203 — 3 BHK  303 — 3 BHK  304 — 3 BHK	Cancellation of flat allotment, If any with Flat number/ Bungalow – Plot etc  N/A			

For Kantyan Developers

Partner

#### XV. BROCHURE / Prospectus

#### XVI Grievance Redressal Officer

Name: Nikhil Kumar Contact No: 8407830376

Email id: nikhilpuppul@gmail.com

Address: Kantyan Bhawan, Link Road, Budha Colony, Patna

### **Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

For Kantyan Developers


Partner


Signature of Promoter


Name:

Date:

Rama Heritago. Block B

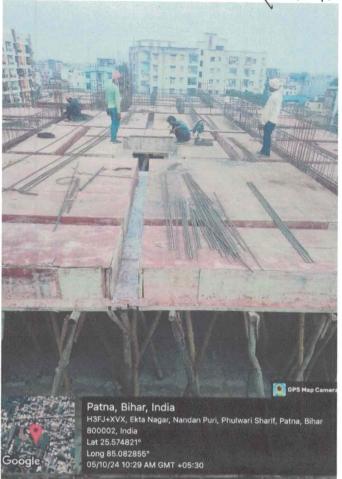

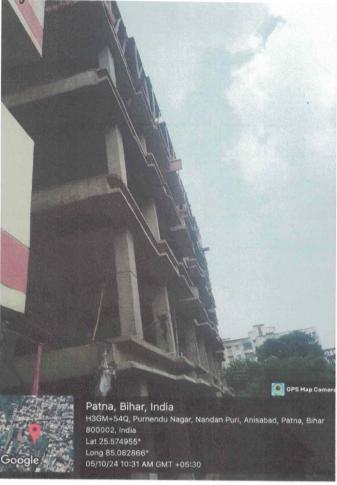

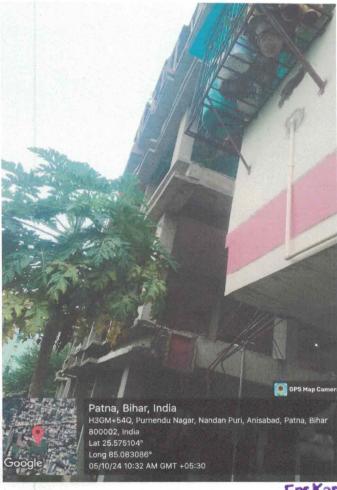



For Kantyan Developers

