

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending of **MAR. 2025 (year)**

I. PARTICULARS OF PROMOTERS			
Promoter's Registration number:	BR/UDHD/BLDR/23-0098.	Name of Firm	SRI MATESHWARI CONSTRUCTIONS
Partnership deed no.:	138		
Firm Address :	108, Hariom Commercial complex, New Dak-bungalow road, Patna, 80001.		
Total Experience of promoter in Real Estate sector	21 Years		
Total Experience in Real Estate after Implementation of RERA	7 Years		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	6 0 0 0	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	5 0 0 0	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00026-10/227/R-1523/2023	Name of Project/Phase of Registered Project	MATHURA TOWER
Name of Promoter	SRI MATESHWARI CONSTRUCTIONS	Project Address	NEAR R. P. SHARMA INSTITUTE OF TECHNOLOGY KOTHWAN PATNA
Name of Co-promoter			
Project Registration is valid up to	28/09/2028		
Starting date of Project or Phase of the Project	02/12/2022		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential- cum-Commercial 4. Plotted project	RESIDENTIAL-CUM-COMMERCIAL	
Period of validity of map by the Competent Authority	29/09/2025		


 For Sri Mateshwari Constructions
 Managing Partner

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share	Total Number of Apartments in Landowner's share
	1. 1 BHK 2. 2 BHK 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.		60	-30 1. Booked /Allotted - 0 (in this qtr.) Total - 7 2. Sold - 0 Percentage of booking - 23.33%	-30 3. Booked/ Alloted -0 4. Sold -0 Percentage of booking-0.00%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people.

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 0
1	0	2. Sold	- 0

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	NA			
2.	Fire N.O.C.	. STATE FIRE DEPT.	01/06/2019	21/08/2019	Already Submitted
3.	Water Supply Permission	Self			
4.	NOC from Airport Authority of India	NA			
5.	Other Approval(s), if any, required for the Project.				

For Sri Mateshwari Constructions
Managing Partner

VI. CONSTRUCTION PROGRESS OF THE PROJECT1. Plan Case No. **105/22-23** (To beaded for each Building / Wing)


S. No. (1)	Tasks / Activity(2)	Percentage of Actual Work Done (As on date of the certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	100%	Completed
3.	Podiums (if any)	NA	NA
4.	Plinth	100%	Completed
5.	Stilt Floor	100%	Completed
6.	Slabs of Super Structure	100%	Completed
7.	Internal walls within Flats, Internal Plaster within Flats, Floorings within Flats, Doors and Windows within Flats/Premises.	70% 60% 0% 0%	31/12/2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	30/06/2027
9.	Staircases, Lifts Wells and Lobbies ateach Floor level, Overhead and Underground Water Tanks.	30%	30/06/2027
10.	External plumbing, External plaster elevation, completion of terraces with waterproofing of the Building/Wing.	0% 80% 0%	30/06/2027
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	0%	30/06/2027

For Sri Mata Shwari Constructions
Managing Partner

	requirements as me be required to complete project as per Specifications in Agreement of Sale.	
	Any other activities.	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS


S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	30/06/2027
2.	Water Supply	YES	0%	30/06/2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30/06/2027
4.	Storm Water Drains	YES	0%	30/06/2027
5.	Landscaping & Tree Planting	YES	0%(landscaping)	30/06/2027
6.	Street Lighting	YES	0%	30/06/2027
7.	Community Buildings	N.A.		-
8.	Treatment and Disposal of Sewage and Sullage Water	N.A.		-
9.	Solid Waste Management & Disposal	YES	0%	30/06/2027
10.	Water Conservation / Rain Water Harvesting	YES	0%	30/06/2027
11.	Energy Management	N.A.		-

For Sri **Matashwari Constructions**

Managing Partner

12.	Fire Protection and Fire Safety Requirements	YES	0%	30/06/2027
13.	Closed Parking	YES	45%	30/06/2027
14.	Open Parking	YES	0%	30/06/2027
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	30/06/2027
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yyyy) Format
1.	Internal Roads and foot paths	NA		
2.	Water Supply	NA		
3.	Sewerage Chambers Septic Tank	NA		
4.	Drains	NA		
5.	Parks, Land Scaping and Tree Planting	NA		
6.	Street Lighting	NA		
7.	Disposal of sewage & sullage water	NA		
8.	Water conservation/Rain Water Harvesting	NA		
9.	Energy Management	NA		

For Sri Mata Shwari Constructions

 Managing Partner

IX. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	UPLOADED
	2.	Rear Elevation	UPLOADED
	3.	Side Elevation	UPLOADED
(B)		Photograph of each floor	UPLOADED

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	922020009106726
2.	Estimated Cost of the Project including land cost at the start of the Project	160000000
3.	Estimated Development Cost of the Project at the Start of the Project. (Excluding Land Cost)	128203000
4.	Any variation in Development Cost which is declared At the start of the Project.	
5.	Amount received during the Quarter	246843
6.	Actual Cost Incurred during the Quarter	2101005
7.	Net amount at end of the Quarter	-1854162
8.	Total expenditure on Project till date	66953755
9.	Cumulative fund collected till the end of Quarter in question	15001652
10.	Cumulative expenditure done till the end of Quarter in question	66953755

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED/DETAILS OF LOAN TAKEN BY PROMOTERS AGAINST THE PROJECT, If any
NA

For Sri Mateshwari Constructions

Managing Partner

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	NO
1.	Case No.	NA
2.	Name of Parties	NA
3.	No of execution Cases against this project Case No. Name of Parties	NA
4.	No. of Suo- Moto cases against this project Case No. Name of Parties	NA
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	0
2.	Agreement for Sale	1
3.	No. of possessions given to allottees	0

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

Answer – The Project in Progress is as per time Schedule. kindly find mile stone chart attached below.

For Sri Maleshwari Constructions

Managing Partner

XIV. UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc.	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc.
1 BHK - 2 BHK, - 3 BHK 4 BHK - Shop - Bungalow - Plot etc.	206,207,211,306,307,312,407.	

XV. BROCHURE /Prospectus- Attached Below**XVI Grievance Redressal Officer**

Name :

Contact No :

Email id :

Address :

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Name:

Date:

For Sri Mateshwari Constructions

Managing Partner

LAXMI PRASAD

14.04.2025

MILE STONE CHART												
PROJECT = MATHURA TOWER												
WORK DETAIL ↓	→ EXPECTED DATE FOR COMPLETION WORK											
Piling Work	Feb 2023 to Mar 2023											
Foundation Work	Apr 2023 to June 2023											
Basement cast	July 2023 to Sept. 2023											
Structure Work Completed	Oct 2023 to Apr 2024											
Brick Work	May 2024 to Nov 2024											
Plastering Work (Internal)	Dec 2024 to Apr 2025											
Plastering Work (External)	May 2025 to Aug 2025											
Window Fitting	Sept 2025 to Dec 2025											
Floor Covering Work	Jan 2026 to June 2026											
Electric Work (Conduct + Cable Pulling)	July 2026 to Nov 2026											
Plumbing Work Fitting	Dec 2026 to May 2027											
Painting Work (Internal + External)	June 2027 to Nov 2027											

For Sri Mateshwari Constructions

Mateshwari

Managing Partner



MATHURA TOWER

COMMERCIAL CUM RESIDENTIAL TOWER

Good Living Made Easy



Sri Mateshwari
Constructions



MATHURA TOWER

Premium retail space & 2-3 BHK flats
in the heart of the city.



Comfort, Convenience,
good construction quality
& Finishing

Quality of Project

- Fully lighted and airy all flat.
- Near Police Chowki & Railway Station.
- No water logging area.
- 24 Hours communication from any other place.
- Nearer to best Schools of Patna.
- A number of Nursing Homes nearer to the project.


The best in the Business





MATHURA
TOWER

LAYOUT PLAN (BASEMENT)

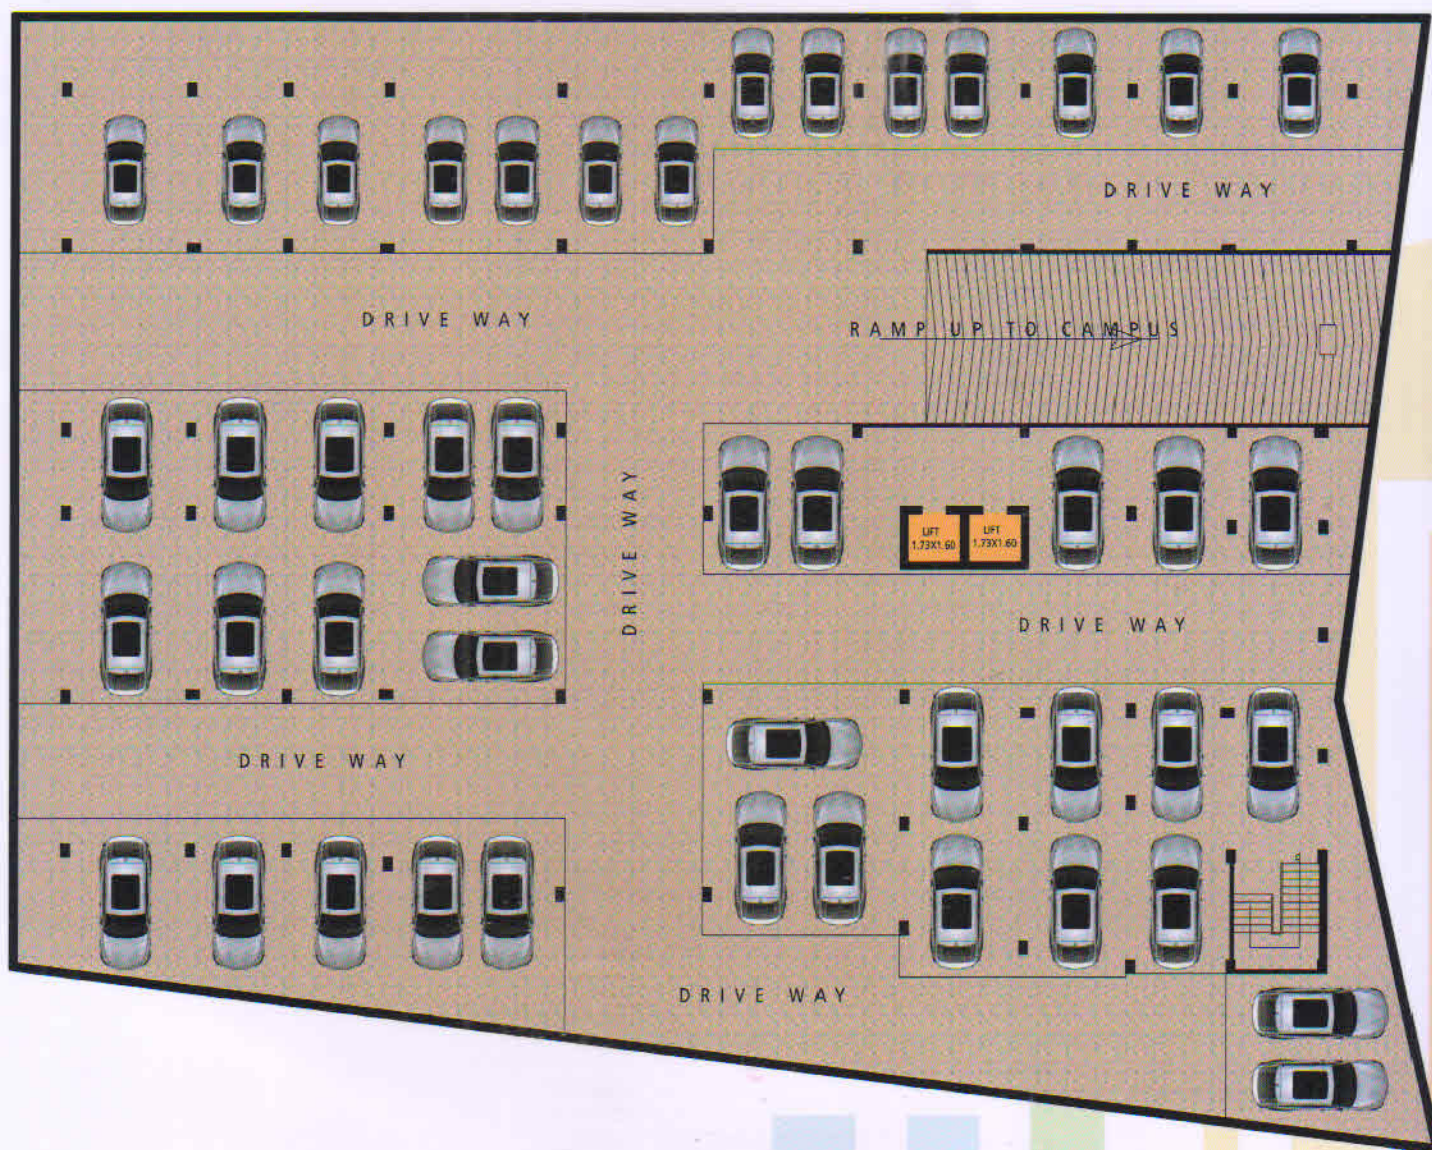



LAYOUT PLAN (2ND TO 4TH FLOOR)



FLAT NO.	BHK	CARPET AREA	BALCONY AREA	WALL AREA	BUILT UP AREA	TOTAL AREA
01	3-BHK	824.00 Sft	83.00 Sft	53.00 Sft	960.00 Sft	1248.00 Sft
02	3-BHK	834.00 Sft	87.00 Sft	52.00 Sft	973.00 Sft	1265.00 Sft
03	2-BHK	577.00 Sft	32.00 Sft	37.00 Sft	646.00 Sft	840.00 Sft
04	2-BHK	577.00 Sft	32.00 Sft	37.00 Sft	646.00 Sft	840.00 Sft
05	3-BHK	834.00 Sft	87.00 Sft	52.00 Sft	973.00 Sft	1265.00 Sft
06	3-BHK	824.00 Sft	83.00 Sft	53.00 Sft	960.00 Sft	1248.00 Sft
07	3-BHK	945.00 Sft	88.00 Sft	55.00 Sft	1088.00 Sft	1415.00 Sft
08	3-BHK	965.00 Sft	88.00 Sft	57.00 Sft	1110.00 Sft	1443.00 Sft
09	2-BHK	634.00 Sft	47.00 Sft	39.00 Sft	720.00 Sft	936.00 Sft
10	2-BHK	634.00 Sft	47.00 Sft	39.00 Sft	720.00 Sft	936.00 Sft
11	3-BHK	852.00 Sft	98.00 Sft	53.00 Sft	1003.00 Sft	1304.00 Sft
12	3-BHK	818.00 Sft	82.00 Sft	51.00 Sft	951.00 Sft	1236.00 Sft




FLAT LAYOUT (2ND TO 4TH FLOOR)

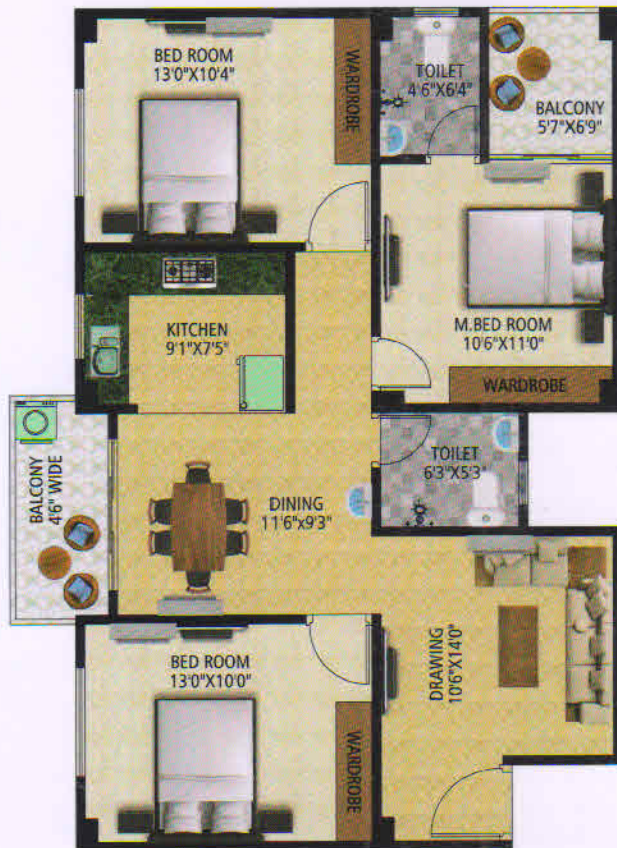


Flat # 01/06
Total Area 1248.00 sq.ft.

-  3 Bedrooms  2 Toilets
-  2 Balconies





Flat # 02/05
Total Area 1265.00 sq.ft.

-  3 Bedrooms  2 Toilets
-  2 Balconies

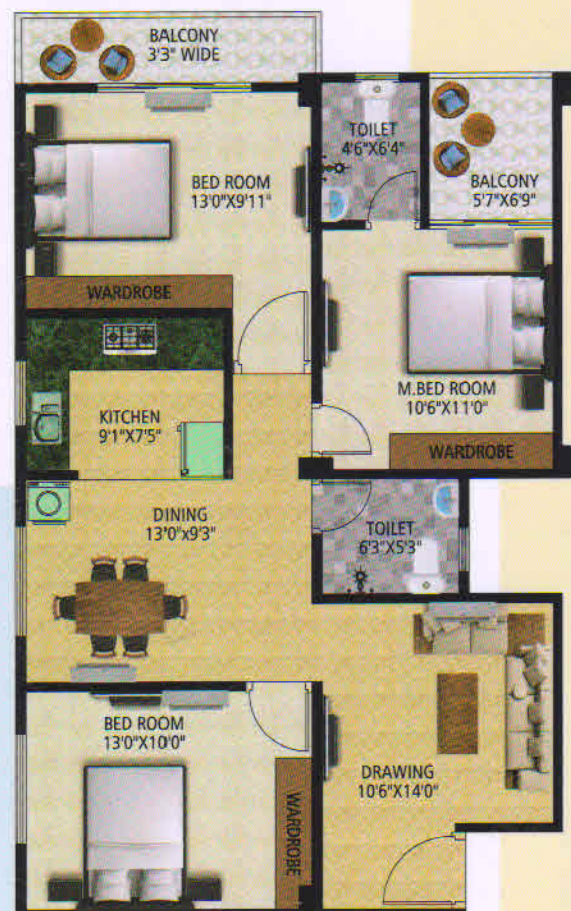


FLAT LAYOUT (2ND TO 4TH FLOOR)

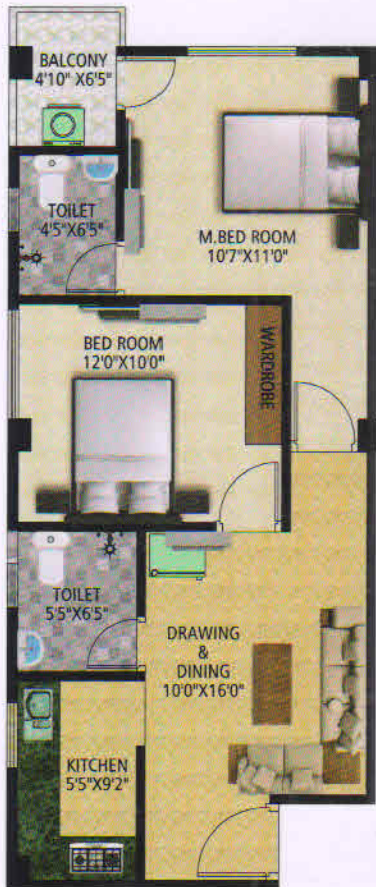

Flat # 03

Total Area 840.00 sq.ft.


- 2 Bedrooms 2 Toilets
- 1 Balcony




Flat # 04

Total Area 840.00 sq.ft.

- 2 Bedrooms 2 Toilets
- 1 Balcony

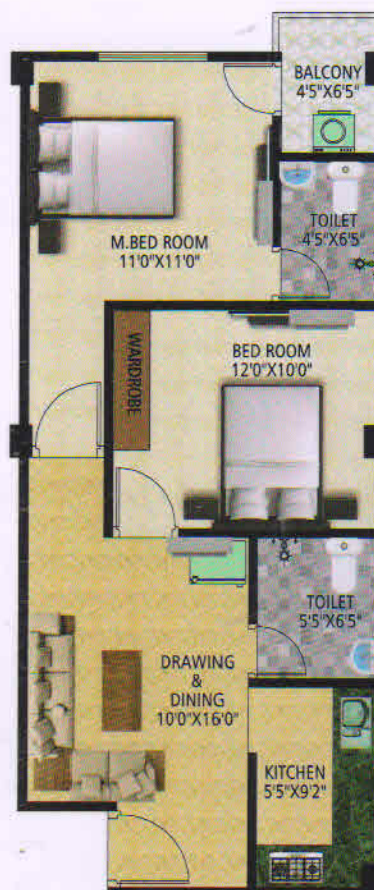


FLAT LAYOUT (2ND TO 4TH FLOOR)



Flat # 07

Total Area 1415.00 sq.ft.

-  3 Bedrooms
-  2 Toilets
-  2 Balconies





Flat # 08

Total Area 1443.00 sq.ft.

-  3 Bedrooms
-  2 Toilets
-  2 Balconies




FLAT LAYOUT (2ND TO 4TH FLOOR)

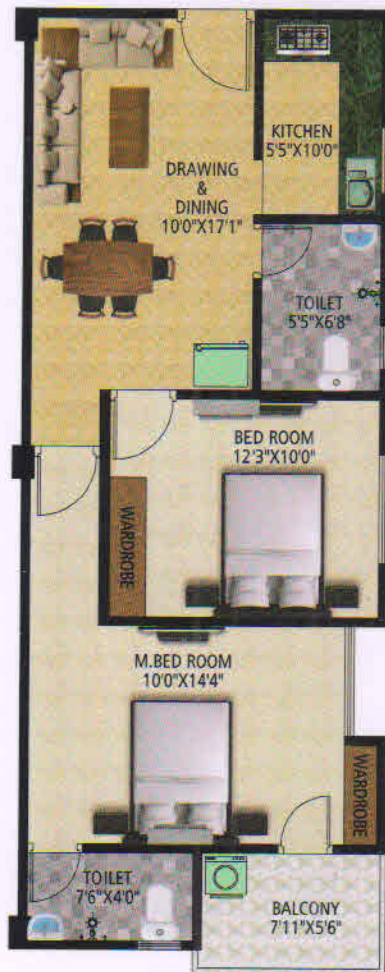

Flat # 09

Total Area 936.00 sq.ft.


- 2 Bedrooms 2 Toilets
- 1 Balcony





Flat # 10

Total Area 936.00 sq.ft.

- 2 Bedrooms 2 Toilets
- 1 Balcony

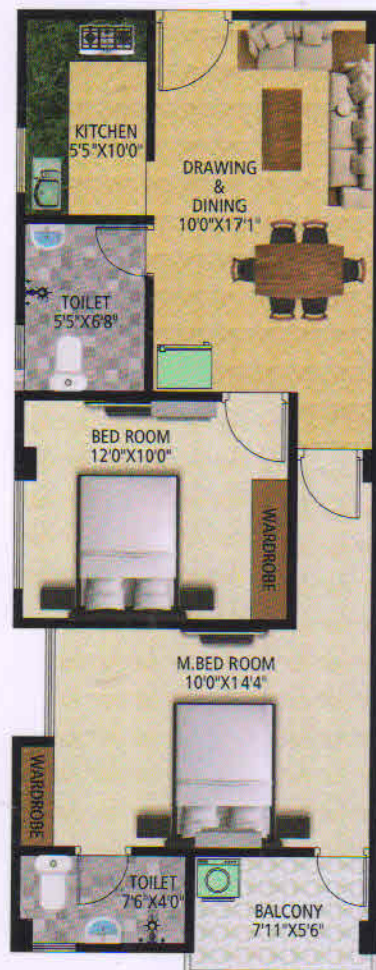


FLAT LAYOUT (2ND TO 4TH FLOOR)

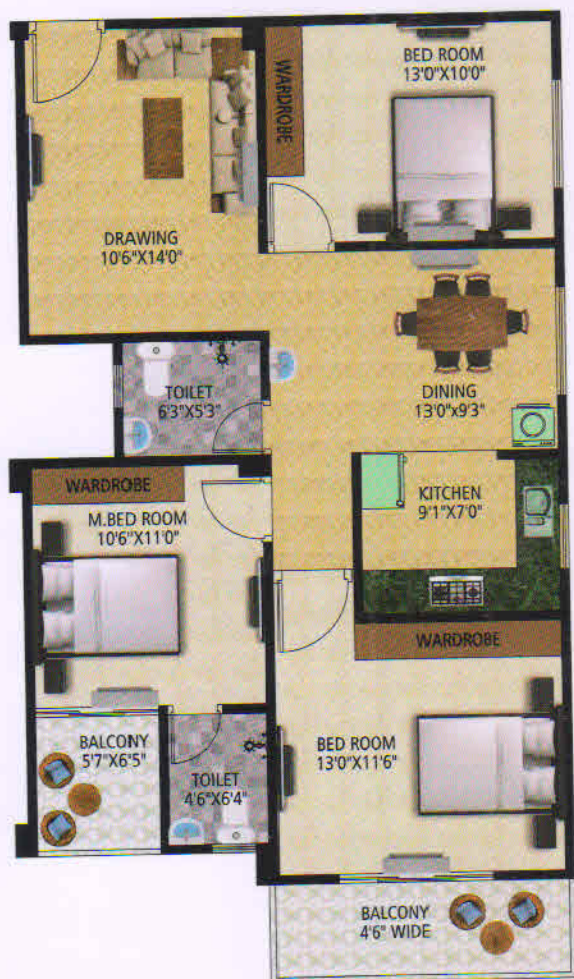

Flat # 11

Total Area 1304.00 sq.ft.


- 3 Bedrooms
- 2 Toilets
- 2 Balconies



Flat # 12

Total Area 1236.00 sq.ft.

- 3 Bedrooms
- 2 Toilets
- 2 Balconies

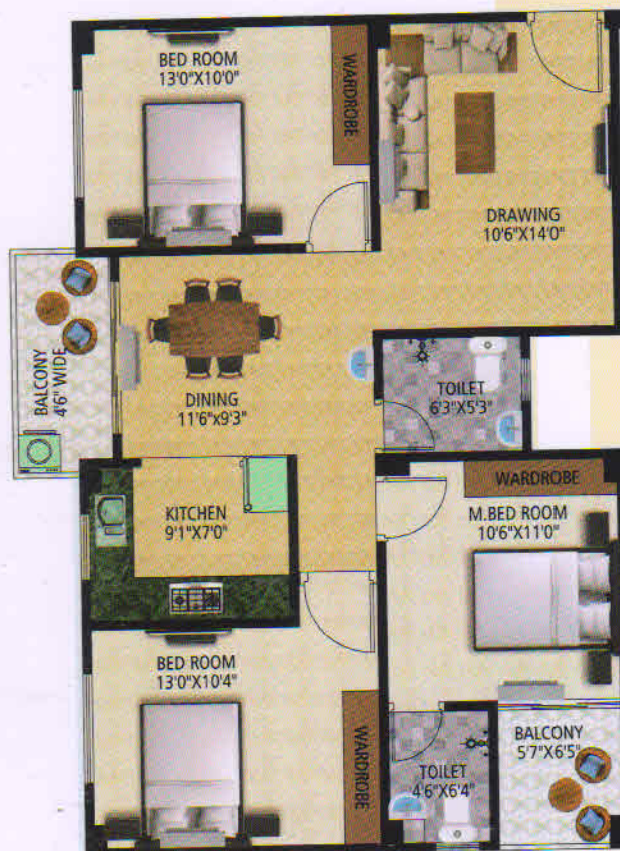

Specifications



STRUCTURE	: RCC Frame Structure with Earthquake resistance.
SUPER STRUCTURE	: 1st Class Brick work in Cement Sand Mortar.
FLOORING	: Vitrified Tiles Flooring inside the Flat. Except Toilet & Kitchen.
DOORS & WINDOWS	: Chowkhat of Salwood, Door Shutter will be of Flush Door Painted with two coats of enamel paint. Fully Glazed window with uPVC/aluminium frame.
KITCHEN	: Kitchen top will be of Granite Stone with Steel Sink, Glaze Tiles dodo upto 2' high from working platform & Floor will be Ceramic Tiles.
TOILETS	: Glazed Tiles on wall up to Lintel level, Floor will be Ceramic tiles, Chinaware will be of Hindware/Parryware make and C.P fitting will be ESSCO/Hindware/Parryware.
ELECTRICAL	: Copper Wiring in Concealed P.V.C Conduits. Power Plug in D/D, Bedrooms, Toilets and Kitchen.
FINISHING	: All walls will be finished with Wall Putty.
SERVICE	: Telephone Point (not connection) in each flat. PBX facility from each flat to security point.
WATER	: 24 Hours water supply from own Tube well.
POWER BACKUP	: 300Watts Power in each flat from silent Gen-Set.
LOANS	: Loan facility available from Bank / Financial Institution.
NOTE	: Payment are to be made by Cheque/Bank Draft in favour of Sri Mateshwari Constructions at Patna.

Features of Building & Common Areas

Parking Space	Sufficient car parking Space provided for all flats and their easy movement to enter and exit the building.
Water Supply	Round the clock water supply, insulated water tanks.
Lift	Of a known, reliable, branded company.
Generator with auto-changer	Suitable capacities silent generator with auto-changer, to be installed.

AMENITIES YOU DESERVE

 24x7 Water Supply	 24x7 Power Back Up	 Security	 2 Lifts	 Car Parking	 Visitors Car Parking
 Intercom	 Earthquake Resistant Structure Design	 Own Transformer	 Heat Treatment	 Fire Safety	 Waterproof

Note: Extra charges for cupboards, shelves, extra electrical points, power plugs, telephone points and modifications or alterations other than agreement shall be borne by flat purchasers only.
Registration charges, GST extra.

PAYMENT SCHEDULE

- At the time of Booking10% of sale price
- After completion of Foundation20%
- After completion of Ground Floor Slab10%
- After completion of 1st Floor Slab10%
- After completion of 2nd Floor Slab10%
- After completion of 3rd Floor Slab10%
- After completion of 4th Floor Slab10%
- After completion of Brick Work10%
- After completion of Plaster Work5%
- One Month before Possession5%




Location

Not to scale

Distances From

Danapur Rly Station.....	3.2 Km
Patliputra Rly Station	6.2 Km
Saguna More	2.6 Km
St. Karen's	1.2 Km
AIIMS	7.0 Km
RPS More.....	1.5 Km

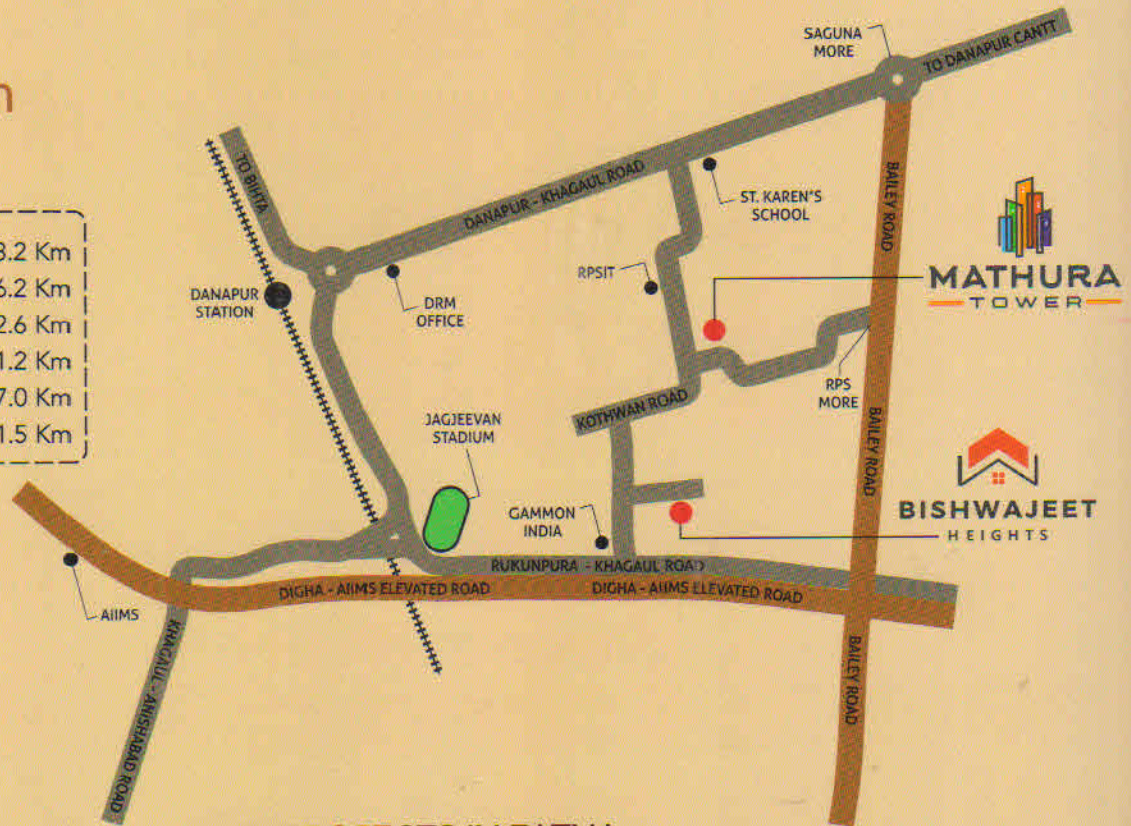

OUR PROJECTS IN PATNA



Girja Complex
Near Patna Central School, Jaganpura, Patna



Jamuna Tower
Ashok Nagar, Patna



Mateshwari Residency
Near Patna Central School, Bypass, Patna



SINGH VILLA
Gola Road, Patna



BISHWAJEET HEIGHT
Kothwan, Danapur, Patna



SRI MATESHWARI CONSTRUCTIONS

Registered Office

108, Hariom Commercial Complex
New Dakbunglow Road, Patna - 800 001 (Bihar)

0612-2216335, 9334117578
9334837720, 7634814814

Architect :
A.R. & ASSOCIATES
Kailash Niwash, Bhikhna Pahari
Patna 800004
Mob. : 9771344539

All details in this booklet are for easy information and concept purpose only, and do not form part of the agreement.
This document is tentative and developers reserve the right to make variations and modifications.

design & print : adzone # 8877111190, 8877788802, info@adzonegraphics.com

