

Submitted/Uploaded on 15/4/21
Kajal

No. SCPL/2020-21/A3

Date:15-04-2021

To,
The Chairman,
Real Estate Regulatory Authority,
6th Floor,
Bihar State Building Construction Corporation Campus,
Hospital Road, Shastri Nagar, Patna-800023

Sub - Quarterly Report of Our Project SAAKAAR'S AQUA CITY 01-010-2020 to 31-12-2020
Ref - RERA Registration No: - BRERAP00027-2/233/R-96/2018

01-01-2021 to 31-03-2021 (4TH QR)
For Saakaar Constructions Pvt. Ltd.

Sanjay Singh
Authorised Signatory

Dear Sir,

With reference to above, as per REAL ESTATE REGULATORY AUTHORITY, BIHAR REAL ESTATE (REGULATION AND DEVELOPMENT) RULES, 2017 CHAPTER IV RULE 16 (D). we are submitting the Quarterly Report of SAAKAAR'S AQUA CITY, Usari, Makdhupur Road, Sandalpur, Khagaul, Danapur, District Patna State Bihar as prescribed details Mentioned below:

- Quarterly up to date status of the project (Physical and Financial).
A) Status of Construction of each building is mentioned below and photographs are attached in RERA website.


Project: SAAKAAR AQUA CITY, DANAPUR		
Site Progress Status		
S.No	Towers	Progress Status
1	Tower 1	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--25%, RETAINING WALL LOWER BASEMENT--25%, LOWER BASEMENT COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, UPPER BASEMENT COLUMNS--0%, RETAINING WALL UPPER BASEMENT--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, GROUND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIRST FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SECOND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRD FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, EIGHTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%
2	TOWER NO: 2,3,4 & 5	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--20%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--70%, CASTING--50%, BRICKWORK--0%, FIRST FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, SECOND FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, THIRD FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--25%, FORM WORK--25%, REBAR WORK--25%, CASTING--0%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, EIGHTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%

Saakaar Constructions Pvt. Ltd.

CIN No. : U00502BR1996PTC007493
5th Floor, Sone Bhawan, Near Hotel Chankaya, R Block Golamber, Patna-800 001
Ph.: 0612-2506506, M : 6202750747
e-mail : info@saakaar.com, website : www.saakaar.com

For Saakaar Constructions Pvt. Ltd.


Sanjay Singh
Authorised Signatory



6	TOWER NO. 14,15 & 16	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, SECOND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, THIRD FLOOR COLUMNS--75%, FORM WORK--75%, REBAR WORK--75%, CASTING--50%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--25%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, Eighth FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%
7	TOWER NO. 17	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--95%, SECOND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--95%, THIRD FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--90%, FOURTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, Eighth FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%
8	TOWER NO. 18,19 & 20	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--0%, CASTING--0%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--100%, SECOND FLOOR COLUMNS--100%, FORM WORK--80%, REBAR WORK--70%, CASTING--70%, BRICKWORK--60%, THIRD FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--60%, FOURTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--60%, FIFTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--0%, Eighth FLOOR COLUMNS--45%, FORM WORK--45%, REBAR WORK--45%, CASTING--35%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%

To be continued

For Saakaar Constructions Pvt. Ltd.



Authorised Signatory

Tower 21	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--0%, CASTING--0%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--95%, FORM WORK--60%, REBAR WORK--40%, CASTING--40%, GROUND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIRST FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SECOND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRD FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, Eighth FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%,
----------	--

- B) --Status of Constructions of each floor that the project is on the RAFT and basement Roof level and photograph are attached in RERA website.
- C) Status of construction of internal infrastructure and common area that the project is on the RAFT and basement Roof level and photograph are attached in RERA website.
- D) Details of fund receiving through booking and other means are details mentioned below.

Opening Balance	Amount Received through booking.	Equity	Loan	Money Spent	Balance Amount	Sourcing of Fund
13,95,89.627.21	31,02,59,095.00	NIL	NIL	21,60,99,129.00	23,37,49,593.00	Bookings and Own funds.

2. List of number and type of apartments.

Residential/Commercial	Type of Apartment	Opening	Booked	Closing Balance	Total No of garages (Covered)	Opening	Booked	Closing balance
Residential	EWS	181	14	167	1266	516	34	482
	LIG	124	64	60				
	2 BHK	56	1	55				
	2.5 BHK	62	7	55				
	3 BHK	155	19	136				
	4 BHK	3	1	2				
Commercial	Studio	75	-	75	116	-	-	116
	Convenience Store	34	-	21				
	OPD (Doctor's Cabin+Medicine Room)	1	-	1				
	Diagnostic Centre (Physiotherapy, X-Ray room, Pathlab)	1	-	1				
	Office Retail	1	-	1				
	Coaching Classes+Staff Room	1	-	9				
	Bank	1	-	1				
	Food Court	1	-	1				
	Play school (8-class room + H.O. + Staff Room)	1	-	1				

Contd.

3. List of approvals taken and the approvals which are pending subsequent to commencement certificate.

- A. Approvals list during the quarter— Nil
- B. Approval applied and expected date of receipt — Nil
- C. Approval to be applied and date planned for application — Nil
- D. Modifications, amendment or revision ,if any, issued by the competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project — Nil


Please acknowledge the receipt.

Thanking You,

Yours

For Saakaar Constructions Pvt. Ltd.

For Saakaar Constructions Pvt. Ltd.



(Authorised Signatory)

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. : - CLUSTER – 1 (Tower-1)


CLUSTER NAME: - ATLANTIS

PROGRESS STATUS:

100% Excavation work has been completed and sand piling work of tower area is 100% completed. Leveling work has been 100% Completed.

30% area of NTA west side & 20% Area of NTA North side casting is completed up to Upper basement Roof slab & rest 80 % Area of NTA North side footing casting is completed & column Reinforcement work is in progress and 30% Area of NTA south side casting is completed up to Lower basement Roof slab & Upper basement column Reinforcement work is in progress.

For Tower area 100% PCC work is completed & Raft reinforcement is completed and raft casting is 25% completed and Balance Work for the cluster is in Progress.

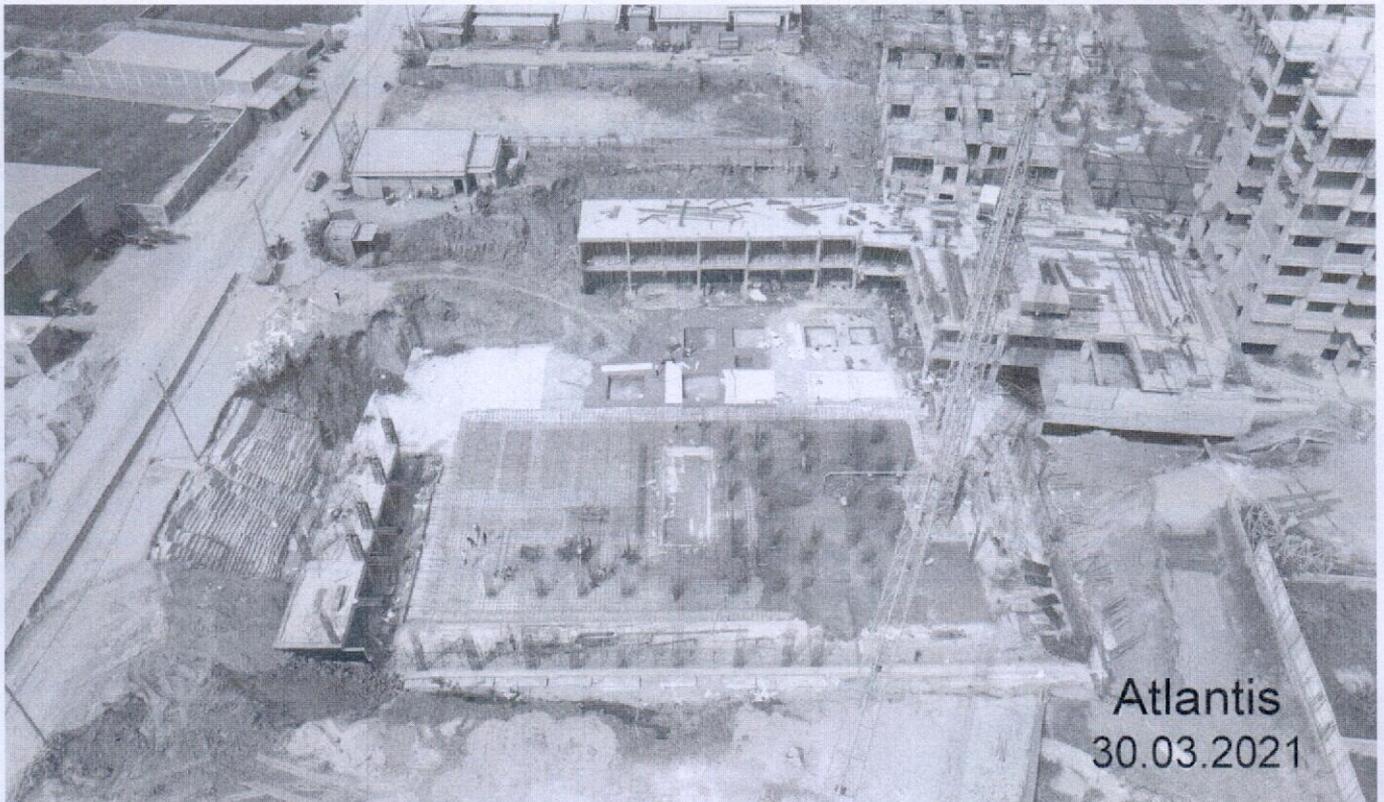

For Saakaar Constructions Pvt. Ltd.

Devin John
Authorised Signatory



Atlantis
30.03.2021



Atlantis
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Devit-John
Authorized Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER - 2 (Tower No-2,3,4 & 5)

CLUSTER NAME: - PACIFIC

PROGRESS STATUS:

For Tower No. 5, 4th Floor roof slab casting work is 100% completed and Reinforcement & Shuttering work of 5th Floor column is in progress.
For Tower No. 4, 5th floor Column casting work is 100% completed and Reinforcement & Shuttering work of 5th floor roof slab is in progress.
For Tower No. 3, Ground floor Column casting 100% completed and Reinforcement & Shuttering work of Ground floor roof slab is in progress.
For Tower No. 2, Ground floor Column casting 100% completed and Reinforcement & Shuttering work of Ground floor roof slab is in progress.




For Sakaar Constructions Pvt. Ltd.

Devi - 504

Authorised Signatory



Pacific
30.03.2021

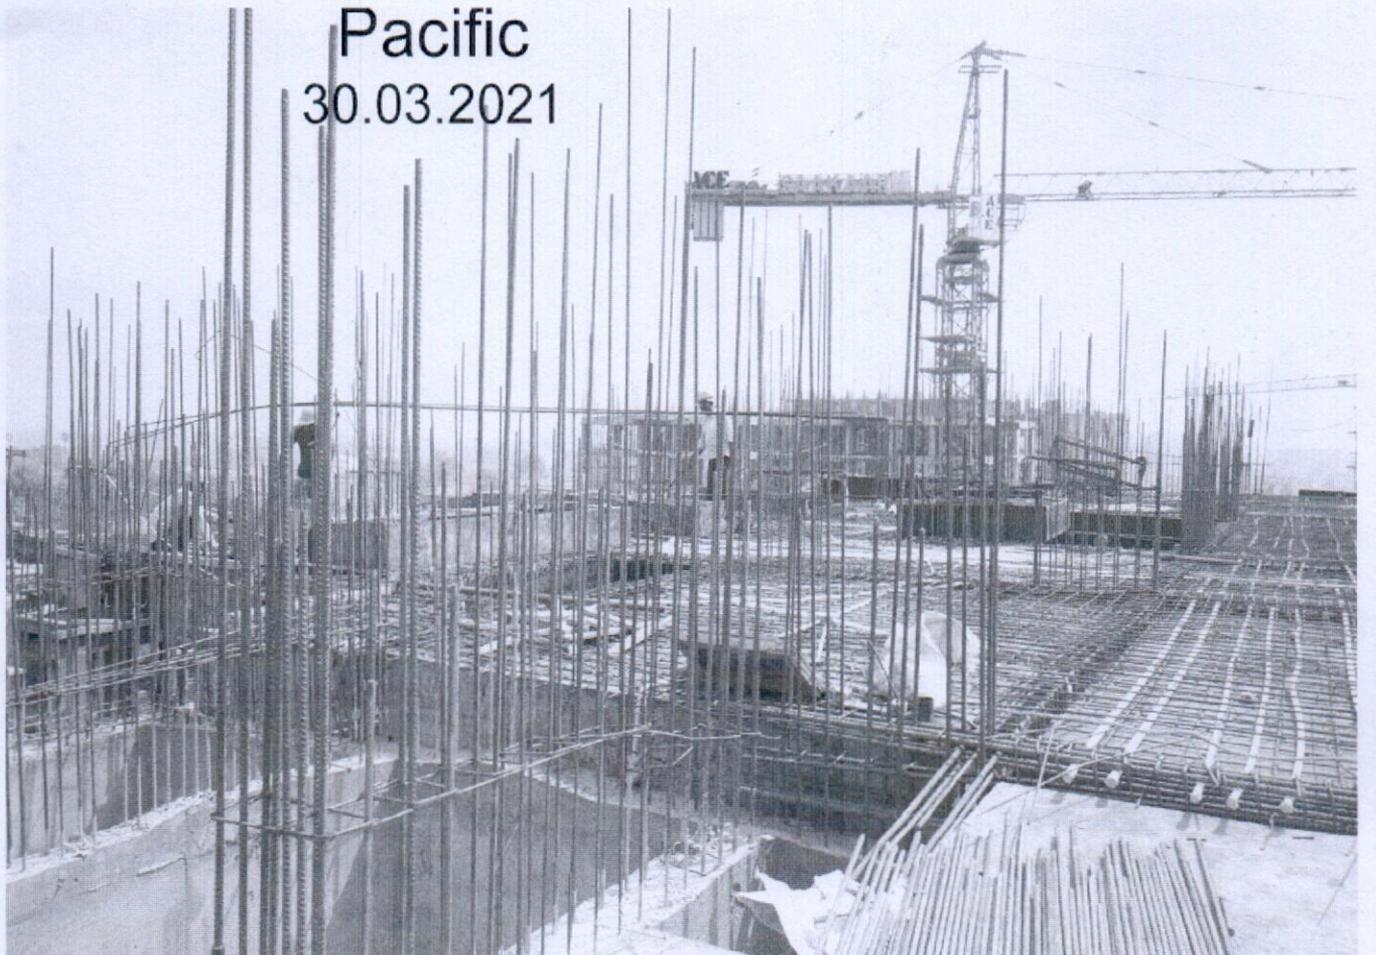

Pacific
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Sanjay Jha
Authorised Signatory

Pacific
30.03.2021



Pacific
30.03.2021



For Sankar Constructions Pvt. Ltd.

[Handwritten Signature]
Authorised Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER - 3 (Tower No 6,7,8 and 9)

CLUSTER NAME:- AMAZON

PROGRESS STATUS:

For Tower No. 6 , 12th Floor roof slab casting is 100% completed & Balance work is in progress.


For Tower No.7, 12th Floor column casting is 100% completed & Reinforcement & Shuttering work of 12th Floor roof slab is in progress.

For Tower 8 & 9, Upto 11th Floor column casting is 100% completed & Reinforcement & Shuttering work of 11th Floor roof slab is in progress.

For Tower No. 6, 7, 8 & 9, 2nd Floor Brickwork 95% completed & Balance work in Progress. 3rd Floor Brickwork 90% work completed & Balance work in Progress. 4th Floor Brickwork 5% work completed & 5th Floor Brickwork Layout work completed.

Amazon
30.03.2021



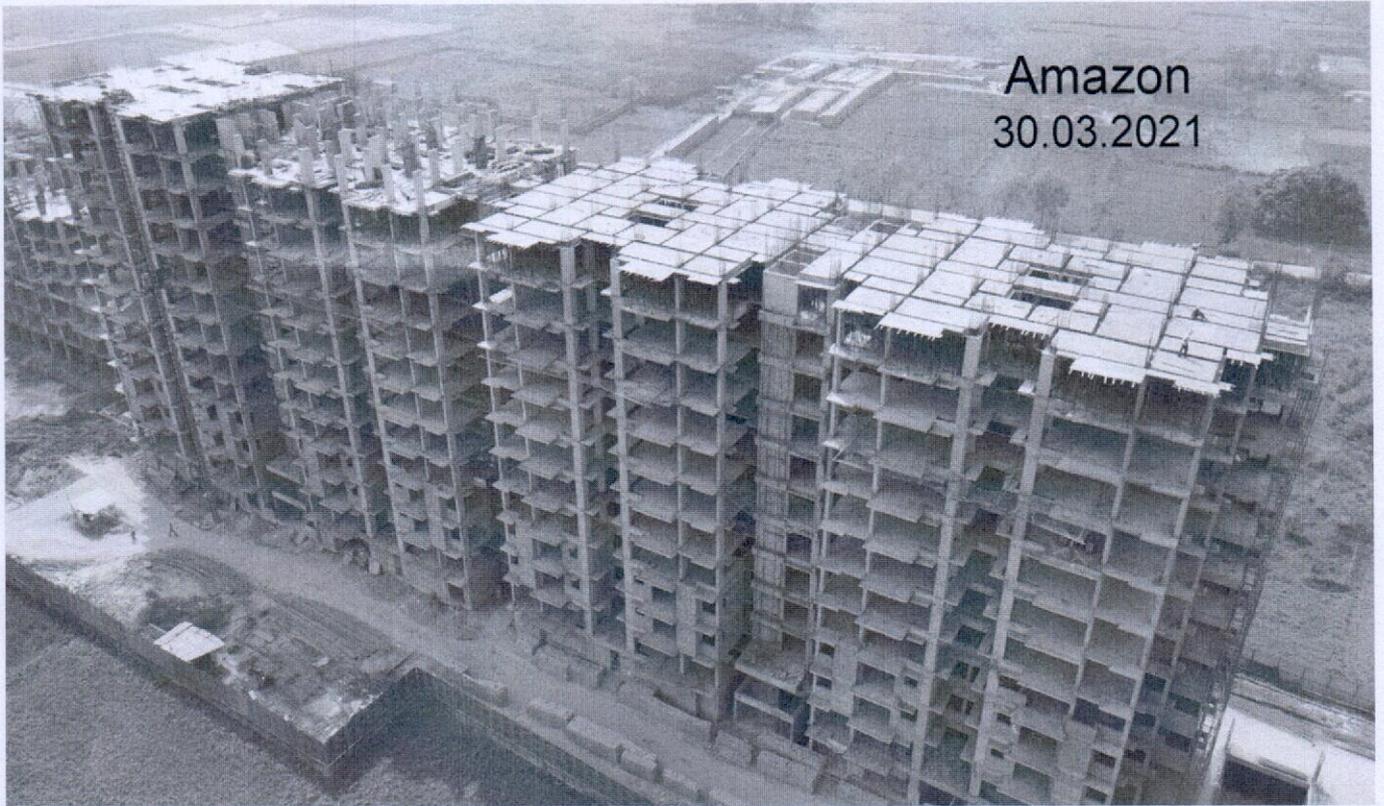

Amazon
30.03.2021



Amazon
30.03.2021





Amazon
30.03.2021



Amazon
30.03.2021

Amazon
30.03.2021



Amazon
30.03.2021



A handwritten signature in blue ink, appearing to read "Anita - 52".

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER - 4 (Tower No- 11 &12)

CLUSTER NAME:- NEPTUNE

PROGRESS STATUS:

For Tower No. 11&11A, 11th Floor roof slab casting is 80% completed & Reinforcement & Shuttering balance work is in progress.

For Tower No. 12, 11th Floor Column casting is 100% completed & Reinforcement & Shuttering work of 11th Floor roof slab is in progress.

3rd Floor Brickwork 50 % completed, 4th floor Brickwork 95 % completed & 5th floor Brickwork only layout is completed & Balance work is in Progress.




For Sakaar Constructions Pvt. Ltd.

Devi Son

Authorised Signatory



Neptune
30.03.2021

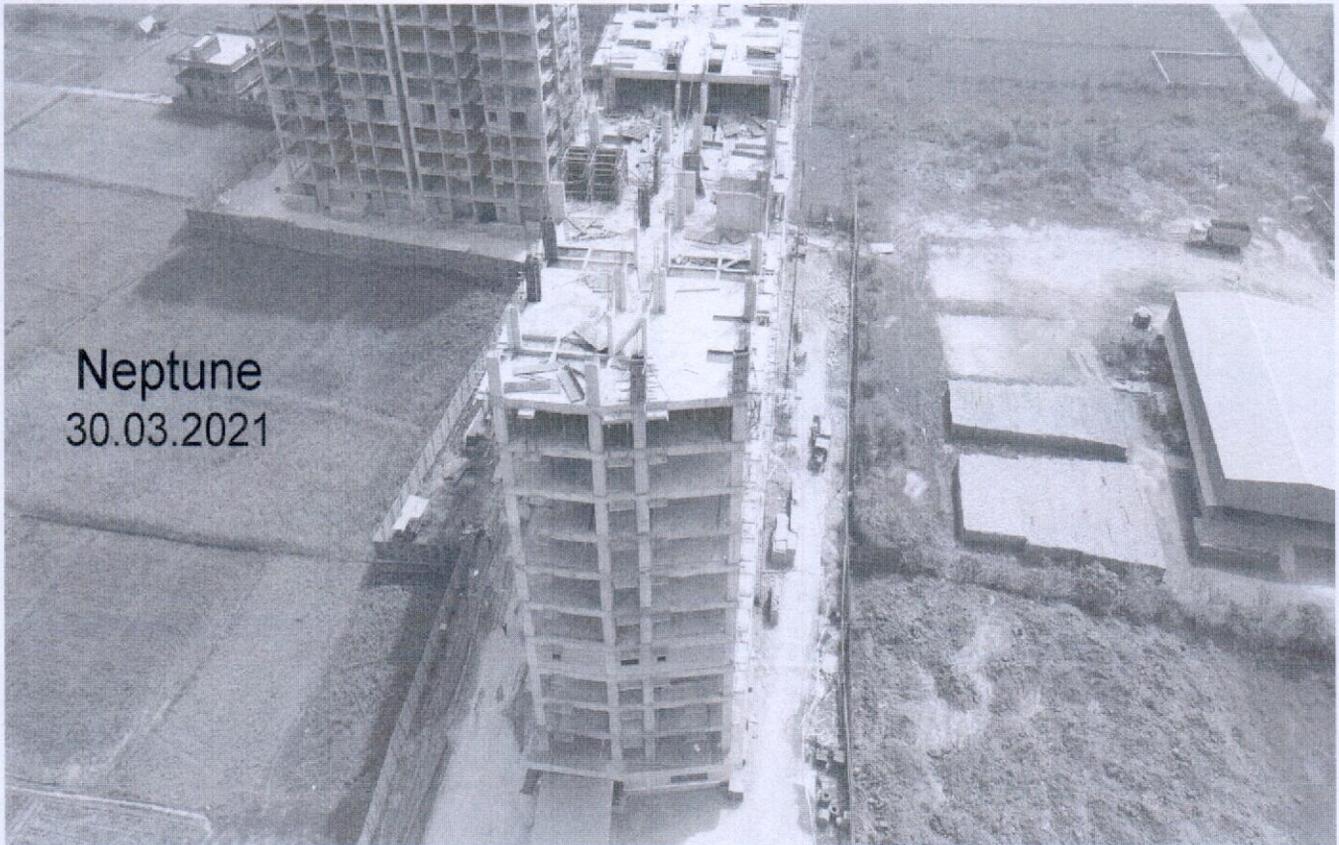

Neptune
30.03.2021



Neptune
30.03.2021



Neptune
30.03.2021

For Saakaar Constructions Pvt. Ltd.

A handwritten signature in blue ink, appearing to read "Sanjay Singh".

Authorised Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021


CLUSTER NO. :- CLUSTER - 5 (Tower No-13)

CLUSTER NAME:- AQUARIOUS

PROGRESS STATUS:

For Tower No. 13(Part A), Casting of 9th floor column is 100 % Completed and Shuttering & Reinforcement Work of 9th floor Roof Slab work is in progress. For Tower No. 13 (Part B), Casting of 9th floor column is 100 % Completed and Shuttering & Reinforcement Work of 9th floor Roof Slab work is in progress.

2nd & 3rd Floor Brickwork only layout is completed and 5th floor Brickwork layout is 60% completed. & 4th floor Brickwork 75% completed and rest Balance work is in Progress.

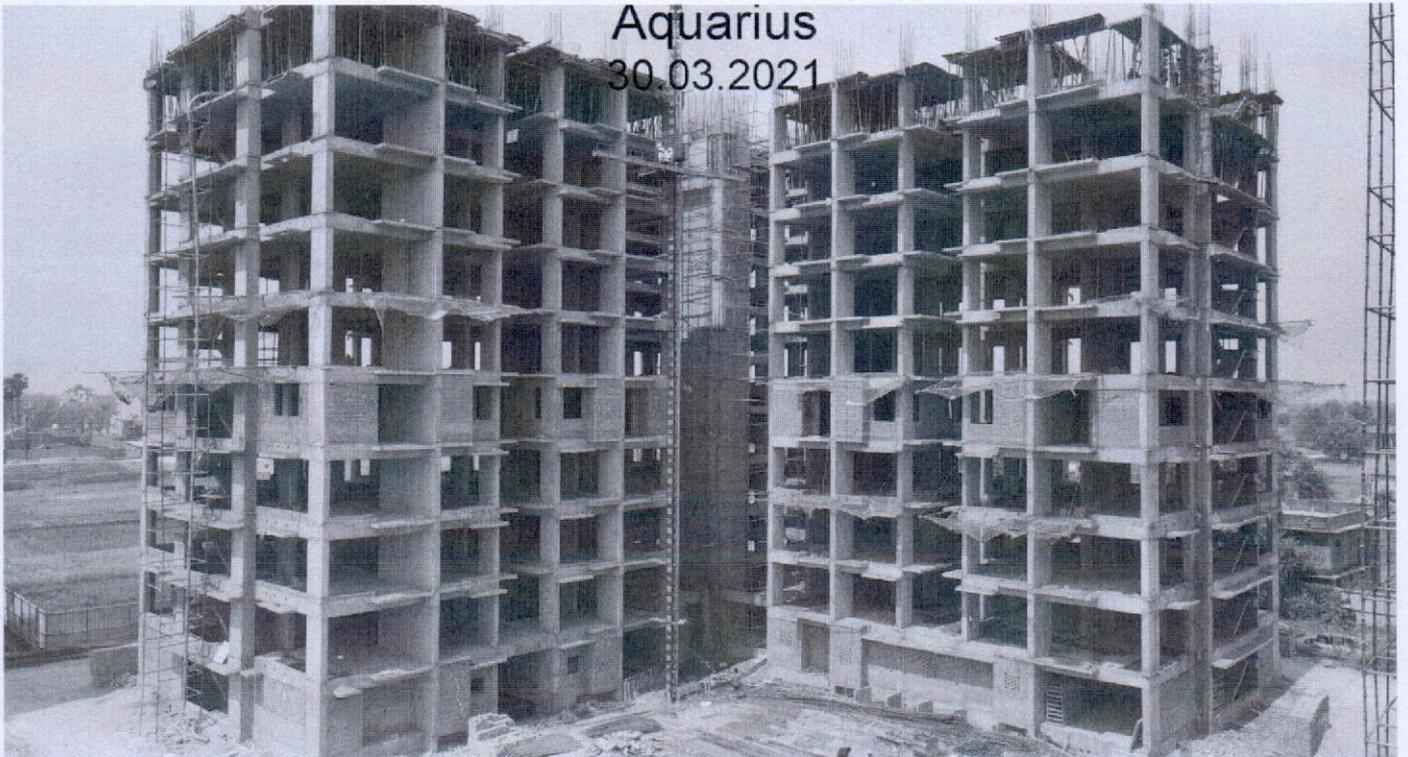

For Saakaar Constructions Pvt. Ltd.

[Signature]
Authorised Signatory




Aquarius
30.03.2021



Aquarius
30.03.2021

For Saakaar Constructions Pvt. Ltd.

[Handwritten Signature]
Authorised Signatory

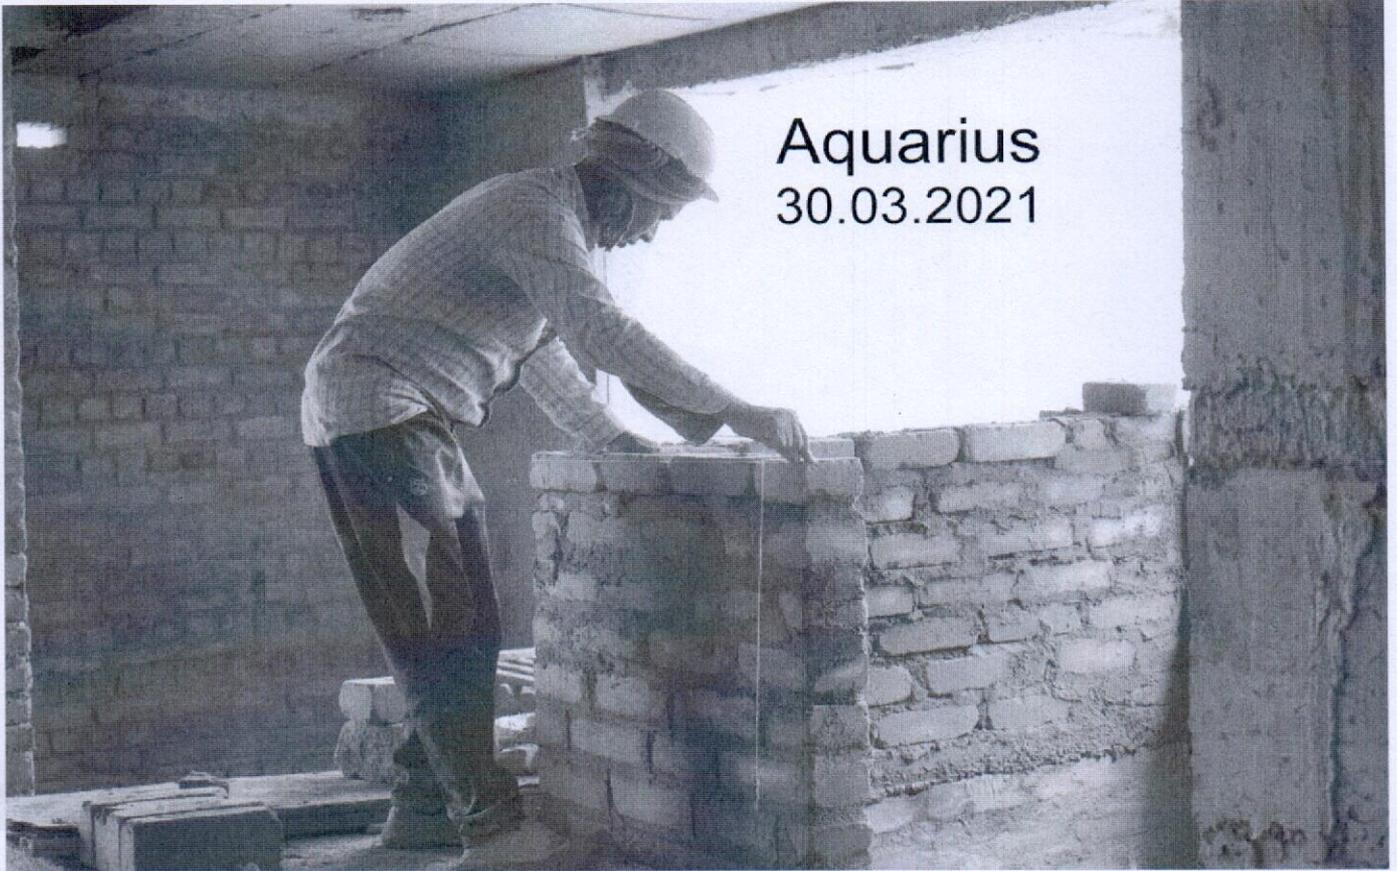

Aquarius
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Authorised Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER - 6 (Tower No- 14,15 and 16)

CLUSTER NAME:- VICTORIA

PROGRESS STATUS:

For Tower No. 14, 5th Floor column casting is 100% completed and reinforcement & Shuttering work of 5th Floor roof slab is in progress is in progress.

For Tower No. 15 (50% area), 5th Floor column casting is 100% completed and reinforcement & Shuttering work of 5th Floor roof slab is in progress is in progress.

For Tower No. 15 (rest 50% area), 3rd floor column casting is 100% completed and reinforcement & Shuttering work Balance 3rd Floor roof slab is in Progress.


For Tower No. 16, 2nd Floor roof slab casting is completed and Reinforcement & Shuttering work of 3rd Floor Column is in progress and Balance work is in Progress.

Brickwork: Ground Floor temporary Brickwork for space planning is started.




For Sakaar Constructions Pvt. Ltd.

[Handwritten Signature]
Authorised Signatory

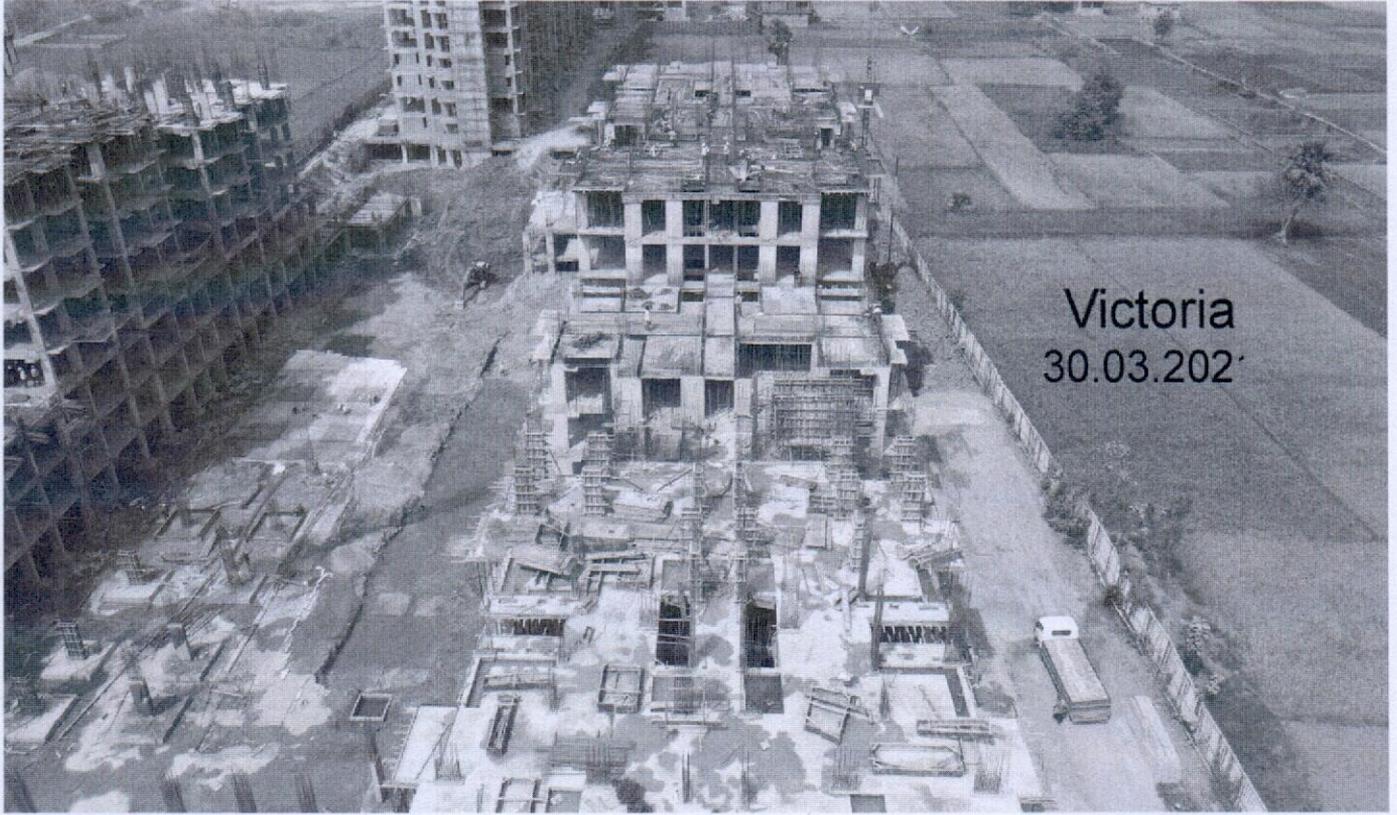

Victoria
30.03.2021

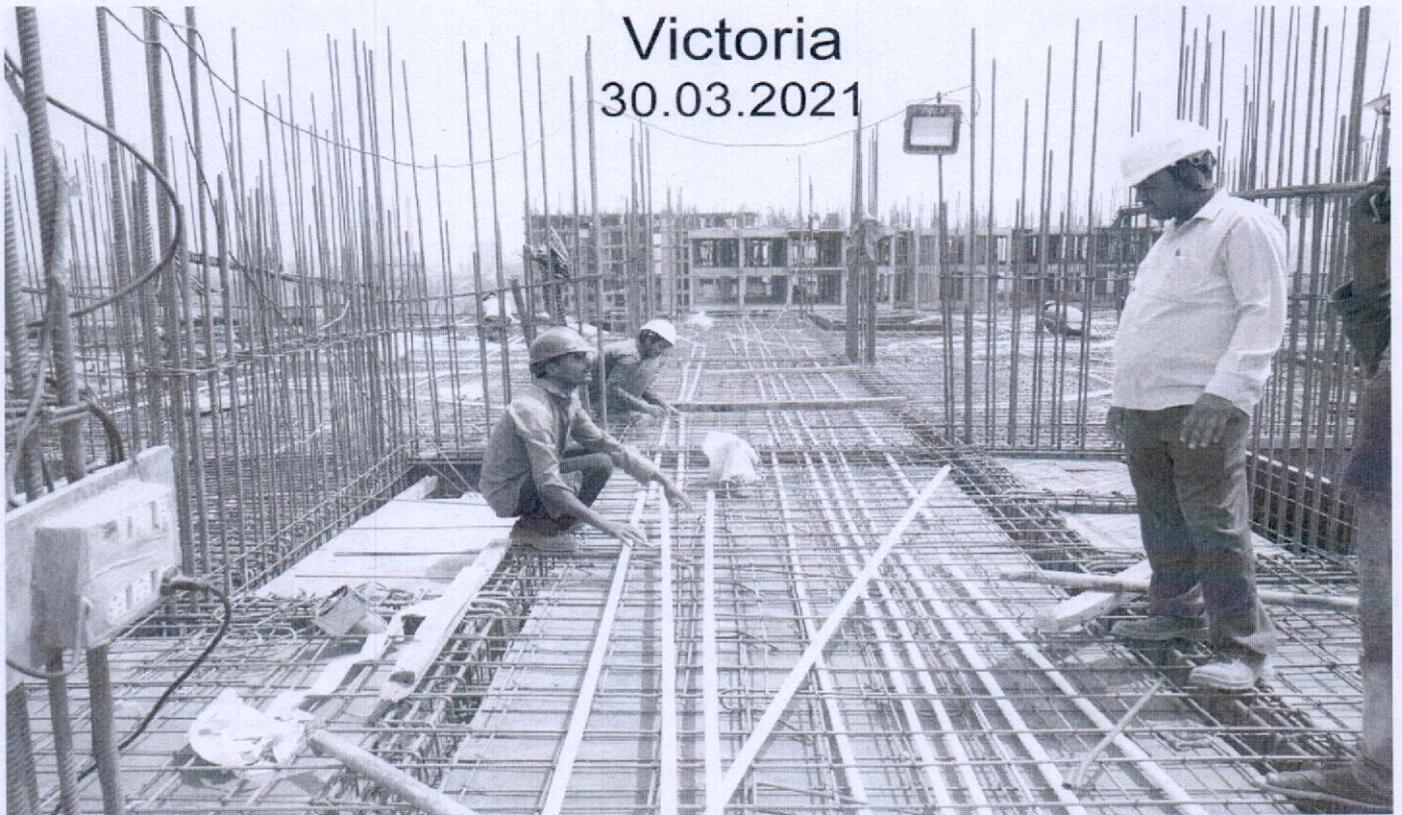


Victoria
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Sanjay John

Authorised Signatory

Victoria
30.03.2021

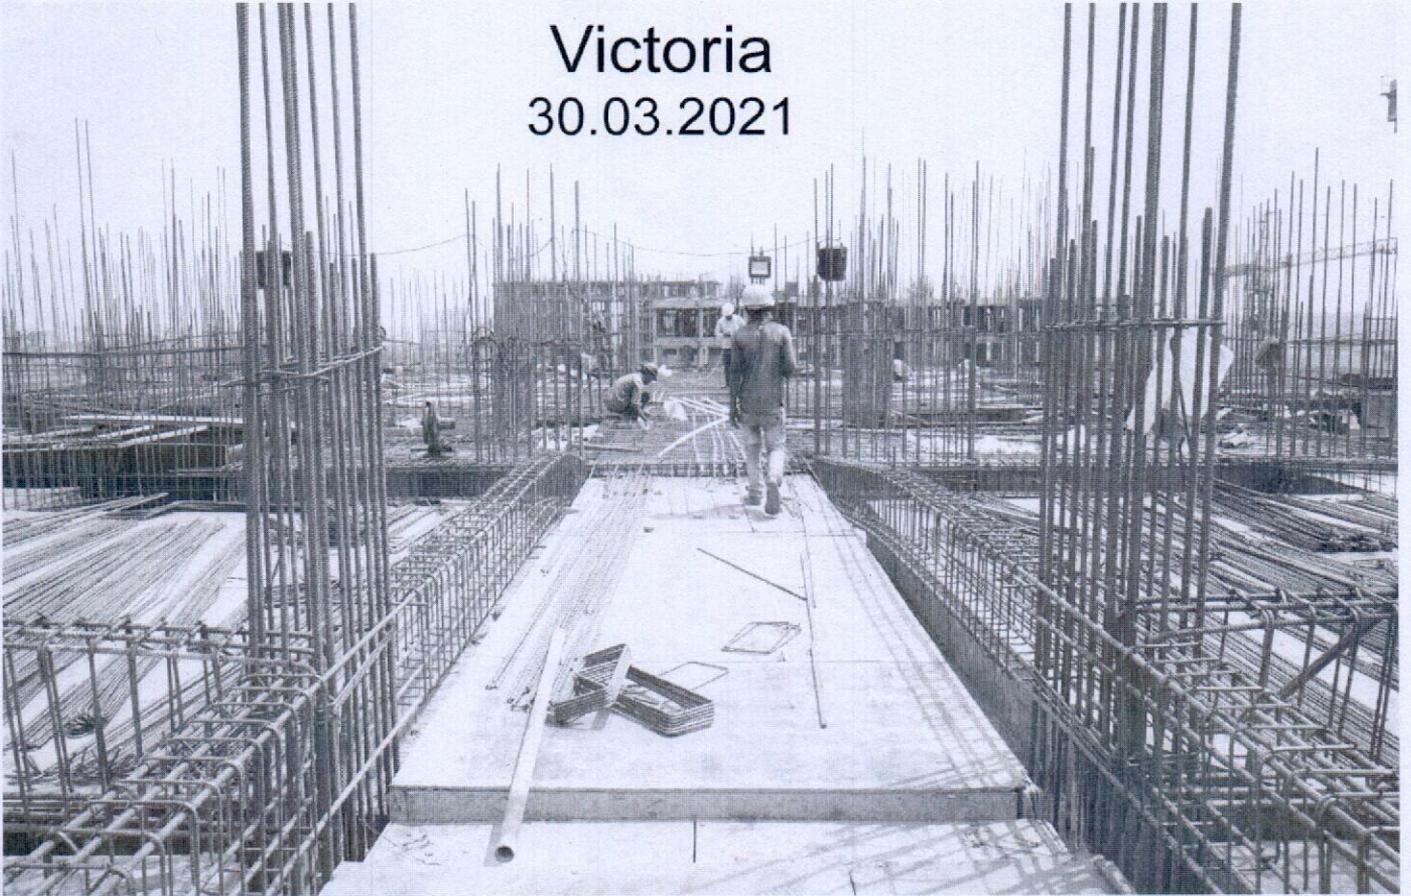

Victoria
30.03.2021



For Saakaar Constructions Pvt. Ltd.

Smita Sen

Authorised Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER – 7 (Tower No-17)


CLUSTER NAME:- NIAGRA

PROGRESS STATUS:


Casting work up to 6th Floor Roof slab Completed.

Layout of Seventh Floor Columns 40% Completed & balance work is in progress.

1st Floor Brickwork 95% Completed, 2nd Floor Brickwork 95% Completed & balance work is in progress. Brickwork of 3rd Floor 90% Completed & 4th Floor only Layout is completed balance work is in progress.

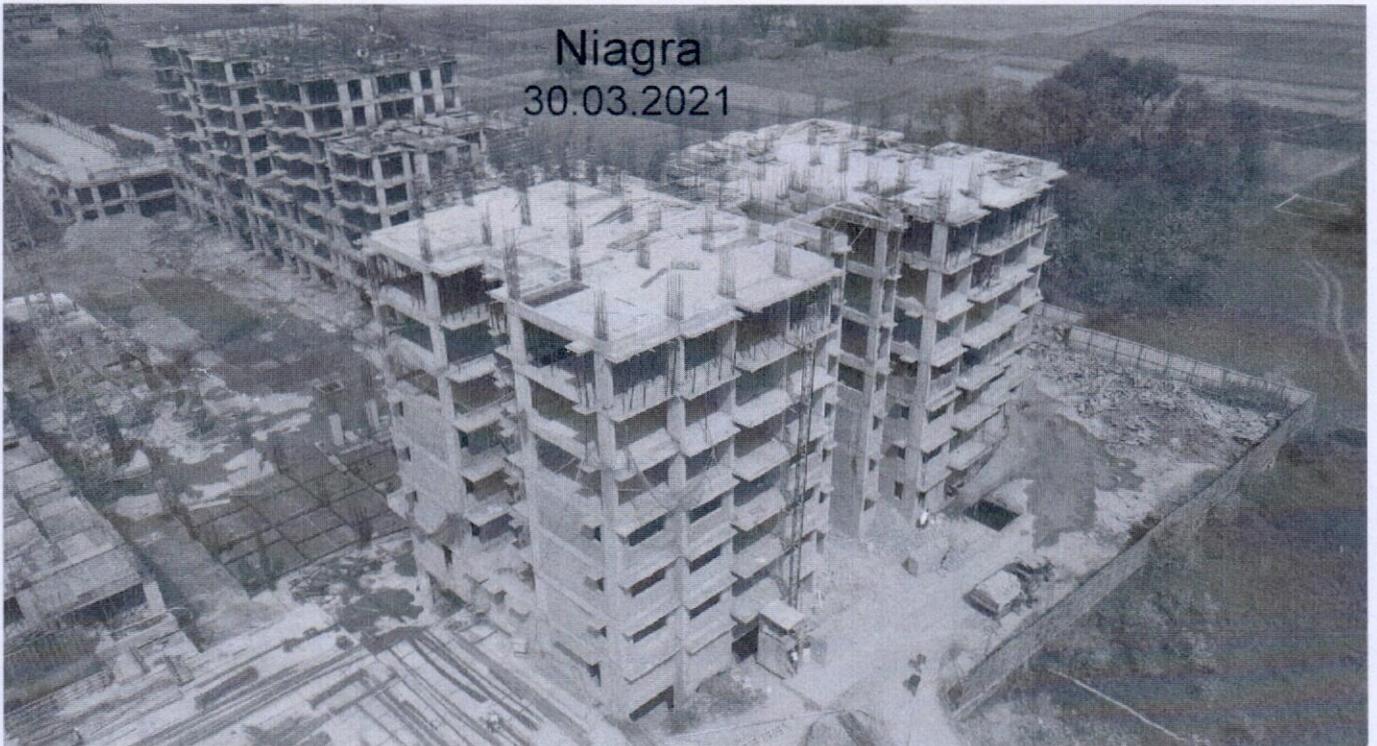

For Sakaar Constructions Pvt. Ltd.



Authorised Signatory



Niagra
30.03.2021



Niagra
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Authorised Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER – 8 (Tower No-18,19 and 20)

CLUSTER NAME:- THAMES

PROGRESS STATUS:

For Tower No. 18, 2nd floor column casting is 100% completed and Reinforcement & Shuttering work 2nd floor roof slab is in progress.

For Tower No. 19, casting of 7th floor roof slab is completed and 8th floor column casting is 50% completed and Reinforcement & Shuttering work of balance 8th floor column is in progress.

For Tower No. 20, 8th Floor Column Casting is 100% completed and Reinforcement & Shuttering work of 8th Floor roof slab is in progress.

For Tower No. 19&20 1st, 2nd & 3rd Floor Brickwork 95% completed, 4th floor brickwork 80% completed, 5th floor brickwork 40% completed, 6th Floor Layout started & Balance work in Progress.



For Saakaar Constructions Pvt. Ltd.

[Handwritten Signature]

Authorised Signatory

Thames
30.03.2021




Thames
30.03.2021



For Saakkar Constructions Pvt. Ltd.

Santosh Jha
Authorised Signatory

Thames
30.03.2021

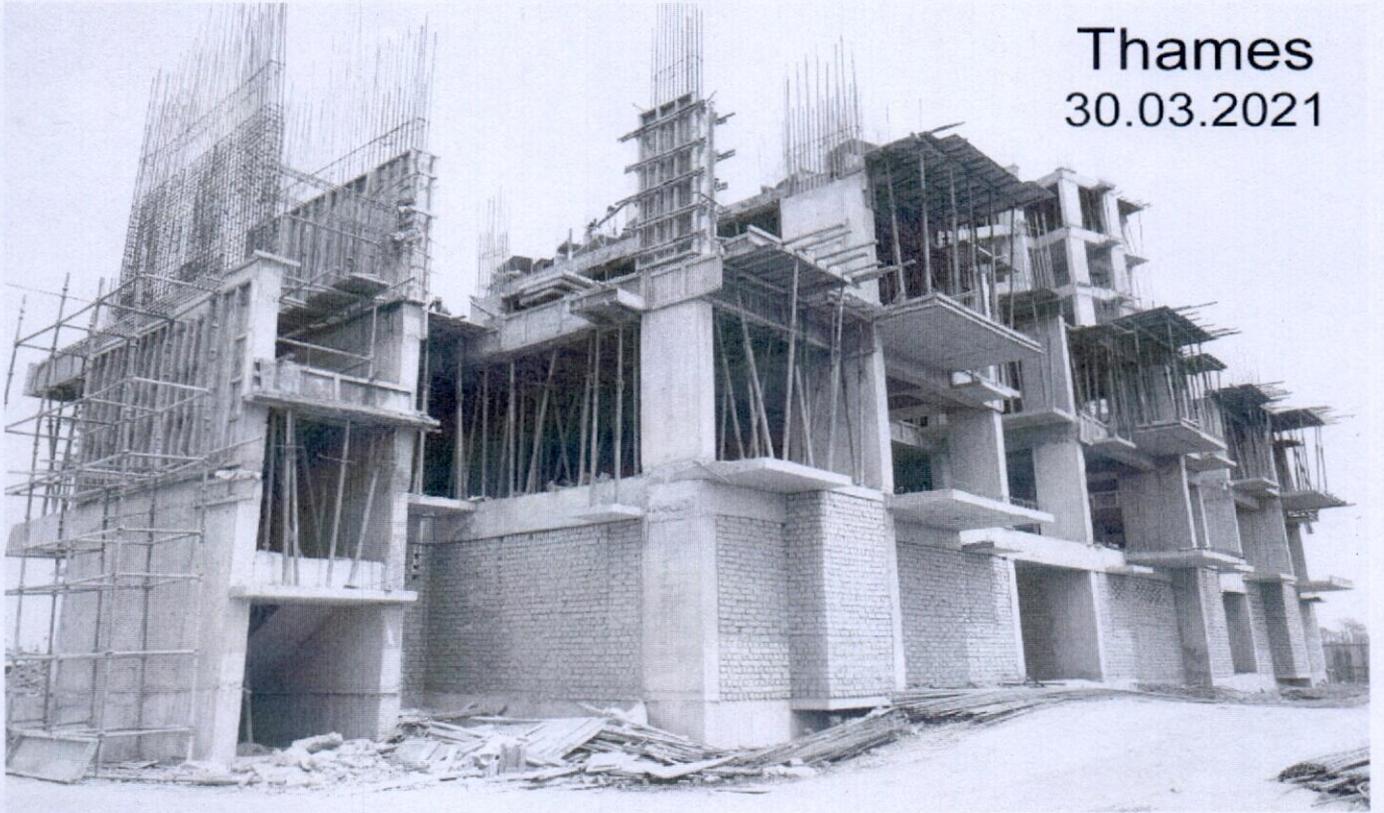

Thames
30.03.2021



For Saakeer Constructions Pvt. Ltd.

Devi Prasad
Authorized Signatory

SAAKAAR AQUACITY, DANAPUR

PROGRESS REPORT

REPORT AS ON: 31-03-2021

CLUSTER NO. :- CLUSTER – 9(Tower- EWS & LIG)

CLUSTER NAME: SAAKAAR RAINBOW

PROGRESS STATUS:

Foundation work Completed. Casting of Basement Columns 100% Completed & Balance Work is in Progress. Basement Roof Slab casting 40% completed and balance area of Basement Roof Slab shuttering & Reinforcement work 70% Completed & Balance Work is in Progress.



For Saakaar Constructions Pvt. Ltd.

Sanjay Singh
Authorised Signatory



Saakaar Rainbow
30.03.2021



Saakaar Rainbow
30.03.2021

For Saakaar Constructions Pvt. Ltd.

Authorised Signatory
