

To,  
The Chairman,  
Real Estate Regulatory Authority,  
6<sup>th</sup> Floor,  
Bihar State Building Construction Corporation Campus,  
Hospital Road, Shastri Nagar, Patna-800023

**Sub - Quarterly Report of Our Project SAAKAAR'S AQUA CITY 01-04-2021 to 30-06-2021**  
**RERA Registration No: - BRERAP00027-2/233/R-96/2018**

Dear Sir,

With reference to above, as per REAL ESTATE REGULATORY AUTHORITY, BIHAR REAL ESTATE (REGULATION AND DEVELOPMENT) RULES, 2017 CHAPTER IV RULE 16 (D). we are submitting the Quarterly Report of SAAKAAR'S AQUA CITY, Usari, Makdhupur Road, Sandalpur, Khagaul, Danapur, District Patna State Bihar as prescribed details Mentioned below:

1. Quarterly up to date status of the project (Physical and Financial).

A) Status of Construction of each building is mentioned below and photographs are attached in RERA website.

Project: SAAKAAR AQUA CITY, DANAPUR		
Site Progress Status		
Sl. No	Tower	Progress Status
1	Tower - 1	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--90%, LOWER BASEMENT COLUMNS--100%, FORM WORK--80%, REBAR WORK--80%, CASTING--80%, UPPER BASEMENT COLUMNS--40%, RETAINING WALL UPPER BASEMENT--40%, FORM WORK--40%, REBAR WORK--40%, CASTING--40%, GROUND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIRST FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SECOND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRD FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, EIGHTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%.
	Tower - 2,3,4 & 5	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--50%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--75%, REBAR WORK--75%, CASTING--50%, BRICKWORK--0%, SECOND FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, THIRD FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--50%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--50%, FORM WORK--50%, REBAR WORK--50%, CASTING--25%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--25%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, EIGHTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%.

For Saakaar Constructions Pvt. Ltd.

*Janita Sol*  
Authorised Signatory


**Saakaar Constructions Pvt. Ltd.**

CIN No. : U00502BR1996PTC007493

5th Floor, Sone Bhawan, Near Hotel Chankaya, R Block Golamber, Patna-800 001

Ph.: 0612-2506506, M : 6202750747

e-mail : info@saakaar.com, website : www.saakaar.com





		FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%,
7	Tower - 17	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--100%, LOWER BASEMENT COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--95%, SECOND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--95%, THIRD FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--90%, FOURTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--30%, FIFTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, Eighth FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%,
8	Tower - 18,19 & 20	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--%, LOWER BASEMENT COLUMNS--%, FORM WORK--%, REBAR WORK--%, CASTING--%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, GROUND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--0%, FIRST FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--67%, SECOND FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--67%, THIRD FLOOR COLUMNS--100%, FORM WORK--100%, REBAR WORK--100%, CASTING--100%, BRICKWORK--67%, FOURTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--67%, FIFTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--67%, SIXTH FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--25%, Eighth FLOOR COLUMNS--70%, FORM WORK--70%, REBAR WORK--70%, CASTING--70%, BRICKWORK--0%, NINTH FLOOR COLUMNS--70%, FORM WORK--35%, REBAR WORK--35%, CASTING--35%, BRICKWORK--0%, TENTH FLOOR COLUMNS--35%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%,
9	Tower - 21	EXCAVATION--100%, PILING & SAND CUSHION--100%, PCC--100%, RAFT--100%, RETAINING WALL LOWER BASEMENT--%, LOWER BASEMENT COLUMNS--%, FORM WORK--%, REBAR WORK--%, CASTING--%, UPPER BASEMENT COLUMNS--100%, RETAINING WALL UPPER BASEMENT--95%, FORM WORK--85%, REBAR WORK--80%, CASTING--80%, GROUND FLOOR COLUMNS--20%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIRST FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SECOND FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRD FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FOURTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, FIFTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SIXTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, SEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, Eighth FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, NINTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, ELEVENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, TWELVETH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%, THIRTEENTH FLOOR COLUMNS--0%, FORM WORK--0%, REBAR WORK--0%, CASTING--0%, BRICKWORK--0%,

- B) --Status of Constructions of each floor that the project is on the RAFT and basement Roof level and photograph are attached in RERA website.
- C) Status of construction of internal infrastructure and common area that the project is on the RAFT and basement Roof level and photograph are attached in RERA website.
- D) Details of fund receiving through booking and other means are details mentioned below.

Opening Balance	Amount Received through booking.	Equity	Loan	Money Spent	Balance Amount	Sourcing of Fund
23,37,49,593.00	17,58,07,856.00	NIL	NIL	11,11.63,933.00	29,83,93,456.00	Bookings and Own funds.

For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory

2. List of number and type of apartments.

Residential/Commercial	Type of Apartment	Opening	Booked	Closing Balance	Total No of garages (Covered)	Opening	Booked	Closing balance
Residential	EWS	167	7	160	196	167	7	160
	LIG	60	14	46	182	60	14	46
	2 BHK	55	1	54	1266	482	6	476
	2.5 BHK	55	1	54				
	3 BHK	136	2	134				
	4 BHK	2	0	2				
Commercial	Studio	75	-	75	116	116		
	Convenience Store	34	-	21				
	OPD (Doctor's Cabin+Medicine Room)	1	-	1				
	Diagnostic Centre (Physiotherapy, X-Ray room, Pathlab)	1	-	1				
	Office Retail	1	-	1				
	Coaching Classes+Staff Room	1	-	9				
	Bank	1	-	1				
	Food Court	1	-	1				
	Play school (8-class room + H.O.D + Staff Room)	1	-	1				

3. List of approvals taken and the approvals which are pending subsequent to commencement certificate.


- Approvals list during the quarter— Nil
- Approval applied and expected date of receipt — Nil
- Approval to be applied and date planned for application — Nil
- Modifications, amendment or revision ,if any, issued by the competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project — Nil

Please acknowledge the receipt.

Thanking You,

Yours

For Saakaar Constructions Pvt. Ltd.  
For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory  
(Authorised Signatory)

# SAAKAAR AQUACITY, DANAPUR

## PROGRESS REPORT

REPORT AS ON: 30.06.2021

CLUSTER NO. : - CLUSTER – 1 (Tower-1)

CLUSTER NAME: - ATLANTIS

### PROGRESS STATUS:


Excavation work, sand piling work of tower area & Leveling work has been 100% Completed.

NTA Area is 45% casting completed Upto Upper Basement Roof slab Level & Tower Area, Upper Basement Column is 100% Completed and Ground Floor Level Slab Reinforcement & Shuttering is in progress.



**Atlantis**  
**29.06.2021**

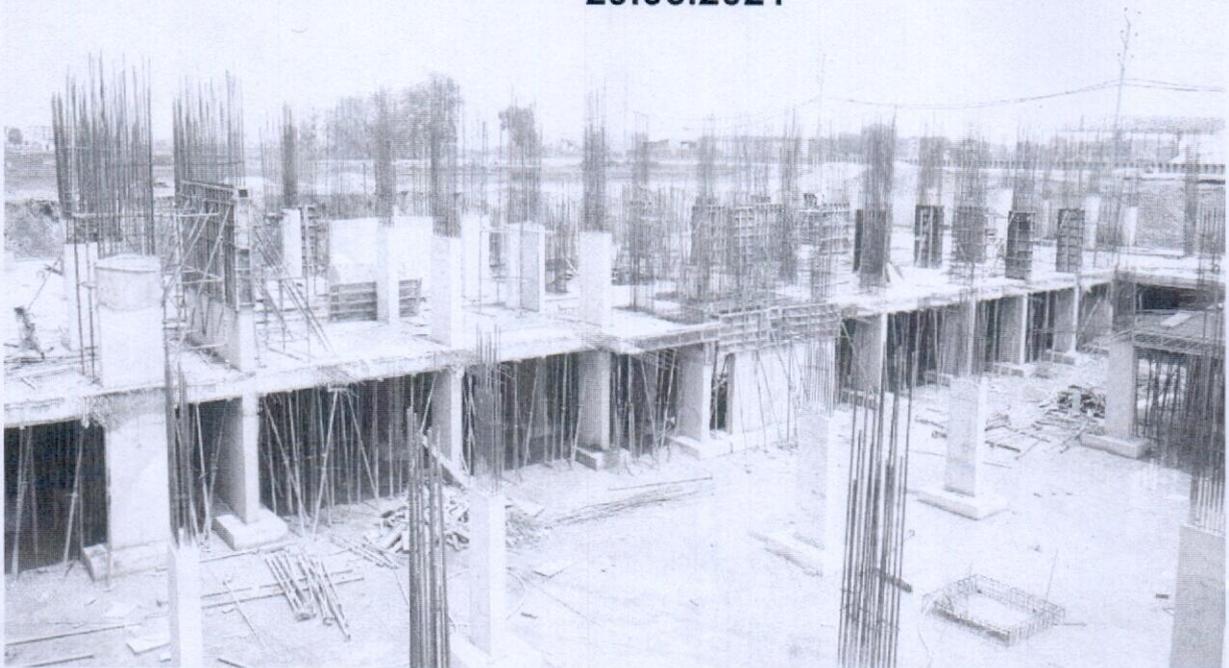
For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory


**Atlantis**  
**29.06.2021**



**Atlantis**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory



**Atlantis**  
29.06.2021



**Atlantis**  
29.06.2021

For Saakaar Constructions Pvt. Ltd.

Authorised Signatory

# SAAKAAR AQUACITY, DANAPUR

## PROGRESS REPORT

REPORT AS ON: 30.06.2021

CLUSTER NO. :- CLUSTER - 2 (Tower No-2,3,4 & 5)

CLUSTER NAME: -PACIFIC

### PROGRESS STATUS:

For Tower No. 5, 5th Floor column casting work is 100% completed and Reinforcement & Shuttering work of 5<sup>th</sup> Floor Roof Slab is Completed & casting is scheduled on 01.07.2021.

For Tower No. 4, 5th floor roof slab Casting is 100% completed and 6<sup>th</sup> floor Column is 70% completed & Reinforcement & Shuttering work of balance 6th floor Column is in progress.

For Tower No. 3, 1<sup>st</sup> floor Column casting 100% completed and Reinforcement & Shuttering work of 1<sup>st</sup> floor roof slab is completed & casting is scheduled.

For Tower No. 2, 1<sup>st</sup> floor Column casting 100% completed and Reinforcement & Shuttering work of 1<sup>st</sup> floor roof slab is in progress.



**Pacific**

29.06.2021

For Sakaar Constructions Pvt. Ltd.

*[Signature]*  
Authorised Signatory



**Pacific**  
**29.06.2021**



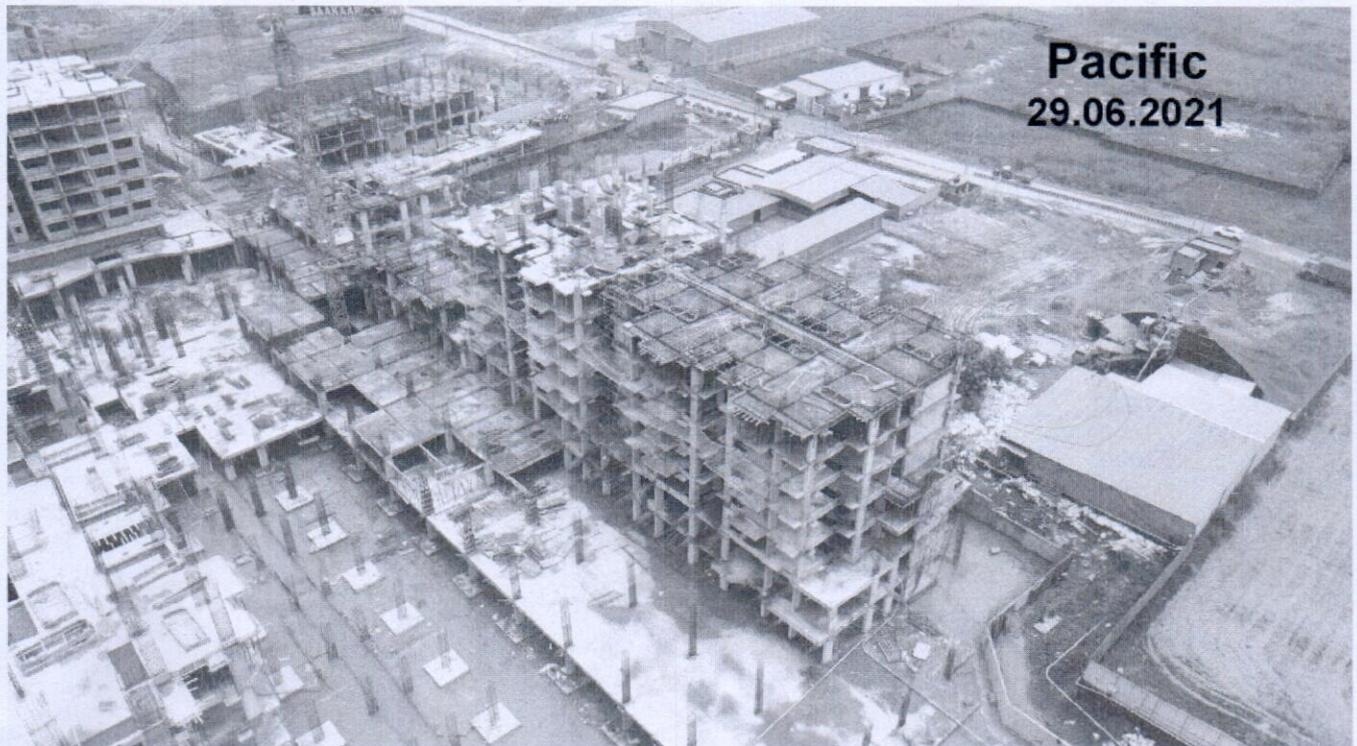
**Pacific**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

*[Handwritten Signature]*  
Authorised Signatory




**Pacific**  
**29.06.2021**



**Pacific**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorized Signatory

# **SAAKAAR AQUACITY, DANAPUR**

## **PROGRESS REPORT**

**REPORT AS ON: 30.06.2021**

**CLUSTER NO. :- CLUSTER - 3 (Tower No 6,7,8 and 9)**

**CLUSTER NAME:-AMAZON**

### **PROGRESS STATUS:**

For Tower No. 6,12<sup>th</sup> Floor roof slab casting is 100% completed & Balance work is in progress.

For Tower No.7, 12<sup>th</sup> Floor column casting is 100% completed & Reinforcement & Shuttering work of 12<sup>th</sup> Floor roof slab is in progress.

For Tower 8 & 9, Upto 11<sup>th</sup> Floor column casting is 100% completed & Reinforcement & Shuttering work of 11<sup>th</sup> Floor roof slab is in progress.

For Tower No. 6, 7, 8 & 9; 2<sup>nd</sup>, 3rd, 4th, 5<sup>th</sup>, 6th & 7<sup>th</sup> Floor Brickwork 90% completed & 8<sup>th</sup> Floor Brickwork 20% completed and Balance work in Progress.

**Amazon**  
**29.06.2021**




For Saakaar Constructions Pvt. Ltd.

*Sait-572*  
Authorised Signatory



For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory

**Amazon**  
**29.06.2021**



**Amazon**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.


2 | Page

*Jain*  
Authorised Signatory



**Amazon**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorized Signatory

# SAAKAAR AQUACITY, DANAPUR

## PROGRESS REPORT

REPORT AS ON: 30.06.2021

CLUSTER NO. : - CLUSTER - 4 (Tower No- 11 &12)

CLUSTER NAME: - NEPTUNE

### PROGRESS STATUS:

For Tower No. 11&11A, 11<sup>th</sup> Floor roof slab casting is 80% completed & Reinforcement & Shuttering balance work of 11<sup>th</sup> Floor roof slabs is in progress.

For Tower No. 12, 11<sup>th</sup> Floor Column casting is 100% completed & Reinforcement & Shuttering work of 11<sup>th</sup> Floor roof slabs is in progress.

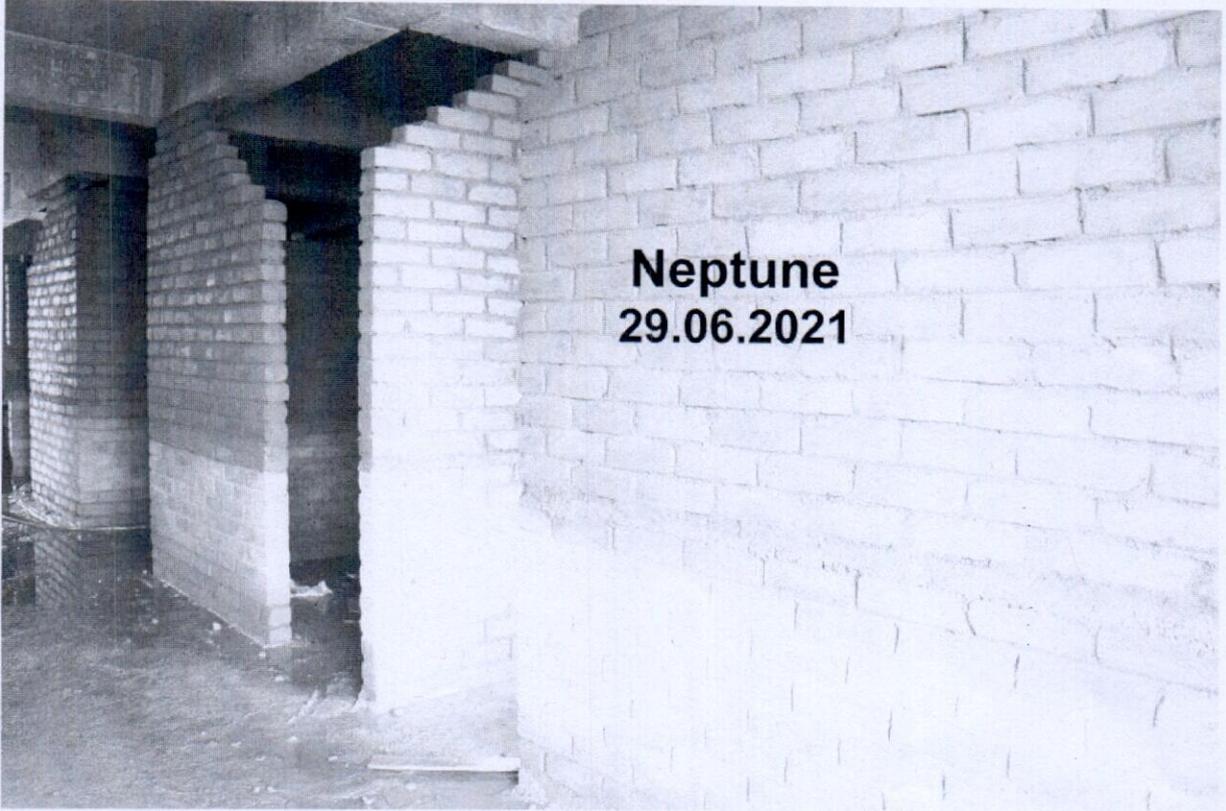
3<sup>rd</sup>, 4<sup>th</sup> & 5<sup>th</sup> Floor Brickwork 95 % completed, & 6<sup>th</sup> floor Brickwork is 60% completed Upto Sill Level & Balance work is in Progress.

**Neptune**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*[Signature]*  
Authorised Signatory




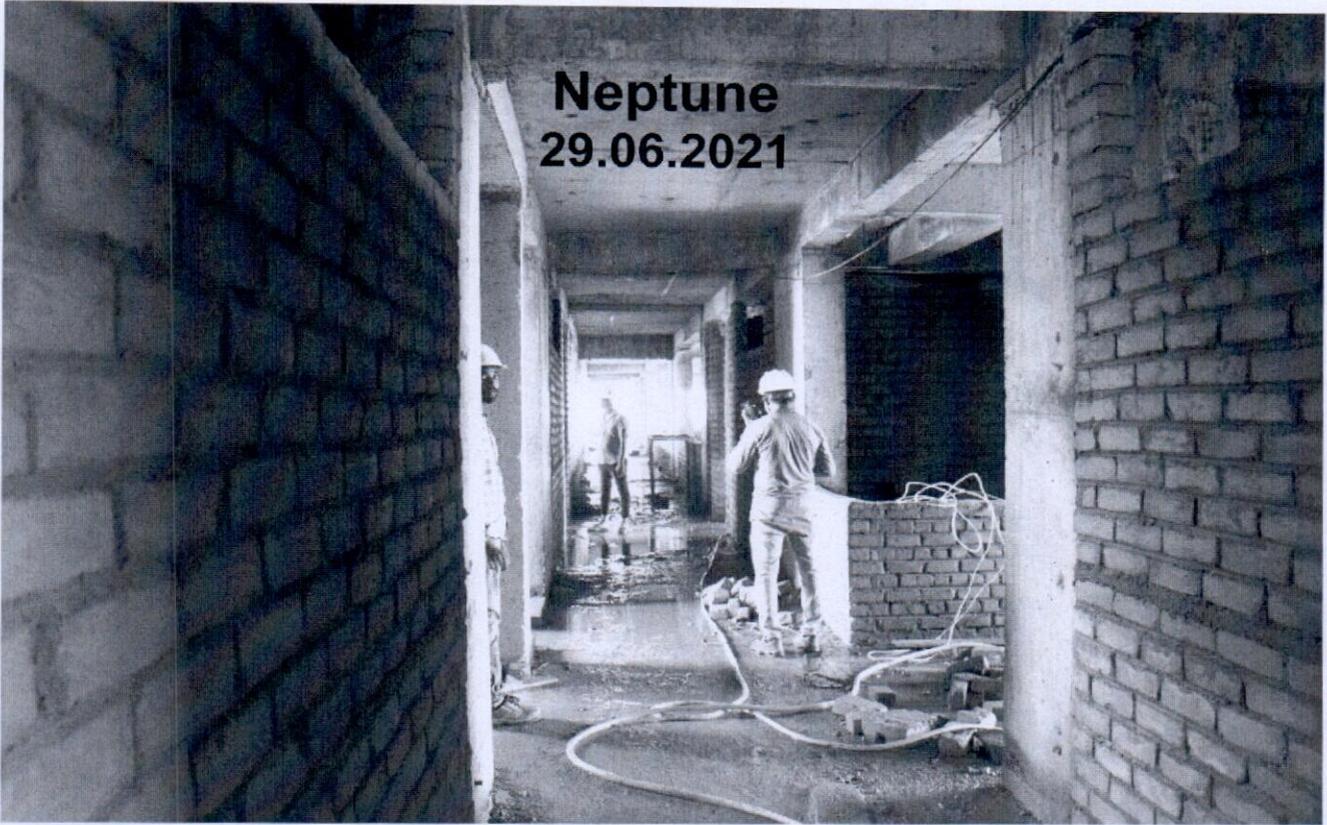
**Neptune**  
**29.06.2021**



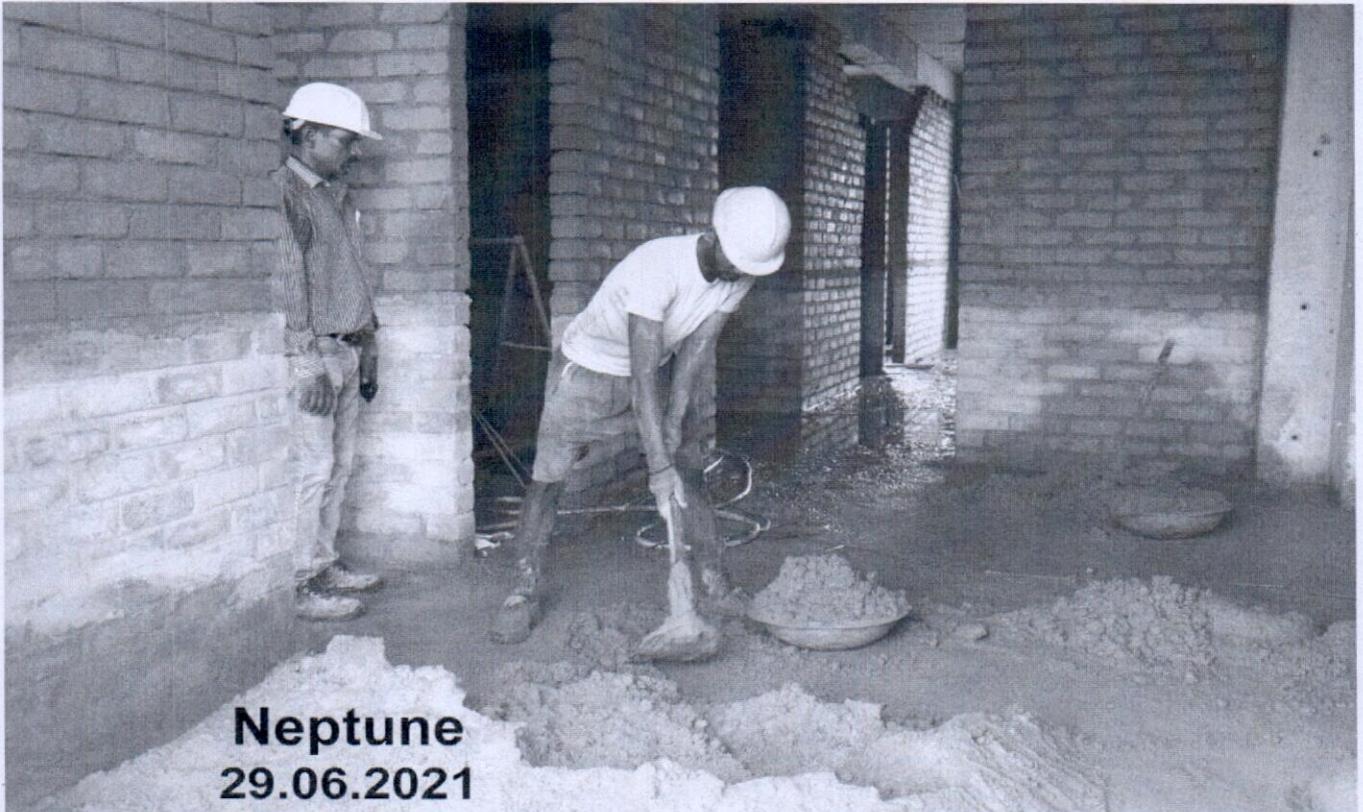
**Neptune**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory




**Neptune**  
**29.06.2021**



**Neptune**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory

**Neptune**  
**29.06.2021**



**Neptune**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*Sanjay Saha*  
Authorised Signatory

**Neptune**  
**29.06.2021**



**Neptune**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*[Handwritten Signature]*  
Authorised Signatory

# SAAKAAR AQUACITY, DANAPUR

## PROGRESS REPORT

REPORT AS ON: 30.06.2021

CLUSTER NO. :- CLUSTER - 5 (Tower No-13)

CLUSTER NAME:-AQUARIOUS

### PROGRESS STATUS:

For Tower No. 13(Part A),Casting of 10th floor column is 100% completed& Shuttering& Reinforcement Work ofbalance 10th floor Roof Slab is in progress.

For Tower No. 13 (Part B)Casting of 9<sup>th</sup> floor Roof Slab is 100 % Completed and, Casting of 10<sup>th</sup> floor column is 30% completed& Shuttering & Reinforcement Work of balance 10<sup>th</sup> floor column work is in progress.

2<sup>nd</sup>FloorBrickwork only layout is completed,3rd floor Brickwork 15% completed 4th floor Brickwork 80% completed and rest Balance work is in Progress.



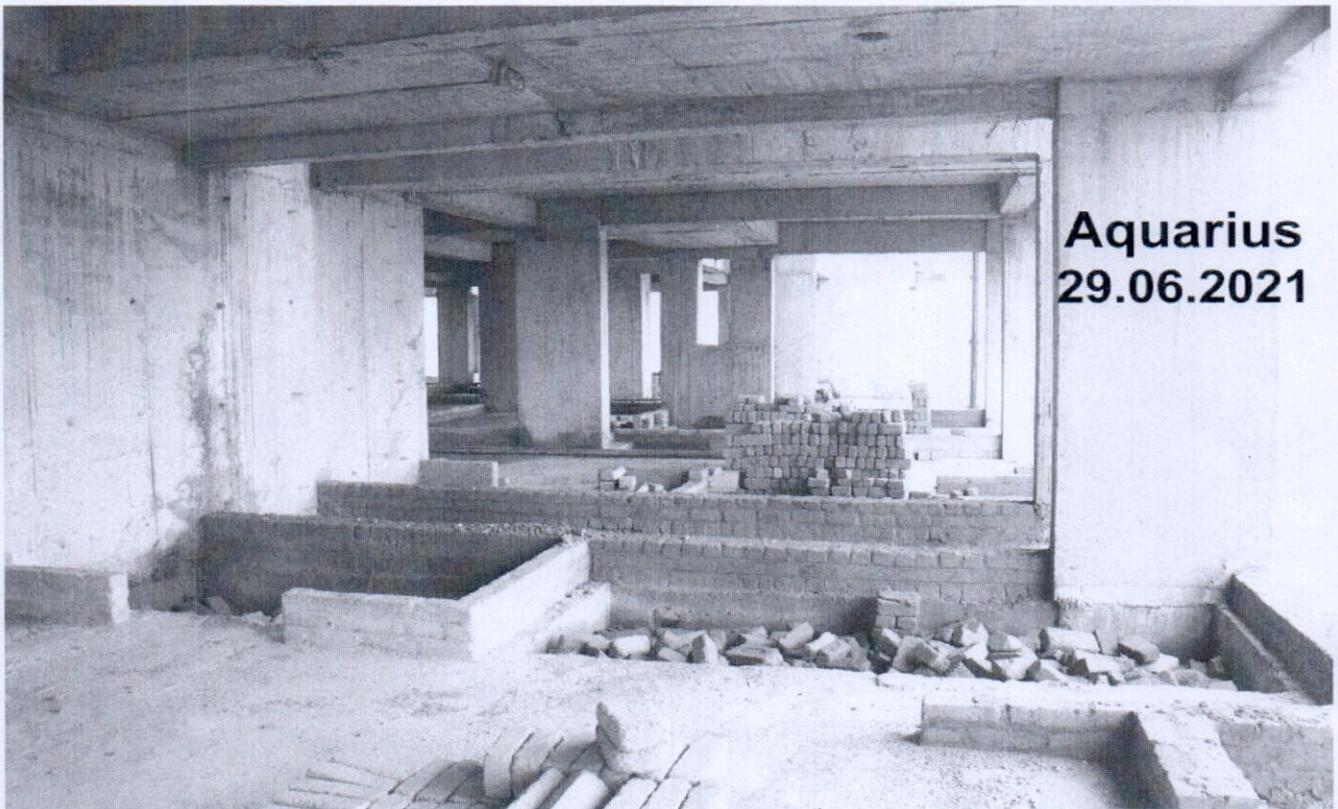
**Aquarius**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

*[Handwritten Signature]*  
Authorised Signatory



**Aquarius**  
**29.06.2021**



**Aquarius**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

*Saita SR*  
Authorised Signatory

**Aquarius**  
**29.06.2021**



**Aquarius**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*Saikaar*  
Authorised Signatory




**Aquarius**  
**29.06.2021**



**Aquarius**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorized Signatory

# **SAAKAAR AQUACITY, DANAPUR**

## **PROGRESS REPORT**

**REPORT AS ON: 30.06.2021**

**CLUSTER NO. : - CLUSTER - 6 (Tower No- 14, 15 and 16)**

**CLUSTER NAME: -VICTORIA**

### **PROGRESS STATUS:**

For Tower No. 14, 6<sup>th</sup> Floor roof slab casting is 100% completed and reinforcement & Shuttering work of 7<sup>th</sup> Floor Column is in progress.

For Tower No. 15 (50% area), 6<sup>th</sup> Floor roof slab casting is 100% completed and reinforcement & Shuttering work of 7<sup>th</sup> Floor Column is in progress.

For Tower No. 15 (rest 50% area), 4<sup>th</sup> Floor Column 100% completed and reinforcement & Shuttering work Balance 4<sup>th</sup> Floor roof slab is in Progress.

For Tower No. 16, 4<sup>th</sup> Floor Column 100% completed and reinforcement & Shuttering work Balance 4<sup>th</sup> Floor roof slab is in Progress.

Brickwork: From 2<sup>nd</sup> Floor Brickwork started & 2nd Floor Brickwork is 75% completed. & 3rd Floor Brickwork is 15% completed.



**Victoria  
29.06.2021**

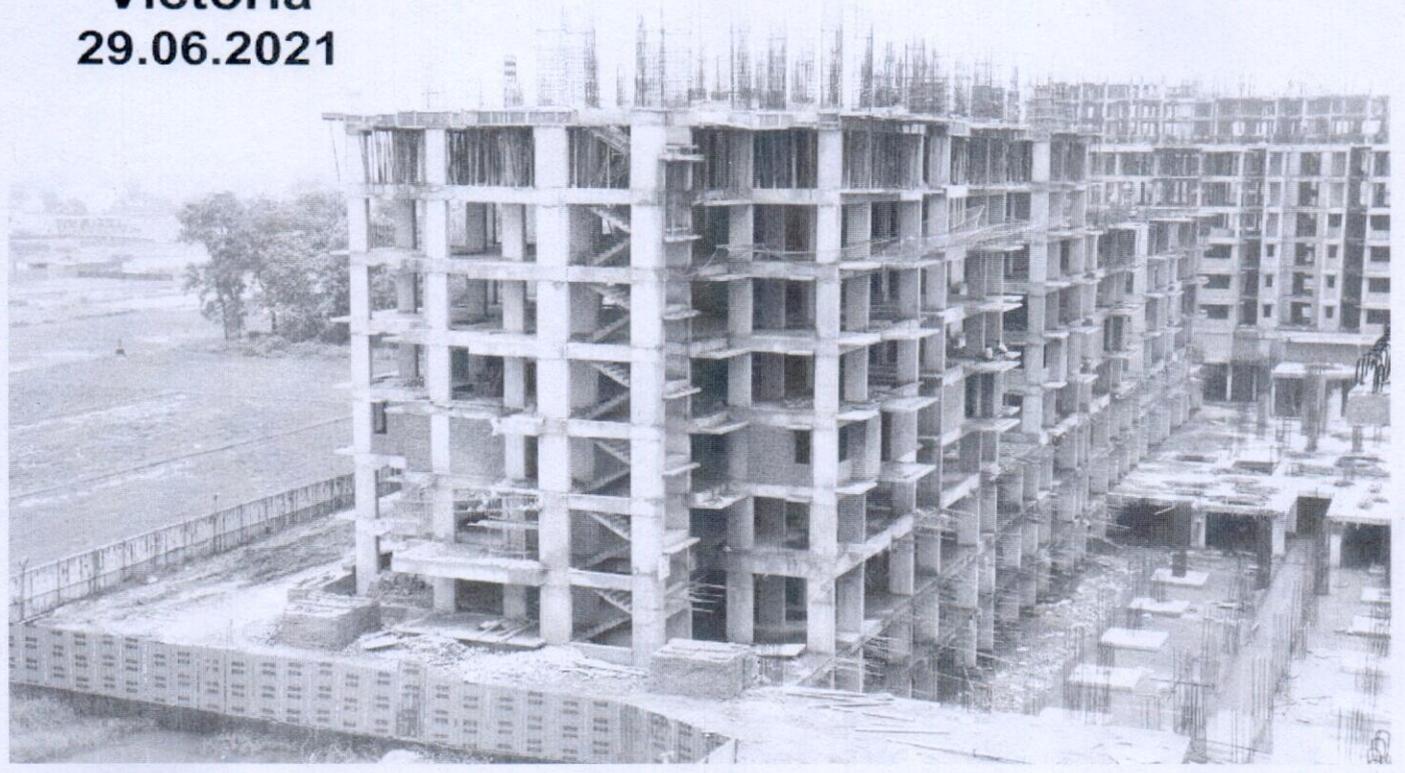
For Saakaar Constructions Pvt. Ltd.

*[Signature]*  
Authorised Signatory

**Victoria**  
**29.06.2021**



**Victoria**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*Said - 01*  
Authorised Signatory




**Victoria**  
**29.06.2021**



**Victoria**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory

# SAAKAAR AQUACITY, DANAPUR

## PROGRESS REPORT

REPORT AS ON: 30.06.2021

CLUSTER NO. :- CLUSTER – 7 (Tower No-17)

CLUSTER NAME:- NIAGRA

### PROGRESS STATUS:

Casting work up to 6<sup>th</sup> Floor Roof slab Completed.

Layout of Seventh Floor Columns 40% Completed & balance work is in progress.

1<sup>st</sup> & 2<sup>nd</sup> Floor Brickwork 95% Completed, Brickwork of 3<sup>rd</sup> Floor 90% Completed & 4<sup>th</sup> Floor 30 % completed balance work is in progress.



For Saakaar Constructions Pvt. Ltd.

*[Signature]*  
Authorised Signatory

**Niagra**  
**29.06.2021**



**Niagra**  
**29.06.2021**



For Saakaar Constructions Pvt. Ltd.

*[Handwritten Signature]*  
Authorised Signatory

# **SAAKAAR AQUACITY, DANAPUR**

## **PROGRESS REPORT**

**REPORT AS ON: 30.06.2021**

**CLUSTER NO. :- CLUSTER – 8(Tower No-18,19 and 20)**

**CLUSTER NAME:-THAMES**

### **PROGRESS STATUS:**

For Tower No. 18, 3<sup>rd</sup> Floor roof slab casting is 100% completed and Reinforcement & Shuttering work balance column & 4<sup>th</sup> Floor column is in progress.

For Tower No. 19, 9<sup>th</sup> Floor Column Casting is 100% completed and Reinforcement & Shuttering work of 9<sup>th</sup> Floor roof slab is in progress.

For Tower No. 20, 10<sup>th</sup> Floor Column casting is 100% completed & 10<sup>th</sup> Floor roof slab is Reinforcement & Shuttering work is in progress.

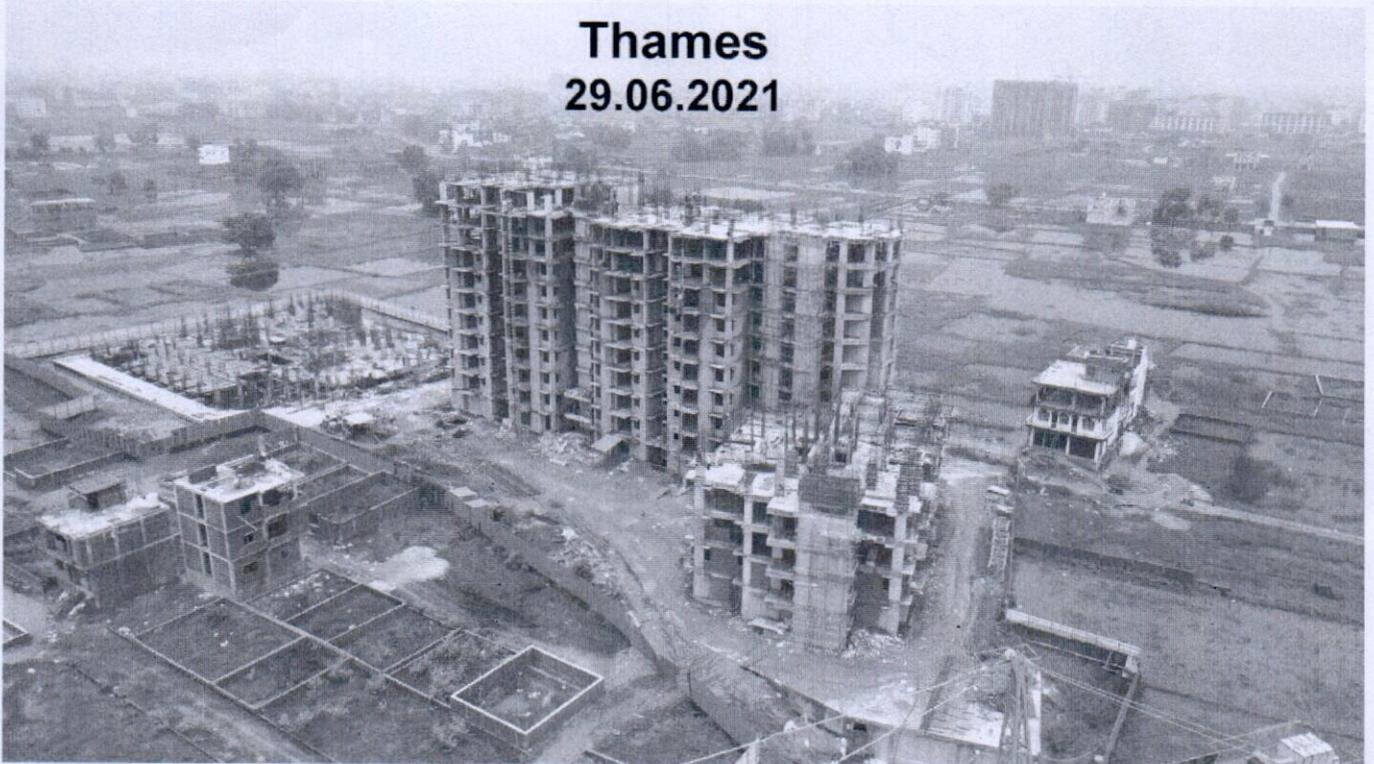
For Tower No. 19&20-1<sup>st</sup>, 2<sup>nd</sup>, 3<sup>rd</sup>, 4<sup>th</sup>, 5<sup>th</sup> & 6<sup>th</sup> Floor Brickwork 95% completed, & 7<sup>th</sup> floor brickwork 70% completed and Balance work in Progress.



For Saakaar Constructions Pvt. Ltd.


*Jai Singh*  
Authorised Signatory

**Thames**  
**29.06.2021**



**Thames**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.


  
Authorised Signatory

**Thames**  
**29.06.2021**



**Thames**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory

# **SAAKAAR AQUACITY, DANAPUR**

## **PROGRESS REPORT**

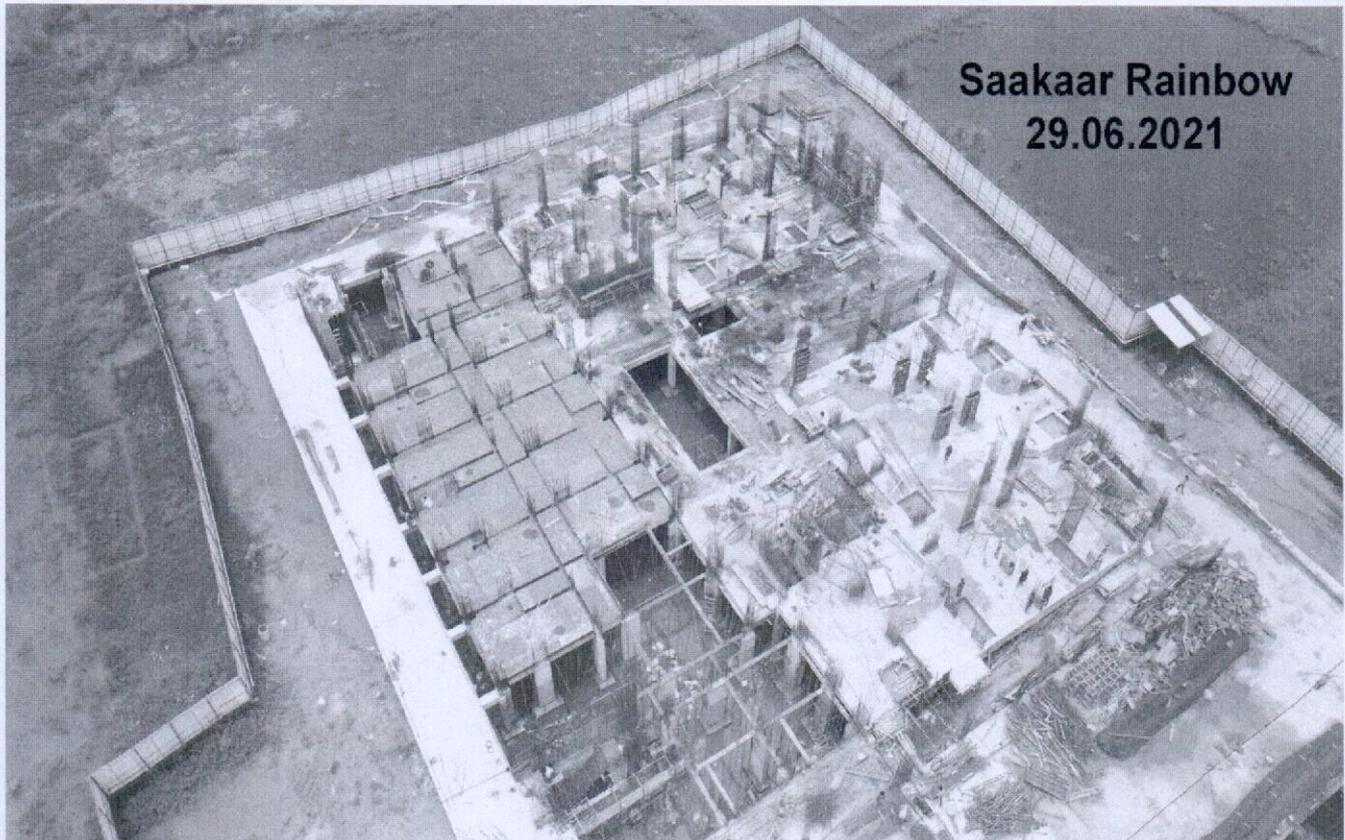
**REPORT AS ON: 30.06.2021**

**CLUSTER NO. : - CLUSTER – 9(Tower- EWS & LIG)**


**CLUSTER NAME:SAAKAAR RAINBOW**

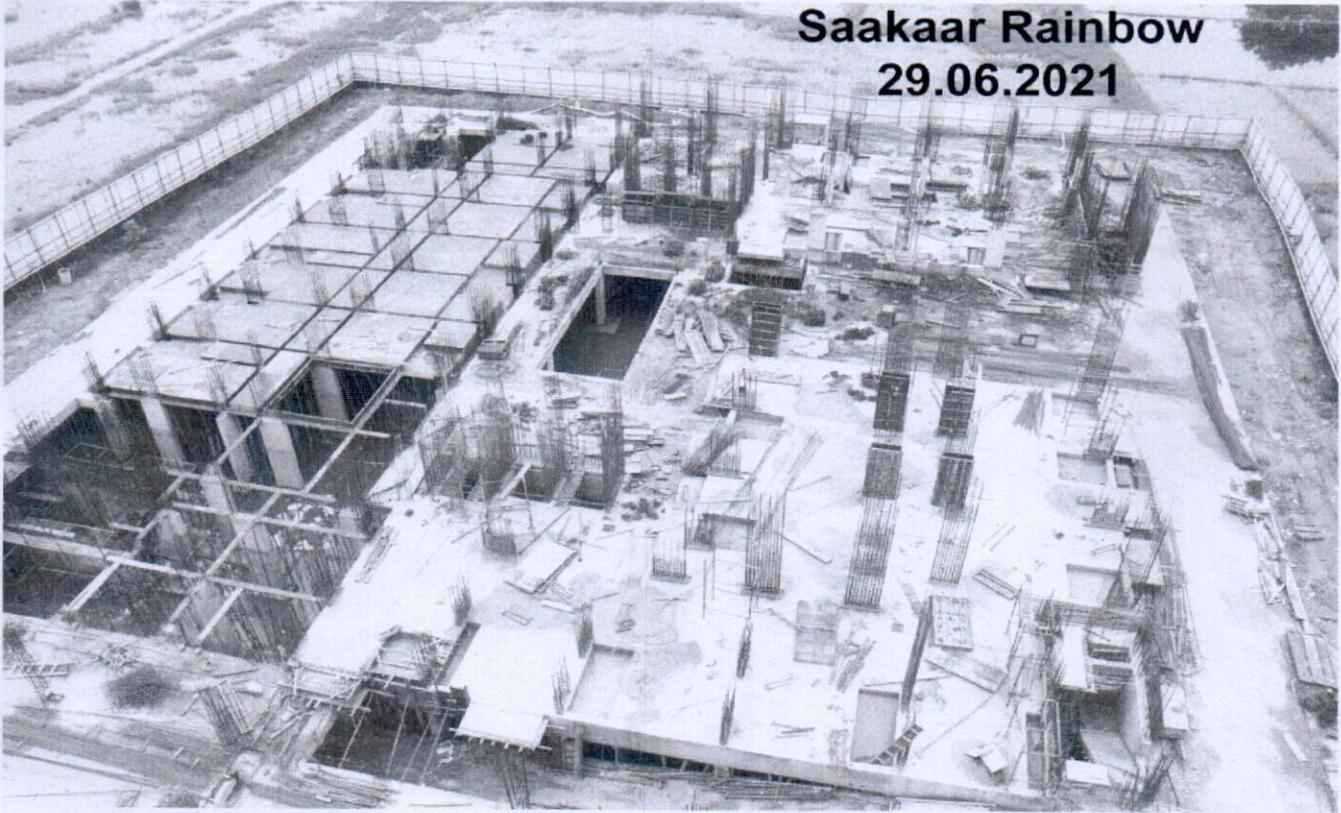
### **PROGRESS STATUS:**

Foundation work Completed.Casting of Basement Columns 100% Completed& Balance Work is in Progress. Basement Roof Slab casting 85% completed and balance15% area of Basement Roof Slab shuttering &Reinforcement work is in Progress and Ground Floor Column Casting is 15% completed & Balance Ground Floor Column Shuttering & reinforcement is in progress.

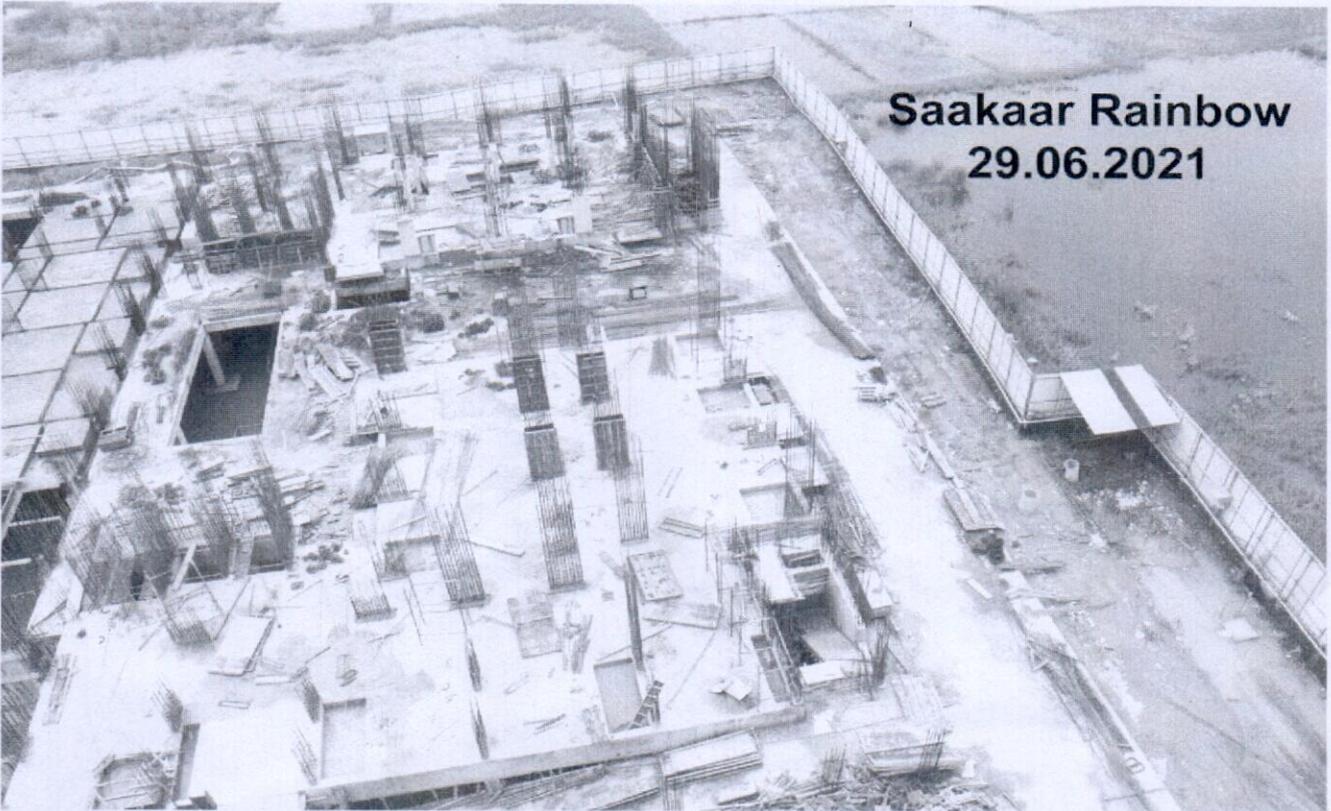


For Saakaar Constructions Pvt. Ltd.

  
Authorised Signatory



**Saakaar Rainbow**  
**29.06.2021**



**Saakaar Rainbow**  
**29.06.2021**

For Saakaar Constructions Pvt. Ltd.

*[Handwritten Signature]*  
Authorised Signatory
