

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Jul-Sep of 2024 (Year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No.	U45200BR2013PTC020682.
Firm Address:	5 th FLOOR, S K PALACE, NEAR SAGUNA MORE, DANAPUR, PATNA Bihar 801503.
Total Experience of promoter in Real Estate Sector	11 Years of Experience.
Total Experience in Real Estate After Implementation of RERA	
No of Project done Before Implementation of RERA	1. Rajendra Smriti Enclave
No of Project done After Implementation of RERA	1. Bhadra Raj Enclave 2. Rajdeo Enclave 3. Ishwar Chandra Enclave 4. Rajdeo Enclave Block – C 5. Patliputra City 6. Kaushal Kishor Heritage 7. Urmila Enclave 8. Sumitra Enclave

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP00043-6/187/R-1500/2022
Name of Project/Phase of Registered Project	KAUSHAL KISHOR HERITAGE
Name of Promoter	SK BUILDERS AND COLONISER PVT. LTD.
Project Address	PLOT NO.- 901, KHATA NO.- 31, THANA NO.- 36, THANA- DANAPUR, MAUZA- MUSTAFAPUR, DIST- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	31/12/2025
Starting date of Project or	15/10/2022

Phase of the Project	
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share- 12	Total Number of Apartments in Landowner's share- 12
KAUSHAL KISHOR HERITAGE	3 BHK	940.00	4	1. Booked/Allotted- 02 2. Sold-0 Percentage of booking- 16.6 %	3. Booked/Allotted- 0 4. Sold-0
KAUSHAL KISHOR HERITAGE	3 BHK	1085.00	4		
KAUSHAL KISHOR HERITAGE	3 BHK	1136.00	4		
KAUSHAL KISHOR HERITAGE	3 BHK	945.00	4		
KAUSHAL KISHOR HERITAGE	3 BHK	953.00	4		
KAUSHAL KISHOR HERITAGE	3 BHK	838.00	4		Percentage of booking-0

- Note:- Association of Allotted not be made because, booking percentage not exceeds 50% yet.**

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
KAUSHAL KISHOR HERITAGE	No Garages available	1. Booked/Allotted - 2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. Construction Progress of the Project**1. Plan Case No.- 94/22-23 (KAUSHAL KISHOR HERITAGE) (To beaded for each Building / Wing)**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	NA	
3.	Podiums (if any)	NA	
4.	Plinth	100%	Completed
5.	Stilt Floor	100%	Completed
6.	Slabs of Super Structure	100%	Completed
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	Completed
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	Completed
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%	Completed

10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	Completed
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	95%	20-10-2024

VII. Amenities and Common Area and External Infrastructure Development Works

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No	NA	
2.	Water Supply	Yes	100%	Completed
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	Completed
4.	Storm Water Drains	No	NA	
5.	Landscaping & Tree Planting	No	NA	
6.	Street Lighting	No	NA	
7.	Community Buildings	No	NA	
8.	Treatment and Disposal of Sewage and Sullage Water	No	NA	
9.	Solid Waste Management & Disposal	No	NA	
10.	Water Conservation / RainWater Harvesting	Yes	100%	Completed
11.	Energy Management	No	NA	

12.	Fire Protection and FireSafety Requirements	Yes	0%	10-02-2025
13.	Closed Parking	Yes	100%	Completed
14.	Open Parking	No	NA	
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	100%	Completed
16.	Others (Option to AddMore)	No	NA	

VIII. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

Not Applicable because our project is Residential/Group Housing.

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor

X. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	41330901844
2	Estimated Cost of the Project including land cost at the start of the Project	526.00/- (in Lakh)
3	Estimated Development Cost of the Project at the start of the Project (Excluding Land Cost)	506.00/- (in Lakh)
4	Any Variation in Development Cost which is declared at the start of the Project	No Any
5	Amount received during the Quarter	13,27,000.00/-
6	Actual Cost Incurred during the Quarter	12,32,000.00/-
7	Net amount at end of the Quarter in A/C 41330900567 (30%)	1,00,293.00
	Net amount at end of the Quarter in A/C 41330901389 (70%)	9,36,600.00/-
8	Total expenditure on Project till date	2,43,67,097.00/-

9	Cumulative fund collected till the end of Quarter in question	26,04,000.00/-
10	Cumulative expenditure done till the end of Quarter in question	2,43,67,097.00/-

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

No Any


XII. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	No Any
2.	Name of Parties	No Any
3.	No of Execution Cases against this project Case No. Name of Parties	No Any
4.	No of Suo - Moto cases against this project Case No. Name of Parties	No Any
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	No Any
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	0
2.	Agreement for Sale	0
3.	No. of possessions given to allottees	0

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

PROGRESS CHART

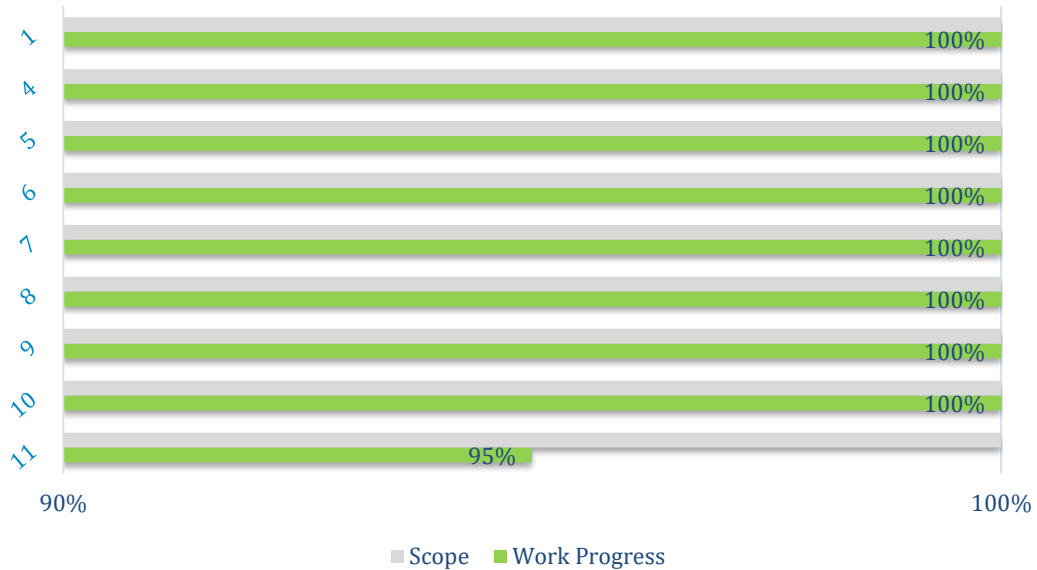

XIV UNITS ALLOCATION DETAILS

Apartment Type	Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc		Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
3 BHK	4	Allotte Name	Flat No.	No Any
3 BHK	4	Shikha Suman	202	
3 BHK	4	Sima Dubey	204	
3 BHK	4			
3 BHK	4			
3 BHK	4			

XV. Brochure Attached

XVI Grievance Redressal Officer


Name :- Gaurav Kumar

Contact No :- 7549121212

Email id :- skbuildersgaurav@gmail.com


Address :-5th floor SK Palace, Saguna More, Danapur, Patna, Bihar

Project Site Photographs

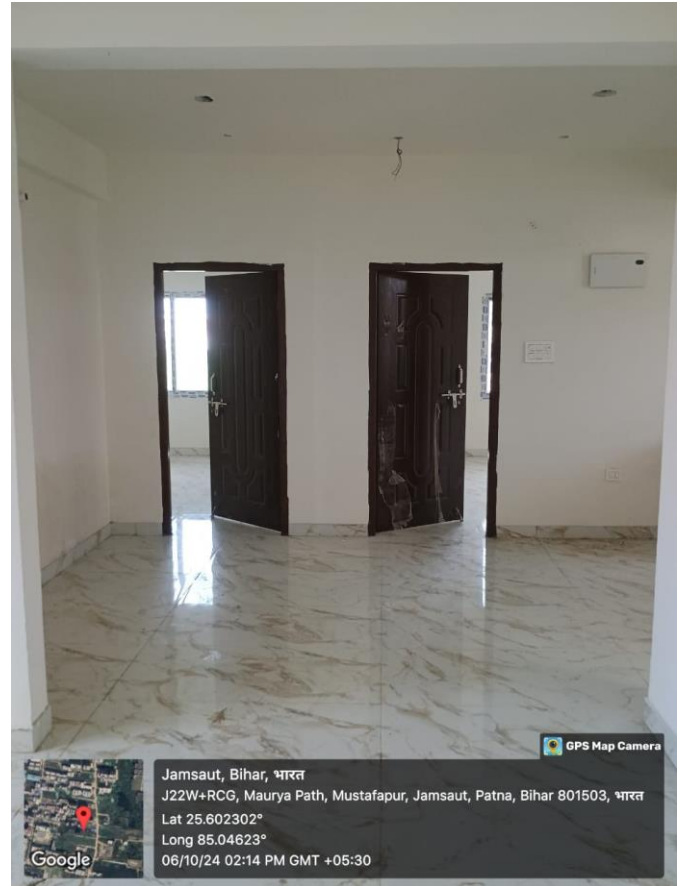



जम्सौत, बिहार, भारत
J23W+29P, मुस्तफापुर, जम्सौत, पटना, बिहार 801503, भारत
Lat 25.60294°
Long 85.046839°
06/10/24 02:15 PM GMT +05:30






GPS Map Camera

जम्सौत, बिहार, भारत
J23W+29P, मुस्तफापुर, जम्सौत, पटना, बिहार 801503, भारत
Lat 25.602418°
Long 85.04614°
06/10/24 02:13 PM GMT +05:30

Google

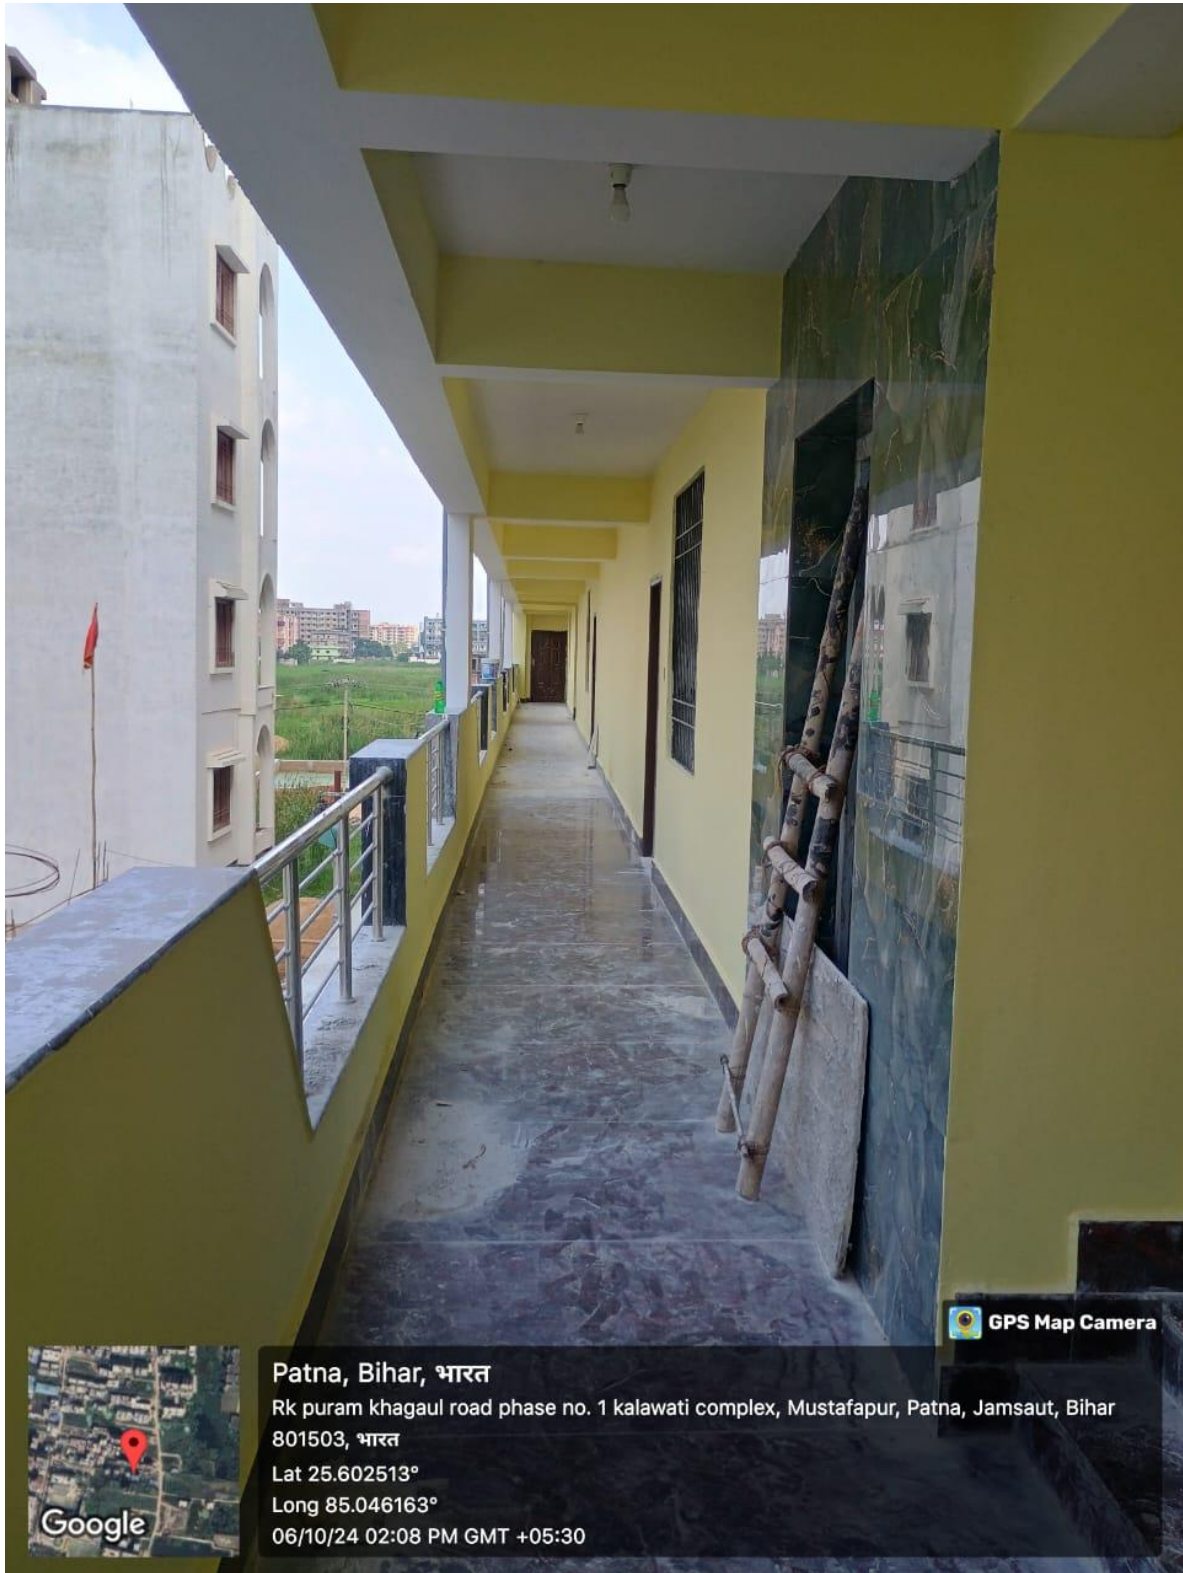

Patna, Bihar, भारत

Rk puram khagaul road phase no. 1 kalawati complex, Mustafapur, Patna, Jamsaut, Bihar
801503, भारत

Lat 25.602513°


Long 85.046163°


06/10/24 02:08 PM GMT +05:30

GPS Map Camera




Jamsaut, Bihar, भारत
J22W+RCG, Maurya Path, Mustafapur, Jamsaut, Patna, Bihar 801503, भारत
Lat 25.602386°
Long 85.046327°
06/10/24 02:14 PM GMT +05:30



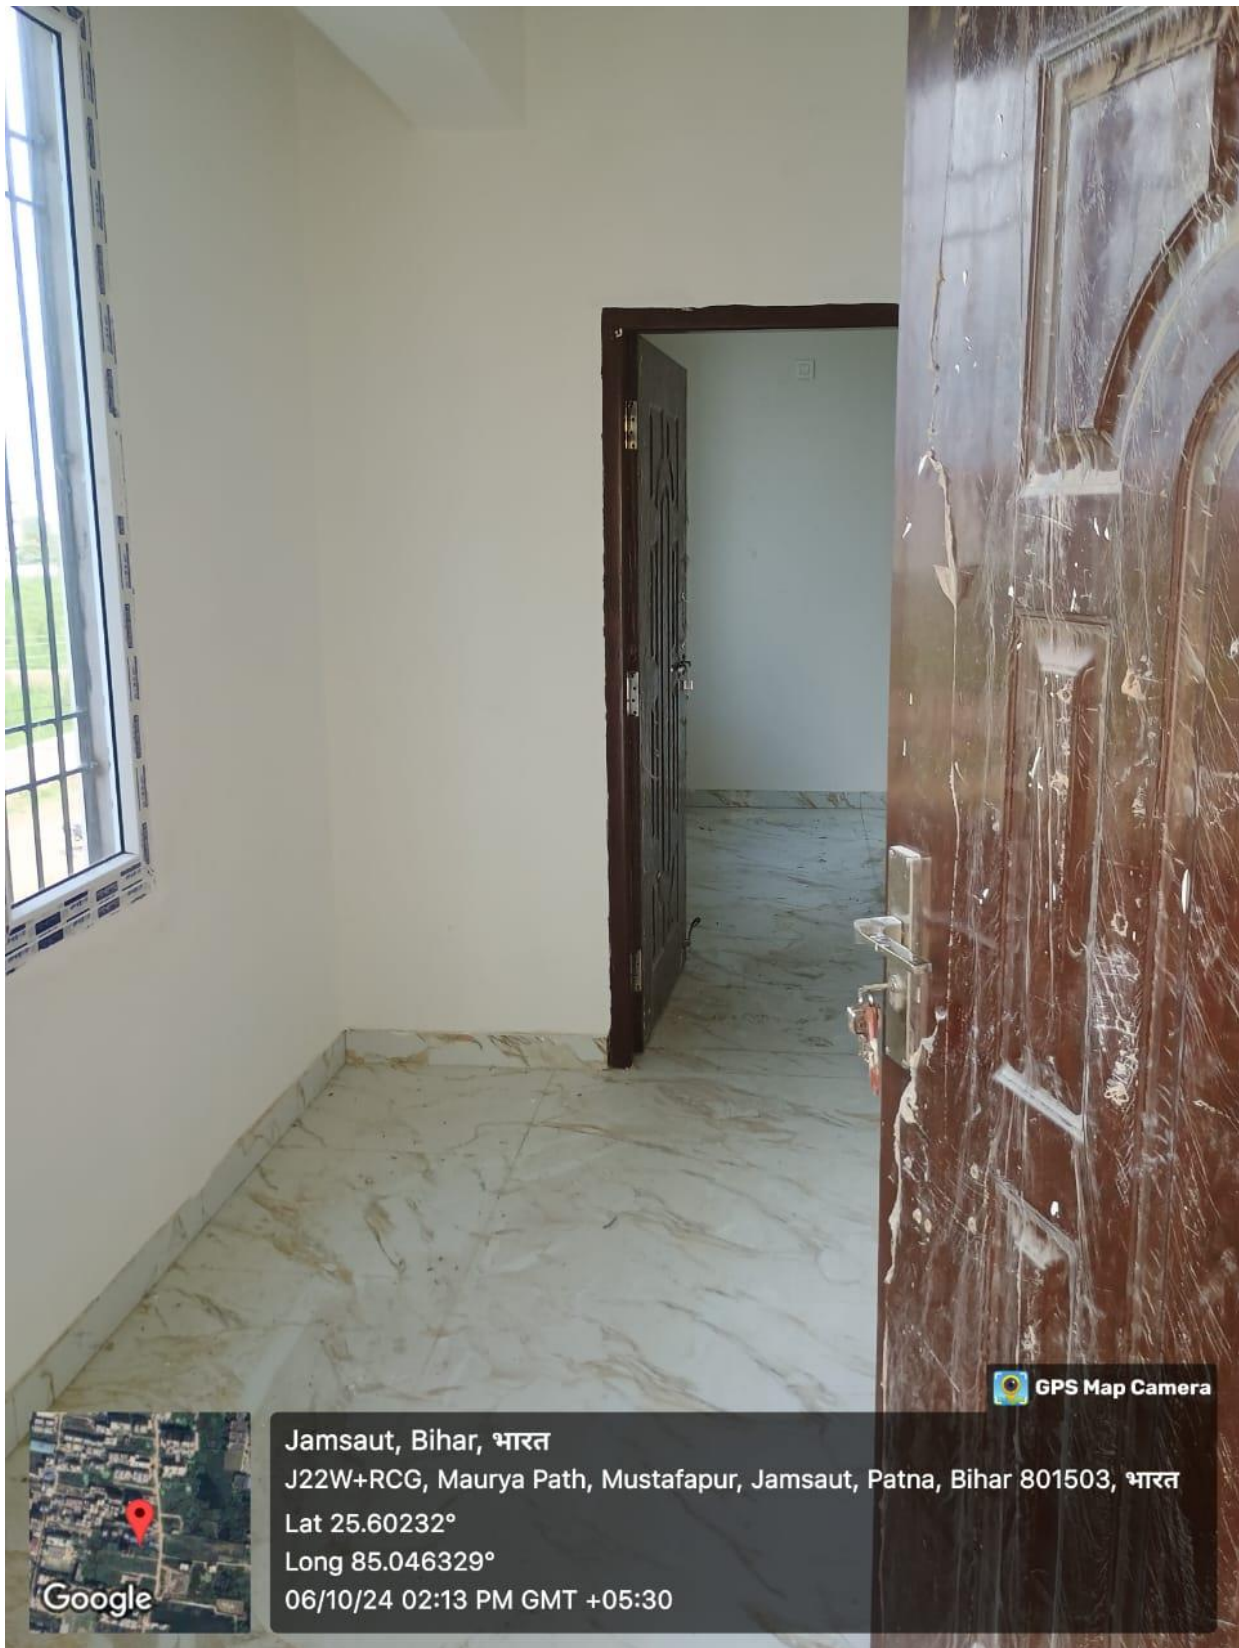

Jamsaut, Bihar, भारत
J22W+RCG, Maurya Path, Mustafapur, Jamsaut, Patna, Bihar 801503, भारत
Lat 25.60232°
Long 85.046329°
06/10/24 02:13 PM GMT +05:30

GPS Map Camera



Patna, Bihar, भारत

Rk puram khagaul road phase no. 1 kalawati complex, Mustafapur, Patna, Jamsaut, Bihar
801503, भारत

Lat 25.602481°

Long 85.046167°

06/10/24 02:08 PM GMT +05:30



GPS Map Camera



दानापुर, बिहार, भारत

J22W+PJX, मौर्या पथ, near RPS Engineering college, मुस्तफापुर, दानापुर, पटना, बिहार 801503, भारत

Lat 25.602154°

Long 85.046481°


06/10/24 02:06 PM GMT +05:30



GPS Map Camera



 GPS Map Camera




Jamsaut, Bihar, भारत

J22W+RCG, Maurya Path, Mustafapur, Jamsaut, Patna, Bihar 801503, भारत

Lat 25.602215°

Long 85.046336°

06/10/24 02:06 PM GMT +05:30

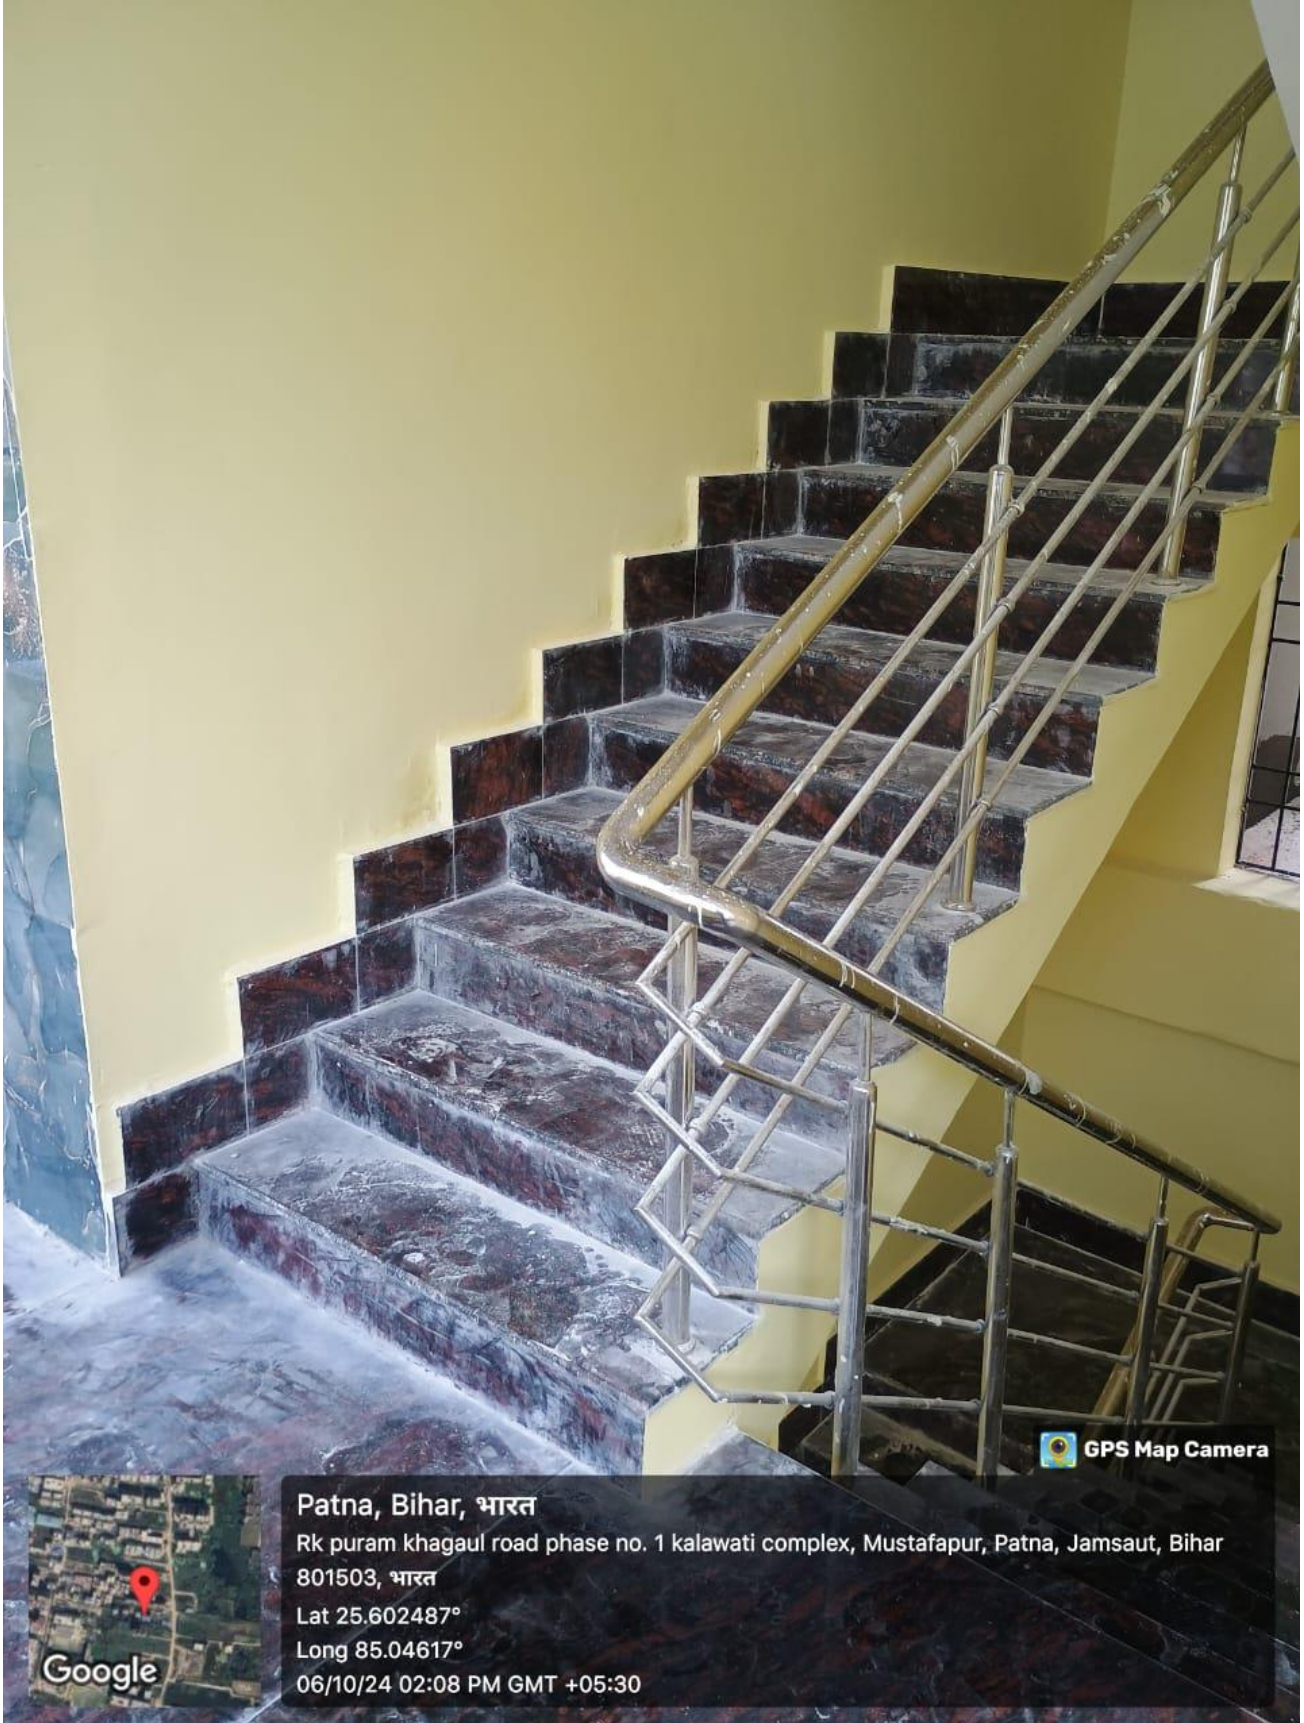

 GPS Map Camera

Patna, Bihar, भारत


Rk puram khagaul road phase no. 1 kalawati complex, Mustafapur, Patna, Jamsaut, Bihar
801503, भारत

Lat 25.602487°

Long 85.04617°

06/10/24 02:08 PM GMT +05:30

Google

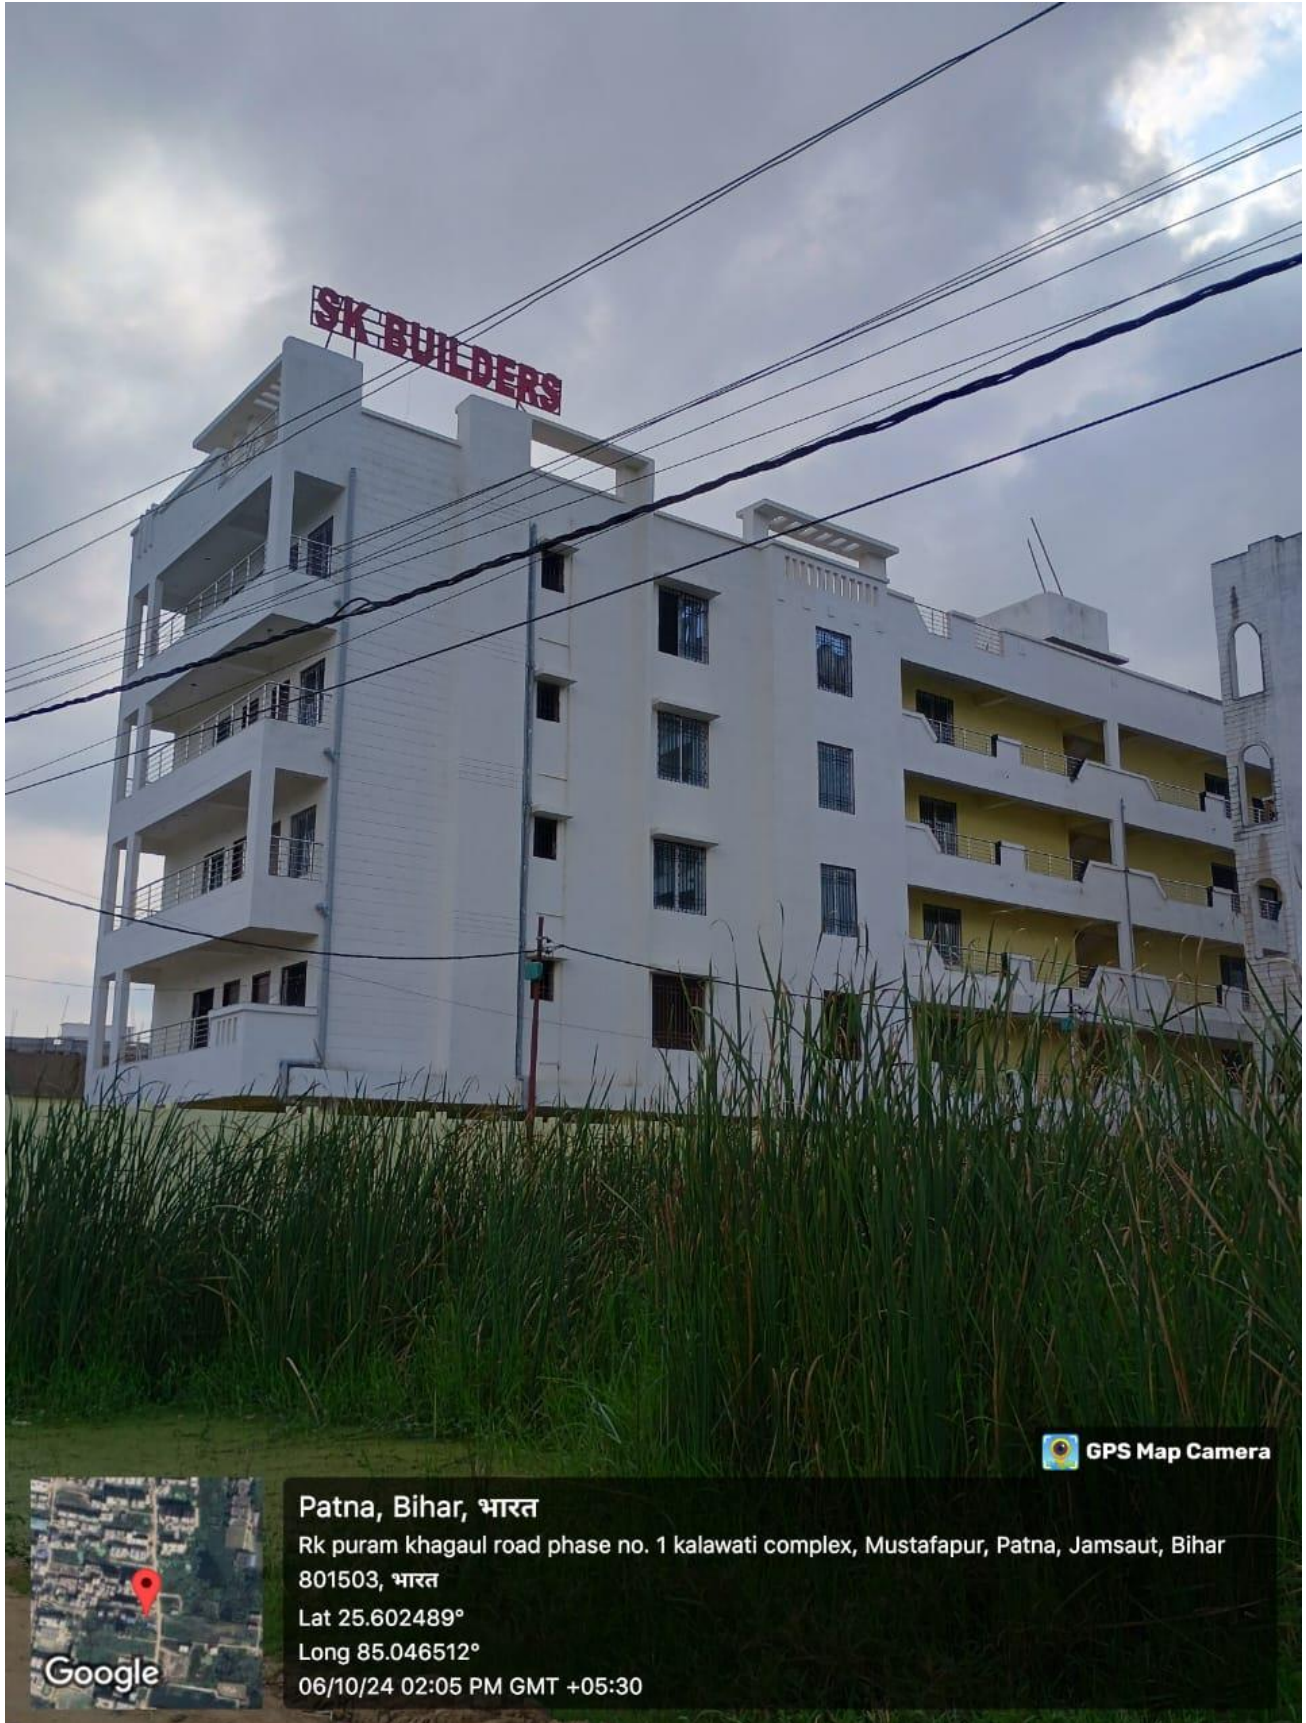

 GPS Map Camera



Patna, Bihar, भारत

Rk puram khagaul road phase no. 1 kalawati complex, Mustafapur, Patna, Jamsaut, Bihar
801503, भारत

Lat 25.602489°

Long 85.046512°

06/10/24 02:05 PM GMT +05:30



दानापुर, बिहार, भारत

J22W+PJX, मोर्या पथ, near RPS Engineering college, मुस्तफापुर, दानापुर, पटना, बिहार 801503, भारत

Lat 25.602211°

Long 85.046593°

06/10/24 02:05 PM GMT +05:30

Google

GPS Map Camera



दानापुर, बिहार, भारत

J22W+PJX, मोर्या पथ, near RPS Engineering college, मुस्तफापुर, दानापुर, पटना, बिहार 801503, भारत


Lat 25.602162°

Long 85.046597°

06/10/24 02:05 PM GMT +05:30

Google

GPS Map Camera



Google



GPS Map Camera

Jamsaut, Bihar, भारत

J22W+RCG, Maurya Path, Mustafapur, Jamsaut, Patna, Bihar 801503, भारत

Lat 25.602236°

Long 85.04643°

06/10/24 02:07 PM GMT +05:30

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

S.K. Builder's & Coloniser Pvt. Ltd.

Managing Director

Name: Pavan Kumar

Date :



MAJOR DISTANCES

AIMS (JALPAI) 130/15 KM	Radiant School 1.5 Km	DRM Office 03 KM	Danapur Jn. 3 KM	Saguna More 1 KM	Bifta Airport 10 KM	Patna Airport 8 KM	Patna Jn. 9 KM	Patliputra Jn. 6 KM
-------------------------	-----------------------	------------------	------------------	------------------	---------------------	--------------------	----------------	---------------------



Completed
ISHWAR CHANDRA



Completed
RAJDEV ENCLAVE A | B



Completed
RAJDEV ENCLAVE C



Completed
BHADRA RAJ ENCLAVE



On Going
PATLIPUTRA CITY



On Going
URMILA ENCLAVE

Our Projects



Project BY

Office Address :
SK BUILDER & COLONISOR PVT. LTD.
5th Floor, SK Palace, Saguna More, Khagaul Road,
Danapur, Patna - Bihar 801503

Site Address :
PGS. More, Behind RPS. Engineering
College, Danapur,
Patna - 801503

Call On ☎ : +91 7360064821 | 7360060502/501 / 524 | 8578002130 / 33

E-mail : skbuildersgaurav@gmail.com

Design & Interior : SKBACH (P) LTD. P: 801503 B: 801503

KAUSHAL KISHOR HERITAGE

At Danapur, Patna



Promising a Home Delivering a Dream

APPROVED BY RERA : BRERAP00043-6/187/R-1500/2022



Area Calculation

FLATE NO	01	02	03	04	05	06
TYPE	3BHK	3BHK	3BHK	3BHK	3BHK	3BHK
SUPER BUILDUP AREA	1951.00 SQFT.	1645.00 SQFT.	1655.00 SQFT.	1475.00 SQFT.	1636.00 SQFT.	1899.00 SQFT.
CARPATE AREA	1136.00 SQFT	945.00 SQFT	953.00 SQFT	838.00 SQFT	940.00 SQFT	1085.00 SQFT



Features and Amenities



Jogging Track



Fire safety



Intercom Facility



Multiple Lifts



Vastu Based



Temple



wifi



24X7 Water Supply



24X7 Power backup



Security



Earthquake Resistant

SPECIFICATION

STRUCTURE

- Foundation
- Reinforced Cement
- Concrete

SUPER STRUCTURE

- Reinforced Cement
- Concrete as per design
- Steel Standard quality

LIVING / DINING / LOBBY SPACE

- Floor
- Vitrified tiles / Equivalent

BEDROOM

- Floor
- Vitrified in all covered area

WALLS

- Plaster

INTERNAL WALLS

All internal walls shall be finished with white putty,

EXTERNAL WALLS

Weather coat paint over wall putty

TOILET

- Floor
- Vitrified tiles
- Ceramic tiles up to 7 feet height
- Fitting / Fixture
- W.C. European type, wash basin, fitting, chromium plated, acrylic fiber glass cistern in white colour

WATER

Deep borewell, 24 hrs. water supply

INTERCOM

- Intercom facility provided in each flat

WINDOW

- Wooden frame and shutter with 3mm clear glass window or UPVC/aluminium with glass/dormer section

MASTER BEDROOM

Floor

- Vitrified tiles

Doors

- Wooden Chalkhat

Internal Doors

- 32mm ISI marked with both side good quality paint

KITCHEN

Floor

- Vitrified tiles

PLATFORM

- Granite slab

GENERATOR

- Silent generator of adequate capacity

ELECTRICAL

Floor

- Concealed wiring and modular switches on demand of extra cost.
- Adequate lighting / Power point sockets outlet provided in each room

TV CABLE / TELEPHONE

- Provided at all suitable points

Our Banking Partner



KAUSHAL KISHOR HERITAGE Payment Plan

Note: Parking and other miscellaneous charges Rs. 4 lakhs/GST and other Gov. Taxes will be as applicable.

At the time of Booking	10 %
On the Commencement of 1st slab	15 %
On the Commencement of 2nd slab	15 %
On the Commencement of 3rd slab	15 %
On the Commencement of 4th slab	15 %
At time of brick work	15 %
On the start of finishing work	10 %
At time of possession	05 %

