

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45200BR2012PTC018267	Name of Firm	SILVER POINT COSTRUCTION PRIVATE LIMITED
Firm Address :	Pratap Palace Krishi Nagar, Behind IGIMS, A.G. Colony Patna-800023		
Total Experience of promoter in Real Estate sector	12 YEARS		
Total Experience in Real Estate after Implementation of RERA	08 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	N/A	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	02 (Including this project)	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00225- 2/1296/R- 1230/2021	Name of Project/Phase of Registered Project	SILVER TOWER
Name of Promoter	SILVER POINT COSTRUCTION PRIVATE LIMITED	Project Address	GHUR DAUR ROAD, NASRIGANJ, DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	16/10/2024		
Starting date of Project or Phase of the Project	26/10/2021		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	26/03/2023		

For SILVER POINT CONSTRUCTION PVT. LTD.
SILVER TOWER

Bahechi Singh
Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share -	Total Number of Apartments in Landowner's share -
ONE	1. 1 BHK	33	31779 Sq. Ft.	FLAT-33	FLAT-13	FLAT-20
	2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.				1. Booked / Allotted -10 2. Sold-NIL	3. Booked/ Allotted-NIL Sold -NIL
					Percentage of booking 76%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
ONE	33	1. Booked/Allotted	10
		2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.				
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER

Bachchi Singh
Director

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. 153/18-19

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 100% 95%	10-10-2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	75% 90%	10-10-2024 10-10-2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100% 100% 100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100% 100% 100% 100%	

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER*Bachchi Singh*
Director

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	80%	10-10-204
		100%	
		95%	10-10-204
		90%	10-10-204
		100%	
		80%	10/10/2024

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	80%	31/08/2024
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	
4.	Storm Water Drains	YES	100%	
5.	Landscaping & Tree Planting	YES	0%	10-10-2024
6.	Street Lighting	YES	20%	10-10-2024
7.	Community Buildings	NO	N/A	

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER

Bachchi Singh
Director

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	80%	10-10-2024
11.	Energy Management	YES	0%	10-10-2024
12.	Fire Protection and Fire Safety Requirements	YES	80%	10-10-2024
13.	Closed Parking	YES	100%	
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER

Bachchi Singh
Director

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	920020064831515
2.	Estimated Cost of the Project including land cost at the start of the Project	5,80,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	15,15,000=00
6.	Actual Cost Incurred during the Quarter	40,60,529=00
7.	Net amount at end of the Quarter	8,48,475=00
8.	Total expenditure on Project till date	4,10,72,356=00
9.	Cumulative fund collected till the end of Quarter in question	3,92,53,726=00
10.	Cumulative expenditure done till the end of Quarter in question	3,70,11,827=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER

Bachchi Singh
Director

XII. MISCELLANEOUS

A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK - 3 BHK-33 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc			Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
	S.NO	FLAT NO.	FLAT TYPE	
	01	A-4	3BHK	
	02	B-4	3BHK	
	03	C-4	3BHK	
	04	D-4	3BHK	
	05	E-4	3BHK	
	06	A-5	3BHK	
	07	B-5	3BHK	
	08	D-5	3BHK	
	09	E-6	3BHK	
	10	D-6	3BHK	
XV. BROCHURE /Prospectus				

For **SILVER POINT CONSTRUCTION PVT. LTD.**
SILVER TOWER

Bachchi Singh
Director

XVI Grievance Redressal Officer

Name : Bachchi Singh

Contact No : 9470484707

Email id : bachchisingh31@gmail.com

Address : Pratap Palace Krishi Nagar, Behind IGIMS Patna 800023

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter



Name:

Date:

**For OLIVE POINT CONSTRUCTION PVT. LTD.
SILVER TOWER**

Bachchi Singh
Director

Silver Tower

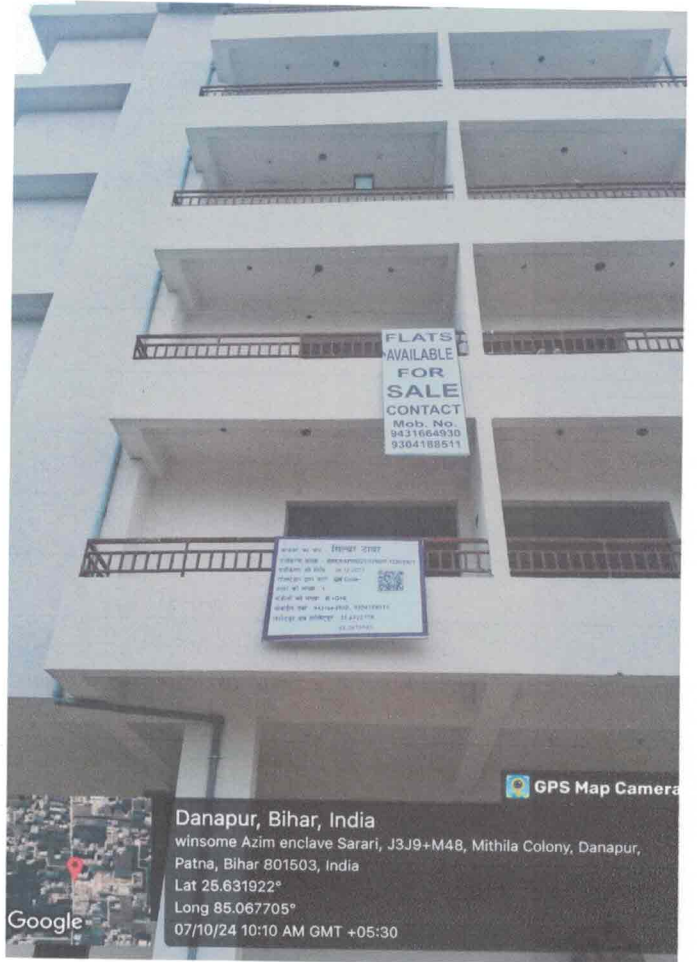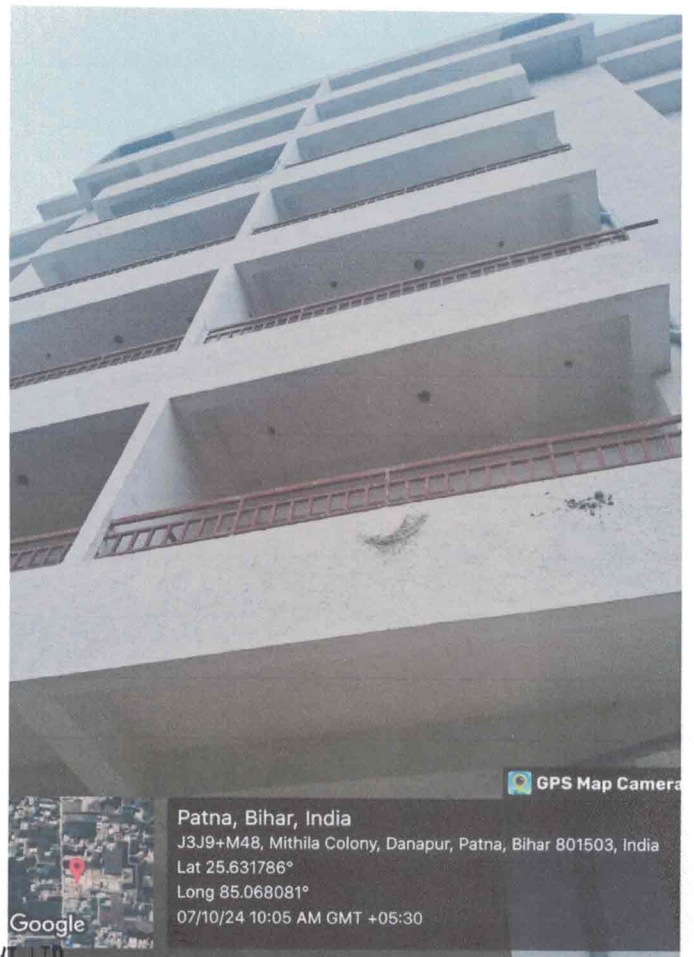

For SILVER POINT CONSTRUCTION PVT. LTD.
SILVER TOWER

Bachchi Singh
Director
