

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies		Name of Firm	PREMA REALTY & COMPANY
Firm Address :	GROUND FLOOR, BLOCK-B, ADITYA VIKASH COMPLEX, BUDH MARG, PATNA-800001		
Total Experience of promoter in Real Estate sector	5 YEARS		
Total Experience in Real Estate after Implementation of RERA	5 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	NIL	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	01	

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00543-003/187/R-1676/2024	Name of Project/Phase of Registered Project	SHREE CHETAN HARI COMPLEX
Name of Promoter	PREMA REALTY & COMPANY	Project Address	PLOT NO.-781, KHATA NO. -629, MAUZA-PAHARI, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	13-05-2027		
Starting date of Project or Phase of the Project	15-04-2024		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	5 YEARS		

PREMA REALTY AND COMPANY

8/25/24/2024

PROPRIETOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-16	Total Number of Apartments in Landowner's share - FLAT-16
	1. 1 BHK	32		32	1. Booked / Allotted -NIL	3. Booked/ Allotted-NIL
	2. 2 BHK, -				2. Sold-NIL	Sold -NIL
	3. 3 BHK					
	4. Shop					
	5. Bungalow					
	6. Plot etc.				Percentage of booking 0%	Percentage of booking 0%

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- NIL
	32	2. Sold	- NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	THE STATE FIRE OFFICER-CUM-DIRECTOR, PATNA	25-02-2021	27-11-2021	ANNEXURE-A
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.	PATNA MUNICIPAL CORPORATION	2021	18-10-2023	ANNEXURE-B

PREMA REALTY AND COMPANY
22/11/2023
PROPRIETOR

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/PAHARI/PRN-G+4/463/2024

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	70%	30-12-2024
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	0%	31-10-2025
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	28-04-2026 30-05-2026 30-10-2026 30-07-2026
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	30-09-2026 30-08-2026
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	31-12-2026 30-06-2026 31-08-2026
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	31-08-2026 31-08-2026 30-06-2026 30-11-2026

PREMA REALTY AND COMPANY
Near agn 24 m. 2)
PROPRIETOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	31-10-2026
		0%	30-06-2026
		0%	30-09-2026
		0%	31-10-2026
		0%	30-06-2026
		0%	30-03-2027
		0%	31-12-2026
	Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	28-02-2027
2.	Water Supply	YES	0%	30-06-2026
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	30-09-2026
4.	Storm Water Drains	YES	0%	31-10-2026
5.	Landscaping & Tree Planting	YES	0%	30-11-2026
6.	Street Lighting	YES	0%	28-02-2027
7.	Community Buildings	NO	N/A	

PREMA REALTY AND COMPANY

नरेश कुमार शर्मा

PROPRIETOR

8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	30-11-2026
10.	Water Conservation / Rain Water Harvesting	YES	0%	31-10-2026
11.	Energy Management	YES	0%	30-06-2026
12.	Fire Protection and Fire Safety Requirements	YES	0%	31-12-2026
13.	Closed Parking	YES	0%	30-04-2027
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)	NO		

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			

PREMA REALTY AND COMPANY

h 225 231121


PROPRIETOR

8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	



PREMA REALTY AND COMPANY
 नई रास्ता लिमिटेड
 PROPRIETOR

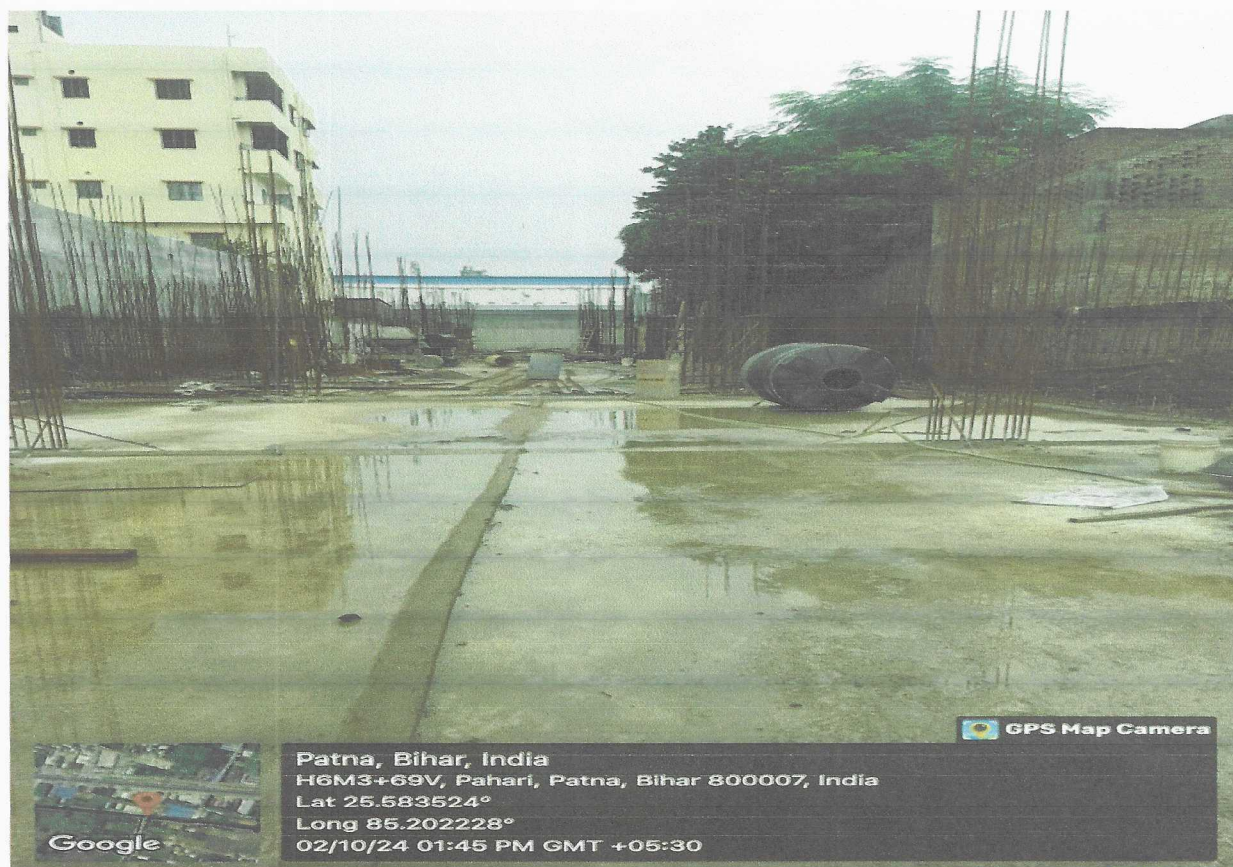

Patna, Bihar, India
H6M3+69V, Pahari, Patna, Bihar 800007, India
Lat 25.583524°
Long 85.202228°
02/10/24 01:45 PM GMT +05:30

GPS Map Camera

PREMA REALTY AND COMPANY
 नंदन अग्रवाल
 PROPRIETOR

X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	431705000963
2.	Estimated Cost of the Project including land cost at the start of the Project	10,37,10,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	8,17,10,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	00=00
6.	Actual Cost Incurred during the Quarter	00=00
7.	Net amount at end of the Quarter	00=00
8.	Total expenditure on Project till date	35,24,471=00
9.	Cumulative fund collected till the end of Quarter in question	00=00
10.	Cumulative expenditure done till the end of Quarter in question	35,24,471=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

PREMA REALTY AND COMPANY

 PROPRIETOR

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK - 3 BHK-32 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc

XV. BROCHURE /Prospectus
XVI Grievance Redressal Officer Name : Contact No : Email id : Address :

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

PREMA REALTY AND COMPANY

MAHESH KUMAR PANISARI
PROPRIETOR

Signature of Promoter

Name: MAHESH KUMAR PANISARI

Date: 14/10/2024
