

# QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Oct – Dec, 2020

## ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

## PROJECT NAME

**AMBITION CORPORATE PARK**

## PROMOTER NAME

**AMBITION HOMES PVT. LTD.**

## RERA REGISTRATION NO.

**BRERAP00138-5/770/R-542/2019**

## PROJECT QUARTERLY PROGRESS STATUS

Quarter: Oct – Dec, 2020

**Project Description:** *Ambition Corporate Park is a luxury commercial complex consisting of premium offices and shops. It consists of Basement Floor + Ground floor + 4 floors and is most conveniently located on Boring Canal Road, Patna, Bihar.*


### Progress Update of each Block/Wing separately

| S. No. | Task/Activity                                     | Applicable (Yes/No) | Percentage of Work Done | Remarks                                                                                                                                                                                   |
|--------|---------------------------------------------------|---------------------|-------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1      | Excavation                                        | Yes                 | 100%                    | Overall Excavation Work Complete.                                                                                                                                                         |
| 2      | Foundation Works                                  | Yes                 | 100%                    | Raft Foundation works complete and footing works also complete.                                                                                                                           |
| 3      | Basement                                          | Yes                 | 65%                     | Basement to ground floor ramp works under progress. Retaining wall construction complete, adjacent backfilling works yet to start. Waterproofing works complete. Plastering works started |
| 4      | Slabs of structure                                | Yes                 | 100%                    | Overall slab casting complete.                                                                                                                                                            |
| 5      | Walls                                             | Yes                 | 50%                     | Brickwork under progress in full swing in Ground floor, 1 <sup>st</sup> floor & 2 <sup>nd</sup> floor, and near about to complete on 3 <sup>rd</sup> floor, and 4 <sup>th</sup> floor.    |
| 6      | Internal Plaster & Putty                          | Yes                 | 20%                     | Internal Plastering works near about to complete on 3 <sup>rd</sup> floor & under progress in full swing on 4 <sup>th</sup> floor.                                                        |
| 7      | Flooring inside units and common areas            | Yes                 | 0%                      |                                                                                                                                                                                           |
| 8      | Doors and Window to each of unit and common areas | Yes                 | 8%                      | Door Frame Installed on 3 <sup>rd</sup> and 4 <sup>th</sup> floor.                                                                                                                        |

**Progress Update of each Block/Wing separately**

| S. No. | Task/Activity                                                                                                                                                                                                                                                                                                                  | Applicable (Yes/No) | Percentage of Work Done | Remarks                                                                                                                                                                            |
|--------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 9      | Sanitary fittings within the unit including water proofing and plumbing                                                                                                                                                                                                                                                        | Yes                 | 24%                     | SWR & CPVC Work completed on 3 <sup>rd</sup> and 4 <sup>th</sup> floor.                                                                                                            |
| 10     | Electrical fitting within the unit                                                                                                                                                                                                                                                                                             | Yes                 | 13%                     | Conduiting laying Jhiri, Pipe Laying, MS Box Laying complete on 3 <sup>rd</sup> and 4 <sup>th</sup> floors.                                                                        |
| 11     | Staircase, lift walls and lobbies at each floor                                                                                                                                                                                                                                                                                | Yes                 | 37%                     | Staircase structure upto terrace complete. Lift wall structure works complete except on ground floor. Lobby structure works complete on 3 <sup>rd</sup> and 4 <sup>th</sup> floor. |
| 12     | Water tank                                                                                                                                                                                                                                                                                                                     | Yes                 | 0%                      |                                                                                                                                                                                    |
| 13     | External Plumbing works and completion of terrace with waterproofing of the building if specified.                                                                                                                                                                                                                             | Yes                 | 25%                     | External plumbing works near about to complete.                                                                                                                                    |
| 14     | External Plaster                                                                                                                                                                                                                                                                                                               | Yes                 | 0%                      |                                                                                                                                                                                    |
| 15     | External Paint                                                                                                                                                                                                                                                                                                                 | Yes                 | 0%                      |                                                                                                                                                                                    |
| 16     | Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works) | Yes                 | 7%                      | One submersible pump has been installed. Septic tank work ongoing.                                                                                                                 |

## PROGRESS CHART

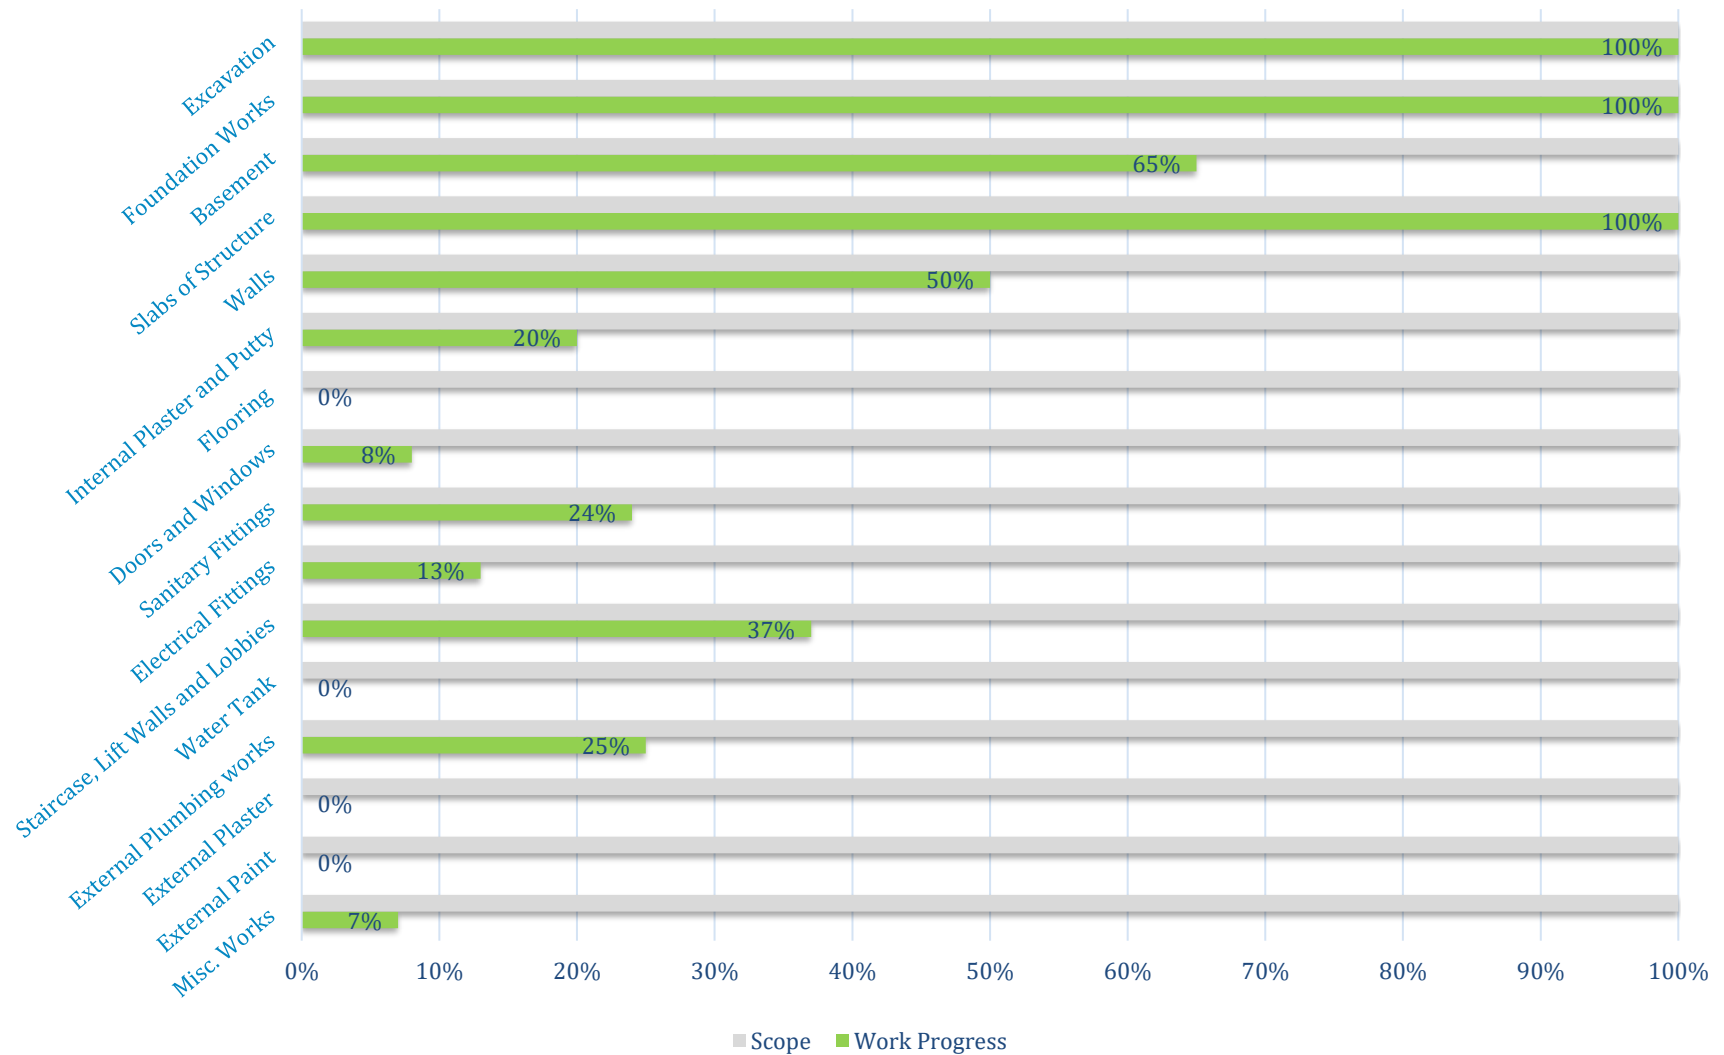

**Progress Update for Common Areas, Facilities and Amenities in the Project**

| S. No. | Description    | Applicable (Yes/No) | Percentage of Work Done | Remarks                                                                                                     |
|--------|----------------|---------------------|-------------------------|-------------------------------------------------------------------------------------------------------------|
| 1      | Compound Walls | Yes                 | 30%                     | Half height of Compound wall construction is complete.                                                      |
| 2      | Water supply   | Yes                 | 50%                     | Single Tube-well Boring works done and the second one is to be executed. Supply pipes installation balance. |

**Update on number and types of shops/offices booked during the quarter***(Builder's share + Land owner's share)*

| S. No | Unit Type    | Total No. of Units | No. of Shops/Offices Booked |                       |                          |                 | Total No. of Parking | No. of Garages/ Covered Parking Booked |                       |                          |                 |
|-------|--------------|--------------------|-----------------------------|-----------------------|--------------------------|-----------------|----------------------|----------------------------------------|-----------------------|--------------------------|-----------------|
|       |              |                    | Opening Balance             | Booked in the quarter | Cancelled in the quarter | Closing Balance |                      | Opening Balance                        | Booked in the quarter | Cancelled in the quarter | Closing Balance |
| 1     | Shop/offices | 27                 | 1                           | 6                     | 0                        | 7               | 83                   | 0                                      | 3                     | 0                        | 3               |

**Status of financials in the project up to 31<sup>st</sup> December, 2020**

| S.No. | Description                                                                   | Amount (in lacs Rs.) |
|-------|-------------------------------------------------------------------------------|----------------------|
| 1     | Amounts received from allottees against booking of units(for builder's share) | 84.63/-              |
| 2     | Expenditure done towards completion of project                                | 432.38/-             |
| 3     | Balance in Designated Bank A/c as on this quarter end                         | 14.61/-              |

**Status of Approvals****A. Approval Received**

| S. No. | Description                  | Date of Receipt |
|--------|------------------------------|-----------------|
| 1      | Provisional Fire Clearance   | 30.11.17        |
| 2      | Airport NOC                  | 23.11.17        |
| 3      | Sanctioning of Building Plan | 08.12.18        |
| 4      | RERA Registration            | 29.03.19        |

**B. Approval Applied**

| S. No. | Description | Expected Date |
|--------|-------------|---------------|
| NA     | NA          | NA            |

**C. Approvals to be applied**

| S. No. | Description | Expected Date of application |
|--------|-------------|------------------------------|
| NA     | NA          | NA                           |

**D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA**

## Project Site Photographs

