

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45201BR1996PTC007421	Name of Firm	ABHINAV AWAS PRIVATE LIMITED
Firm Address :	Abhinav Vihar Colony, Gola Road, P.O. -Danapur Cant, P.S. - Danapur, District-Patna-801503, Bihar, India		
Total Experience of promoter in Real Estate sector	10 YEARS		
Total Experience in Real Estate after Implementation of RERA	07 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00143-3/107/R-1300/2022	Name of Project/Phase of Registered Project	BADRINATH TOWER,BLOCK-D
Name of Promoter	ABHINAV AWAS PRIVATE LIMITED	Project Address	NEAR ST. KAREN'S SCHOOL, GOLA ROAD, DANAPUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/10/2025		
Starting date of Project or Phase of the Project	14/03/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	15/10/2025		

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT. LTD.

Pravin Kumar

MANAGING DIRECTOR

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - Flat-22	Total Number of Apartments in Landowner's share - Flat-15
	1. 1 BHK				1. Booked / Allotted -18	3. Booked/ Allotted-NIL
	2. 2 BHK, -	20	12405			
	3. 3 BHK	17	16640	37	2. Sold-NIL	Sold -NIL
	4. Shop					
	5. Bungalow				Percentage of booking 81.81%	Percentage of booking 0%
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	18
	37	2. Sold	0

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIG HG & FS CUM STATE FIRE OFFICER, BIHAR, PATNA		29-01-2021	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT LTD.

Pramin Kumar
MANAGING DIRECTOR

VI. CONSTRUCTION PROGRESS OF THE PROJECT**1. Plan Case No. 14/21-22**

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	100%	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100% 100% 40% 90%	30-11-2024 30-11-2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	80% 80%	31-12-2024 31-12-2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 80% 75%	30-11-2024 30-11-2024 31-12-2024
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	25% 100% 75% 75%	31-10-2024 31-12-2024 31-12-2024

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT. LTD.

Pramin Kumar
MANAGING DIRECTOR

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	31-01-2025
		25%	31-12-2024
		40%	31-12-2024
		80%	31-12-2024
		25%	31-01-2025
		20%	31-01-2025
		0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	60%	28-02-2025
2.	Water Supply	YES	25%	31-12-2024
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	25%	31-12-2024
4.	Storm Water Drains	YES	0%	28-02-2025
5.	Landscaping & Tree Planting	YES	0%	31-03-2025
6.	Street Lighting	YES	0%	31-03-2025
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	YES	25%	28-02-2025
9.	Solid Waste Management & Disposal	YES	0%	28-02-2025

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS, PVT. LTD.

Pramod Kumar

MANAGING DIRECTOR

10.	Water Conservation / Rain Water Harvesting	YES	25%	28-02-2025
11.	Energy Management	YES	0%	28-02-2025
12.	Fire Protection and Fire Safety Requirements	YES	40%	31-12-2024
13.	Closed Parking	YES	80%	28-02-2025
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	25%	31-01-2025
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			


BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT. LTD.

Premjit Kumar
MANAGING DIRECTOR

9.	Energy Management			
----	-------------------	--	--	--

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	Attach

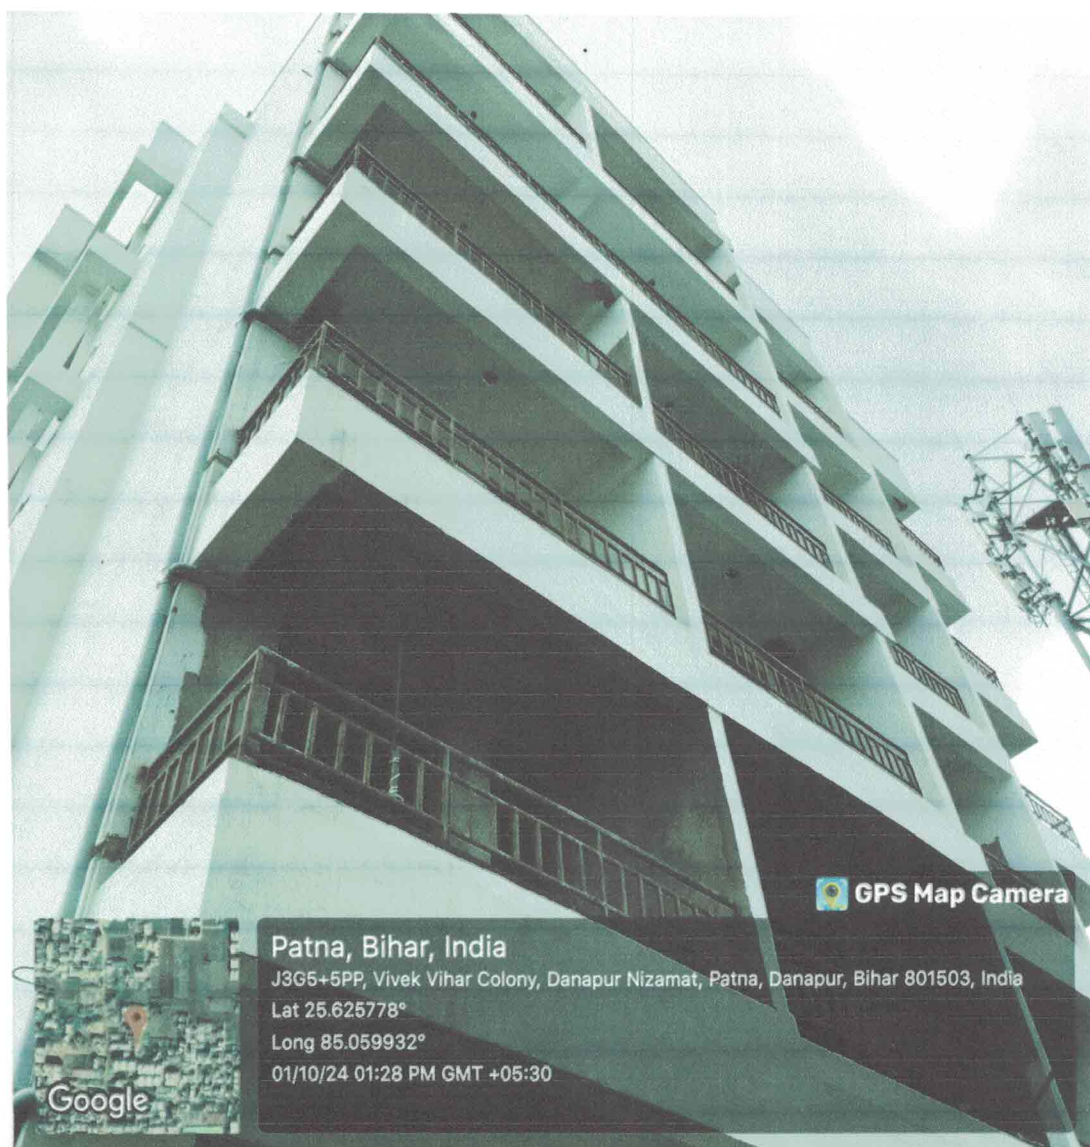

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT LTD.

Pravin Kumar
MANAGING DIRECTOR



BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT LTD.

Pravin Kumar
MANAGING DIRECTOR



X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	40293636054
2.	Estimated Cost of the Project including land cost at the start of the Project	7,57,00,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	5,00,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project .	NO
5.	Amount received during the Quarter	47,76,122=00
6.	Actual Cost Incurred during the Quarter	49,06,978=44
7.	Net amount at end of the Quarter	28,536=28
8.	Total expenditure on Project till date	
9.	Cumulative fund collected till the end of Quarter in question	
10.	Cumulative expenditure done till the end of Quarter in question	

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

BADRI NATH TOWER BLOCK-(D)
 ABHINAV AWAS PVT. LTD.

Pramil Kumar

MANAGING DIRECTOR

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	01
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
1 BHK -	D-301 — 3BHK	N/A
2 BHK, - 20	D-302 — 3BHK	
3 BHK 17	D-304 — 2BHK	
4 BHK -	D-305 — 3BHK	
Shop-	D-306 — 2BHK	
Bungalow -	D-307 — 2BHK	
Plot etc	D-401 — 3BHK	
	D-402 — 3BHK	
	D-403 — 2BHK	
	D-404 — 2BHK	

XV. BROCHURE /Prospectus

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT. LTD.

Pravin Kumar
MANAGING DIRECTOR

XVI Grievance Redressal Officer**Name :** PRAVIN KUMAR**Contact No :** 9334089068**Email id :** Pravinkumar14166@gmail.com**Address :** HOUSE OF BN DAS, ESI COLONY, AMBEDKAR PATH, BAILEY RD PATNA**Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

BADRI NATH TOWER BLOCK-(D)
ABHINAV AWAS PVT LTD.



Signature of Promoter

Name:

Date:
