



Apna Awas Construction Pvt. Ltd.

Registered Office : 001, Sundaram Enclave, Kitab Bhawan Lane
North S.K. Puri, Patna - 800 013

Ref..AAC/1007.....

Date...15/07/2024.....

To,
The Chairman
Real Estate Regulatory Authority,
Bihar, Patna.

SUB: Submission of Quarterly Progress Report of First Quarter (2024 – 2025) of "SUHASHINI NIKETAN", Mahodaypuri, Gardanibagh, Patna.

RERA Registration No – **BRERAP00243-16/1207/R-1026/2020.**

Dear Sir,

With reference to the above-mentioned subject and as per the requirement of quarterly reports compliance, we are hereby submitting the **QUARTERLY PROGRESS REPORT** for the FIRST QUARTER (2024 – 2025) for the project named "**SUHASHINI NIKETAN**" located at Mahodaypuri, Gardanibagh, Patna.

A detailed quarterly progress report of the project is attached along with this letter as Annexure - A.

Kindly acknowledge the receipt of the same.

Thanking you.

Sincerely yours
APNA AWAS CONSTRUCTION PVT. LTD



DIRECTOR


FOR APNA AWAS CONSTRUCTION PVT. LTD.

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending March/June/sept/December of 2024
- 25 -

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	U45200BR2001PTC009553	Name of Firm	APNA AWAS CONSTRUCTION PVT LTD
Firm Address :	001, SUNDARAM ENCLAVE, KITAB BHAWAN LANE, NORTH S.K. PURI, PATNA - 800013		
Total Experience of promoter in Real Estate sector	23 YEARS		
Total Experience in Real Estate after Implementation of RERA	07 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	26 00 03 00	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	08 00 00 00	


II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00243-16/1207/R-1026/2020	Name of Project/Phase of Registered Project	SUHASHINI NIKETAN
Name of Promoter	APNA AWAS CONSTRUCTION PVT LTD	Project Address	Mahodayapuri, Gardanibagh, Patna
Name of Co-promoter	-		
Project Registration is valid up to	31/10/2025		
Starting date of Project or Phase of the Project	01/02/2020		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential- cum-Commercial 4. Plotted project	RESIDENTIAL	
Period of validity of map by the Competent Authority	Map sanctioned on 31/12/2019		



II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS						
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share	Total Number of Apartments in Landowner's share
SUHASHINI NIKETAN	1. 2 BHK	02	850.19 & 831.45 Sq.ft.	15	- 08	share - 07
	2. 3 BHK	13	959.92, 1003.41, 926.64, 924.76, 1034.55 Sq.ft.		1. Booked/ Allotted - 08	3. Booked/ Allotted - 02
					2. Sold - 00	4. Sold -
					Percentage of Booking - 100 %	Percentage of Booking - 28.57%

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 08
SUHASHINI NIKETAN	15 (TOTAL), DEVELOPER - 08	2. Sold	- 00

V. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	NA			
2.	Fire N.O.C.	State Fire Officer, Bihar		28/04/2018	
3.	Water Supply Permission	Own Boring			
4.	NOC from Airport Authority of India	NA			
5.	Other Approval(s), if any, required for the Project.	NA			.



VI. CONSTRUCTION PROGRESS OF THE PROJECT1. Plan Case No. **P/DHAKANPURA-PRN-B+G+3/299/2018**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	100%	
3.	Podiums (if any)	NA	
4.	Plinth	100%	
5.	Stilt Floor	95%	31/12/2024
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	95%	31/12/2024
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	85%	31/12/2024
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	80%	31/12/2024
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	80%	31/12/2024
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	35%	31/03/2025



	requirements as me be required to complete project as per Specifications in Agreement of Sale.		
	Any other activities.		

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actualWork Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Own Boring	Boring done	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	75%	31/12/2024
4.	Storm Water Drains	Yes	25%	31/12/2024
5.	Landscaping & Tree Planting	Yes	0%	31/03/2025
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	Yes	0%	31/03/2025
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / Rain Water Harvesting	Yes	25%	31/03/2025
11.	Energy Management	No		
12.	Fire Protection and Fire Safety Requirements	Yes	25%	31/03/2025
13.	Closed Parking	Covered Car Parking		




14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	0%	31/03/2025
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	At the end attached
	2.	Rear Elevation	At the end attached




	3.	Side Elevation	At the end attached
(B)		Photograph of each floor	At the end attached

VIII. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2968002100011035
2.	Estimated Cost of the Project including land cost at the start of the Project	Rs. 6,91,57,500/-
3.	Estimated Development Cost of the Project at the start of the Project. (Excluding Land Cost)	Rs. 4,36,57,500/-
4.	Any Variation in Development Cost which is declared at the start of the Project.	-
5.	Amount received during the Quarter	NIL
6.	Actual Cost Incurred during the Quarter	Rs. 11,25,713/-
7.	Net amount at end of the Quarter	Rs. 11,842/-
8.	Total expenditure on Project till date	Rs. 4,61,52,214/-
9.	Cumulative fund collected till the end of Quarter in question	Rs. 5,28,12,616/-
10.	Cumulative expenditure done till the end of Quarter in question	Rs. 4,61,52,214/-

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED




X. MISCELLANEOUS		
A	List of Legal Cases (if any)	NONE
1.	Case No.	
2.	Name of Parties	
3.	No of Execution Cases against this project Case No. Name of Parties	
4.	No of Suo - Moto cases against this project Case No. Name of Parties	
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

APNA AWAS CONSTRUCTION PVT. LTD

DIRECTOR

Signature of Promoter

Name: **Prabhat Kumar Singh**

Date: 15/07/2024



Ar. Navratna Raghuvanshi

601, Signature Tower,
Kurjipul, Kurji,
Patna- 800010.

Mob :- 8863094547
LIC. NO : CA/2013/58586

Letter no. : 206/24-25

Date :- 15/07/2024


TO WHOMSOEVER IT MAY CONCERN

Sub : Construction work progress report in **Quarter April – June, 2024-25** of the **Project – SUHASHINI NIKETAN, Gardanibagh, Patna** (Mauza – Dhakanpura, Survey Plot No – 1846, 1847 & 1765, Khata No – 130 & 149, Tauzi No – 390, Thana No – 7, Mohalla – Mahodaypuri, Gardanibagh). On the request of Client, visited the Site, **SUHASHINI NIKETAN** on **05/07/2024**. It's a Residential Project located at (Mauza – Dhakanpura, Survey Plot No – 1846, 1847 & 1765, Khata No – 130 & 149, Tauzi No – 390, Thana No – 7, Mohalla – Mahodaypuri, Gardanibagh).

RERA Registration No – BRERAP00243-16/1207/R-026/2020.
Developer – Apna Awas Construction Pvt Ltd.

Current Construction Status on Site :

Brick work completed.
Internal plaster completed.
Outside plaster completed.
Plumbing and electrical work in progress.
P.O.P & Putty work completed.
Flooring work completed.
Construction of Overhead Water Tank and Fire Tank are completed.
Terrace Treatment alongside treatment of Basement completed.
Septic Tank completed.
Construction of Boundary wall in progress.
Laying of texture on outer wall in progress.


AR.NAVRATNA RAGHUVANSHI
(CA/2013/58586)

AR.NAVRATNA RAGHUVANSHI
UDHD EMP NO -AR/00818
COA.-CA/2013/58586

N. R. Baid & Co.

Chartered Accountants

1E, 1st Floor, Block B, Ashiana Orchids,
Beni Babu's Garden, Rajendra Path,
Near Sarvodaya Hotel, Patna - 800 001

Tel : 0612-2320716, Mob: 09334257406



email: info@nrbaid.com

CERTIFICATE NO.: CERT/NRBC/HO/2024-25/021

Date: 05/07/2024

CHARTERED ACCOUNTANTS FUND UTILIZATION CERTIFICATE

To

THE REAL ESTATE REGULATORY AUTHORITY

6th Floor, BSBCCL Campus,
Hospital Road, Shastri Nagar
Patna-800023

Subject: Statutory Auditors Certificate for Quarter-1 of Financial Year 2024-25

Reference: RERA Regn. No. BRERAP00243-16/1207/R-1026/2020

Project- SUHASHINI NIKETAN

Sir,

We have been requested by M/s Apna Awas Construction Private Limited, CIN U45200BR2001PTC009553, PAN: AAECA0832B to issue Statutory Auditors Certificate in accordance with Direction no. 1 of 2019 of the Authority.

In relation to the above, we confirm the following information:

Name of the Account Holder: Apna Awas Construction Private Limited

Designated Account Number: 2968002100011035

Bank Name: Punjab National Bank

IFSC Code: PUNB0296800

Branch Name: Punaichak



N. R. Baid & Co.

Chartered Accountants

1E, 1st Floor, Block B, Ashiana Orchids,
Beni Babu's Garden, Rajendra Path,
Near Sarvodaya Hotel, Patna - 800 001

Tel : 0612-2320716, Mob: 09334257406



email: info@nrbaid.com

	Particulars	INR in Rs.
1	Opening Balance in the Designated Account as on 01/04/2024	52,900
2	Total Amount deposited in designated account during this Quarter (Net Fund Received from Customers as Booking Advance Rs. Nil including GST, deposited in Designated account Rs. Nil, amount deposited in other account of the Company Rs. Nil and Rs. Nil relating to other projects deposited in this account.)	Nil
3	Total Amount paid during the 1 st Quarter up to 30/06/2024 from the said account (Total Amount utilised for the Project during the quarter is Rs. 11,25,713 rest utilised for Business Administrative Expenses and Others)	41,058
4	Closing Balance as on 30/06/2024 in this bank account	11,842

We certify that out of the funds deposited in this bank account Rs. Nil and a sum of Rs. 41,058 has been paid from this account details of which are as under: -

Project Expenses	32,850
Administrative Expenses (including Taxes if any)	4,208
Other Payments	4,000
Total Payments	41,058

In this context it may be noted that the overall project expenditure in this quarter is Rs. 11,25,713. The excess amount (if any) booked under this project is on account of expenditure incurred but which has not been paid from this designated account. The excess amount (if any) paid from Bank towards Project Expenses includes payment to suppliers of goods or services of this project which were less paid during earlier period. At the end of this quarter, a sum of Rs. 11,842 remains closing balance in the said designated account. Expenditures incurred for the purpose for which the funds were received is verified with the vouchers produced before us at the time of issue of this certificate and that we have exercised the checks to see that the money was actually utilized for the purpose for which it was received.

Yours faithfully,

For N. R. Baid & Co.

Firm Registration No. 002104C

Chartered Accountants



(CA. A. Baid)

Partner

M. No. 408360

UDIN: 24408360BKEGWM8682

Note: All the figures in this certificate pertain to quarter-1 of FY 2024-25 only and are as per the designated Bank Account or Books of the Company.

FRONT SIDE


SUHASHINI NIKETAN



LEFT SIDE



 GPS Map Camera

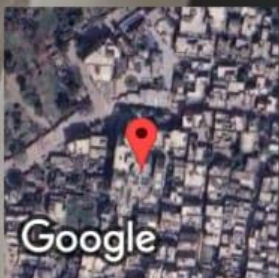

Patna, Bihar, India

H4Q8+WQP, Sadhnapuri, Patna, Bihar 800001, India

Lat 25.589683°

Long 85.116706°

07/07/24 04:40 PM GMT +05:30

RIGHT SIDE



 GPS Map Camera



Patna, Bihar, India
H4Q8+WQP, Sadhnepuri, Patna, Bihar 800001, India
Lat 25.589984°
Long 85.116956°
07/07/24 04:38 PM GMT +05:30

SUHASHINI



 GPS Map Camera



Patna, Bihar, India
H4Q8+WQP, Sadhnepuri, Patna, Bihar 800001, India
Lat 25.589923°
Long 85.116986°
07/07/24 04:37 PM GMT +05:30

STAIR



GR. FL.



BASEMENT



GR. FL. FLAT





GR. BATHROOM



GR.- KITCHEN





1ST FL FLAT



1ST FLOOR BATHROOM



1ST BALCONY



1ST KITCHEN



1ST STAIR





2ND FL STAIR



2ND KITCHEN



2ND BATHROOM



2ND STAIR





3RD FL BATHROOM



3RD BALCONY





3RD STAIR



TARACE



WATER TANK

