

QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Apr - Jun, 2019

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

RAM PADARATH ENCLAVE

PROMOTER NAME

SHRI BALAJEE NEST BUILDER PVT.LTD.

RERA REGISTRATION NO.

BRERAP00075-1/189/R-310/2018



PROJECT QUARTERLY PROGRESS STATUS

Quarter: Apr-Jun, 2019

Project Description: A B+G+4 Floor residential project consisting of 34 flats.


Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall excavation works complete.
2	Foundation Works	Yes	100%	Overall foundation works complete.
3	Basement	Yes	80%	Ramp works in basement is yet to start. Lift wall structure complete. Finishing works have started, plaster complete and primer works ongoing. Flooring works 85% complete.
4	Slabs of structure	Yes	100%	All slab casting complete including parapet walls on the terrace and mumty slabs.
5	Walls	Yes	100%	Overall brickwork completed in the project.
6	Internal Plaster& Putty	Yes	77%	Plastering works complete in the all the units of all the floors. Putty works single coat complete in all units of all the floors and second coat under progress.
7	Flooring inside units and common areas	Yes	83%	Flooring in units on different floors in under progress. Flooring in common areas is complete on floors 1-4. Flooring works on ground floor is in progress.
8	Doors and Window to each of unit and common areas	Yes	65%	Door frames in all units complete on all floors. Door fixing complete on 2 nd floor and on all other floor's door fixing is yet to be completed. Window frames

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
				installation complete on 3rd floor and on all other floors window installation is progress.
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	90%	SWR, CPVC, Waterproofing, Koba- 100% complete in all flats. Sanitary fittings 50% complete on all floors.
10	Electrical fitting within the unit	Yes	67%	Electrical conduiting and wire laying complete on all floors. Switch board installation pending.
11	Staircase, lift walls and lobbies at each floor	Yes	76%	Staircase structure complete overall. Staircase finishing only 30% complete- Plastering works complete. Lift wall structure and finishing almost complete. Lift lobby structure complete and lift lobby finishing under progress.
12	Water tank	Yes	40%	Over-head water tank 80% complete. Plastering-internal and external complete.
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	100%	External plumbing works complete.
14	External Plaster	Yes	100%	External plastering on all 4 elevations- Complete
15	External Putty &Paint	Yes	31%	External putty works ongoing.
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	12%	Installation of fire-fighting pipes under progress. Installation of lift rails and lift machine under progress. Sewage septic tank construction complete.

PROGRESS CHART

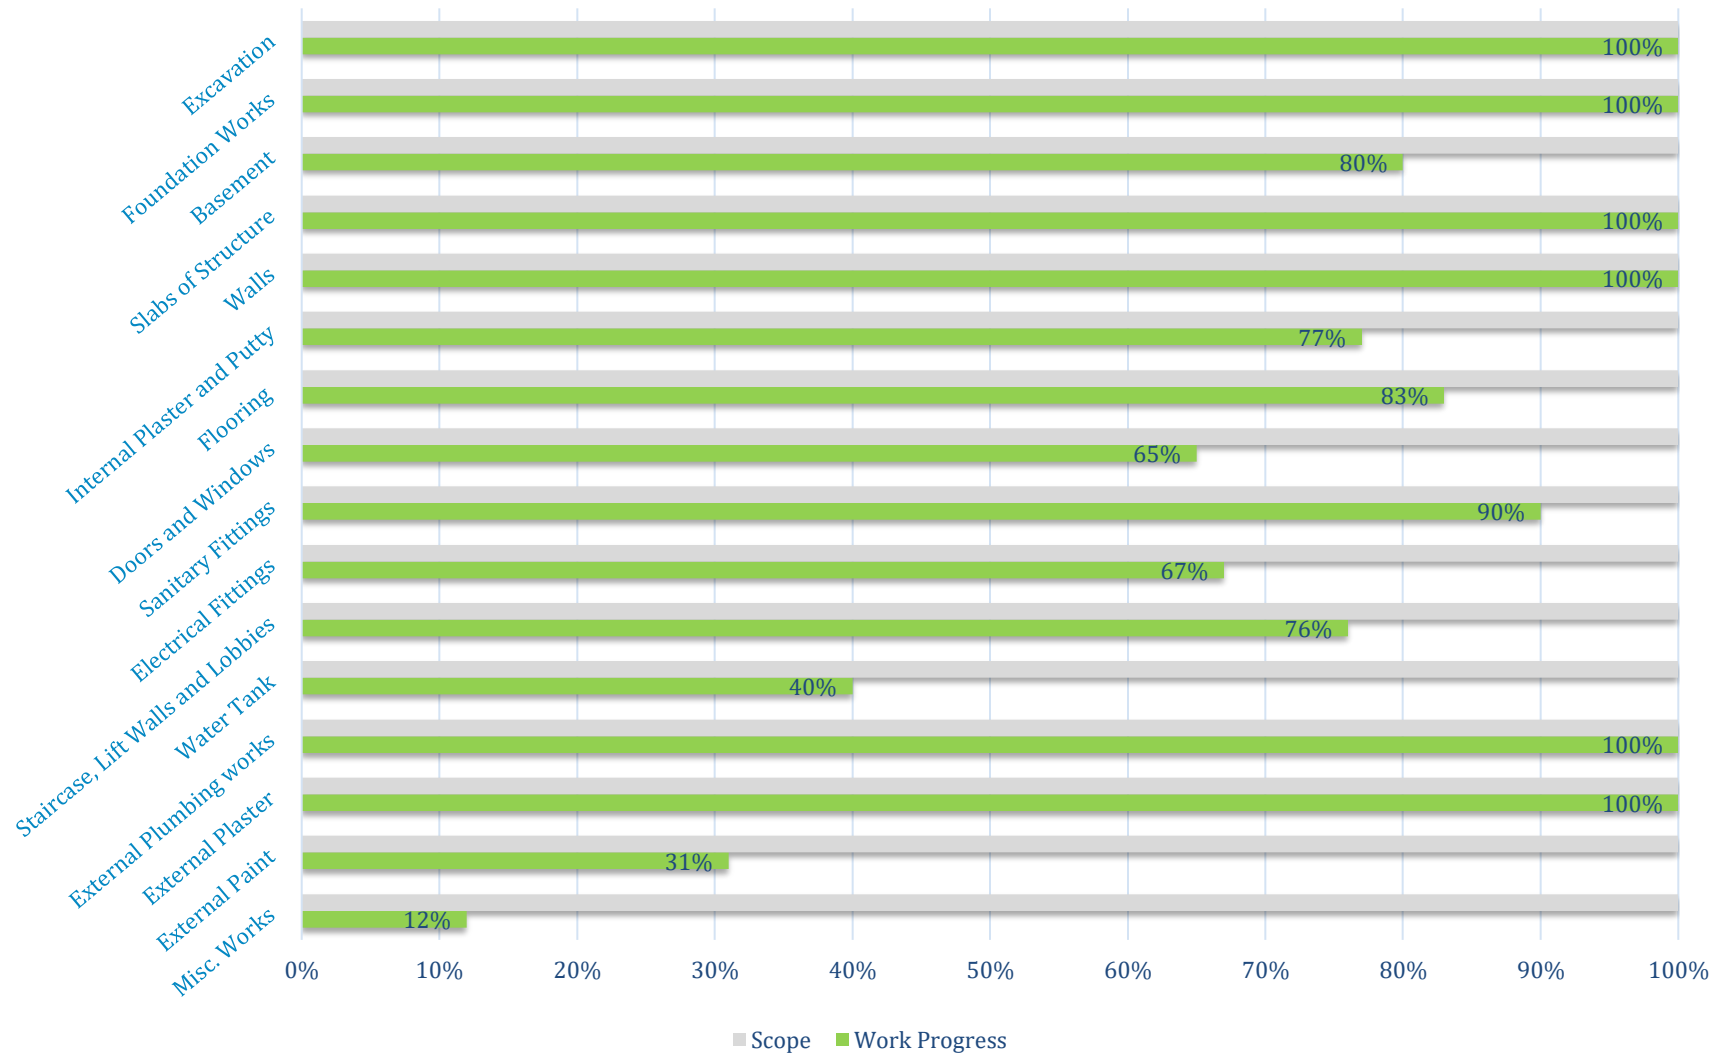

Progress Update for Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	25%	Compound wall works under progress
2	Water supply	Yes	50%	Boring works complete of 1 bore well. 2 nd bore well construction yet to start.

Update on number and types of flats/plots booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats / Plot Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	3 BHK	8	7	1	0	8	7	1	0	8
2	2 BHK	6	5	0	0	5	5	0	0	5

Status of financials in the project up to 30th June, 2019

S.No.	Description	Amount (in Rs.)
1	Amounts received from allottees against booking of units(for builder's share)	4,81,19,074.90
2	Expenditure done towards completion of project	4,79,63,387.04
3	Balance in Designated Bank A/c as on thisquarter end	68,81,295.71

Status of Approvals**A. Approval Received**

S. No.	Description	Date of Receipt
1	Provisional Fire Clearance	02.01.16
2	RERA Registration	18.12.18

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs



