

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Apr-Jun of 2024 (Year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No.	U45200BR2011PTC017199
Firm Address:	Dr Alok Sahay Compound, Near Dewati Apartment, Behind Cogress Maidan, Patna BR 800003
Total Experience of promoter in Real Estate Sector	4 Years
Total Experience in Real Estate After Implementation of RERA	4 Years
No of Project done Before Implementation of RERA	No Any
No of Project done After Implementation of RERA	1. Ram Padarath Enclave 2. Shukdeo Enclave 3. Shri Balajee Bhanu Regency

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP00075-3/1072/R-882/2020
Name of Project/Phase of Registered Project	SHUKDEO ENCLAVE
Name of Promoter	SHRI BALAJEE NEST BUILDER PRIVATE LIMITED
Project Address	MOHALLA - OLD BYEPASS ROAD, MAUZA - LOHANIPUR, PARGANA AZIMABAD PS- KANKARBAGH, KHATA NO- 44, THANA NO- 06, TAUZI NO- 156,PLOT NO-218, PATNA, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	18/07/2024
Starting date of Project or Phase of the Project	15/11/2019
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share –	Total Number of Apartments in Landowner's share –
Shukdeo Enclave	3 BHK	849.00	4	1. Booked/ Alloted- 06 2. Sold- 03 Percentage of booking-	3. Booked/ Alloted- 4. Sold-
Shukdeo Enclave	3 BHK	865.00	4		
Shukdeo Enclave	3 BHK	1000.00	4		
Shukdeo Enclave	3 BHK	977.00	4		
Shukdeo Enclave	SHOP	139.00	1		Percentage of booking-
Shukdeo Enclave	SHOP	89.77	1		
Shukdeo Enclave	SHOP	220.45	1		
Shukdeo Enclave	SHOP	286.00	1		
Shukdeo Enclave	SHOP	272.00	1		
Shukdeo Enclave	SHOP	343.59	1		
Shukdeo Enclave	SHOP	1825.78	1		

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Shukdeo Enclave	No Garages available	1. Booked/Allotted - 2. Sold -	

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission /Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. Construction Progress of the Project

1. Building / Wing / Layout Number- Shukdeo Enclave (To be added for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	Completed
2.	Basements (if any)	100%	
3.	Podiums (if any)	NA	
4.	Plinth	100%	
5.	Stilt Floor	NA	
6.	Slabs of Super Structure	100%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	
9.	Staircases, Lifts Walls and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.	100%	
	Any other activities.		

VII. Amenities and Common Area and External Infrastructure Development Works

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yyyy) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		Completed
2.	Water Supply	Yes	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and Fire Safety Requirements	Yes	100%	
13.	Closed Parking	Yes	100%	
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to Add More)	No		

VIII. EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

Not Applicable because our project is Residential/Group Housing.

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor

X. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	634905600830
2	Estimated Cost of the Project including land cost at the start of the Project	430.00/- (In Lakh)
3	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost) (In Lakh)	400.00/-
4	Any Variation in Development Cost which is declared at the start of the Project.	No Any
5	Amount received during the Quarter	0.00/-
6	Actual Cost Incurred during the Quarter	10,84,064.48/-
7	Net amount at end of the Quarter	5 ,16,694.90/-
8	Total expenditure on Project till date	3 ,04,14,022.03/-
9	Cumulative fund collected till the end of Quarter in question	2,96,23,809.86/-
10	Cumulative expenditure done till the end of Quarter in question	3 ,04,14,022.03/-

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED


XII. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
3.	No of Execution Cases against this project Case No. Name of Parties	
4.	No of Suo - Moto cases against this project Case No. Name of Parties	
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	04
2.	Agreement for Sale	

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

PROGRESS CHART

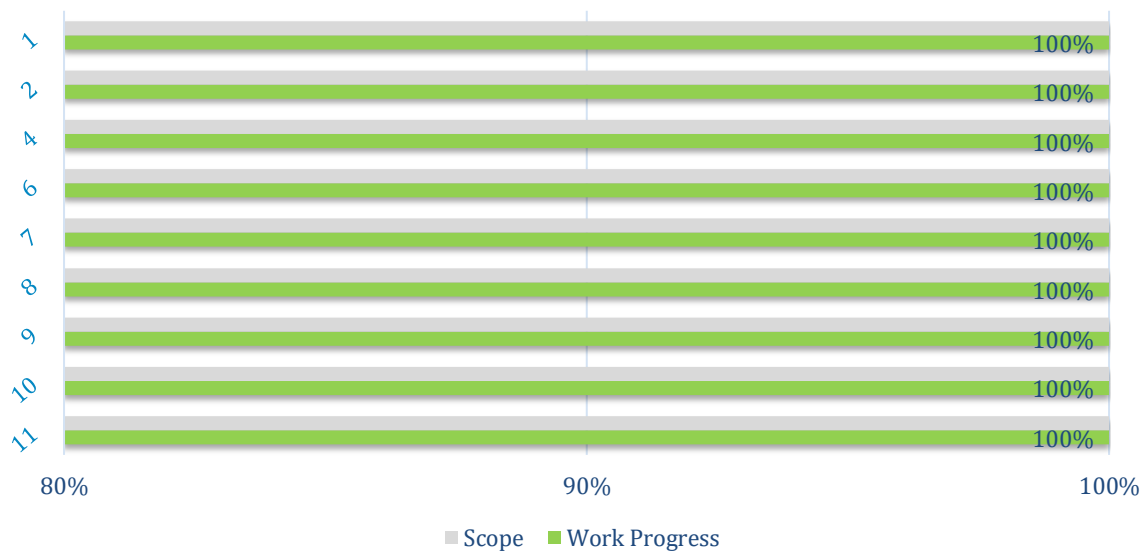

Project Site Photographs

Front Elevation




Side Elevation





GPS Map Camera



Patna, Bihar, India

J43X+C56, Main Rd, Kankarbagh Colony More, Kankarbagh, Patna, Bihar 800020, India

Lat 25.603305°

Long 85.148106°

06/07/24 10:18 AM GMT +05:30

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Shri Balajee Nest Builder Private Limited.



Date :
