

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Apr-Jun of 2023 (Year)

I. PARTICULARS OF PROJECT

Project Registration Number	BRERAP61621-2/191/R-1484/2022
Name of Project/Phase of Registered Project	AMBER AJAY PALACE
Name of Promoter	SAI SAMPANN INFRA LLP
Project Address	PLOT NO.- 2317 P, THANA NO.- 30, TAUZI NO.- 5456, KHATA NO.- 166, AT MAUZA- JAMSAUT, THANA- DANAPUR, DIST- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	31/03/2025
Starting date of Project or Phase of the Project	20/10/2022
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Five Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Amber Ajay Palace	3 BHK	807.75	3	1. Booked/ Alloted - 03 2. Sold –
Amber Ajay Palace	3 BHK	826.58	7	
Amber Ajay Palace	3 BHK	749.32	3	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Amber Ajay Palace	No Garages available	1. Booked/Allotted - 2. Sold -	

For SAI SAMPANN INFRA LLP

Rohit Kumar

Designated Partner

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project**1. Plan Case Number-75/22-23 Amber Ajay Palace (To be added for each Building / Wing)**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	NA
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	80%
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	20%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	37%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%

For SAI SAMPANN INFRA LLP

Rohit Kumar

Designated Partner

11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	11%
-----	---	-----

VI. Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	NO	NA	
2.	Water Supply	Yes	50%	Pump Installed.
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	0%	
4.	Storm Water Drains	No	NA	
5.	Landscaping & Tree Planting	No	NA	
6.	Street Lighting	No	NA	
7.	Community Buildings	No	NA	
8.	Treatment and Disposal of Sewage and Sullage Water	No	NA	
9.	Solid Waste Management & Disposal	No	NA	
10.	Water Conservation / RainWater Harvesting	No	NA	
11.	Energy Management	No	NA	
12.	Fire Protection and Fire Safety Requirements	No	NA	
13.	Closed Parking	Yes	0%	

For SAI SAMPANN INFRA LLP

Rohit Kumar

Designated Partner

14.	Open Parking	No	NA	
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	0%	
16.	Others (Option to AddMore)	No	NA	

VII. Geo Tagged And Date Photograph Of(Each Block) Of The Project

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor- Attached Below

VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	1866102000007658
2	Estimated Cost of the Project including land cost at the start of the Quarter	246.00/- (In Lakh)
3	Amount received during the Quarter (Excluding GST)	93,85,813.00/-
4	Actual Cost Incurred during the Quarter	71,11,818.00/-
5	Net amount at end of the Quarter	1,74,300.00/-
6	Total expenditure on Project till date	1,97,60,813.00/-
7	Cumulative fund collected till the end of Quarter in question (Excluding GST)	1,54,36,507.46/-
8	Cumulative expenditure done till the end of Quarter in question	1,97,60,813.00/-

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

For SAI SAMPANN INFRA LLP

Rohit Kumar


Designated Partner

X. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	03

XI. Percentage Of Work Along With Milestone Chart


Weather the project in progress is as per time schedule or lagging behind?

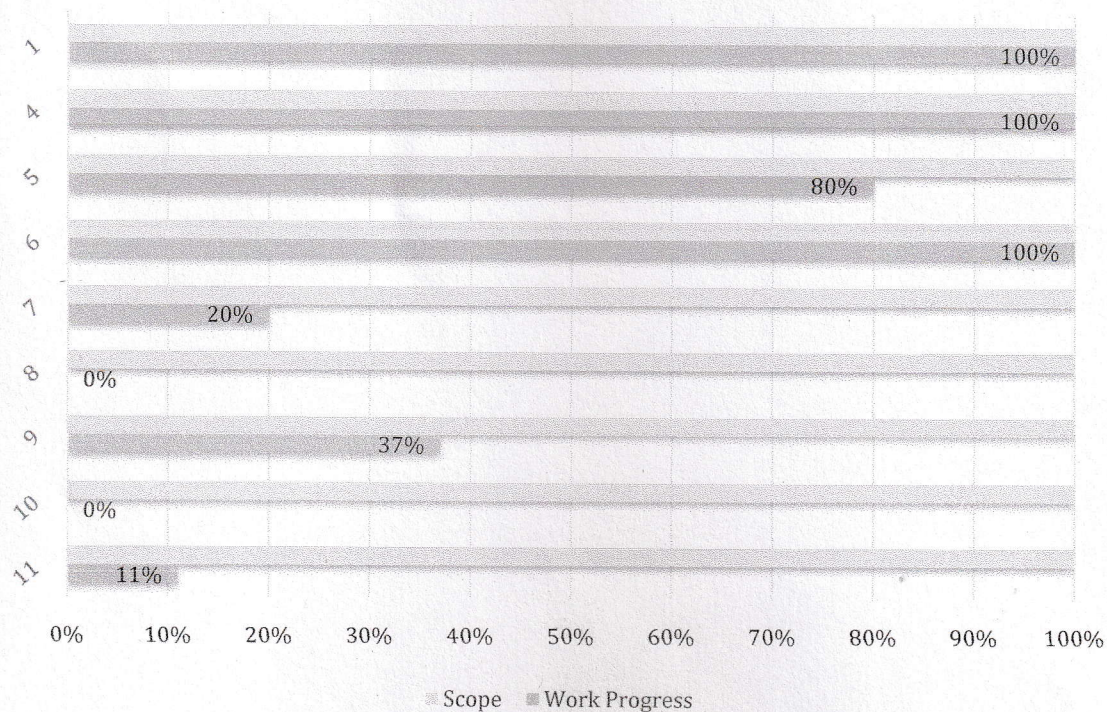PROGRESS CHART

For SAI SAMPANN INFRA LLP

Rohit Kumar
Designated Partner


Project Site Photographs

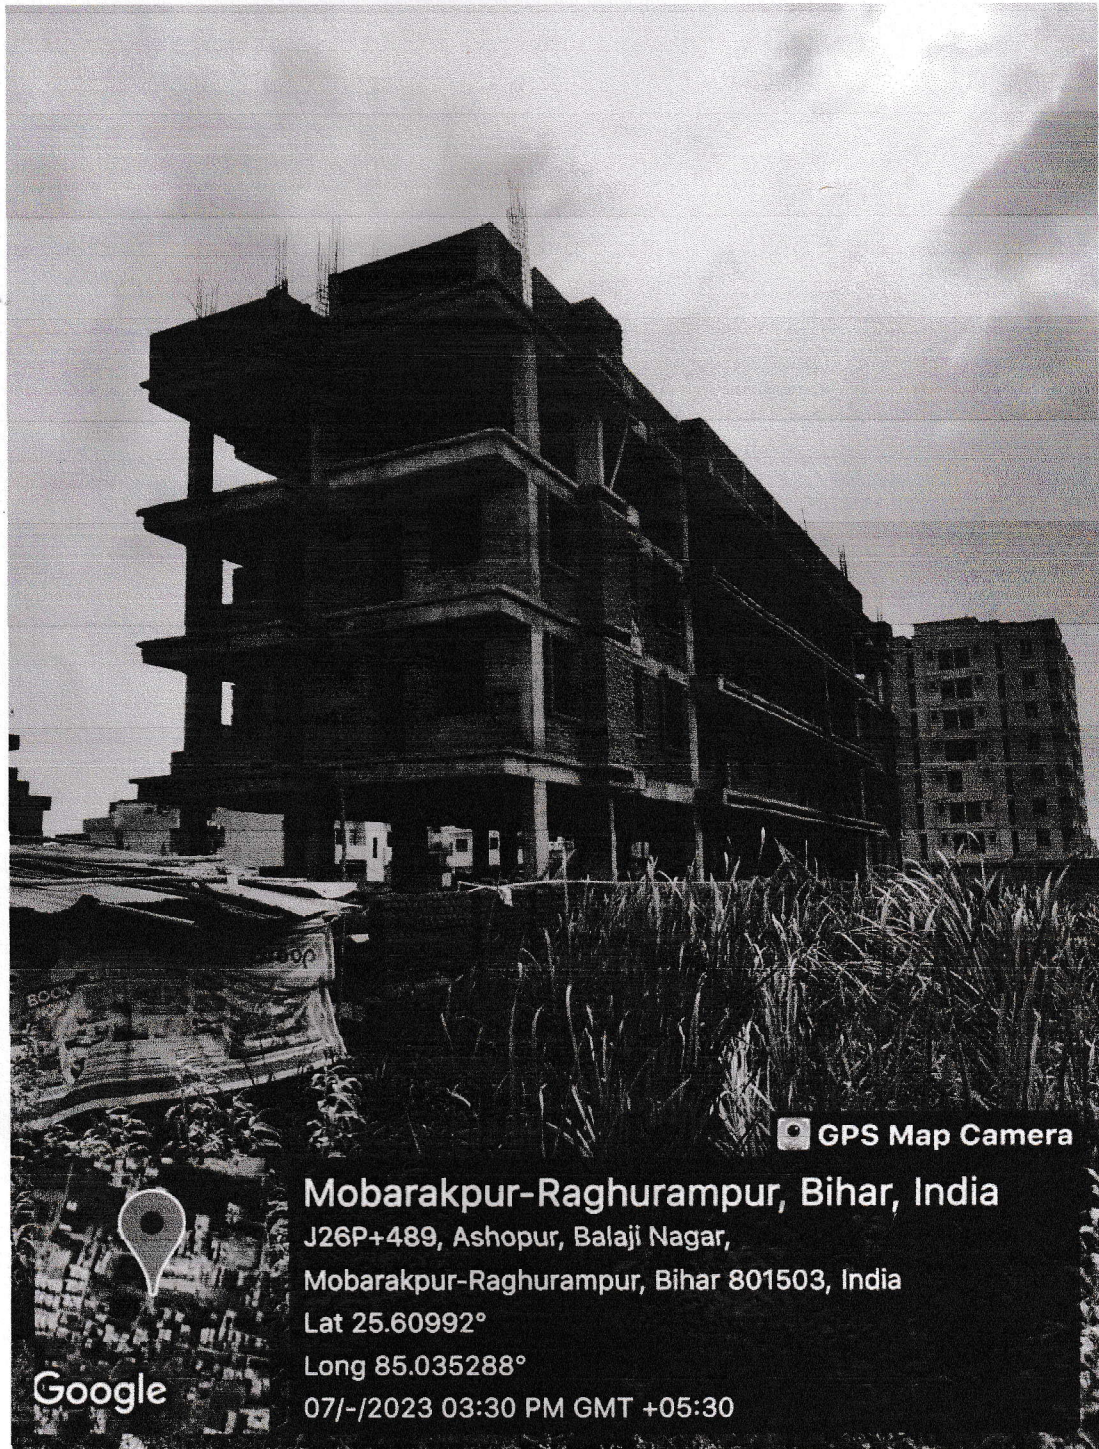

For SAI SAMPANN INFRA LLP

Rohit Kumar

Designated Partner

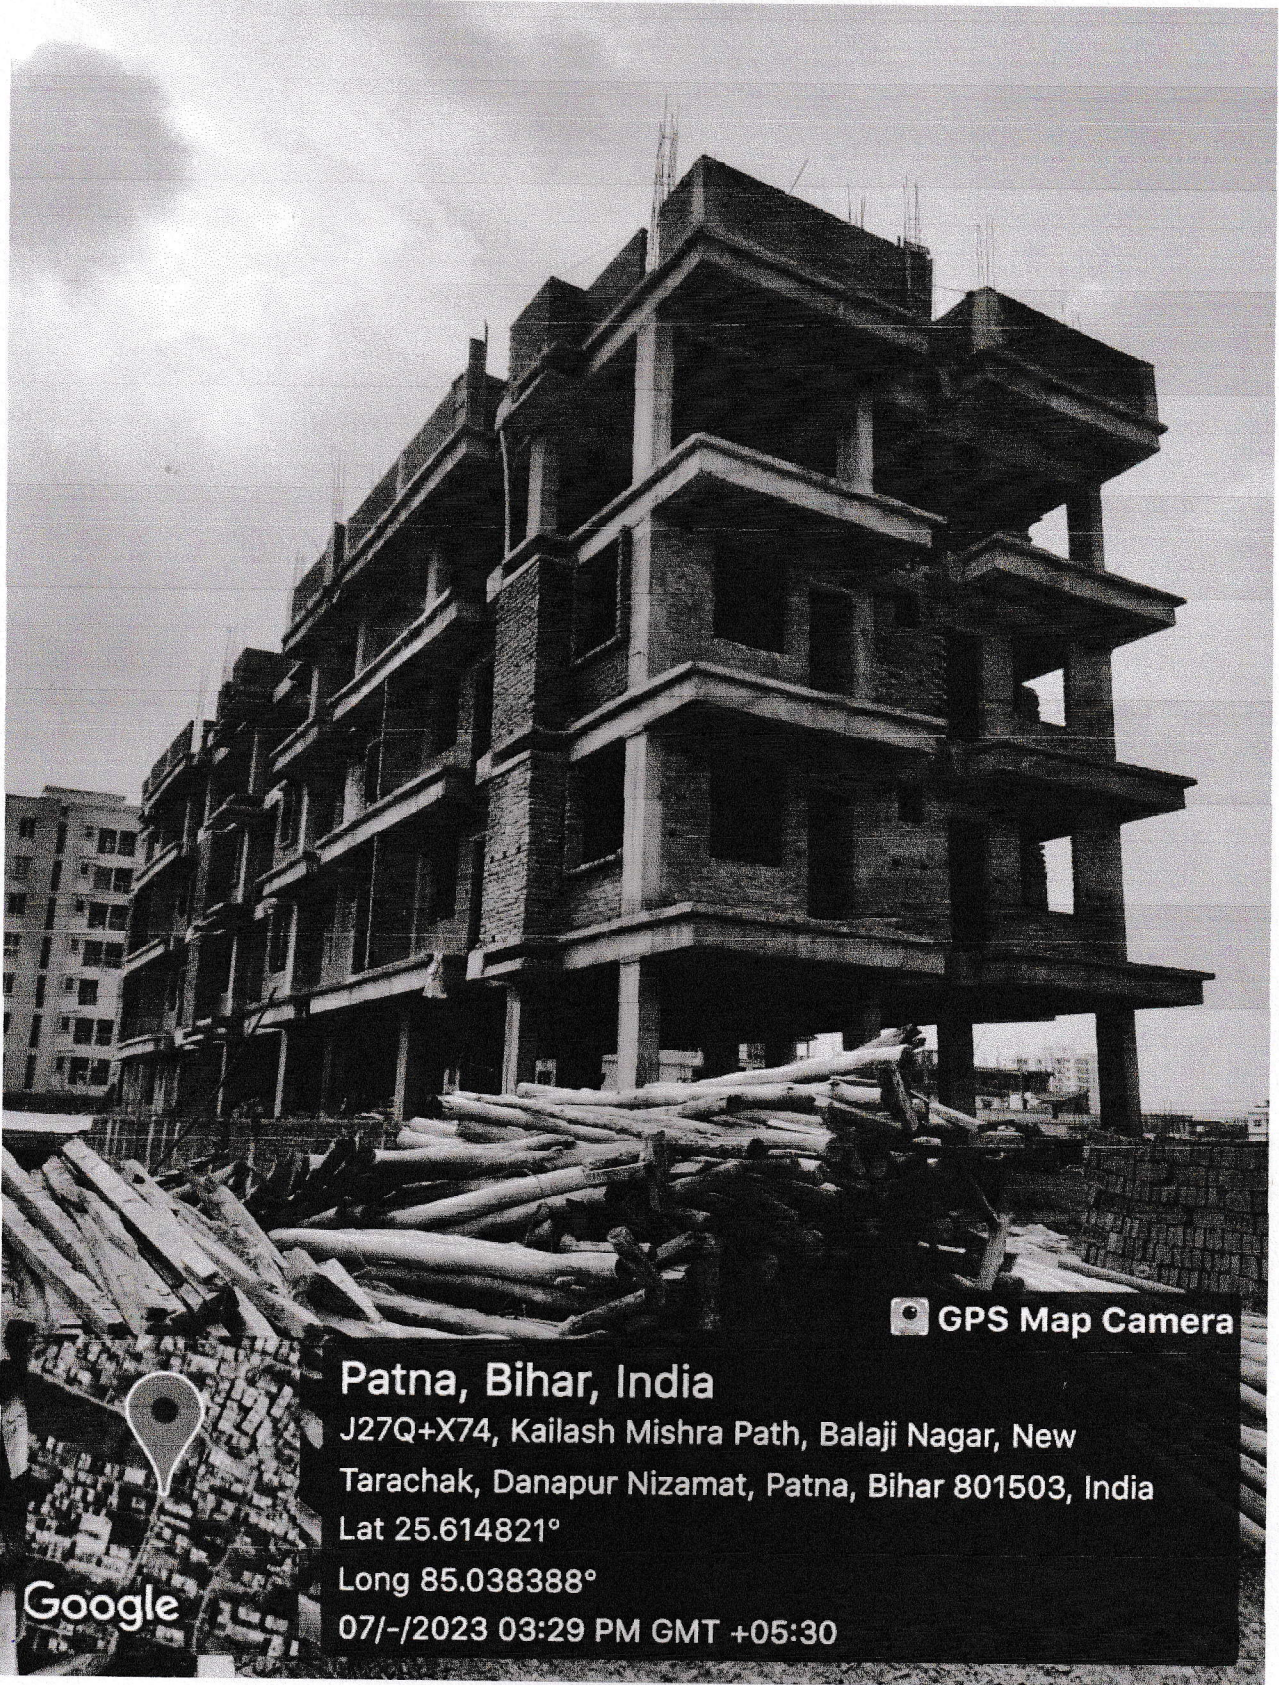

GPS Map Camera

Patna, Bihar, India

J27Q+X74, Kailash Mishra Path, Balaji Nagar, New

Tarachak, Danapur Nizamat, Patna, Bihar 801503, India

Lat 25.614821°

Long 85.038388°

07/-/2023 03:29 PM GMT +05:30

For SAI SAMPANN INFRA LLP

Rohit Kumar

Designated Partner

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

For SAI SAMPANN INFRA LLP

Rohitkumar

Designated Partner

Name: Sai Sampann Infra LLP.

Date :
