

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Apr-Jun of 2023 (Year)

I. PARTICULARS OF PROJECT

Project Registration Number	BRERAP91535-1/1174/R-1033/2020
Name of Project/Phase of Registered Project	GREEN RESIDENCY
Name of Promoter	TAJ HERITAGE BUILDCON PRIVATE LIMITED
Project Address	FEDRAL COLONY, ISOPUR, PHULWARI, PATNA, PLOT No.- 4159, PATNA, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	16/10/2022
Starting date of Project or Phase of the Project	20/01/2020
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Bismillah Complex	2 BHK	649.90	3	1. Booked-05 2. Sold-
Bismillah Complex	2 BHK	633.97	3	
Bismillah Complex	2 BHK	667.98	3	
Bismillah Complex	3 BHK	770.95	3	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Bismillah Complex	No Garages available	1. Booked/Allotted -	
		-	
		2. Sold -	

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project

1. Plan Case Number- 59/2017-18 (Bismillah Complex) (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	NA
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	95%
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	95%
9.	Staircases, Lifts Walls and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%
11.	Installation of Lifts, water pumps, Fire Fighting	85%

	Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	
--	---	--

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	100%	Pump Installed
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / Rain Water Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and Fire Safety Requirements	No		
13.	Closed Parking	Yes	100%	
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to Add More)	No		

VII. Geo Tagged And Date Photograph Of(Each Block) Of The Project

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor- Attached Below

VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	920020009802831
2	Estimated Cost of the Project including land cost at the start of the Quarter (In Lakh)	202.00/-
3	Amount received during the Quarter	5,74,000.00/-
4	Actual Cost Incurred during the Quarter	6,45,864.00/-
5	Net amount at end of the Quarter	8,940.46/-
6	Total expenditure on Project till date	1,03,53,641.90/-
7	Cumulative fund collected till the end of Quarter in question	1,03,09,312.00/-
8	Cumulative expenditure done till the end of Quarter in question	1,03,53,641.90/-


IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

X. MISCELLANEOUS

A	List of Legal Cases (if any)
1.	Case No. NA

2.	Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	
2.	Agreement for Sale	01

XI.	Percentage Of Work Along With Milestone Chart
	Weather the project in progress is as per time schedule or lagging behind?

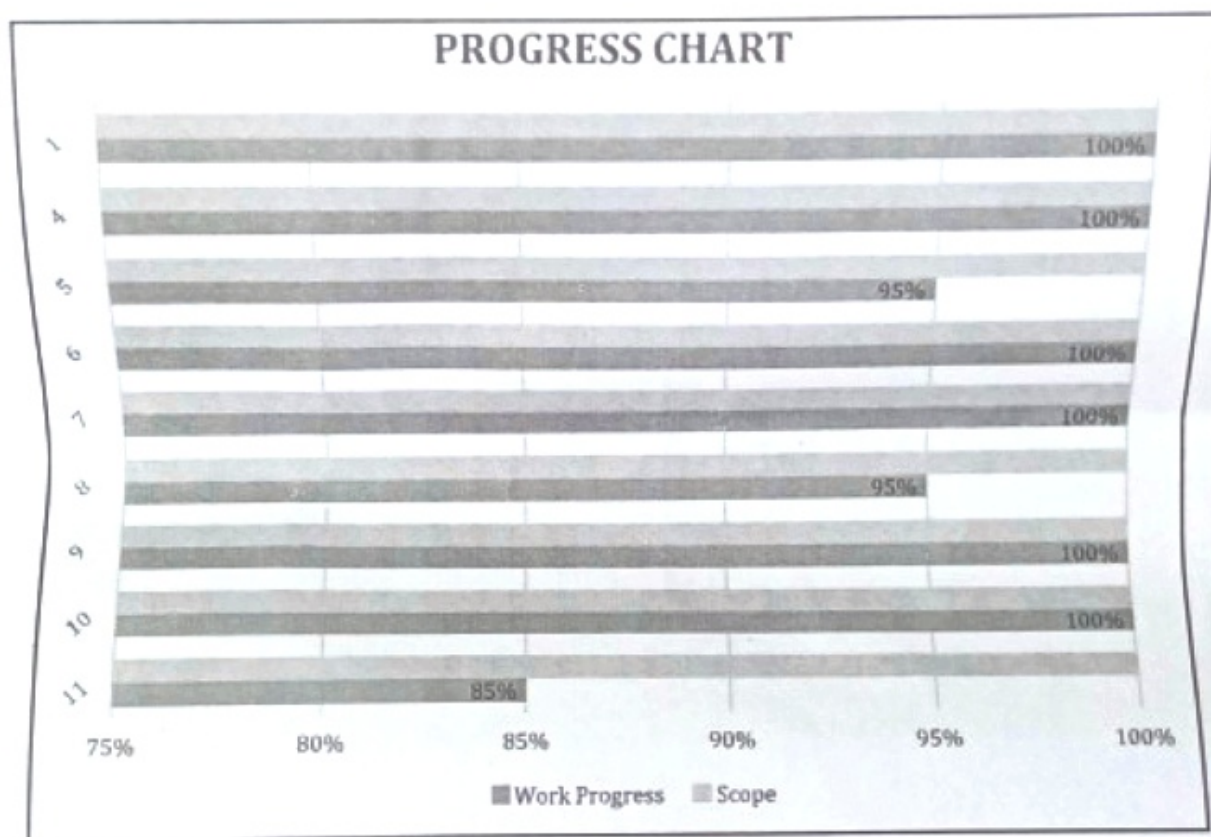

Project Site Photographs
Front Elevation



 GPS Map Camera

Patna, Bihar, India

Khalilpura Road Tam -Tam Padao Near Church, H3HC+M8F, Quazi Nagar, Birla
Colony, Phulwari Sharif, Patna, Bihar 801505, India

Lat 25.579134°

Long 85.071007°

05/08/23 05:29 PM GMT +05:30

Google

Side Elevation





Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter **Hentage Buildcon Pvt Ltd**

Name: Aftab Hussain

Date: 30-8-23

Aftab Hussain
Managing Director
