

# FORM-7

## [REGULATION-9]

Quarterly Progress Report for quarter ending June of 2023

| I. PARTICULARS OF PROJECT                            |                                                                                        |                                             |                                                                                  |
|------------------------------------------------------|----------------------------------------------------------------------------------------|---------------------------------------------|----------------------------------------------------------------------------------|
| Project Registration Number                          | BRERAP94350/1266/R-1040/2020                                                           | Name of Project/Phase of Registered Project | ARADHYA RESIDENCY                                                                |
| Name of Promoter                                     | AYURADHYA CONSTRUCTION PVT. LTD.                                                       | Project Address                             | POLE NO.10 DEO NAGAR PIPRA ROAD, NEW JAGANPURA ROAD, PS- RK NAGAR, PATNA-800030. |
| Name of Co-promoter                                  | N/A                                                                                    |                                             |                                                                                  |
| Project Registration is valid up to                  | 30/06/2024                                                                             |                                             |                                                                                  |
| Starting date of Project or Phase of the Project     | 07/09/2020                                                                             |                                             |                                                                                  |
| Type of Project or Phase of the Project              | 1. Residential<br>2. Commercial<br>3. Residential-cum-Commercial<br>4. Plotted project | Residential                                 |                                                                                  |
| Period of validity of map by the Competent Authority | 5 YEARS                                                                                |                                             |                                                                                  |

| II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS |                |      |                |                                            |                                         |
|-------------------------------------------------------|----------------|------|----------------|--------------------------------------------|-----------------------------------------|
| Building/Block Number                                 | Apartment Type |      | Carpet Area    | Total Number of sanctioned apartments - 01 | Total Number of Apartments - 13         |
| 01                                                    | 1. 3 BHK       | - 13 | 10671.48 sqft. |                                            | Land owner share                        |
|                                                       |                |      |                |                                            | 06                                      |
|                                                       |                |      |                |                                            | 07                                      |
|                                                       |                |      |                |                                            | 1. Booked /Allotted - 0<br>2. Sold - 01 |

| III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES |                                    |                          |      |
|-------------------------------------------------------|------------------------------------|--------------------------|------|
| Building / Block Number                               | Total Number of Sanctioned Garages | Total Number of Garages: |      |
| ARADHYA RESIDENCY                                     | 16                                 | 1. Booked/Allotted       | - 01 |
|                                                       |                                    | 2. Sold                  | - 01 |

**IV. DETAILS OF BUILDING APPROVALS**

(If already filed along with Registration Application, then there is no need of Further filing)

| S.NO. | Name of the Approval /<br>N.O.C. / Permission /<br>Certificate | Issuing<br>Authority | Applied<br>Date | Issuance<br>Date | Enclosed as<br>Annexure<br>No. |
|-------|----------------------------------------------------------------|----------------------|-----------------|------------------|--------------------------------|
| 1.    | NOC for Environment                                            |                      |                 |                  |                                |
| 2.    | Fire N.O.C                                                     |                      |                 |                  |                                |
| 3.    | Water Supply<br>Permission                                     |                      |                 |                  |                                |
| 4.    | NOC from Airport<br>Authority of India                         |                      |                 |                  |                                |
| 5.    | Other Approval (S), if<br>any, required for the Project        |                      |                 |                  |                                |

**V. Construction Progress of the Project**

1. Building / Wing / Layout Number \_\_\_\_\_ (To beaded for each Building / Wing)

| S. No.<br>(1) | Tasks / Activity<br>(2)          | Percentage of Actual Work Done<br>(As on date of the Certificate)<br>(3) |
|---------------|----------------------------------|--------------------------------------------------------------------------|
| 1.            | Excavation (if any)              | 100%                                                                     |
| 2.            | Basements (if any)               | 100%                                                                     |
| 3.            | Podiums (if any)                 | 100%                                                                     |
| 4.            | Plinth                           | 100%                                                                     |
| 5.            | Stilt Floor                      | 100%                                                                     |
| 6.            | Slabs of Super Structure         | 100%                                                                     |
| 7.            | Internal walls, Internal Plaster | 100%                                                                     |
| 7.            | Floorings                        | 100%                                                                     |
|               |                                  |                                                                          |

|     |                                                                                                                                                                                                                                                                                                                                                                                                                                               |      |
|-----|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|
| 8.  | Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises                                                                                                                                                                                                                                                                                                                                                      | 100% |
| 9.  | Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.                                                                                                                                                                                                                                                                                                                                                | 100% |
| 10. | External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.                                                                                                                                                                                                                                                                                                                            | 100% |
| 11. | Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.<br><br>Any other activities. | 100% |

| VI. Amenities and Common Area and External Infrastructure Development Works) |                                            |                   |                                                                |         |
|------------------------------------------------------------------------------|--------------------------------------------|-------------------|----------------------------------------------------------------|---------|
| S. No.                                                                       | Common Areas and Facilities                | Proposed (Yes/No) | Percentage of actual Work Done (As on date of the Certificate) | Details |
| (1)                                                                          | (2)                                        | (3)               | (4)                                                            | (5)     |
| 1.                                                                           | Internal Roads & Footpaths                 |                   |                                                                |         |
| 2.                                                                           | Water Supply                               | YES               |                                                                |         |
| 3.                                                                           | Sewerage (Chamber, Line, Septic Tank, STP) | YES               |                                                                |         |
| 4.                                                                           | Storm Water Drains                         |                   |                                                                |         |
| 5.                                                                           | Landscaping & Tree Planting                |                   |                                                                |         |
| 6.                                                                           | Street Lighting                            | YES               |                                                                |         |

|     |                                                       |     |  |  |
|-----|-------------------------------------------------------|-----|--|--|
| 7.  | Community Buildings                                   |     |  |  |
| 8.  | Treatment and Disposal of Sewage and Sullage Water    |     |  |  |
| 9.  | Solid Waste Management & Disposal                     |     |  |  |
| 10. | Water Conservation / Rain Water Harvesting            |     |  |  |
| 11. | Energy Management                                     |     |  |  |
| 12. | Fire Protection and Fire Safety Requirements          |     |  |  |
| 13. | Closed Parking                                        |     |  |  |
| 14. | Open Parking                                          |     |  |  |
| 15. | Electrical Meter Room, Sub-Station, Receiving Station | YES |  |  |
| 16. | Others (Option to Add More)                           |     |  |  |

**VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT**

|    |                                         | Proposed<br>(Yes/No) | Percentage of actual<br>Work Done (As on<br>date of the<br>Certificate) | Details |
|----|-----------------------------------------|----------------------|-------------------------------------------------------------------------|---------|
| 1. | Internal Roads & Footpaths              |                      |                                                                         |         |
| 2. | Water Supply                            |                      |                                                                         |         |
| 3. | Sewerage Chambers<br>Septic Tank        |                      |                                                                         |         |
| 4. | Drains                                  |                      |                                                                         |         |
| 5. | Parks, Landscaping and Tree<br>Planning |                      |                                                                         |         |
| 6. | Street Lighting                         |                      |                                                                         |         |
| 7. | Disposal of sewage &<br>Sullage Water   |                      |                                                                         |         |

|    |                                           |  |  |  |
|----|-------------------------------------------|--|--|--|
| 8. | Water conservation/ Rain Water Harvesting |  |  |  |
| 9. | Energy Management                         |  |  |  |

| VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT |         |                          |        |
|--------------------------------------------------------------------|---------|--------------------------|--------|
| (A)                                                                | Sr. No. |                          |        |
|                                                                    | 1.      | Front Elevation.         | Attach |
|                                                                    | 2.      | Rear Elevation           | Attach |
|                                                                    | 3.      | Side Elevation           | Attach |
| (B)                                                                |         | Photograph of each floor |        |

| VIII. Financial Progress of the Project |                                                                               |                 |
|-----------------------------------------|-------------------------------------------------------------------------------|-----------------|
| S. No.                                  | Particulars                                                                   | Amount (In Rs.) |
| (1)                                     | (2)                                                                           | (3)             |
| 1.                                      | Project Account No.                                                           | 920020047009946 |
| 2.                                      | Estimated Cost of the Project including land cost at the start of the Project | 2,81,71,000/-   |
| 3.                                      | Amount received during the Quarter                                            | 4,50,000/-      |
| 4.                                      | Actual Cost Incurred during the Quarter                                       | 6,12,223/-      |
| 5.                                      | Net amount at end of the Quarter                                              | 2,99,994/-      |
| 6.                                      | Total expenditure on Project <b>till date</b>                                 | 3,38,13,441/-   |
| 7.                                      | Cumulative fund Collected till the end of Quarter in question                 | 9,12,000/-      |
| 8.                                      | Cumulative expenditure done till the end of Quarter in question               | 5,62,223/-      |

| IX. Details of Mortgage or Charge if any created |
|--------------------------------------------------|
|                                                  |
|                                                  |
|                                                  |

| X. MISCELLANEOUS                                                           |                                            |    |
|----------------------------------------------------------------------------|--------------------------------------------|----|
| <b>A</b>                                                                   | List of Legal Cases (if any)               |    |
| 1.                                                                         | Case No.                                   | NO |
| 2.                                                                         | Name of Parties                            | NO |
| <b>B</b>                                                                   | Sale/Agreement for Sale during the Quarter |    |
| 1.                                                                         | Sale Deed                                  | 01 |
| 2.                                                                         | Agreement for Sale                         |    |
| <b>XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART</b>                   |                                            |    |
| Weather the project in progress is as per time schedule or lagging behind? |                                            |    |

**Undertaking:**

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

FOR AYURADHYA CONSTRUCTION PVT. LTD.


*Saurav Kumar*  
Director  
Signature of Promoter

Name: SAURAV KUMAR


Date: 09-09-2023





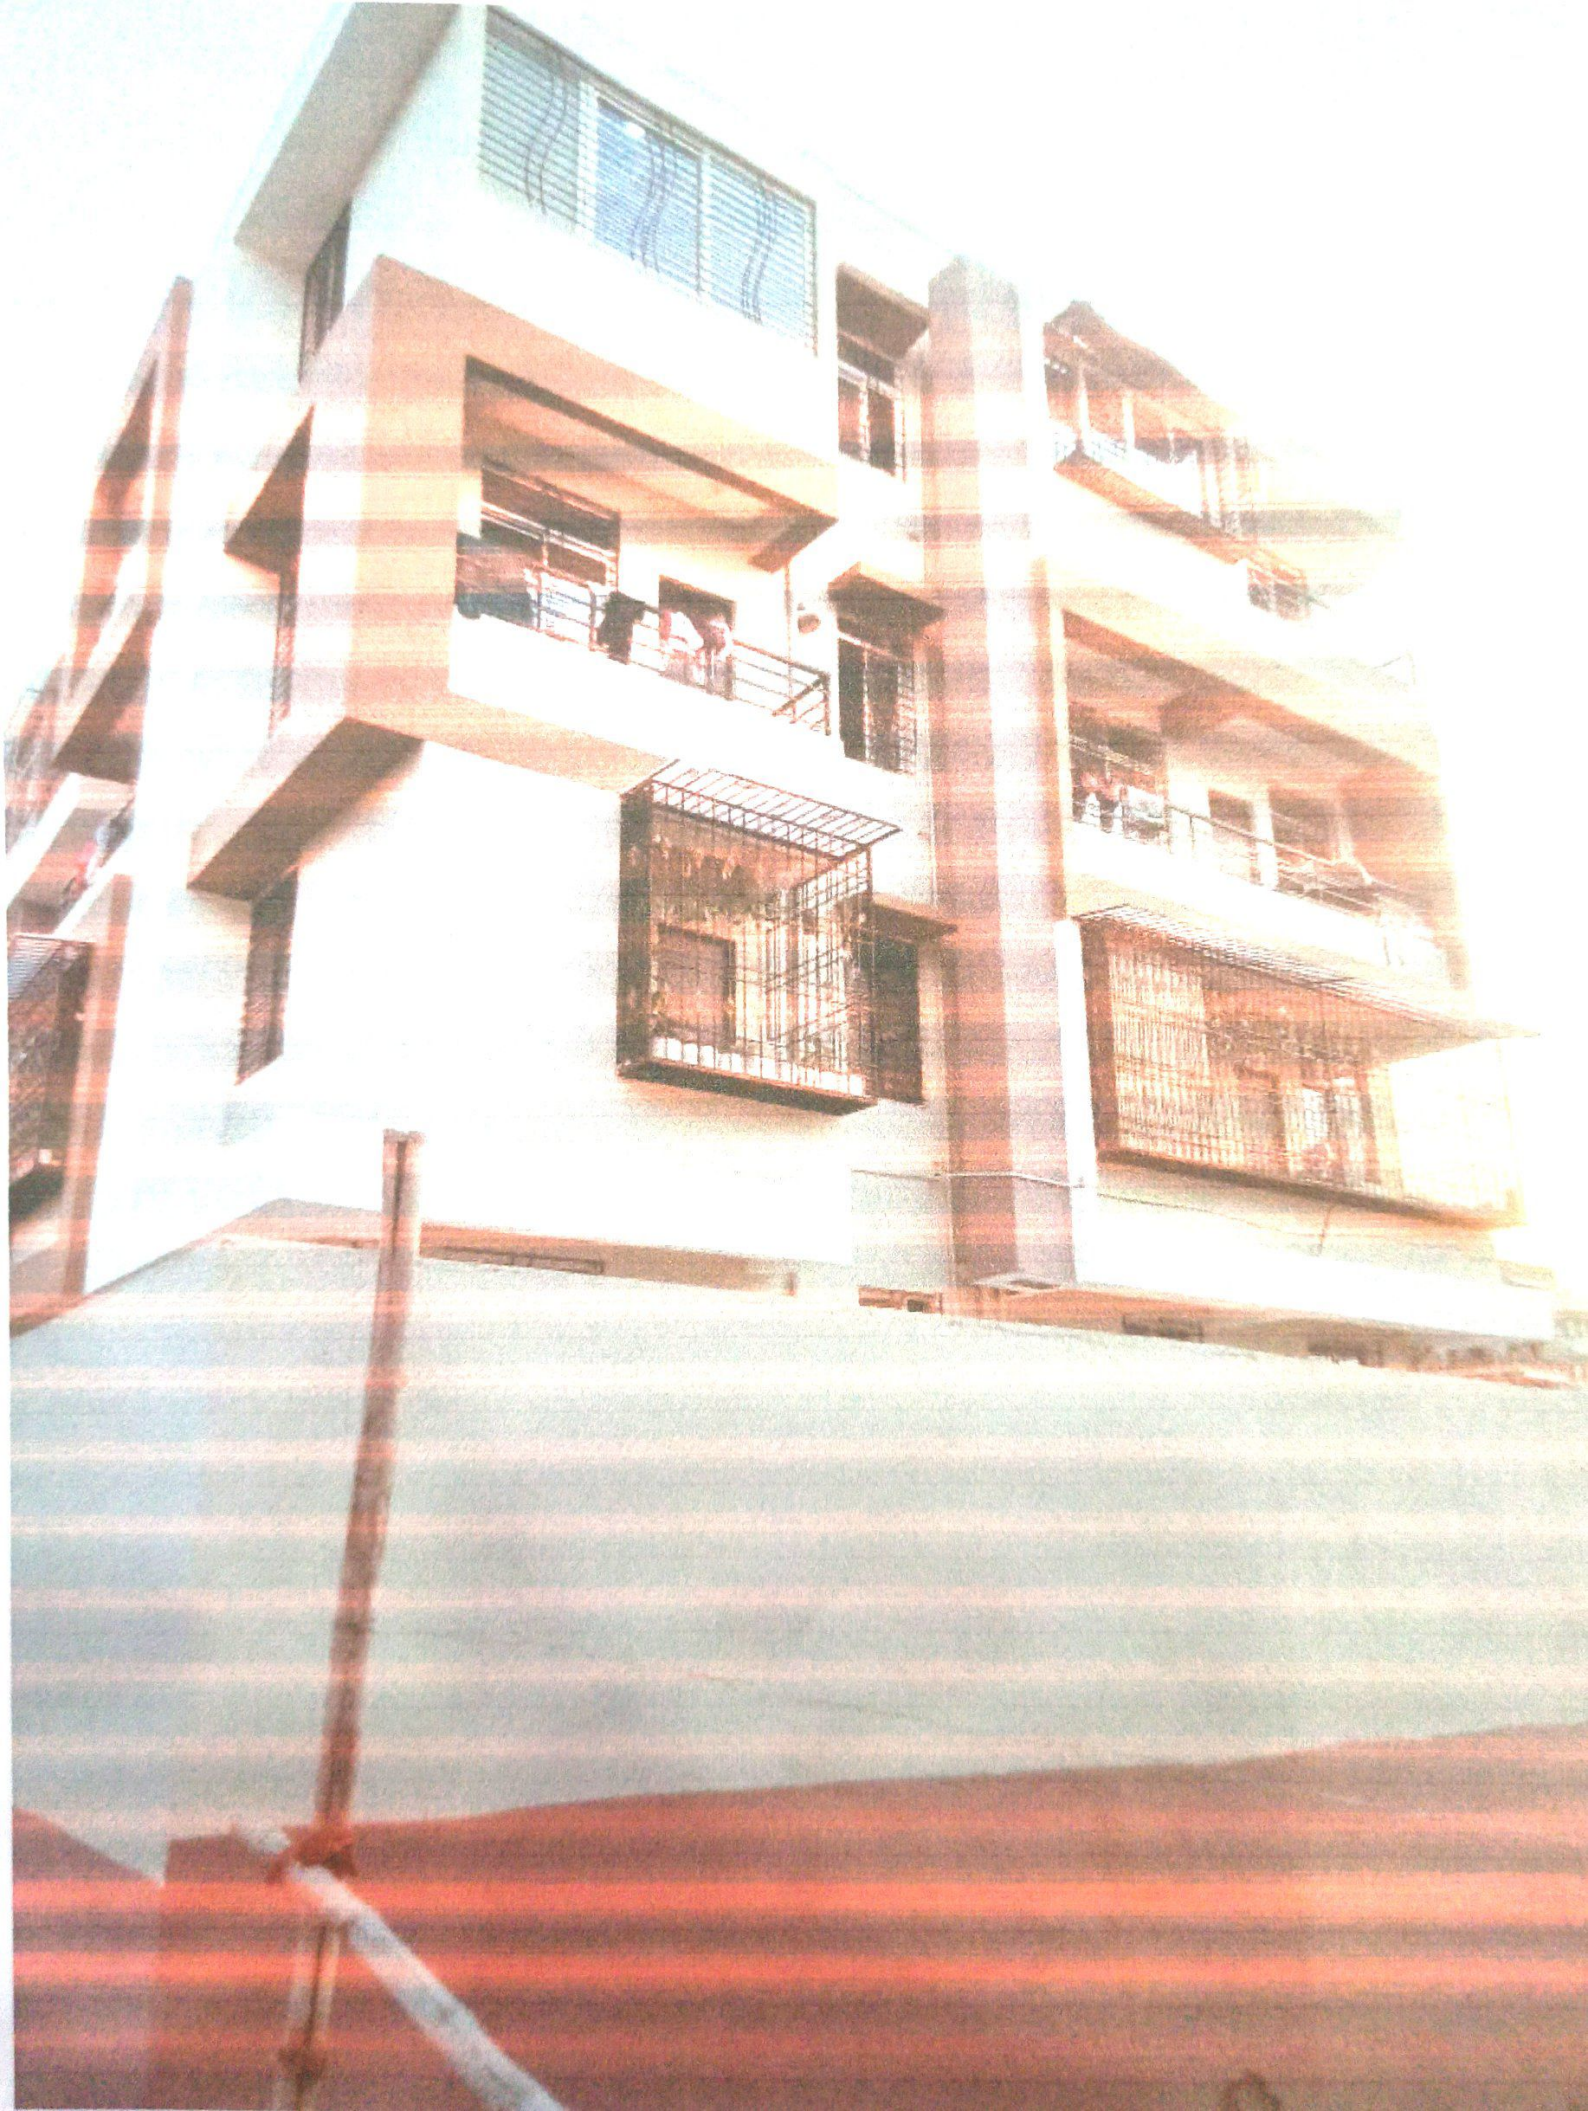



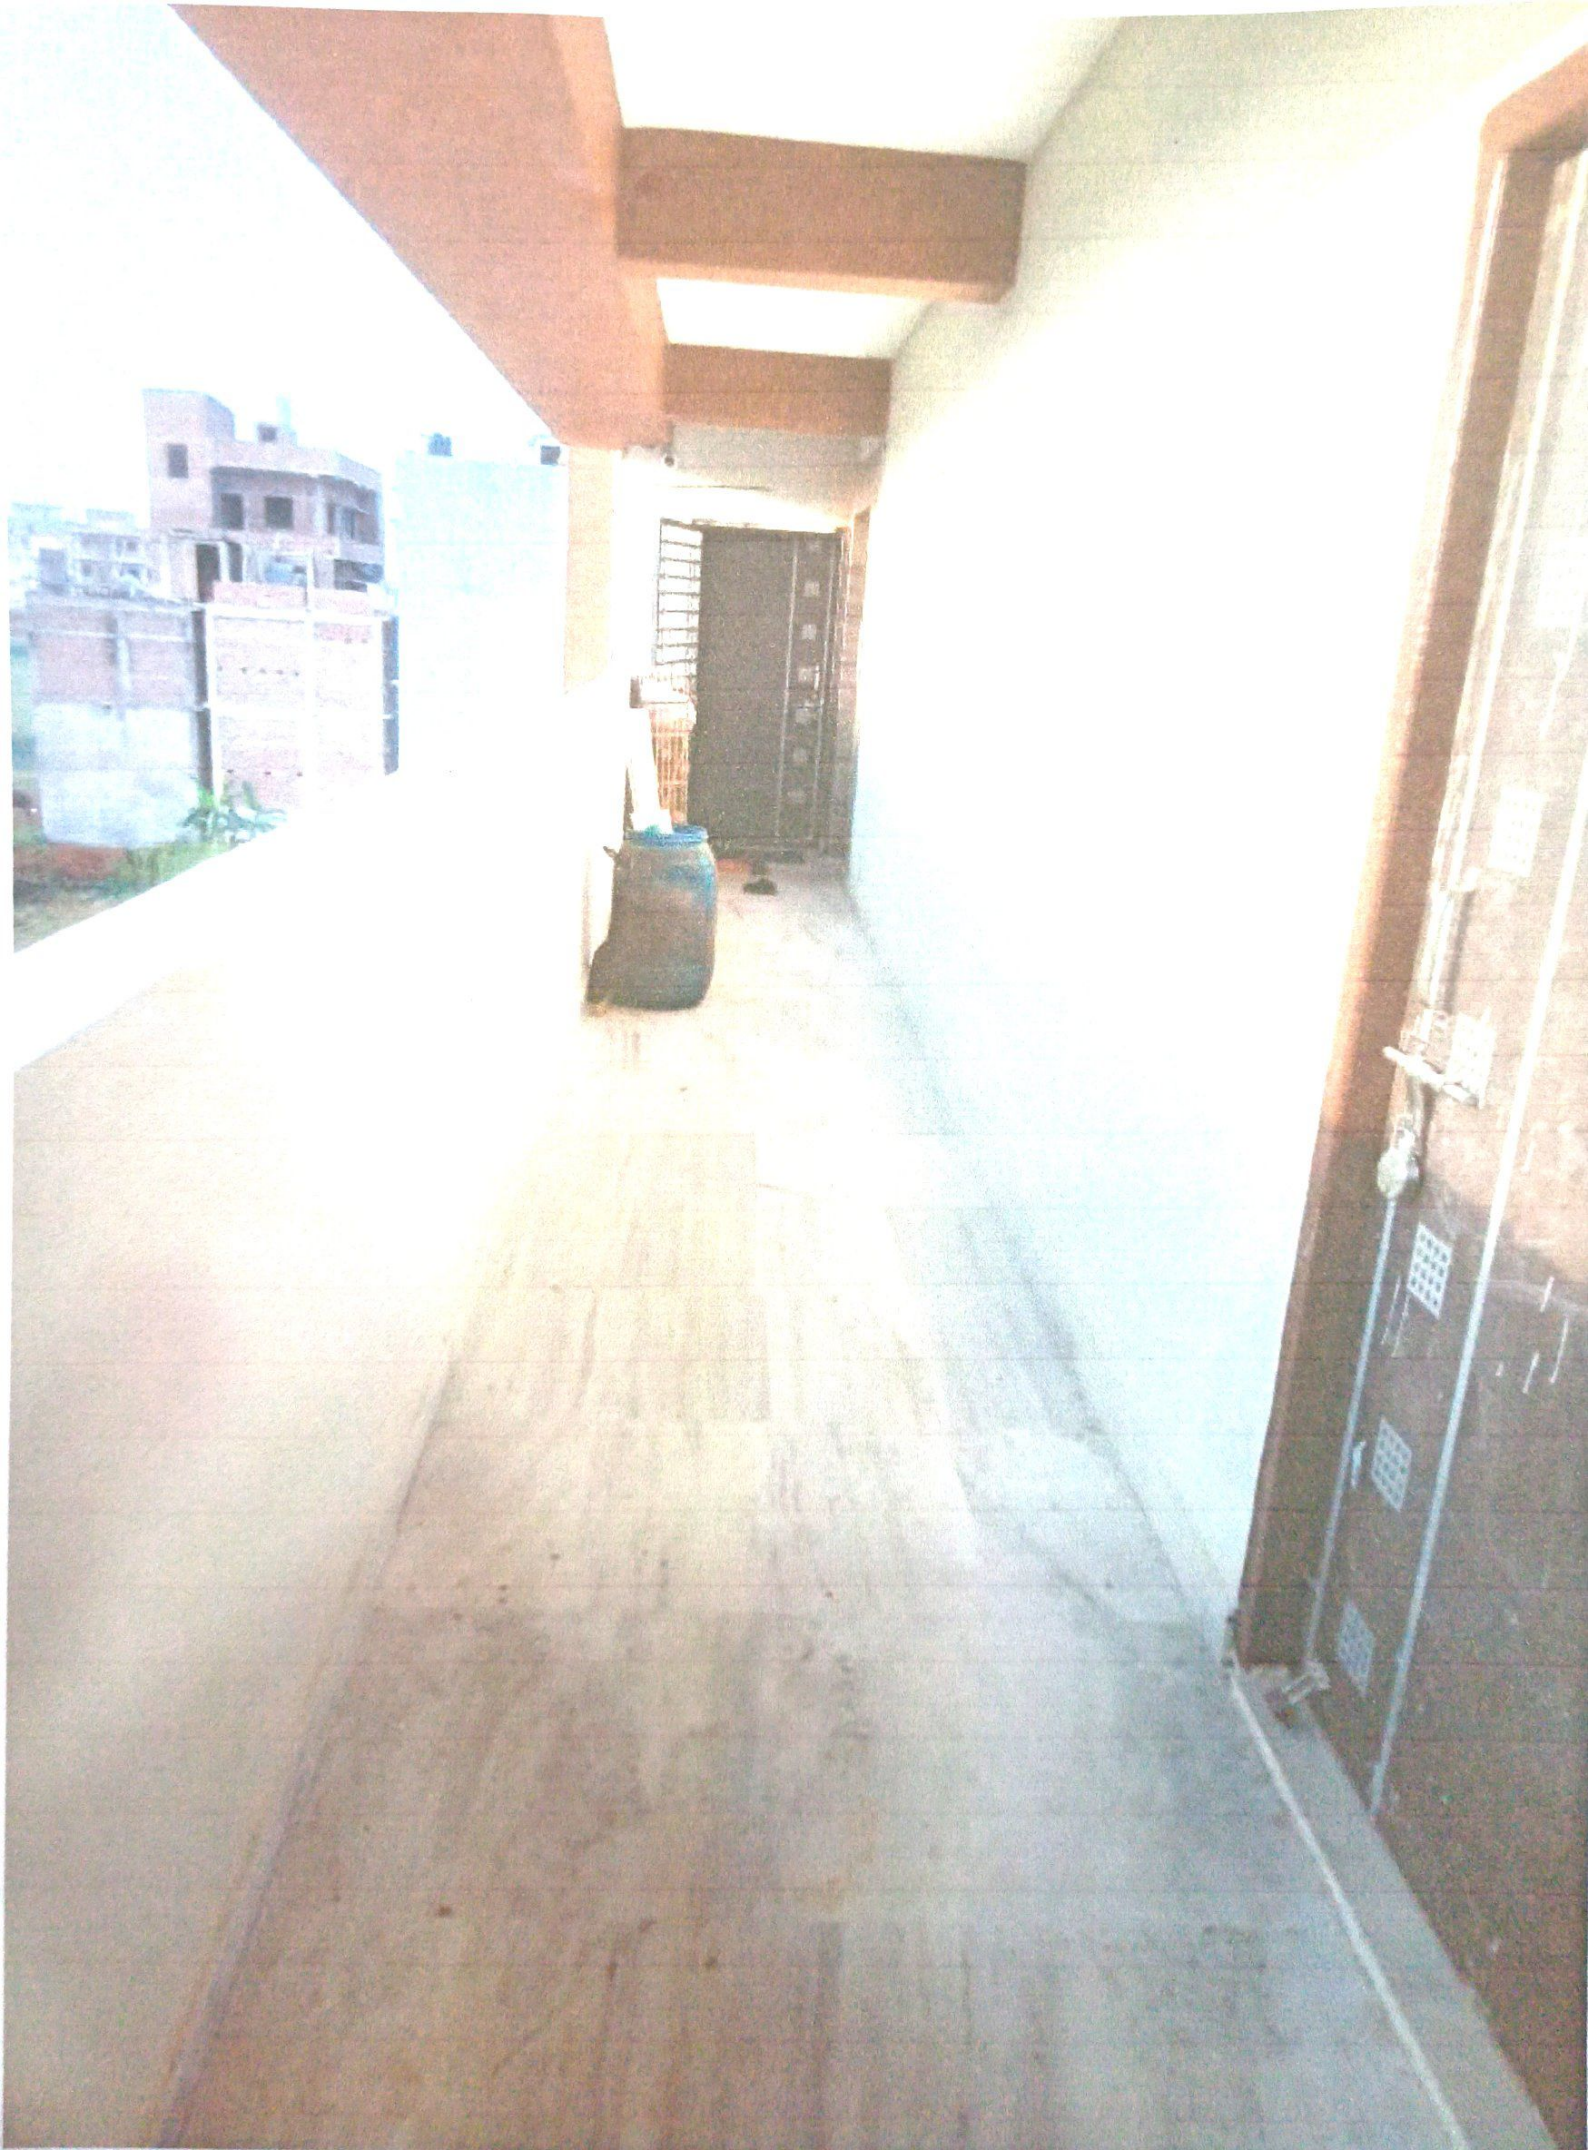



DRIVE WAY


DRIVE WAY





| AYURADHYA CONSTRUCTION PVT. LTD.   |                                            |                          |
|------------------------------------|--------------------------------------------|--------------------------|
| NAME OF PROJECT- ARADHYA RESIDENCY |                                            |                          |
| S/L                                | PERIOD OF REPORT                           | 01/04/2023 TO 30/06/2023 |
| 1                                  | Opening balance cash                       | 217                      |
| 2                                  | Opening balance bank                       | 4,45,545                 |
| 3                                  | Amount Collected during quarter            | 4,455                    |
| 4                                  | GST                                        | 4,62,000                 |
| 5                                  | Corporate Receipt                          | -                        |
| 6                                  | Other Income                               | 9,12,217                 |
|                                    | <b>TOTAL</b>                               | -                        |
|                                    | <b>Amount Expenses :</b>                   | -                        |
| 1                                  | Fixed Assets                               | -                        |
| 2                                  | Loan & Adv. And Liabilities                | -                        |
| 3                                  | Land Payment                               | -                        |
| 4                                  | Material Purchase Supplier payment         | 3,70,133                 |
| 5                                  | Labour & Contractor (Construction Expense) | 1,90,000                 |
| 6                                  | Salary and wages                           |                          |
| 7                                  | Site Maintenance/Direct Expenses           |                          |
| 8                                  | Office Maintenance/Indirect Expenses       |                          |
| 9                                  | Legal Exp                                  |                          |
| 10                                 | Customer cancellation+Refund               | -                        |
| 11                                 | Rera Expenses                              |                          |
| 12                                 | Tax deposit (EPF+ESIC+GST+TDS )            |                          |
| 13                                 | Corporate Payment                          | 50,000                   |
| 14                                 | Bank Charges                               | 2,090                    |
| 15                                 | Cash In Hand                               | -                        |
| 16                                 | Cash At Bank                               | 2,99,994                 |
|                                    | <b>TOTAL</b>                               | 9,12,217                 |

For ANKIT CHATURVEDI & ASSOCIATES  
CHARTERED ACCOUNTANTS



(Ankit Chaturvedi)

Proprietor

Membership. No.- 422506

Place : Patl

Date : 09/009/2023

UDIN for this document is 23422506BGRNKJ2053
