


PROJECT NAME – RAM NAGINA ENCLAVE

PROMOTER NAME – SCB ENGICON PRIVATE LIMITED

RERA REGISTRATION NO. BRERAP02626-2/75/R-1402/2022

QUARTERLY PROGRESS REPORT FOR RERA, BIHAR

Period – JULY TO SEP. 2023



FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending September of 2023

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP02626-2/75/R-1402/2022	Name of Project/Phase of Registered Project	RAM NAGINA ENCLAVE
Name of Promoter	SCB ENGICON PRIVATE LIMITED	Project Address	AT NEAR PETROL PUMP NEW BYPASS ALKAPURI LANE PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	05/12/2024		
Starting date of Project or Phase of the Project	31/05/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments -
	1. 1 BHK	-			1. Booked/Allotted - 04
	2. 2 BHK,	- 8	5536.00		2. Sold -NIL
	3. 3 BHK	- 16	15064.00	24	
	4. Shop	-			
	5. Bungalow	-			
	6. Plot etc.	-			

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 04
	24	2. Sold	- NIL

SCB ENGICON PVT. LTD.
Rejeen Khan
 DIRECTOR
 DIRECTOR

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of Further filing)

S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project

1. Building / Wing / Layout Number _____ (To be filled for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	5 th Slab 100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	15%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	5%

SCB ENGICON PVT. LTD.

Rejwan Rehan

DIRECTOR

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	5%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	10%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	Water Pump Installed - 100% 0%

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	NO		
2.	Water Supply	YES	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES		
4.	Storm Water Drains	NO		
5.	Landscaping & Tree Planting	NO		
6.	Street Lighting	NO		
7.	Community Buildings	NO		

SCB ENGICON PVT. LTD.

Rejwan R Khan

DIRECTOR

8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	NO		
10.	Water Conservation / Rain Water Harvesting	NO		
11.	Energy Management	NO		
12.	Fire Protection and Fire Safety Requirements	NO		
13.	Closed Parking	YES	0%	
14.	Open Parking	NO		
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO		
16.	Others (Option to Add More)			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			
8.	Water conservation/ Rain Water Harvesting			

SCB ENGICON PVT. LTD.

Rijew Rian

DIRECTOR

9.	Energy Management			
----	-------------------	--	--	--

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	2078102000005814
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Amount received during the Quarter	4,50,000=00
4.	Actual Cost Incurred during the Quarter	2,06,768=00
5.	Net amount at end of the Quarter	2,65,620=41
6.	Total expenditure on Project till date	1,05,26,933=01
7.	Cumulative fund Collected till the end of Quarter in question	1,40,52,202=00
8.	Cumulative expenditure done till the end of Quarter in question	2,65,620=41

IX. Details of Mortgage or Charge if any created

X. MISCELLANEOUS

SCB ENGICON PVT. LTD.

Rejwan Ryan

DIRECTOR

A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

SCB ENGICON PVT. LTD.



Rijew Rian

Name:

DIRECTOR

Date:

Project Name - Ram Nagina Enclave

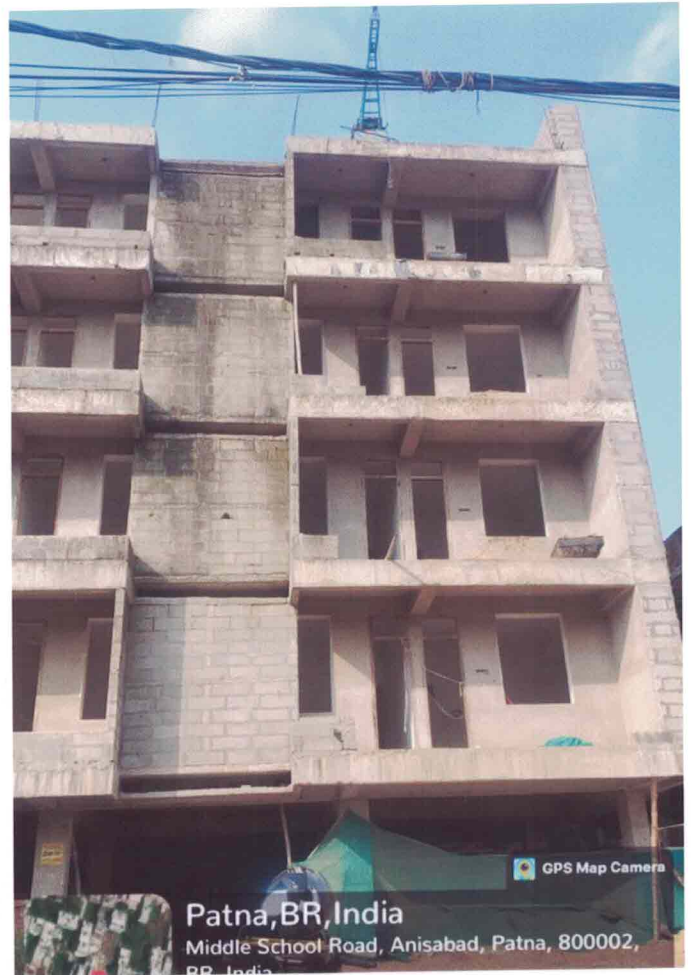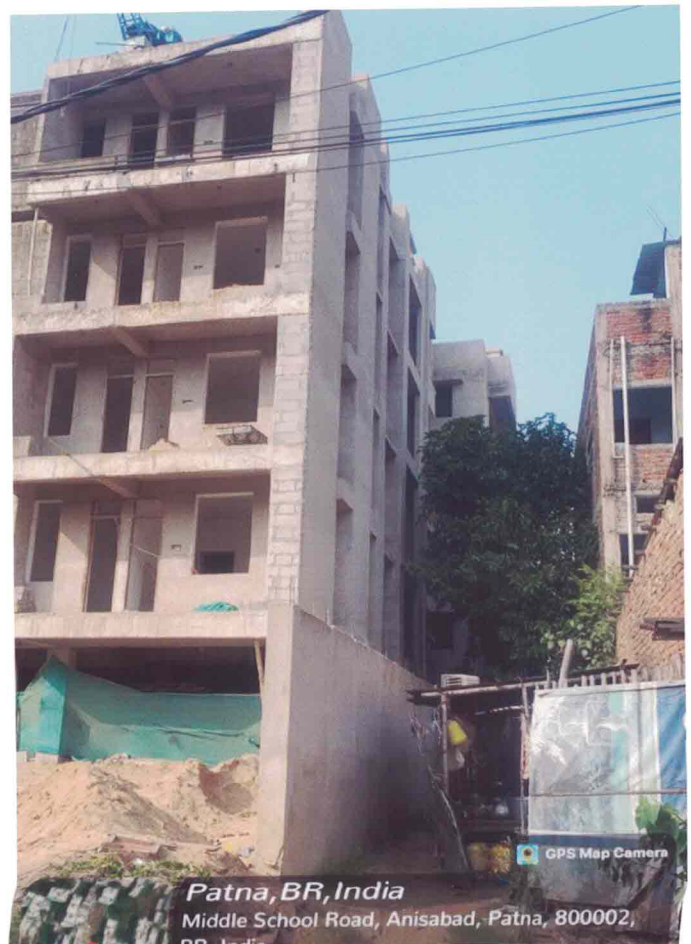

SCB ENGICON PVT. LTD.

Rajesh Ramesh

DIRECTOR
