



Apna Awas Construction Pvt. Ltd.

Registered Office : 001, Sundaram Enclave, Kitab Bhawan Lane
North S.K. Puri, Patna - 800 013

Ref...AAC/898.....

Date...13/10/2023.....

To,
The Chairman
Real Estate Regulatory Authority,
Bihar, Patna.

SUB : Submission of Quarterly Progress Report of Second Quarter (2023-24) of Project – "INDRAPRABHA", Anandpuri, Patna.

RERA Registration No – **BRERAP00243-14/998/R-751/2019.**

Dear Sir,

With reference to the above-mentioned subject and as per the requirement of quarterly progress reports compliance, we are hereby submitting the **QUARTERLY PROGRESS REPORT** for the **SECOND QUARTER (2023 – 2024)** for the project named "INDRAPRABHA" located at Anandpuri, West Boring Canal Road, Patna.

A detailed quarterly progress report of the project is attached along with this letter as Annexure - A.

Kindly acknowledge the receipt of the same.

Thanking you.

Sincerely yours



APNA AWAS CONSTRUCTION PVT. LTD.

DIRECTOR

FOR APNA AWAS CONSTRUCTION PVT LTD

FORM-7
[REGULATION-9]

Quarterly progress report for quarter ending March/June/sept/December of 2023-2024 (year)

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00243-14/998/R-751/2019	Name of Project/Phase of Registered Project	INDRAPRABHA
Name of Promoter	APNA AWAS CONSTRUCTION PVT LTD	Project Address	Anandpuri, Patna
Name of Co-promoter	-		
Project Registration is valid up to	14/06/2024		
Starting date of Project or Phase of the Project	20/05/2019		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	Residential	
Period of validity of map by the Competent Authority	Map sanctioned on 15/05/2019		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS				
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments
INDRAPRABHA (Developer's Share)	1. 3 BHK	- 11	991, 1006, 912, 1049, 1111, 1097, 1101, 910, 1066, 1113, 905	23
				Booked before this quarter - 7
				1. Booked/Allotted during this quarter - 0
				2. Sold during this quarter - 0

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Garages sold before this quarter	7
INDRAPRABHA (Developer's Share)	11	1. Booked/Allotted during this quarter	0
		2. Sold during this quarter	0

IV. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	NA			
2.	Fire N.O.C.	State Fire Officer, Bihar		15/09/2017	



3.	Water Supply Permission	Own Boring			
4.	NOC from Airport Authority of India	NA			
5.	Other Approval(s), if any, required for the Project.	-			

V. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/RajapurHasan-PRN-B+G+3/562/2017

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	80%
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	80%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	50%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	50%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	50%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	0%



	requirements as may be required to complete project as per Specifications in Agreement of Sale.	
	Any other activities.	

VI. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	0%	
2.	Water Supply	Own Boring		
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	30%	
4.	Storm Water Drains	Yes	0%	
5.	Landscaping & Tree Planting	Yes	0%	
6.	Street Lighting	Yes	0%	
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	Yes	10%	
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / Rain Water Harvesting	Yes	0%	
11.	Energy Management	No		
12.	Fire Protection and Fire Safety Requirements	Yes	0%	
13.	Closed Parking	Covered Parking		



14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	0%	
16.	Others (Option to Add More)			

VI A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUAL WORK DONE (As on date of certificate)	Details
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attached at the end of document
	2.	Rear Elevation	Attached at the end of document



	3.	Side Elevation	Attached at the end of document
(B)		Photograph of each floor	Attached at the end of document

VIII. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	2968002100010993
2.	Estimated Cost of the Project including land cost at the start of the Project	Rs.5,72,75,350/-
3.	Amount received during the Quarter	Rs. 61,90,476/-
4.	Actual Cost Incurred during the Quarter	Rs. 53,58,526/-
5.	Net amount at end of the Quarter	Rs. 0,15,450/-
6.	Total expenditure on Project till date	Rs. 4,72,88,094/-
7.	Cumulative fund collected till the end of Quarter in question	Rs. 4,98,68,112/-
8.	Cumulative expenditure done till the end of Quarter in question	Rs. 4,72,88,094/-

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED


X. MISCELLANEOUS		
A	List of Legal Cases (if any)	NONE
1.	Case No.	
2.	Name of Parties	
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

APNA AWAS CONSTRUCTION PVT. LTD.



DIRECTOR

Signature of Promoter

Name: Prabhat Kr. Singh

Date: 13/10/2023



N. R. Baid & Co.

Chartered Accountants

1E, 1st Floor, Block B, Ashiana Orchids,
Beni Babu's Garden, Rajendra Path,
Near Sarvoday Hotel, Patna - 800 001

Tel : 0612-2320716, Mob: 09334257406



email: info@nrbaid.com

CERTIFICATE NO.: CERT/NRBC/HO/2023-24/028

Date: 13/10/2023

CHARTERED ACCOUNTANTS FUND UTILIZATION CERTIFICATE

To

THE REAL ESTATE REGULATORY AUTHORITY

6th Floor, BSBCCCL Campus,
Hospital Road, Shastri Nagar
Patna-800023

Subject: Statutory Auditors Certificate for Quarter-2 of Financial Year 2023-24

Reference: RERA Regn. No. BRERAP00243-14/998/R-751/2019

Project- INDRA PRABHA

Sir,

We have been requested by M/s Apna Awas Construction Private Limited, CIN NO. U45200BR2001PTC009553, PAN: AAECA0832B to issue Statutory Auditors Certificate in accordance with Direction no. 1 of 2019 of the Authority.

In relation to the above, we confirm the following information:


Name of the Account Holder: Apna Awas Construction Private Limited

Designated Account Number: 2968002100010993

Bank Name: Punjab National Bank

IFSC Code: PUNB0296800

Branch Name: Punaichak



N. R. Baid & Co.

Chartered Accountants

1E, 1st Floor, Block B, Ashiana Orchids,
Beni Babu's Garden, Rajendra Path,
Near Sarvoday Hotel, Patna - 800 001

Tel : 0612-2320716, Mob: 09334257406



email: info@nrbaid.com

	Particulars	INR in Rs.
1	Opening Balance in the Designated Account as on 01/07/2023	5,26,365
2	Total Amount deposited in designated account during this Quarter (Fund Received from Customers as Booking Advance Rs. 65,00,000 including GST, deposited in designated account Rs. 46,00,000, rest amount deposited in other accounts of the Company Rs. 19,00,000 and Rs. 18,56,000 relating to other projects deposited in this account)	64,56,000
3	Total Amount paid during the 2 nd quarter up to 30/09/2023 from the said account (Total Amount utilised for the Project during the quarter is Rs. 43,98,508 rest utilised for Business Administrative Expenses and Others)	69,66,915
4	Closing Balance as on 30/09/2023 in this Bank	15,450

We certify that out of the funds deposited in Bank account Rs. 64,56,000 a sum of Rs. 69,66,915 has been paid from this account details of which are as under: -

Project Expenses	43,98,508
Administrative Expenses (Including taxes if any)	10,20,407
Other Payments	15,48,000
Total Payments	69,66,915

In this context it may be noted that the overall project expenditure in this quarter is Rs. 53,58,526. The excess amount (if any) booked under this project is on account of expenditure which has not been paid from this designated account. The excess amount (if any) paid from Bank towards Project Expenses includes payment to suppliers of goods or services of this project which were less paid during earlier period. At the end of this quarter, a sum of Rs. 15,450 remains closing balance in the said designated account. Expenditures incurred for the purpose for which the funds were received is verified with the vouchers produced before us at the time of issue of this certificate and that we have exercised the checks to see that the money was actually utilized for the purpose for which it was received.

Yours faithfully,

For N. R. Baid & Co.
Firm Registration No. 002104C
Chartered Accountants



UDIN: 23408360BGXPWB2308

(CA. A. Baid)

Partner

M. No. 408360

Note: All the figures in this certificate pertain to quarter-2 of FY 2023-24 only and are as per the designated Bank Account or Books of the Company.

Ar. Navratna Raghuvanshi

601, Signature Tower,
Kurjipul, Kurji,
Patna- 800010.

Mob :- 8863094547

LIC. NO : CA/2013/58586

Letter no. : 246/23-24

Date :- 10/10/2023

TO WHOMSOEVER IT MAY CONCERN


Sub : Construction work progress report in Quarter July – September, 2023-24 of the **Project – INDRAPRABHA, Anandpuri, Patna** (Mauza – Rajapur Hasan, Tauzi No – 5453, Thana No – 3, Khata No – 33, Survey Plot No (P) – 407). On the request of Client, visited the Site, INDRAPRABHA on 05/10/2023. It's a Residential Project located at (Mauza – Rajapur Hasan, Tauzi No – 5453, Thana No – 3, Khata No – 33, Survey Plot No (P) – 407).

RERA Registration No – BRERAP00243-14/998/R-751/2020.

Developer – Apna Awas Construction Pvt Ltd.

Current Construction Status on Site :

Brick work completed.
Internal plaster completed.
External plaster completed.
Plumbing and electrical work in progress.
P.O.P. and Putty work in progress.
Construction of Overhead Water Tank & Fire Tank in progress.
Construction of Septic Tank in progress.
Flooring work has started.


AR.NAVRATNA RAGHUVANSHI
(CA/2013/58586)

FRONT VIEW

INDRAPRBHA, ANNANDPURI



SIDE VIEW



 **GPS Map Camera**

Patna, Bihar, India

80, Anandpuri, Patna, Bihar 800001, India

Lat 25.621367°

Long 85.119526°

10/10/23 05:08 PM GMT +05:30

 Google

BACK VIEW



 **GPS Map Camera**

Patna, Bihar, India

J4C9+QWW, Anandpuri, Patna, Bihar 800001, India

Lat 25.621898°

Long 85.119731°

10/10/23 05:15 PM GMT +05:30



Google

GROUND FLOOR





1ST FLOOR

BATHROOM




LOBBY



FLATS 1ST FLOOR



2ND FLOOR LOBBY

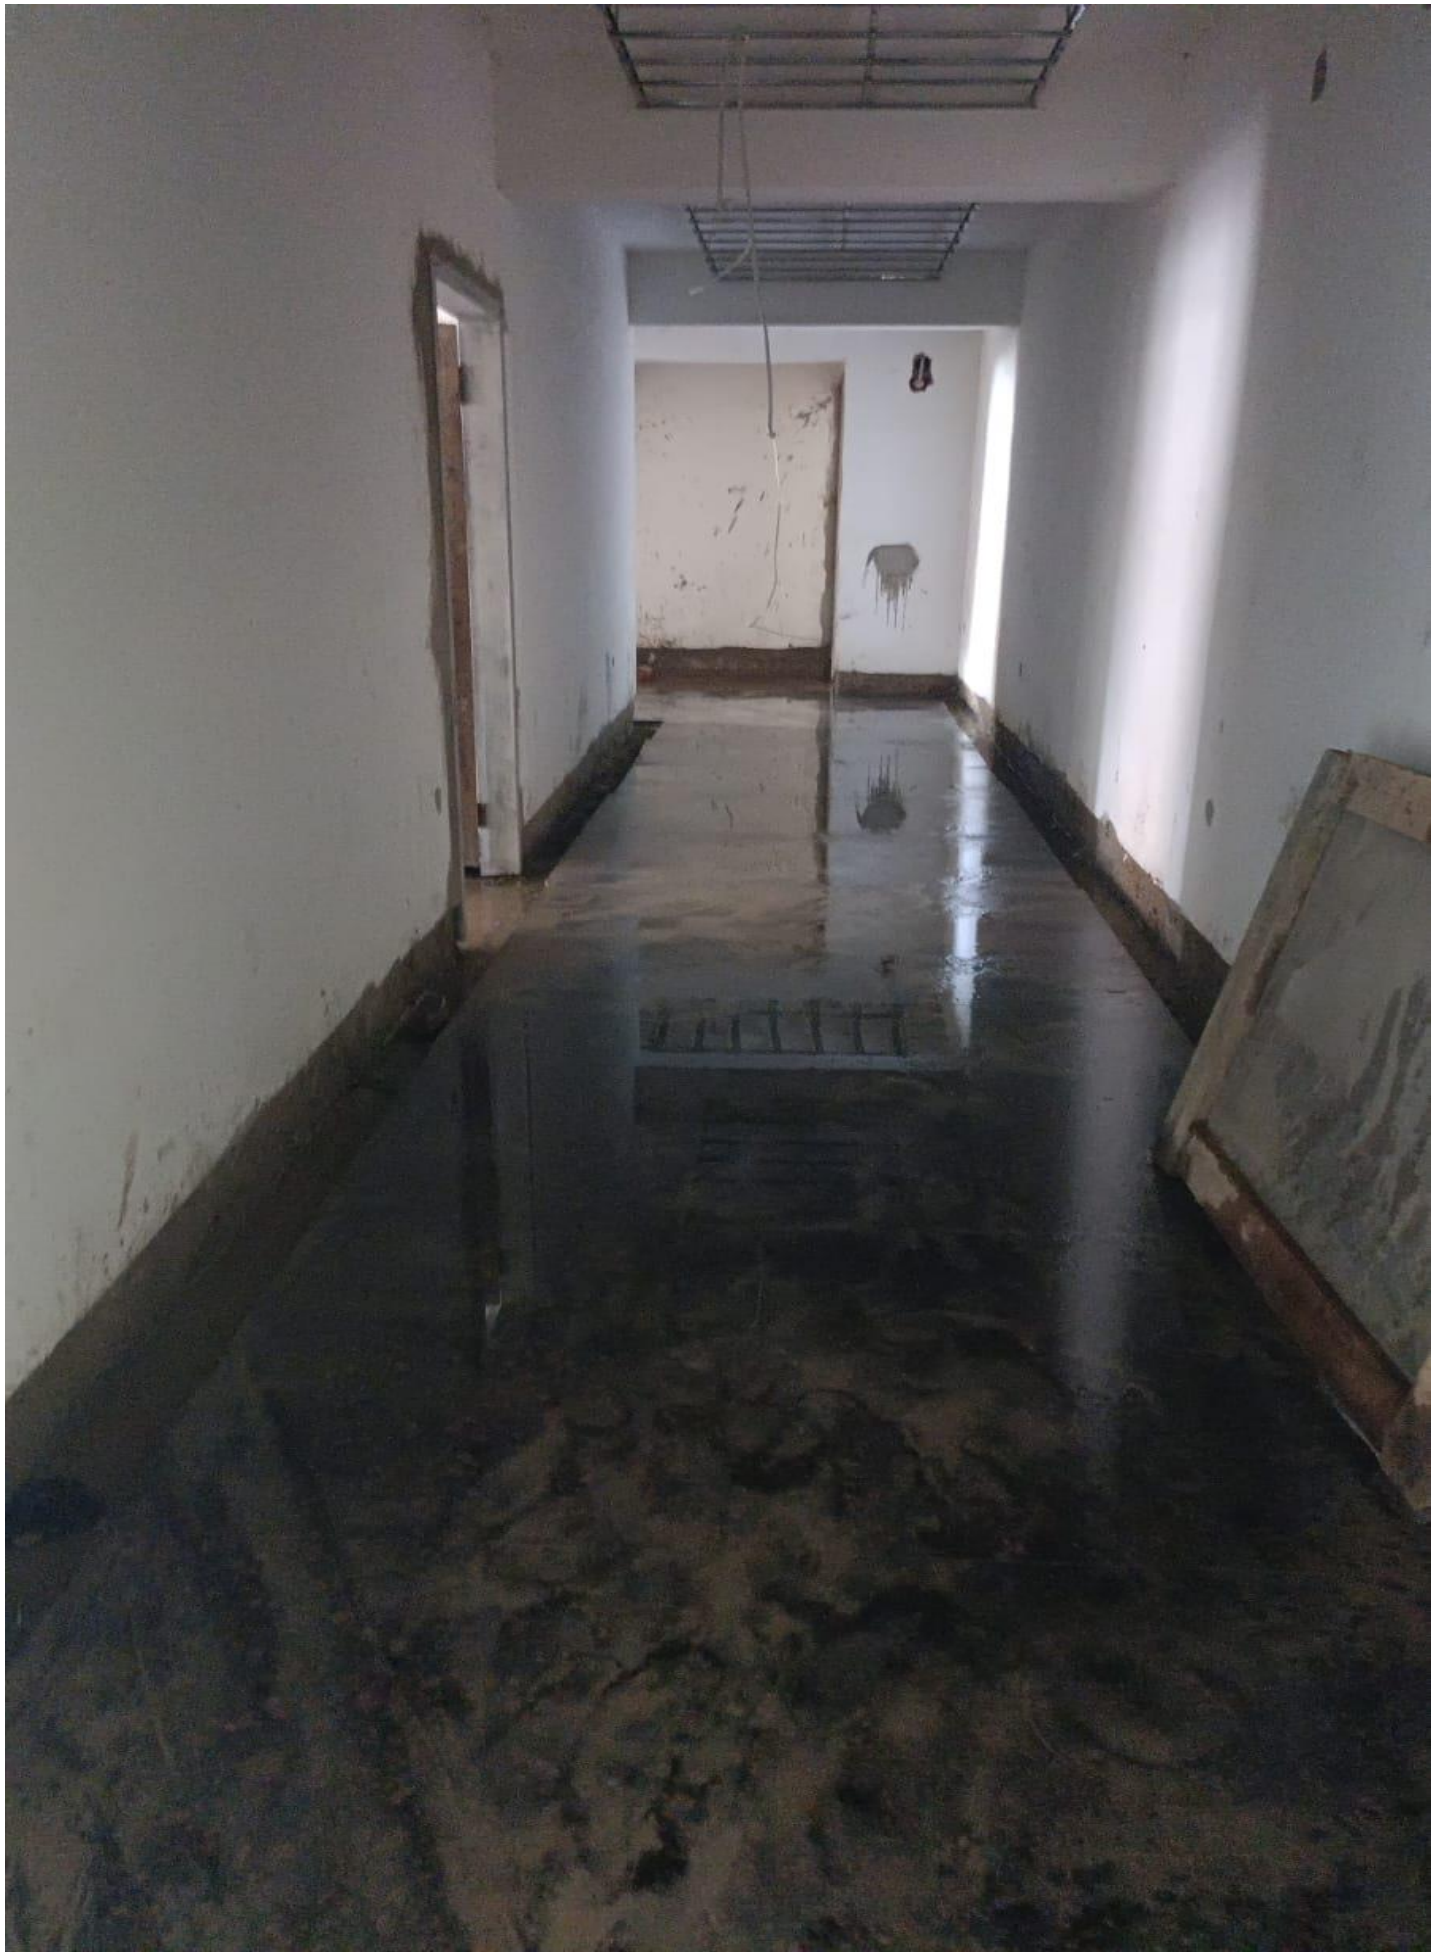

BATHROOM



FLATS 2ND FLOOR





3RD FLOOR

LOBBY



FLATS





TOP FLOOR



WATER TANK

