


FORM-7**[REGULATION-9]**Quarterly Progress Report for quarter ending 30TH SEPTEMBER of 2023**I. PARTICULARS OF PROJECT**

Project Registration Number	BRERAP00190-1/91/R-588	Name of Project/Phase of Registered Project	GREEN GHAR
Name of Promoter	GREEN GHAR INFRASTRUCTURE AND CONSTRUCTION PVT. LTD.	Project Address	DIGHARA RAMPUR SAH, MUZAFFARPUR, BIHAR
Name of Co-promoter	N.A		
Project Registration is valid up to	30-09-2023		
Starting date of Project or Phase of the Project	01-04-2016		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	10-09-2025 Zila Prasad-30, Muzaffarpur		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment / Building Type		Carpet Area (In Sq.ft.)	Total Number of sanctioned apartments	Total Number of Apartments -	
					Booked/ Allotted	Sold
Aleena 4BHK Duplex	4 BHK	19	963.18	02	19	11
AANCHAL DUPLEX	5 BHK	13	1437	02	13	04
SAGUN	4 BHK	06	1210.00	02	06	03
PUSHPAM DUPLEX	3 BHK	36	1189.00	02	35	17
KALASH ROW HOUSE	2 BHK	06	488.00	01	06	03
ALEENA SIMPLEX	2 BHK	12	481.59	01	12	11
A Block (2BHK-750)	2 BHK	16	604.00	05	16	00
B Block	2 BHK- "01"	04	603.76	05	01	00
B Block	2 BHK- "02"	04	507.62	05	04	00
B Block	2 BHK- "03"	04	538.00	05	02	00
B Block	2 BHK- "04"	04	274.76	05	04	00
B Block	2 BHK- "05"	04	557.47	05	02	00
B Block	2 BHK- "06"	04	397.7	05	03	00
B Block	2 BHK- "07"	04	598.14	05	04	00
B Block	2 BHK- "08"	04	306.24	05	02	00
Shop " A Block"	Shop	02	342.18	05	02	02
Shop " B Block"	Shop	02	317.38	05	00	00

Green Ghar Infrastructure & Cons. Pvt. Ltd.

 Managing Director

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 4
A Block	9	2. Sold	- 0
B Block	24		2

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filling)

S.NO.	Name of the Approval / N.O.C / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1	NOC for Environment	N.A			
2	Fire N.O.C	N.A			
3	Water Supply Permission	N.A			
4	NOC From Airport Authority of India	N.A			
5	Other Approval(s), if any, required for the project	N.A			


V. Construction Progress of the Project

1. Plan Case NO:- 940 & 896 Dated 17-09-2017 and Plan Case no:- 22/2022

Details Attached in **Table-A** Below;

VI. Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on 30.09.2023)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	Yes	85% done	On progress
2.	Water Supply	Yes	90% Done	On progress
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	85% Done	On progress
4.	Storm Water Drains	Yes	85% Done	On progress
5.	Landscaping & Tree Planting	Yes	85% Done	On progress
6.	Street Lighting	Yes	100%	Completed

Green Ghar Infrastructure & Com.

 Managing Director


(Q2/2023-24)

7.	Community Buildings	NO	NO	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	NO	
9.	Solid Waste Management & Disposal	NO	NO	
10	Water Conservation / Rain Water Harvesting	Yes	85% Done	On progress
11.	Energy Management	NO	NO	
12.	Fire Protection and Fire Safety Requirements	Yes	NO	
13.	Closed Parking	Yes	Yes	
14.	Open Parking	NO	NO	
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	100%	Completed
16.	Others (Option to Add More)	No	NO	

VIA EXTERNAL AND INTERNAL DEVELOPMENT WORK IN CASE OF PLOTTED DEVELOPMENT

1.	Internal Roads & Footpaths	NA	NA	
2	Water Supply	NA	NA	
3	Sewerage (Chamber, Line, Septic Tank, STP)	NA	NA	
4	Drains	NA	NA	
5	Parks, Land Scaping and Tree Planting	NA	NA	
6	Street Light	NA	NA	
7	Disposal of Sewage & sullage water	NA	NA	
8	Water conservation / Rain Water Harvesting	NA	NA	
9	Energy Management	NA	NA	

Green Ghar Infrastructure & Con. Pvt. Ltd.


 Managing Director


VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCKS) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Attached below
	2.	Side Elevation	Attached below
	3.	Rear Elevation	Attached below
(B)		Photograph of each Floors / Street	Attached below

VIII. Financial Progress of the Project (as per CA certificate 31-12-2022)

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	50200017966872
2.	Estimated Cost of the Project including land cost at the start of the Quarter	2156.75 (Lakhs)
3.	Amount received during the Quarter	36,67,872.00/-
4.	Actual Cost Incurred during the Quarter	33,15,151.78/-
5.	Net amount at end of the Quarter	3,52,720.89/-
6.	Total expenditure on Project till date	16,04,80,756.07/-
7.	Cumulative Fund Collected till the end of Quarter in question	No
8.	Cumulative expenditure done till the end of Quarter in question	No

Green Ghar Infrastructure & Con. Pvt. Ltd.


 Managing Director


(Q2/2023-24)

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	No
2.	Name of Parties	No
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	00
2.	Agreement for Sale	00
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Only A & B Block work is delay due to Natural Calamities' Next Quarter I will be completed my milestone		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Green Ghar Infrastructure & Cons. Pvt. Ltd.



Managing Director

Signature of Promoter

Name: SHAHID AHMED

Date : 30-09-2023

V. Construction Progress of the Project As on 30-09-2023

TABLE-A

Building / Wings No.	Excavation	Number of Plinth	Number of Podiums	Stilt Floor	Number of Slabs of Super Structure	Internal Walls, Internal Plaster, Floorings within Premises, Doors and Windows to each of the Premises	Sanitary Fittings within the Premises, Electrical Fitting within the Premises	Staircases, and Lobbies at each Floor level connecting Staircases, Overhead Water Tanks.	The external plumbing and external plaster, elevation, completion of terraces With IPS Flooring	Installation of water pumps, Electrical fittings to common Areas, electro, mechanical equipment, plinth protection, paving of areas appurtenant to Building, Compound Wall and all other requirements as may be required to obtain Occupation / Completion Certificate.
PS-13, RD-07	100%	100%	N.A	N.A	25%	5%	5%	5%	10%	40%
PS-14, RD-07	100%	100%	N.A	N.A	50%	5%	5%	5%	10%	40%
PS-15, RD-07	100%	100%	N.A	N.A	50%	5%	5%	5%	10%	40%
AC-10, RD-05	100%	100%	N.A	N.A	100%	100%	10%	100%	20%	40%
PW-01, RD-06	100%	100%	N.A	N.A	25%	10%	10%	10%	10%	40%
PW-02, RD-06	100%	100%	N.A	N.A	25%	10%	10%	10%	10%	40%
PE-02, RD-06	100%	100%	N.A	N.A	100%	25%	10%	10%	10%	40%
PW-04, RD-07	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
SN-02, NORTH	100%	100%	N.A	N.A	100%	100%	50%	50%	10%	40%
ALE-04, RD-08	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
ALW-03, RD-09	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
ALW-04, RD-09	100%	100%	N.A	N.A	100%	50%	20%	20%	10%	40%
ALE-01, RD-09	100%	100%	N.A	N.A	100%	100%	50%	50%	50%	40%
ALE-02, RD-09	100%	100%	N.A	N.A	100%	100%	50%	50%	50%	40%
ALE-03, RD-09	100%	100%	N.A	N.A	100%	100%	50%	50%	50%	40%
ALE-04, RD-09	100%	100%	N.A	N.A	100%	100%	50%	50%	50%	40%
AL-07, RD-10	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
AL-08, RD-10	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
AL-11, RD-11	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
AL-12, RD-11	100%	100%	N.A	N.A	50%	20%	20%	20%	20%	40%
KL-01, Rd-11	100%	100%	N.A	N.A	50%	20%	20%	20%	10%	40%
KL-02, Rd-11	100%	100%	N.A	N.A	50%	20%	20%	20%	10%	40%
KL-03, Rd-11	100%	100%	N.A	N.A	100%	100%	100%	100%	100%	100%
A Block	100%	100%	N.A	100%	100%	100%	95%	95%	95%	95%
B Block	100%	100%	N.A	20%	10%	10%	10%	10%	10%	10%


 ARCHITECT
 MD RASHID
 COA NO.-CA2018/108716

FORM No. 2
[Regulation 3]
ENGINEER'S CERTIFICATE
(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account- Project wise)

Date:- 30-09-2023

To,

GREEN GHAR INFRASTRUCTURE
AND CONSTRUCTION PVT. LTD.
Flat No:-403C, Ashiyana Plaza, Bhagwanpur Chowk,
Muzaffarpur, Bihar-842001

Subject : Certificate of Cost Incurred for Development of **GREEN GHAR** for Construction of **94** no. of building(s)/ Wing(s) of the **BRERAP00190-1/91/R-588** situated on the Plot bearing Khata No. 434, 410, 40, 229 Plot No. 2246, 2247, 2258, 2257, 2243(P), 2252(P), 2249(P), 2248(P), demarcated by its boundaries (**26.071616, 8** and **26.070848, 8** of the end points) of the land Area **14,791.13** Sq. Mtr. situated in Kanhauli Vishnudat Panchayat Area, Mauza:- Dighra Rampur Sah, Thana No:- 276, Block Mushari, division Muzaffarpur District Muzaffarpur, Bihar PIN 842001, admeasuring **15,477.02** sq.mts., area being developed by the Promoter **GREEN GHAR INFRASTRUCTURE AND CONSTRUCTION P LTD.**

Ref:
Sir,

Bihar RERA Registration Number **BRERAP00190-1/91/R-588**

I **Er. Ashok Kumar** have undertaken assignment of certifying Cost for the Subject Real Estate Project registered under RERA, Bihar of **94** no. of Building(s)/ Wing(s) of the Green Ghar Project situated on the plot bearing Khata No. 434, 410, 40, 229 Plot No. 2246, 2247, 2258, 2257, 2243(P), 2252(P), 2249(P), 2248(P) of Village Kanhauli Vishnudat Panchayat Area, Mauza:- Dighra Rampur Sah, Thana No:- 276, Block Mushari, division Muzaffarpur District Muzaffarpur, Bihar PIN 842001, admeasuring **15,477.02** sq.mts., area being developed by the Promoter **GREEN GHAR INFRASTRUCTURE AND CONSTRUCTION P LTD.**

1. Following technical professionals are appointed by Owner / Promoter: --

- (i) Mr. Ar. Md. Rashid as Architect;
- (ii) Mr. Er. Ashok Kumar as Structural Engineer
- (iii) Mr. Er. Gautam Kumar as Civil Engineer
- (iv) Mr. Ramesh Kumar as Site Supervisor

2. We have estimated the cost of the completion to obtain Occupation Certificate/ Completion Certificate, of the Civil, MEP and Allied works, of the building(s) of the project. Our estimated cost calculations are based on the Schedule of rates (Building Construction Department Schedule Rate) 1100 Per Sq. ft. and Drawings/plans made available to us for the project under reference by the Developer and Consultants and the quantity for the entire work as calculated by Quantity Surveyor* appointed by Developer/Engineer, and the assumption of the



cost of material, labour and other inputs made by developer, and the site inspection carried out by us.

3. We estimate Total Estimated Cost of completion of the building(s) of the aforesaid project under reference as **Rs. 2091.75 Lakhs**, (Total of Table A and B). The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for the purpose of obtaining occupation certificate / completion certificate for the building(s) from the **Muzaffarpur**, being the Planning Authority under whose jurisdiction the aforesaid project is being implemented.
4. The Estimated Cost Incurred till date is calculated at **Rs. 17,24,31,435.00/-** (Total of Table A and B). The amount of Estimated Cost incurred is calculated on the base of amount of Total Estimated Cost.
5. The Balance cost of Completion of the Civil, MEP and Allied works of the building(s) of the subject project to obtain Occupation Certificate / Completion Certificate from Muzaffarpur Rural Area Authority is estimated at **Rs.3,67,43,565.00/-** (Total of Table A and B).
6. I certify that the Cost of the Civil, MEP and allied work for the aforesaid Project as completed on the date of this certificate is as given in Table A and B below:

TABLE A

TABEL-A

Building / Wings No.	Total Estimated cost of the building	Cost incurred (Based on the Estimated cost)	Work done in % (As % of the estimated cost)	Balance Cost to be Incurred (Based on Estimated Cost)	Cost Incurred on Additional /Extra Items (Annexure-A)
	1	2	3	4	5
AC-03, RD-03	24,20,000.00	24,20,000.00	100%	-	
AC-02, RD-03	24,20,000.00	24,20,000.00	100%	-	
AC-01, RD-03	24,20,000.00	24,20,000.00	100%	-	
AC-06, RD-03	24,20,000.00	24,20,000.00	100%	-	
AC-04, RD-05	24,20,000.00	24,20,000.00	100%	-	
AC-05, RD-05	24,20,000.00	24,20,000.00	100%	-	
AC-06, RD-05	24,20,000.00	24,20,000.00	100%	-	
AC-09, RD-05	24,20,000.00	24,20,000.00	100%	-	
AC-08, RD-05	24,20,000.00	24,20,000.00	100%	-	



PW-03, RD-07	15,95,000.00	15,95,000.00	100%	-	
PS-01, RD-05	15,95,000.00	15,95,000.00	100%	-	
PS-02, RD-05	15,95,000.00	15,95,000.00	100%	-	
PS-15, RD-03	15,95,000.00	15,95,000.00	100%	-	
PES-01, RD-07	15,95,000.00	15,95,000.00	100%	-	
PES-02, RD-07	15,95,000.00	15,95,000.00	100%	-	
SG-01, RD-07	17,60,000.00	17,60,000.00	100%	-	
SG-02, RD-07	17,60,000.00	17,60,000.00	100%	-	
SN-01, RD-07	17,60,000.00	17,60,000.00	100%	-	
SG-06, RD-03	17,60,000.00	17,60,000.00	100%	-	
SG-07, RD-03	17,60,000.00	17,60,000.00	100%	-	
ALE-01, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALE-02, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALE-03, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-01, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-02, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-03, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-04, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-01, RD-09	17,60,000.00	17,60,000.00	100%	-	
ALW-02, RD-09	17,60,000.00	17,60,000.00	100%	-	
AL-01, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-02, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-03, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-04, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-05, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-06, RD-10	8,80,000.00	8,80,000.00	100%	-	



AC-07, RD-05	24,20,000.00	24,20,000.00	100%	-	
AC-01, RD-07	24,20,000.00	24,20,000.00	100%	-	
AC-06, RD-07	24,20,000.00	24,20,000.00	100%	-	
PS-01, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-02, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-03, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-04, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-05, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-06, RD-01	15,95,000.00	15,95,000.00	100%	-	
PS-07, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-08, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-09, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-10, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-11, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-12, RD-02	15,95,000.00	15,95,000.00	100%	-	
PS-01, RD-03	15,95,000.00	15,95,000.00	100%	-	
PS-02, RD-03	15,95,000.00	15,95,000.00	100%	-	
PS-03, RD-03	15,95,000.00	15,95,000.00	100%	-	
PS-04, RD-03	15,95,000.00	15,95,000.00	100%	-	
PS-05, RD-03	15,95,000.00	15,95,000.00	100%	-	
PS-01, RD-04	15,95,000.00	15,95,000.00	100%	-	
PS-02, RD-04	15,95,000.00	15,95,000.00	100%	-	
PE-01, RD-07	15,95,000.00	15,95,000.00	100%	-	
PS-01, RD-07	15,95,000.00	15,95,000.00	100%	-	
PW-01, RD-07	15,95,000.00	15,95,000.00	100%	-	
PW-02, RD-07	15,95,000.00	15,95,000.00	100%	-	



AL-09, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-10, RD-10	8,80,000.00	8,80,000.00	100%	-	
KL-06, RD-11	7,15,000.00	7,15,000.00	100%	-	
KL-05, RD-11	7,15,000.00	7,15,000.00	100%	-	
KL-04, RD-11	7,15,000.00	7,15,000.00	100%	-	
ALE-01, RD-07	17,60,000.00	17,60,000.00	100%	-	
ALE-02, RD-07	17,60,000.00	17,60,000.00	100%	-	
ALE-03, RD-07	17,60,000.00	17,60,000.00	100%	-	
PS-13, RD-07	15,95,000.00	3,98,750.00	25%	11,96,250.00	
PS-14, RD-07	15,95,000.00	3,98,750.00	25%	11,96,250.00	
PS-15, RD-07	15,95,000.00	3,98,750.00	25%	11,96,250.00	
AC-10, RD-05	24,20,000.00	16,94,000.00	70%	7,26,000.00	
PW-01, RD-06	15,95,000.00	3,19,000.00	20%	12,76,000.00	
PW-02, RD-06	15,95,000.00	3,19,000.00	20%	12,76,000.00	
PE-02, RD-06	15,95,000.00	7,97,500.00	50%	7,97,500.00	
PW-04, RD-07	15,95,000.00	15,95,000.00	100%	-	
SN-02, NORTH	17,60,000.00	13,20,000.00	75%	4,40,000.00	
ALE-04, RD-08	17,60,000.00	17,60,000.00	100%	-	
ALW-03, RD-09	17,60,000.00	17,60,000.00	100%	-	
ALW-04, RD-09	17,60,000.00	10,56,000.00	60%	7,04,000.00	
ALE-01, RD-09	17,60,000.00	13,20,000.00	75%	4,40,000.00	
ALE-02, RD-09	17,60,000.00	11,44,000.00	65%	6,16,000.00	
ALE-03, RD-09	17,60,000.00	17,60,000.00	100%	-	
ALE-04, RD-09	17,60,000.00	10,56,000.00	60%	7,04,000.00	
AL-07, RD-10	8,80,000.00	8,80,000.00	100%	-	
AL-08, RD-10	8,80,000.00	8,80,000.00	100%	-	



AL-11, RD-11	8,80,000.00	8,80,000.00	100%	-	
AL-12, RD-11	8,80,000.00	5,28,000.00	60%	3,52,000.00	
KL-01, Rd-11	7,15,000.00	2,86,000.00	40%	4,29,000.00	
KL-02, Rd-11	7,15,000.00	2,86,000.00	40%	4,29,000.00	
KL-03, Rd-11	7,15,000.00	7,15,000.00	100%	-	
A Block	1,48,50,000.00	1,41,07,500.00	95%	7,42,500.00	
B Block	2,69,75,300.00	67,43,825.00	25%	2,02,31,475.00	
GRAND TOTAL	18,95,55,300.00	15,68,03,075.00	83%	3,27,52,225.00	

TABLE B

(To be prepared for the entire registered phase of the Real Estate Project)

Sr. No.	Particulars	Amounts
1	Total Estimated cost of the Internal and External Development Works including amenities and Facilities in the layout as on 30-09-2023 date of Registration is Rs. 1,96,19,700.00/-	1,96,19,700.00/-
2	Cost incurred as on 30.09.2023 (Based on the Estimated cost).	1,56,28,360.00/-
3	Work done in Percentage (As Percentage of the estimated cost).	80%
4	Balance Cost to be Incurred (Based on Estimated Cost).	39,91,340.00/-
5	Cost Incurred on Additional /Extra Items as on N.A not included in the Estimated Cost (Annexure A).	N.A

Yours Faithfully,



Er. Ashok Kumar
MMC, Reg No:- C-06/15

*** Note:**

1. The scope of work is to complete entire Real Estate Project as per drawings approved from time to time so as to obtain Occupancy Certificate/Completion Certificate.
2. (*) Quantity survey can be done by office of Engineer or can be done by an independent Quantity Surveyor, whose certificate of quantity calculated can be relied upon by the Engineer. In case of independent Quantity Surveyor being appointed by Developer, the name has to be mentioned at the place marked (*) and in case quantity are being calculated by office of Engineer, the name of the person in the office of Engineer, who is responsible for the quantity calculated should be mentioned at the place marked (*).
3. The estimated cost includes all labour, material, equipment and machinery required to carry out entire work.
4. As this is an estimated cost, any deviation in quantity required for development of the Real Estate Project will result in amendment of the cost incurred / to be incurred.
5. All components of work with specifications are indicative and not exhaustive.

Annexure A

List of Extra/Additional Items executed with Cost
(Which were not part of the original Estimate of Total Cost)



Dighra Patti, Bihar, India

3CFC+373, Dighra Patti, Bihar 843126, India

Lat 26.071035°

Long 85.419874°

15/10/23 02:03 PM GMT +05:30



GPS Map Camera

Dighra Rampur Shah, Bihar, India

3CCC+FCF, Dighra Rampur Shah, Bihar 843126, India

Lat 26.071001°

Long 85.420566°

15/10/23 02:01 PM GMT +05:30





GPS Map Camera

Dighra Rampur Shah, Bihar, India

3CCC+FCF, Dighra Rampur Shah, Bihar 843126, India

Lat 26.071333°

Long 85.42062°

15/10/23 02:00 PM GMT +05:30



Google



GPS Map Camera




Dighra Rampur Shah, Bihar, India

3CCC+FCF, Dighra Rampur Shah, Bihar 843126, India

Lat 26.070971°

Long 85.420862°

15/10/23 01:58 PM GMT +05:30

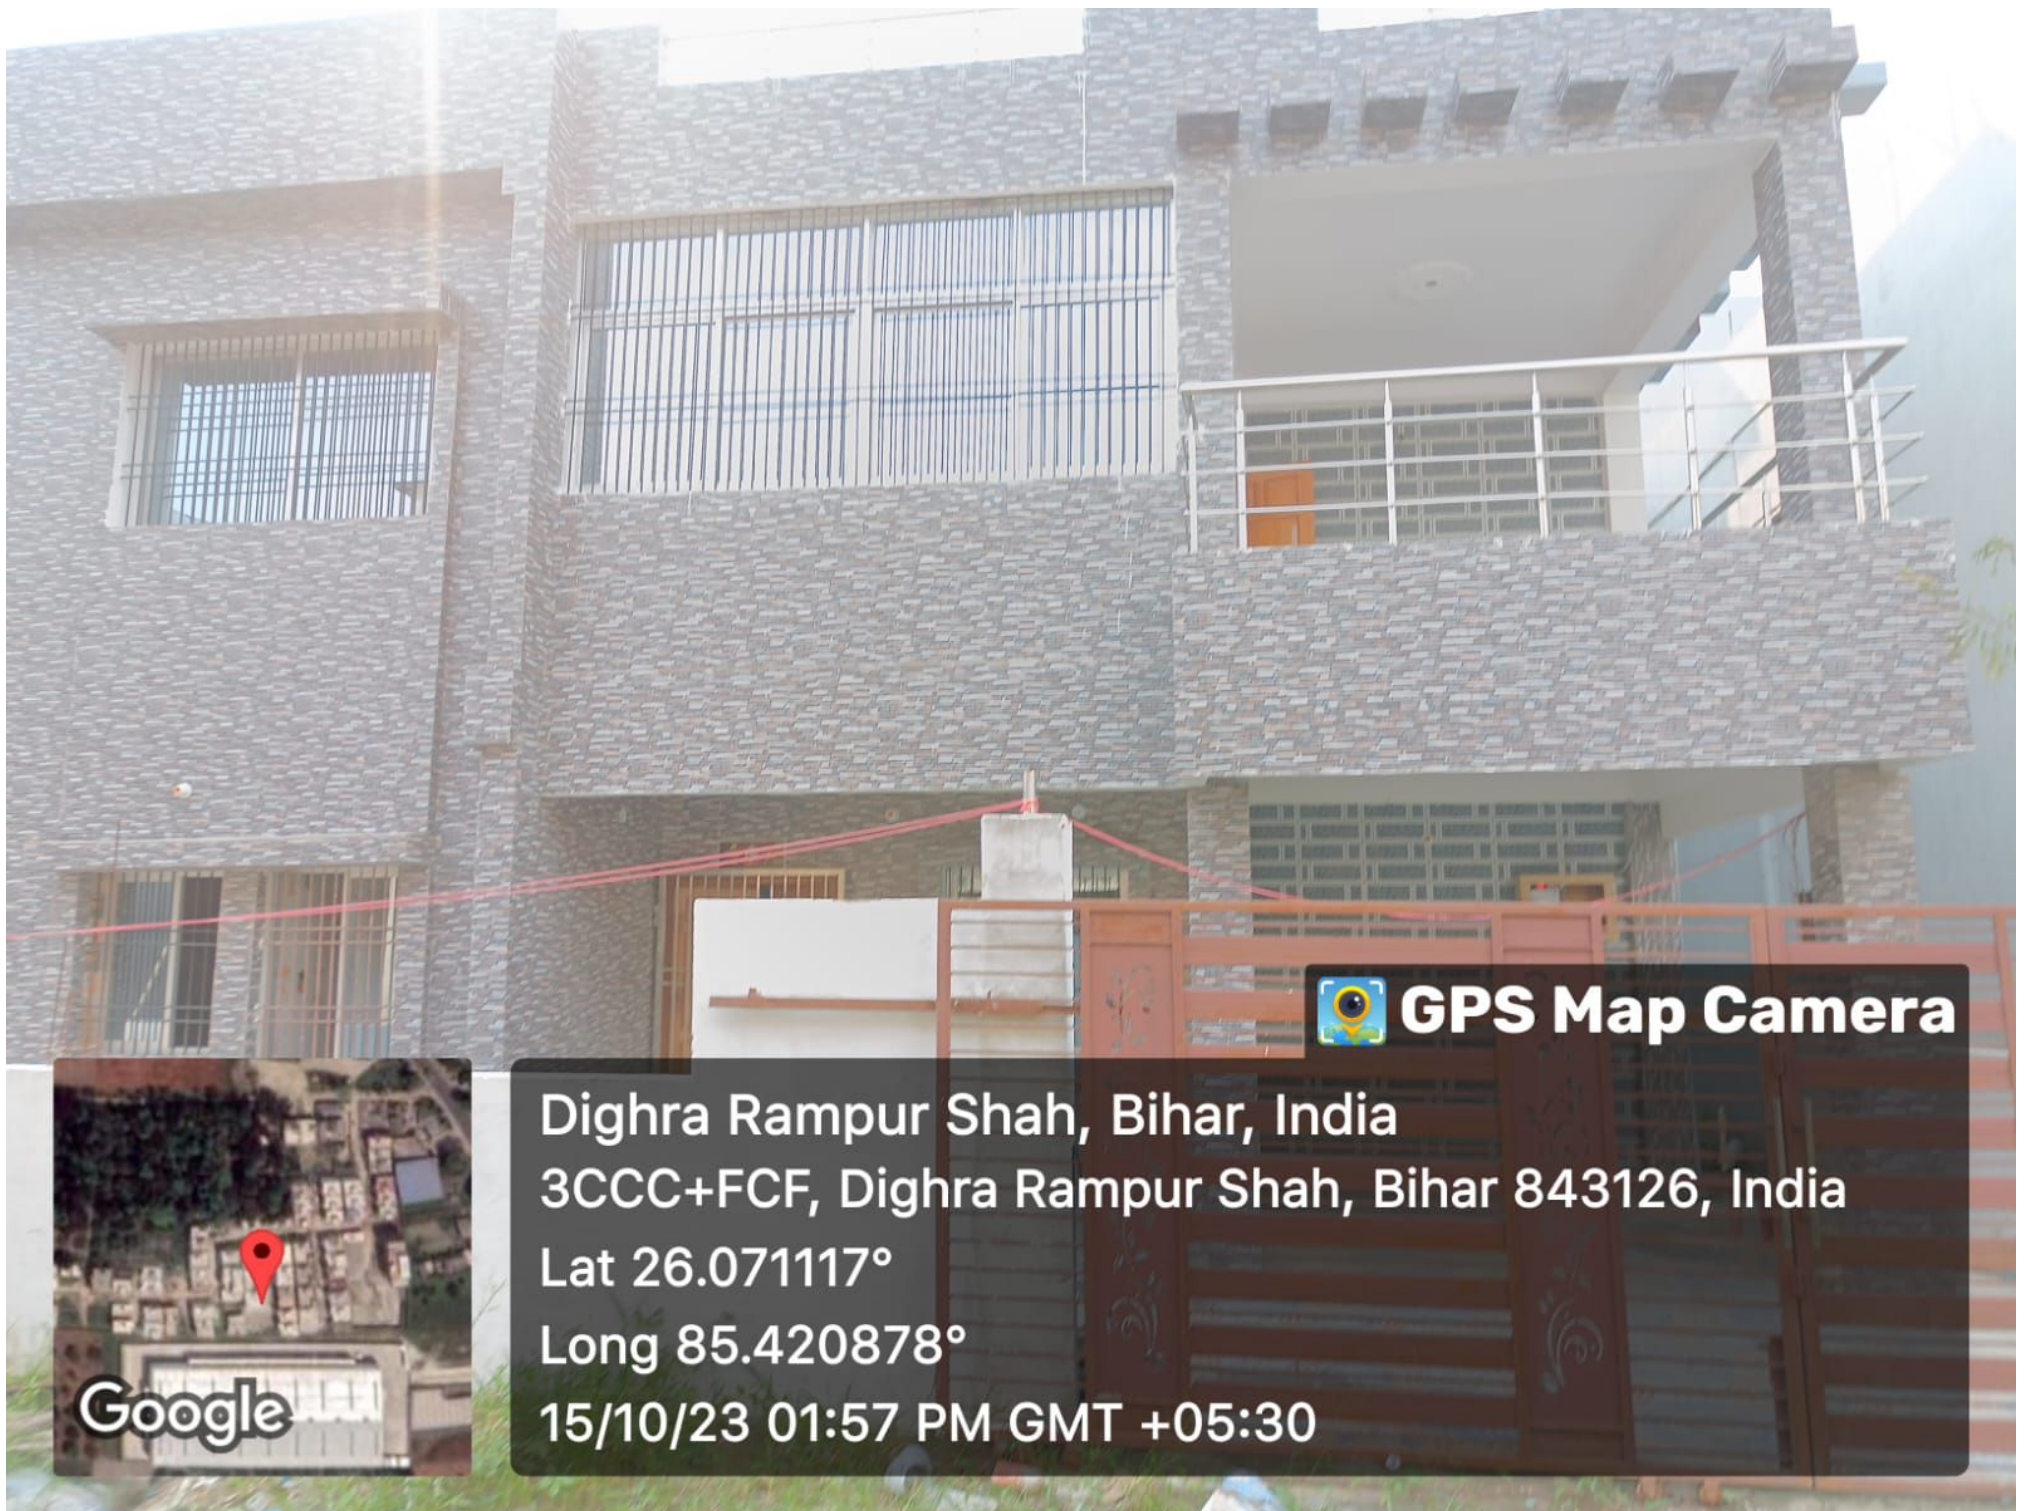

GPS Map Camera

Dighra Rampur Shah, Bihar, India

3CCC+FCF, Dighra Rampur Shah, Bihar 843126, India

Lat 26.071117°


Long 85.420878°

15/10/23 01:57 PM GMT +05:30





GPS Map Camera

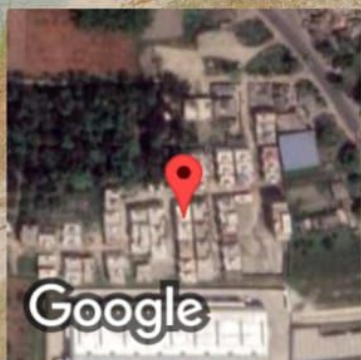

Dighra Rampur Shah, Bihar, India

3CCC+HC3, Dighra Rampur Shah, Bihar 843126, India

Lat 26.071343°

Long 85.420996°

15/10/23 01:56 PM GMT +05:30



 **GPS Map Camera**

Dighra Rampur Shah, Bihar, India

3CCC+HC3, Dighra Rampur Shah, Bihar 843126, India

Lat 26.071298°

Long 85.421169°

15/10/23 01:54 PM GMT +05:30

Google



 **GPS Map Camera**

Dighra Rampur Shah, Bihar, India

3CCC+JC5, Dighra Rampur Shah, Bihar 843126, India

Lat 26.07147°

Long 85.421068°

15/10/23 01:53 PM GMT +05:30





 **GPS Map Camera**

Dighra Rampur Shah, Bihar, India

3CCC+FCF, Dighra Rampur Shah, Bihar 843126, India

Lat 26.07119°

Long 85.4212°

15/10/23 02:25 PM GMT +05:30

