

**FORM-7**  
**[REGULATION-9]**

Quarterly Progress Report for quarter ending Jul-Sep 2023 (Year)

**I. PARTICULARS OF PROJECT**

|                                                      |                                                                                                                                                           |
|------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|
| Project Registration Number                          | BRERAP00554-1/486/R-501/2019                                                                                                                              |
| Name of Project/Phase of Registered Project          | SINGH MANSION                                                                                                                                             |
| Name of Promoter                                     | MILANDEEP CONSTRUCTION PRIVATE LIMITED                                                                                                                    |
| Project Address                                      | MAUZA- ABDULLAHCHAK, SURVEY THANA- PHULWARI, PLOT NO.- 456, PRESENT THANA- GOPALPUR, SUB REGISTRY OFFICE PHULWARI SHARIF DIST. REG. OFFICE + DIST.- PATNA |
| Name of Co-promoter                                  | NA                                                                                                                                                        |
| Project Registration is valid up to                  | 22/08/2023                                                                                                                                                |
| Starting date of Project or Phase of the Project     | 11/03/2019                                                                                                                                                |
| Type of Project or Phase of the Project              | Mixed Development(residential and commercial)                                                                                                             |
| Period of validity of map by the Competent Authority | Three Years from the date of passing of MAP                                                                                                               |

**II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS**

| Building/Block Number | Apartment Type | Carpet Area (In Sq. ft.) | Total Number of sanctioned apartments | Total Number of apartments        |
|-----------------------|----------------|--------------------------|---------------------------------------|-----------------------------------|
| Singh Mansion         | 3 BHK          | 861.72                   | 4                                     | 1. Booked- 03<br>2. Cancelled- 00 |
| Singh Mansion         | 3 BHK          | 804.70                   | 4                                     |                                   |
| Singh Mansion         | SHOP           | 274                      | 1                                     |                                   |
| Singh Mansion         | SHOP           | 252                      | 1                                     |                                   |
| Singh Mansion         | SHOP           | 216                      | 1                                     |                                   |
| Singh Mansion         | SHOP           | 171                      | 1                                     |                                   |

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Heena Chaudhary*  
Director

**II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS**

| Building/Block Number | Apartment Type | Carpet Area (In Sq. ft.) | Total Number of sanctioned apartments | Total Number of apartments |
|-----------------------|----------------|--------------------------|---------------------------------------|----------------------------|
| Singh Mansion         | SHOP           | 150                      | 1                                     |                            |

**III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES**

| Building / Block Number | Total Number of Sanctioned Garages | Total Number of Garages:          |  |
|-------------------------|------------------------------------|-----------------------------------|--|
| Singh Mansion           | No Garages available               | 1. Booked/Allotted -<br>2. Sold - |  |

**IV. DETAILS OF BUILDING APPROVALS**

(If already filed along with Registration Application, then there is no need of further filing)

| S. No. | Name of the Approval / N.O.C./ Permission / Certificate | Issuing Authority | Applied Date | Issuance Date | Enclosed as Annexure No. |
|--------|---------------------------------------------------------|-------------------|--------------|---------------|--------------------------|
| 1.     | NOC for Environment                                     |                   |              |               |                          |
| 2.     | Fire N.O.C.                                             |                   |              |               |                          |
| 4.     | NOC from Airport Authority of India                     |                   |              |               |                          |
| 5.     | Other Approval(s), if any, required for the Project.    |                   |              |               |                          |

**V. Construction Progress of the Project****1. Building / Wing / Layout Number- SINGH MANSION (To beaded for each Building / Wing)**

| S. No.<br>(1) | Tasks / Activity<br>(2) | Percentage of Actual Work Done (As on date of the Certificate)<br>(3) |
|---------------|-------------------------|-----------------------------------------------------------------------|
| 1.            | Excavation (if any)     | 100%                                                                  |
| 2.            | Basements (if any)      | 90%                                                                   |

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Heilan Chayda*  
Director

Page 2 of 9

|     |                                                                                                                                                                                                                                                                                                                                                                                                                                               |      |
|-----|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|
| 3.  | Podiums (if any)                                                                                                                                                                                                                                                                                                                                                                                                                              | NA   |
| 4.  | Plinth                                                                                                                                                                                                                                                                                                                                                                                                                                        | 100% |
| 5.  | Stilt Floor                                                                                                                                                                                                                                                                                                                                                                                                                                   | NA   |
| 6.  | Slabs of Super Structure                                                                                                                                                                                                                                                                                                                                                                                                                      | 45%  |
| 7.  | Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.                                                                                                                                                                                                                                                                                                                                                        | 10%  |
| 8.  | Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises                                                                                                                                                                                                                                                                                                                                                      | 0%   |
| 9.  | Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.                                                                                                                                                                                                                                                                                                                                                | 14%  |
| 10. | External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.                                                                                                                                                                                                                                                                                                                            | 0%   |
| 11. | Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.<br><br>Any other activities. | 11%  |

**VI. Amenities and Common Area and External Infrastructure Development Works**

| S. No. | Common Areas and Facilities | Proposed (Yes/No) | Percentage of actual Work Done (As on date of the Certificate) | Details |
|--------|-----------------------------|-------------------|----------------------------------------------------------------|---------|
|        |                             |                   |                                                                |         |

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Seelan Chayler*  
Director

Page 3 of 9

| (1) | (2)                                                   | (3) | (4) | (5)               |
|-----|-------------------------------------------------------|-----|-----|-------------------|
| 1.  | Internal Roads & Footpaths                            | No  |     |                   |
| 2.  | Water Supply                                          | Yes | 50% | Pump is Installed |
| 3.  | Sewerage (Chamber, Line, Septic Tank, STP)            | Yes | 0%  |                   |
| 4.  | Storm Water Drains                                    | No  |     |                   |
| 5.  | Landscaping & Tree Planting                           | No  |     |                   |
| 6.  | Street Lighting                                       | No  |     |                   |
| 7.  | Community Buildings                                   | No  |     |                   |
| 8.  | Treatment and Disposal of Sewage and Sullage Water    | No  |     |                   |
| 9.  | Solid Waste Management & Disposal                     | No  |     |                   |
| 10. | Water Conservation / Rain Water Harvesting            | No  |     |                   |
| 11. | Energy Management                                     | No  |     |                   |
| 12. | Fire Protection and Fire Safety Requirements          | Yes | 0%  |                   |
| 13. | Closed Parking                                        | Yes | 0%  |                   |
| 14. | Open Parking                                          | No  |     |                   |
| 15. | Electrical Meter Room, Sub-Station, Receiving Station | No  |     |                   |
| 16. | Others (Option to Add More)                           | No  |     |                   |

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Milan Chaudhary*  
Director

| VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT |        |                                  |
|-------------------------------------------------------------------|--------|----------------------------------|
| (A)                                                               | S. No. | Particulars                      |
|                                                                   | 1.     | Front Elevation.- Attached Below |
|                                                                   | 2.     | Rear Elevation.- Attached Below  |
|                                                                   | 3.     | Side Elevation.- Attached Below  |
| (B)                                                               |        | Photograph of each floor         |

| VIII. Financial Progress of the Project |                                                                               |                  |
|-----------------------------------------|-------------------------------------------------------------------------------|------------------|
| Sl. No.                                 | Particulars                                                                   | Amount (in Rs.)  |
| 1                                       | Project Account No.                                                           | 622401010050443  |
| 2                                       | Estimated Cost of the Project including land cost at the start of the Quarter | 2,69,15,478.00/- |
| 3                                       | Amount received during the Quarter                                            | 0.00/-           |
| 4                                       | Actual Cost Incurred during the Quarter                                       | 19,70,688.00/-   |
| 5                                       | Net amount at end of the Quarter                                              |                  |
|                                         | 622401010050443                                                               | 0.00/-           |
|                                         | 622401010050627                                                               | 16,03,870.00/-   |
|                                         | 622401010050628                                                               | 14,750.00/-      |
| 6                                       | Total expenditure on Project till date                                        | 2,04,67,032.00/- |
| 7                                       | Cumulative fund collected till the end of Quarter in question                 | 42,85,750.00/-   |
| 8                                       | Cumulative expenditure done till the end of Quarter in question               | 2,04,67,032.00/- |

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Milandeep Chaudhary*  
Director

**IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED**


|  |
|--|
|  |
|  |
|  |

**X. MISCELLANEOUS**

|    |                                            |    |
|----|--------------------------------------------|----|
| A  | List of Legal Cases (if any)               |    |
| 1. | Case No.                                   | NA |
| 2. | Name of Parties                            | NA |
| B  | Sale/Agreement for Sale during the Quarter |    |
| 1. | Sale Deed                                  |    |
| 2. | Agreement for Sale                         | 3  |

**XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART**

Weather the project in progress is as per time schedule or lagging behind?

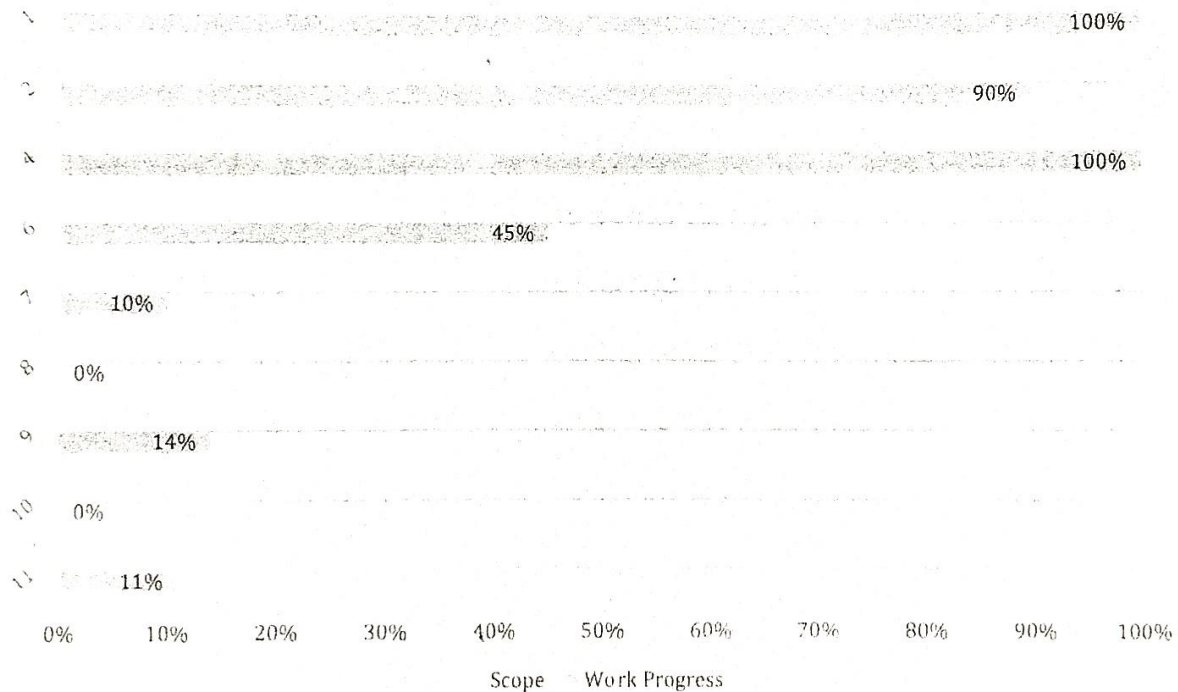**PROGRESS CHART**


MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Heena Chaudhary*  
Director

Page 6 of 9

Project Site Photographs

Front Elevation

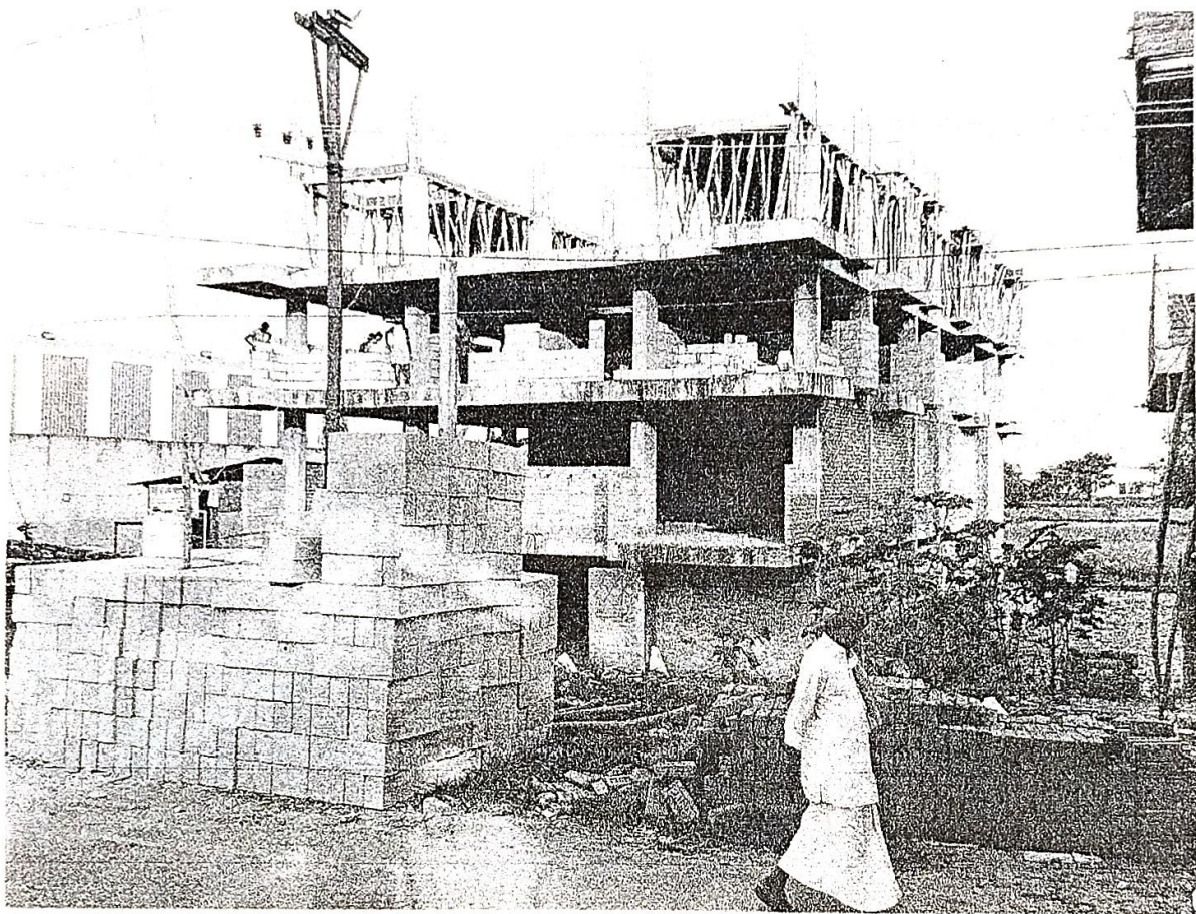


MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Lilans Chayde*  
Director


Page 7 of 9

Side Elevation

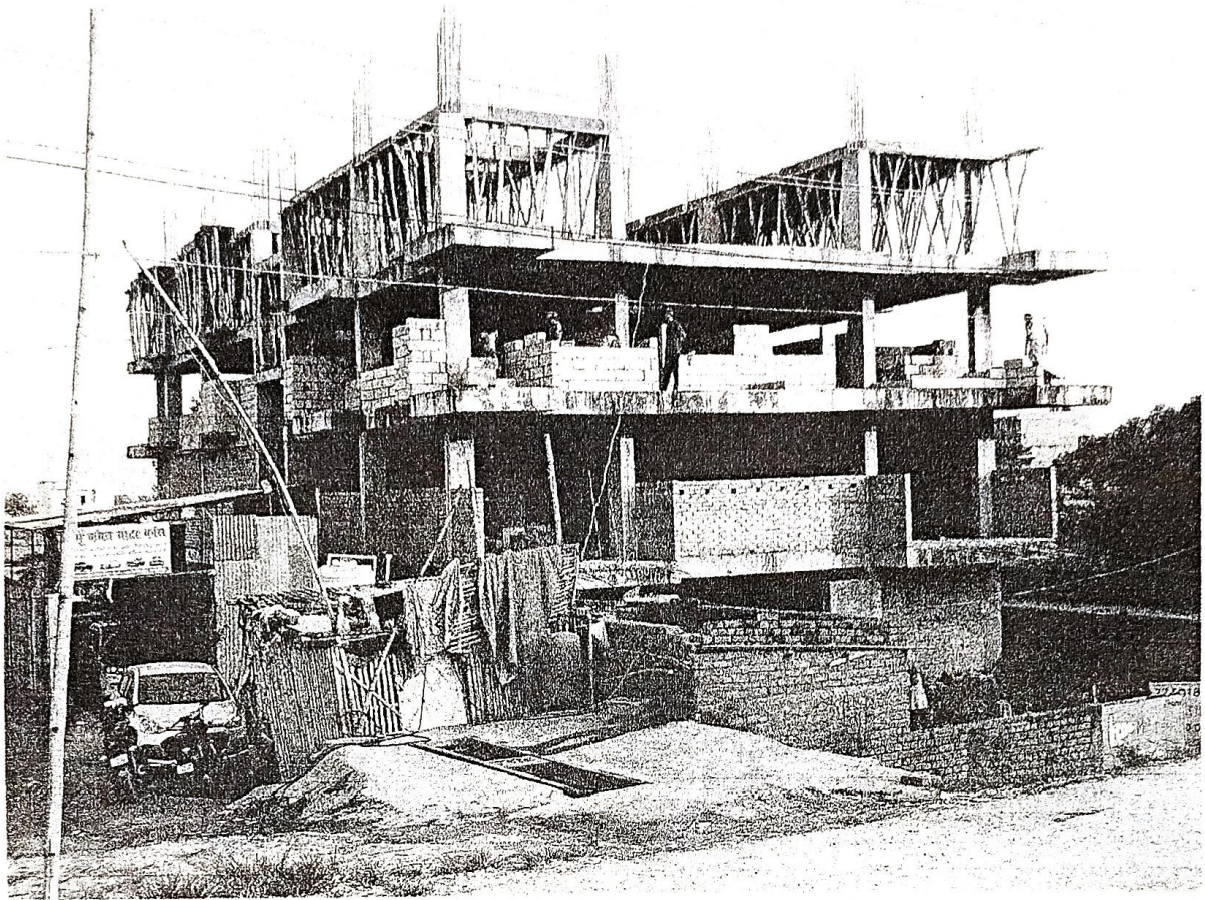

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Milans Chavde*  
Director

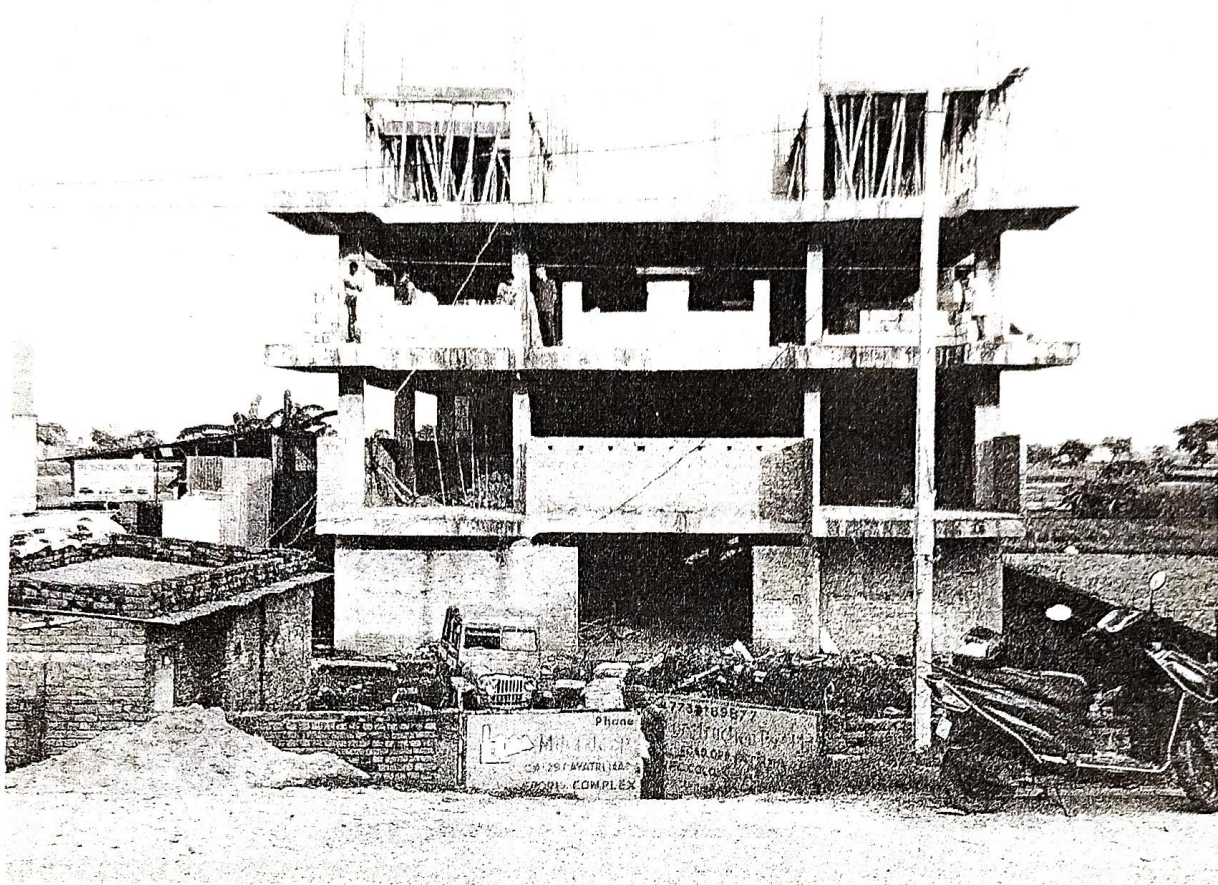

Undertaking:

*I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.*

Signature of Promoter

MILANDEEP CONSTRUCTION PRIVATE LIMITED

*Milan Chongdar*  
Director

Name: MILAN CHONGDAR

Date :
