

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending September of 2023

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP14418-1/123/R-1444/2022	Name of Project/Phase of Registered Project	MANORAMA RAJMANI BUILDING
Name of Promoter	GANDIV BUILDER AND ENGINEERS PRIVATE LIMITED	Project Address	PILLAR NO--56, MAUZA-SALEMPUR DUMRA, RAJA BAZAR, BAILEY ROAD, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/06/2026		
Starting date of Project or Phase of the Project	27/07/2022		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	Commercial	
Period of validity of map by the Competent Authority	3 YEARS		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments -
	1. 1 BHK	-	13485		1. Booked/ Allotted
	2. 2 BHK,	-			-
	3. 3 BHK	-			-
	4. Shop	-			-
	5. Bungalow	-			-
	6. Plot etc.	-			-

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Amind Kumar

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	-
		2. Sold	-

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of Further filing)

S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project

1. Building / Wing / Layout Number _____ (To be filled for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	NO
4.	Plinth	NO
5.	Stilt Floor	NO
6.	Slabs of Super Structure	4 Slab Completed.
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%

Amind Kumar

8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	NO		

Arvind Kumar

7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	YES	0%	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	15%	
14.	Open Parking	YES	80%	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			

Arind Kumar

8.	Water conservation/ Rain Water Harvesting			
9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	3869002100012396
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Amount received during the Quarter	NIL
4.	Actual Cost Incurred during the Quarter	13,90,432=00
5.	Net amount at end of the Quarter	1,20,000=00
6.	Total expenditure on Project till date	1,67,38,967=00
7.	Cumulative fund Collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	


IX. Details of Mortgage or Charge if any created	

Arvind Kumar

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:


I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



Signature of Promoter

Name:

Date:

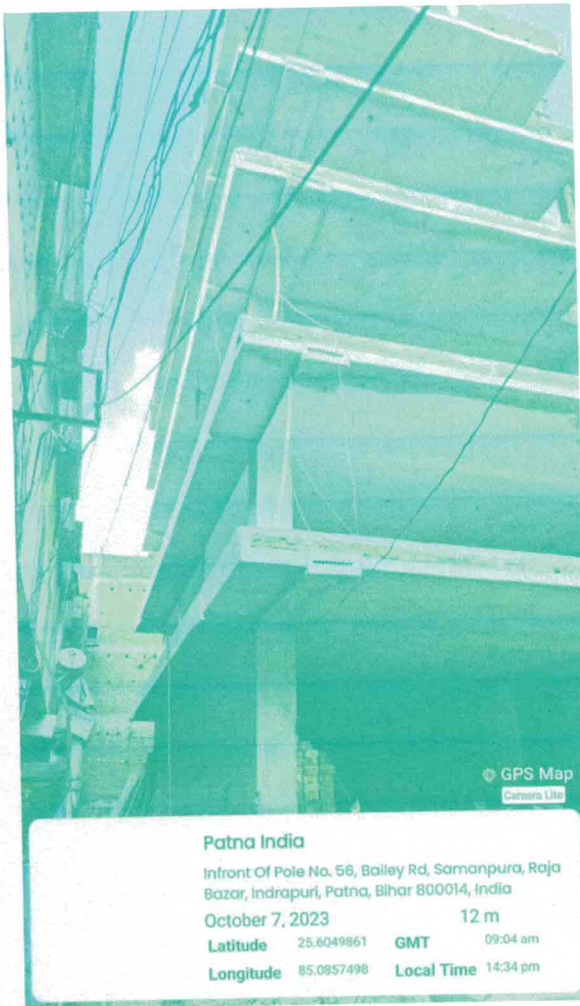


Patna India

Infront Of Pole No. 56, Bailey Rd, Samanpura, Raja Bazar, Indrapuri, Patna, Bihar 800014, India

October 7, 2023 12 m

Latitude 25.6049861 GMT 09:04 am

Longitude 85.0857498 Local Time 14:34 pm

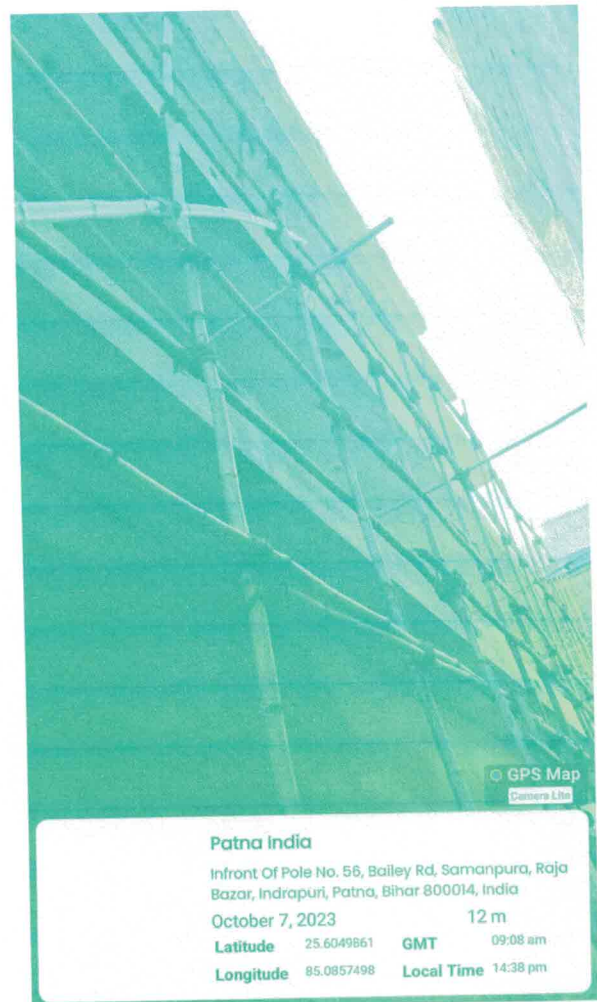


Patna India

Infront Of Pole No. 56, Bailey Rd, Samanpura, Raja Bazar, Indrapuri, Patna, Bihar 800014, India

October 7, 2023 12 m

Latitude 25.6049861 GMT 09:08 am

Longitude 85.0857498 Local Time 14:38 pm

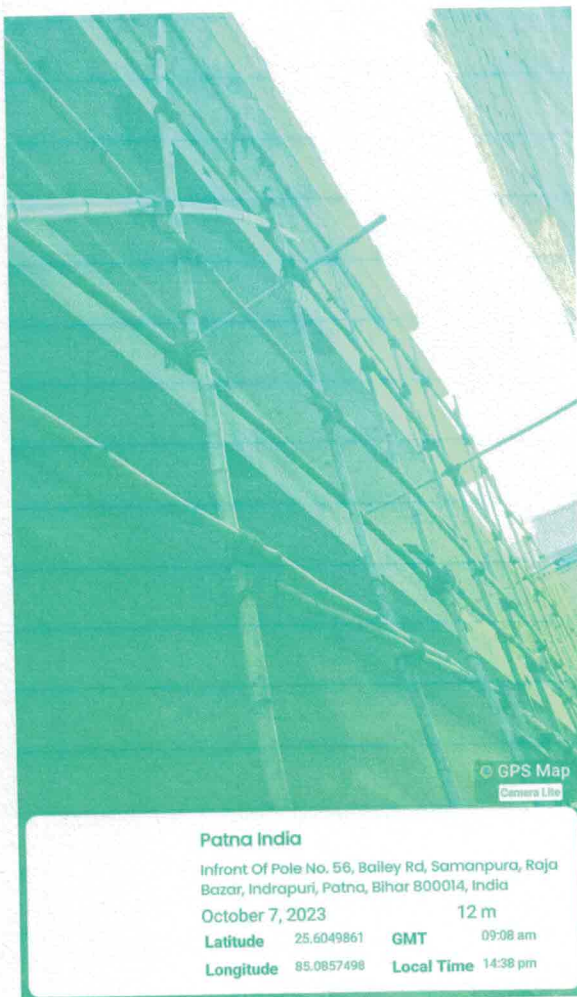

Patna India

Infront Of Pole No. 56, Bailey Rd, Samanpura, Raja Bazar, Indrapuri, Patna, Bihar 800014, India

October 7, 2023 12 m

Latitude 25.6049861 GMT 09:08 am

Longitude 85.0857498 Local Time 14:38 pm



Patna India

Infront Of Pole No. 56, Bailey Rd, Samanpura, Raja Bazar, Indrapuri, Patna, Bihar 800014, India

October 7, 2023 12 m

Latitude 25.6049861 GMT 09:03 am

Longitude 85.0857498 Local Time 14:33 pm
