



KUMAR CONSTRUCTIONS & DEVELOPERS

BUILDERS & DEVELOPERS

GST No : 10AAWFK9979N1Z6

PAN No : AAWFK9979N

HEAD OFFICE : L-3/2, Sri Krishnapuri, Boring Road, Patna – 800001, MOB NO : 7909000017.

E-MAIL ID : kumarconstruction9979@gmail.com

REF : _____

DATE : _____

To,

Real Estate Regulatory Authority

Patna, Bihar

Sub:- Submitting quarter ended 31st December 2023 report of **Bishundeo Saraswati Apartment**, Kanhauli, Bishundutt, Muzaffarpur, RERA Reg no.- **BRERAP01453-1/226/R-1522/2023**.

This is to state that hereby I am submitting quarter ended 31st December 2023 report certified by Engineer and photographs of above mentioned project.

1. Quarterly Report- 1 Page.

Thanking you,

Kumar Constructions And Developers

KUMAR CONSTRUCTIONS AND DEVELOPERS

Soumya Kumar

Partner

FORM-7
[REGULATION-9]

Quarterly progress report for quarter ending **December of 2023** (year)

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP01453-1/226/R-1522/2023	Name of Project/Phase of Registered Project	BISHUNDEO SARSWATI APARTMENT
Name of Promoter	Kumar Constructions And Developers	Project Address	Kanhauli, Bishundutt, Muzaffarpur
Name of Co-promoter			
Project Registration is valid up to	15/01/2028		
Starting date of Project or Phase of the Project	06/03/2023		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	Residential	
Period of validity of map by the Competent Authority			

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments -
	1. 1 BHK -				
	2. 2 BHK, -	08	35520		1. Booked/
	3. 3 BHK -	12	109488	20	Allotted -1
	4. Shop -				
	5. Bungalow -				2. Sold -
	6. Plot etc. -				

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 1
	20	2. Sold	-

IV. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	N/A			

KUMAR CONSTRUCTIONS AND DEVELOPERS

Sunby Kumar

Partner

3.	Water Supply Permission	Self Boring			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

V. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. _____ (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	N/A
3.	Podiums (if any)	
4.	Plinth	90%
5.	Stilt Floor	Second Slab work Completed (First floor Roof)
6.	Slabs of Super Structure	5
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	NO
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	NO
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	NO
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	NO
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	NO

KUMAR CONSTRUCTIONS AND DEVELOPERS

Soumya Kumar

Partner

	requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities.	NO
--	--	----

VI. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage (Chamber, Line, Septic Tank, STP)			
4.	Storm Water Drains			
5.	Landscaping & Tree Planting			
6.	Street Lighting			
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water			
9.	Solid Waste Management & Disposal			
10.	Water Conservation / Rain Water Harvesting			
11.	Energy Management			
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking			

KUMAR CONSTRUCTIONS AND DEVELOPERS

Sandeep Kumar

Partner

14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station			
16.	Others (Option to Add More)			

VI A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUALWORK DONE (As on date of certificate)	Details
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	
	2.	Rear Elevation	

KUMAR CONSTRUCTIONS AND DEVELOPERS

Sandeep Kumar

Partner

	3.	Side Elevation	
(B)		Photograph of each floor	

VIII. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	922020063642338
2.	Estimated Cost of the Project including land cost at the start of the Project	Rs. 2,12,23,000.00
3.	Amount received during the Quarter (including GST) (RERA +Current)	Rs. 05,00,000.00
4.	Actual Cost Incurred during the Quarter(RERA+Current)	Rs. 17,34,574.00
5.	Net amount at end of the Quarter(RERA A/c)	Rs. 4,70,168.10
6.	Total expenditure on Project till 31/12/2023	Rs. 35,21,751.00
7.	Cumulative fund collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

X. MISCELLANEOUS	
A	List of Legal Cases (if any)
1.	Case No.
2.	Name of Parties
B	Sale/Agreement for Sale during the Quarter
1.	Sale Deed
2.	Agreement for Sale
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART	
Weather the project in progress is as per time schedule or lagging behind?	

KUMAR CONSTRUCTIONS AND DEVELOPERS

Saurabh Kumar

Partner

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

KUMAR CONSTRUCTIONS AND DEVELOPERS

Sanjay Kumar

Signature of Promoter **Partner**

Name: *SANJAY KUMAR*

Date:

ARCHITECT'S CERTIFICATE

(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account)

Date : _____

To
Kumar Constructions And Developers
L-3/2, Srikrishnapuri
Boring Road
Patna -800001.

Subject: Certificate of Percentage of Work executed in the project

Having 1 No. of Building(s)/ 1 Wing(s) of the Phase bearing the registration no. [Bihar RERA Registration Number] - **BRERAP01453-1/226/R-1522/2023** and being developed on the plot bearing CS No/Khata No. - 67 Keshra/Plot No. - **413 K, KH** demarcated by its boundaries (latitude and longitude of the end points) 26.1033 ° N & 85.4182 ° E of the land **BISHUNDEO SARASWATI APARTMENT** situated in **Kanhauli, Bishundutt** Village - **Muzaffapur**, District : **Muzaffapur** PIN - **842002**.

Admeasuring : **1425.03 Sq.mts.** Area being developed by the promoter [Name] : **Kumar Constructions And Developers.**

Sir,

I, We **MUKESH KUMAR GUPTA** have undertaken assignment as Architect / Licensed Surveyor of certifying Percentage of execution of Work of the **Bishundeo Saraswati Apartment** Building(s)/Wing(s) of the Phase of the Project, Situated on the plot bearing C.S. No./Survey No. Khata No : **67**, /Plot No. : **413 K, KH** of Village : **Muzaffarpur**, District : **Muzaffarpur**, PIN : **842002** admeasuring : **1425.03 Sq.mts.** area being developed by [Promoter's Name: **Kumar Constructions And Developers.**]

1. Following technical professionals are appointed by Owner / Promoter :-

- (i) M/s /Shri/Smt. **MUKESH KUMAR GUPTA** as L.S. / Architect.
- (ii) M/s /Shri/Smt. **MUKESH KUMAR** as Structural Consultant.
- (iii) M/s /Shri/Smt. _____ as Mechanical/Electrical/Plumbing Consultant (MEP).
- (iv) M/s /Shri/Smt. **ASHUTOSH RAJ** as Site Supervisor.

Based on site Inspection, with respect to reach of the Building/ Wing of the aforesaid Real Estate Project, I certify that as on the date of this certificate, the Percentage of Work done for each of the building/Wing of the Real Estate Project as registered vide number : **BRERAP01453-1/226/R-1522/2023** Under Bihar RERA is as per table A herein below. The percentage of the work executed with respect to each of the activity of the entire phase is detailed in Table B.

Mukesh Kumar Gupta
Mukesh Kumar Gupta
Certified Civil Engineer
Urban Development and Housing Department
Reg. No -BR/UDHD/CE/23-0231

ENGINEER'S CERTIFICATE

(To be submitted at the time of Registration of Ongoing Project and for withdrawal of Money from Designated Account-Project Wise)

To,
Kumar Constructions And Developers
L-3/2, Srikrishnapuri
Boring Road
Patna -800001

Date :

Subject : Certificate of Cost Incurred for Development of [Project Name :- **BISHUNDEO SARASWATI APARTMENT** for Construction of building(s) (Bihar RERA Registration Number) **BRERAP01453-1/226/R-1522/2023** situated on the plot bearing C.S.No./ Khata No. - **67** /Survey No. Thana No. **411**, Tauzi No. - **5174** /Plot No. - **413 K, KH** demarcated by its boundaries (latitude and longitude of the end points) **26.1033 ° N & 85.4182 ° E, Kanhauli, Bishundutt** Village: **Muzaffarpur** District : **Muzaffarpur** PIN : **842002** Admeasuring **1425.03 Sq.mts.** area being developed by [Promoter] **Kumar Constructions And Developers.**

Ref: Bihar RERA Registration Number **BRERAP01453-1/226/R-1522/2023.**


Sir,

I, We **MUKESH KUMAR** have undertaken assignment of certifying Cost for the Subject Real Estate Project registered under RERA, Bihar of **BISHUNDEO SARASWATI APARTMENT** Building(s) situated on the plot bearing/ CTS No./Survey No./ Plot No. - **67** of Village : **Muzaffarpur**, District : **Muzaffarpur** PIN : **842002** admeasuring : **1425.03 Sq.mts.** area being developed by **Kumar Constructions And Developers.**

1. Following technical professionals are appointed by Owner / Promoter :-

- (i) M/s /Shri/Smt. **MUKESH KUMAR GUPTA** as L.S. / Architect;
- (ii) M/s /Shri/Smt. **MUKESH KUMAR** as Structural Consultant
- (iii) M/s /Shri/Smt. _____ as MEP Consultant
- (iv) M/s /Shri/Smt. **ASHUTOSH RAJ** as Quantity Surveyor*

2. We have estimated the cost of the completion to obtain Occupation Certificate/ Completion Certificate, of the Civil, MEP and Allied works, of the building(s) of the project. Our estimated cost calculations are based on the Schedule of rates (name of the schedule of Rates) and Drawings/plans made available to us for the project under reference by the Developer and Consultants and the quantity for the entire work as calculated by **ASHUTOSH RAJ** Quality Surveyor* appointed by Developer/Engineer, and the assumption of the cost of material, labour and other inputs made by developer, and the site inspection carried out by us.


ER. MUKESH KUMAR
CIVIL ENGINEER
EMP No. BR/UDHD/SE/23-0037
UDHD, BIHAR (PATNA)

3. We estimate Total Estimated Cost of completion of the building(s) Excluding the land Cost of the aforesaid project under reference as **Rs 2,13,23,000.00 (Two Crores Thirteen Lakhs Twenty Three Thousand Only)** (Total of Table A and B). The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for the purpose of obtaining occupation certificate / completion certificate for the building(s) from the **MUZAFFARPUR NAGAR NIGAM** being the planning Authority under whose jurisdiction the aforesaid project is being implemented.
4. The Estimated Cost Incurred till date is calculated at **Rs. 35,21,751.00** (Total of Table A and B). The amount of Estimated Cost incurred is calculated on the base of amount of Total Estimated Cost.
5. The Balance cost of Completion of the Civil, MEP and Allied works of the building(s) of the subject project to obtain Occupation Certificate/ Completion Certificate from **Muzaffarpur Nagar Nigam** (planning Authority) is estimated at **Rs.1,78,01,249.00** (Total of Table A and B).
6. I certify that the Cost of the Civil, MEP and allied work for the aforesaid Project as completed on the date of this certificate is as given in Table A and B below:

TABLE - A
Building/Wing bearing Number or called Bishundeo Saraswati Apartment
(To be prepared separately for each Building/Wing of the Real Estate Project)

Sr. No.	Particulars	Amount
1.	Total Estimated cost of the building/wing Excluding Land Cost as on <u>21/02/2023</u> date of Registration is	<u>Rs. 2,13,23,000.00</u>
2.	Cost incurred up to <u>31-12-2023</u> (Based on the Estimated cost)	<u>Rs. 35,21,751.00</u>
3.	Work done in Percentage (As Percentage of the estimated cost)	<u>16%</u>
4.	Balance Cost to be Incurred (Based on Estimated Cost)	<u>Rs. 1,78,01,249.00</u>
5.	Cost Incurred on Additional/Extra Items as on _____ not included in the Estimated Cost (Annexure A)	N/A

TABLE - B
(To be prepared for the entire registered phase of the Real Estate Project)

Sr. No.	Particulars	Amounts
1.	Total Estimated cost of the Internal and External Development Works including amenities and Facilities in the layout as on _____ date of Registration is	N/A
2.	Cost incurred as on _____ (Based on the Estimated cost).	N/A
3.	Work done in Percentage (As Percentage of the estimated cost).	N/A


ER. MUKESH KUMAR
CIVIL ENGINEER
EMP No. BR/UDHD/SE/23-0037
UDHD RIHAD / DATNA

4.	Balance Cost to be Incurred (Based on Estimated Cost).	N/A
5.	Cost Incurred on Additional/Extra Items as on _____ not included in the Estimated Cost (Annexure A).	N/A

Yours Faithfully,


ER. MUKESH KUMAR
CIVIL ENGINEER
EMP No. BR/UDHD/SE/23-0037
UDHD, BIHAR (PATNA)


Signature of Engineer. (License No :)

*Note :

1. The scope of work is to complete entire Real Estate Project as per drawings approved from time to time so as to obtain Occupancy Certificate/Completion Certificate.
- 2.(*).Quantity survey can be done by office of Engineer or can be done by an independent Quantity Surveyor, whose certificate of quantity calculated surveyor being appointed by Developer, the name has to be mentioned at the place marked (*) and in case quantity are being calculated by office of Engineer, the name of the person in the office of Engineer, who is responsible for the quantity calculated should be mentioned at the placemarked (*).
3. The estimated cost includes all labour, material, equipment and machinery required to carry out entire work.
4. As this is an estimated cost, any deviation in quantity required for development of the Real Estate Project will result in amendment of the cost incurred / to be incurred.
5. All components of work with specifications are indicative and not exhaustive.

Annexure A
List of Extra/Additional Items executed with cost
(Which were not Part of the original Estimate of Total Cost)

Biohundo Saraswati

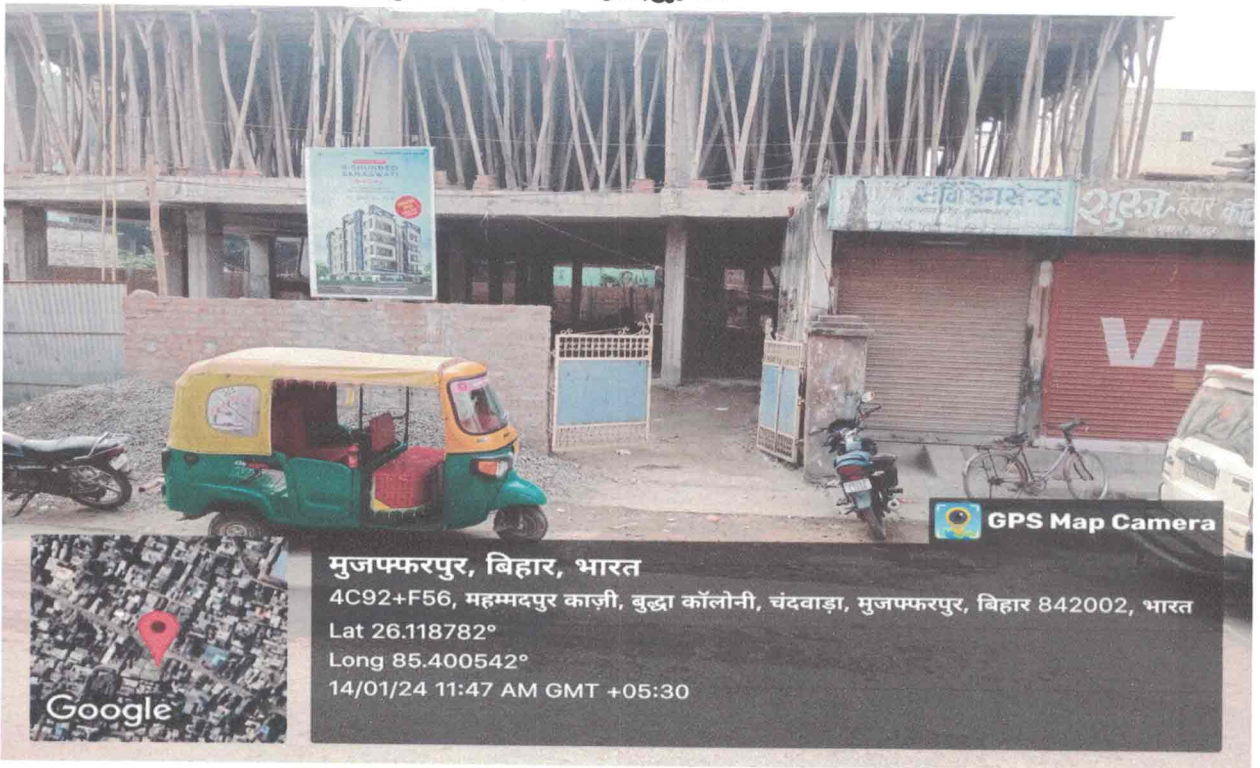



GPS Map Camera

मुजफ्फरपुर, बिहार, भारत

4C92+F56, महम्मदपुर काज़ी, बुद्धा कॉलोनी, चंदवाड़ा, मुजफ्फरपुर, बिहार 842002, भारत

Lat 26.118721°

Long 85.400644°

14/01/24 11:48 AM GMT +05:30

Google
