

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Oct-Dec of 2023 (Year)

I. PARTICULARS OF PROJECT

Project Registration Number	BRERAP31918-1/949/R-628/2019
Name of Project/Phase of Registered Project	MIRA REGENCY
Name of Promoter	UNIVERSAL GREEN HEIGHTS LLP.
Project Address	MOHHRRAMPUR,THANA-KANKARBAGH,PLOT NO-69,57,1340,1462, PATNA, DIST.- PATNA
Name of Co-promoter	NA
Project Registration is valid up to	31/12/2024
Starting date of Project or Phase of the Project	31/05/2019
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Mira Regency	3 BHK	1095.44	36	1. Booked/Alloted- 16 2. Sold- 7
Mira Regency	3 BHK	1096.52	1	
Mira Regency	3 BHK	1096.52	1	
Mira Regency	3 BHK	1096.52	1	
Mira Regency	3 BHK	1096.52	1	

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Mira Regency	No Garages available	1. Booked/Allotted - 2. Sold -	

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission /Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project**1. Plan Case No.- P/Moharrampur-PRN-B+G+6/08/2018 (Mira Regency) (To be added for each Building / Wing)**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	95%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	90%
6.	Slabs of Super Structure	100%
7.	Internal walls Flats /Premises.	100%
8.	Internal Plaster & Putty within Flats /Premises	95%
9.	Floorings within Flats /Premises	95%
10.	Doors and Windows within Flats /Premises	90%
11.	Sanitary Fittings within the Flat/Premises	80%
12.	Electrical Fittings within the Flat/Premises	80%
13.	Staircases, Lifts Walls and Lobbies at each Floor level	90%
14.	Overhead and Underground Water Tanks.	100%
15.	External plumbing	95%

16.	External plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	90%
17.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	70%

VI. Amenities and Common Area and External Infrastructure Development Works				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	80%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / Rain Water Harvesting	No		
11.	Energy Management	No		

12.	Fire Protection and Fire Safety Requirements	Yes	70%	
13.	Closed Parking	Yes	90%	Basement and Stilt floor structure work complete and finishing work under progress in full swing.
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to Add More)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor

VIII. Financial Progress of the Project

S.No. (1)	Particulars (2)	Amount (in Rs.) (3)
1	Project Account No.	634905600891
2	Estimated Cost of the Project including land cost at the start of the Quarter	704.50/- (In Lakh)
3	Amount received during the Quarter	6,42,857.00/-
4	Actual Cost Incurred during the Quarter	42,36,107.36/-
5	Net amount at end of the Quarter ICICI 70%	2,97,500.40/-
	Net amount at end of the Quarter ICICI 30%	8,05,444.94/-
6	Total expenditure on Project till date	11,04,58,565.83/-
7	Cumulative fund collected till the end of Quarter in question	11,41,16,191.04/-
8	Cumulative expenditure done till the end of Quarter in question	11,04,58,565.83/-

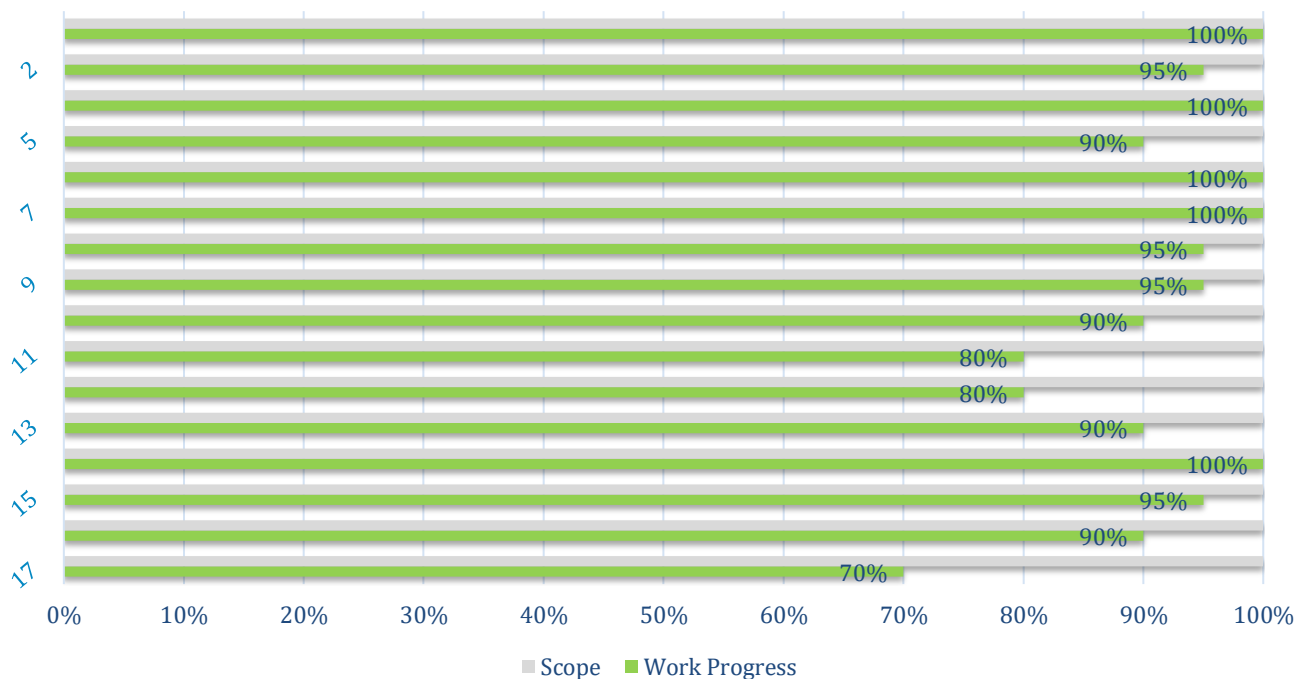
IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

X. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	07
2.	Agreement for Sale	03

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

PROGRESS CHART

Project in progress is as per time schedule

Project Site Photographs

Front Elevation









Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter

Universal Green Heights LLP.

For UNIVERSAL GREEN HEIGHTS LLP



Designated Partner

Date :
