

FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending March of 2024

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00985-1/773/R-459/2019	Name of Project/Phase of Registered Project	APEX TWIN TOWER
Name of Promoter	MOHINI CONSTRUCTIONS	Project Address	NEAR RANIPUR POOL, RANIPUR ROAD, PHULWARISHARIF, PATNA.
Name of Co-promoter	N/A		
Project Registration is valid up to	30/11/2021		
Starting date of Project or Phase of the Project	26/02/2019		
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	Residential	
Period of validity of map by the Competent Authority	3 YEARS+ 9 Month Covid 19		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS				
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments
Block-A, B And C	1. 1 BHK	-		104
	2. 2 BHK,	-	54	
	3. 3 BHK	-	50	
	4. Shop	-		
	5. Bungalow	-		
	6. Plot etc.	-		
				Total Number of Apartments = 1. Booked/Allotted - NIL 2. Sold - NIL

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Block-A, B And C	104	1. Booked/Allotted	- NIL
		2. Sold	- NIL

Mohini Constructions
[Signature]
Partner

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of Further filing)

S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project

1. Building / Wing / Layout Number _____ (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done(As on date of the Certificate) (3)		
		BLOCK-A	BLOCK-B	BLOCK-C
1.	Excavation (if any)	0%	100%	0%
2.	Basements (if any)	N/A	100%	N/A
3.	Podiums (if any)	N/A	N/A	N/A
4.	Plinth	N/A	100%	N/A
5.	Stilt Floor	0%	100%	0%
6.	Slabs of Super Structure	0%	3 rd Slab 100%	0%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	1 st Floor Brick work 75%	0%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	60%	0%

Mohini Constructions

 Partner

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	0%	0%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	0%	0%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%	0%	0%

VI. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO		


Mohini Constructions
 Director

8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	NO		
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT


		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			
8.	Water conservation/ Rain Water Harvesting			

Mohini Constructions

 Partner

9.	Energy Management			
----	-------------------	--	--	--

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

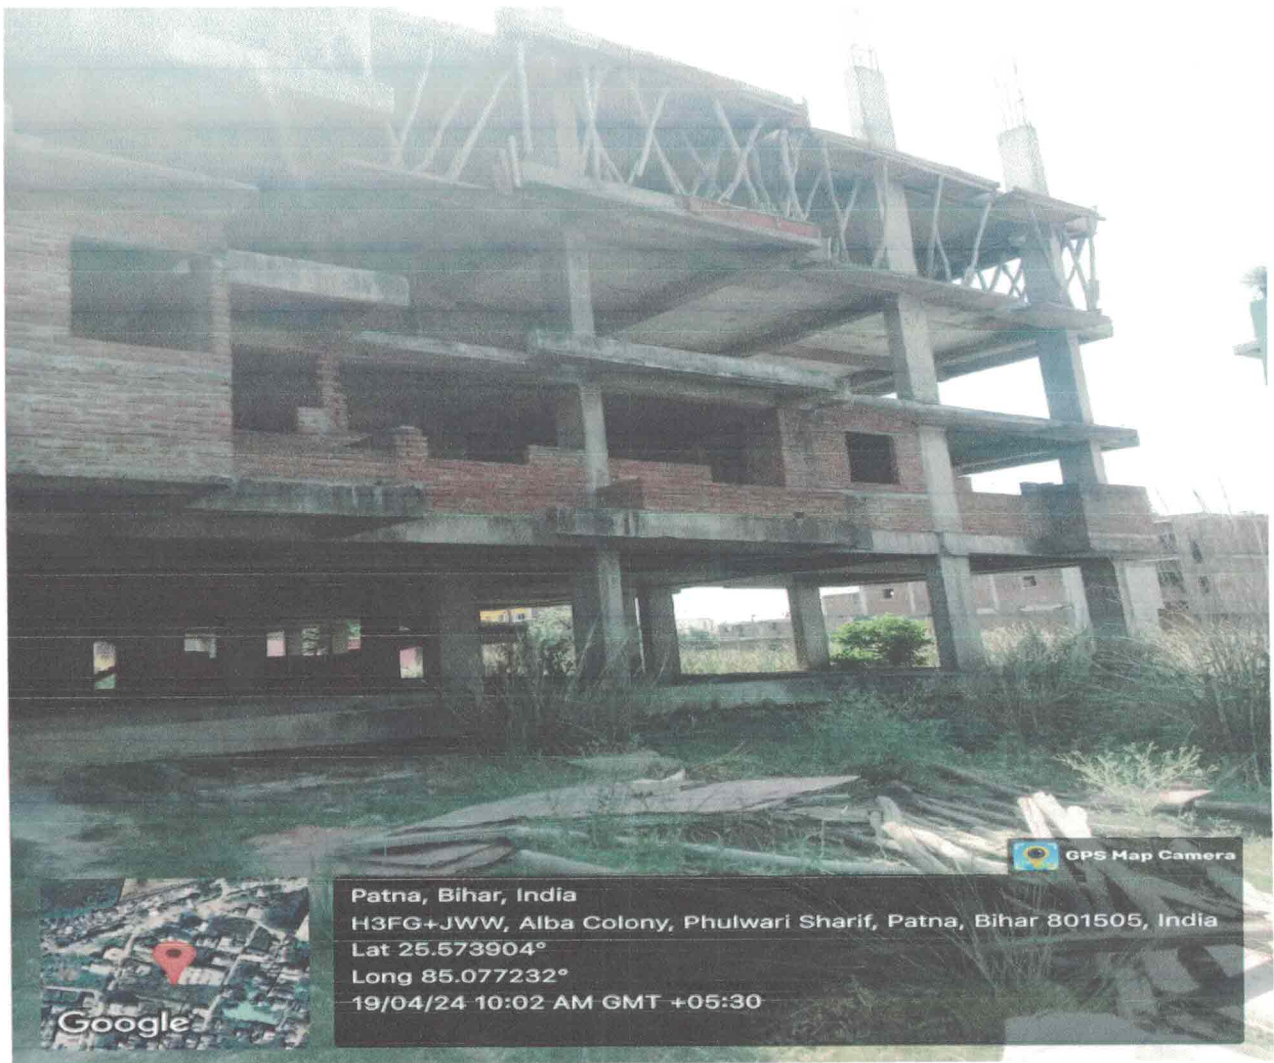

Mohini Constructions

 Partner



Mohini Constructions

Partner



VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	33121013939
2.	Estimated Cost of the Project including land cost at the start of the Project	
3.	Amount received during the Quarter	NIL
4.	Actual Cost Incurred during the Quarter	
5.	Net amount at end of the Quarter	
6.	Total expenditure on Project till date	
7.	Cumulative fund Collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	


Mohini Constructions
 Partner

IX. Details of Mortgage or Charge if any created

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



Mohini Constructions

Partner

Signature of Promoter

Name:

Date:
