



SRI ANUANAND CONSTRUCTION PRIVATE LIMITED

CIN: U45203BR2009PTC014563

Corp. Office: 102, Kumar Tower, 1st Floor, Boring Road Crossing, Patna

**SAI ENCLAVE
VIJAY SINGH YADAV PATH, Patna**

RERA No. BRERAP00393-4/286/R-278/2018

Quarterly Reports for the Quarter Ended – 31.07.2021 to 31.09.2021

(1)	Quarterly up to date status of the Project (Physical and Financial)		
	Status of the Project , -		SAI ENCLAVE
	A	Status of Construction of each building with photographs	ATTACHED
	B	Status of Construction of each floor with photographs	ATTACHED
	C	Status of Construction of Internal Infrastructure and common area with photographs	ATTACHED
(2)	Quarterly up-to date the list of number and types of apartments or plots, as case may be booked		
	A	List of Number and types of Apartments	Total 14 towers

Following works completed at Site –

C Block	July 2021 to September 2021
10/06/2021 TO 31/09/2021	Chakar tiles work and grouting work in parking area



E – Block	July 2021 to September 2021
01/07/2021 To 25/08/2021	8 th floor electrical conduiting work is completed
02/07/2021 To 05/09/2021	8 th floor chipping work is completed
03/07/2021 To 10/09/2021	8 th floor plaster work is completed
10/09/2021 To	9 th floor plaster work
25/07/2021 To 28/09/2021	top roof parapet wall plaster work is completed
01/08/2021 To ...ongoing	Down slab waterproofing work
18/08/2021 To ongoing	Cpvc plumbing & testing work in progress
11/07/2021 To ongoing	SWR plumbing work
16/08/2021 To ongoing	Balcony line fitting work
09/08/2021 To ongoing	Main door fitting work
09/08/2021 To ongoing	Putty work in progress



F - Block	July 2021 to September 2021
05 /07/2021 To 15/09/2021	9 th floor brick work is completed
05 /07/2021 To 15/09/2021	9 th floor brick work is completed
16/07/2021 To ongoing..	Top parapet wall brick work in progress
21/07/2021 To 30/09/2021	flat no 206 electrical work in completed
18/07/2021 To 10/09/2021	flat no 206 cpvc pipe line work in progress
03/07/2021 To 10/09/2021	8 th floor conduiting work in progress
13/07/2021 To ongoing	6 th floor marble fitting work in progress



G - Block	July 2021 to September 2021
03/07/2021 TO 22/08/2021	6 th floor plaster work is completed
10/07/2021 TO 26/07/2021	8 th floor brick work is completed
29/07/2021 TO	9 th floor brick work in progress
29/07/2021 TO	4 th floor tiles work in progress
25/07/2021 TO 31/08/2021	top water tank work is completed
01/07/2021 TO 13/07/2021	Top parapet wall brick work in progress
15/07/2021 TO	1 st floor brick work in progress



H – Block	July 2021 to September 2021
01/07/2021 To 24/09/2021	7 th floor brick work is completed
25/09/2021 To	8 th floor brick work in progress
09/07/2021 TO 21/08/2021	10 th last Slab column casting work is completed
22/07/2021 TO 03/09/2021	4 th floor plaster work is completed
25/07/2021 TO 31/08/2021	4 th floor electrical conduiting work is completed
15/06/2021 TO 25/06/2021	4 th floor chiiping work is completed
04/09/2021 TO ...	5 th floor plaster work in progress
28/07/2021 TO 29/09/2021	flat no HG5 tiles work in progress
30/07/2021 TO 03/08/2021	flat no HG5 cpvc pipe line work is completed




I Block	July 2021 to September 2021
02/07/2021 TO 08/09/2021	4 th floor brick work is completed



J Block	July 2021 to September 2021
13/07/2021 To 18/08/2021	3 rd floor brick work is completed



K - Block	July 2021 to September 2021
13/07/2021 TO 18/08/2021	6 th slab column reinforcement work is completed
25/07/2021 TO 31/07/2021	6 th casting column casting work is completed
15/07/2021 TO 25/07/2021	6 th slab shuttering work in progress
20/07/2021 TO 25/09/2021	6 th slab reinforcement work is completed
26/09/2021 TO 30/09/2021	6 th slab casting work is completed

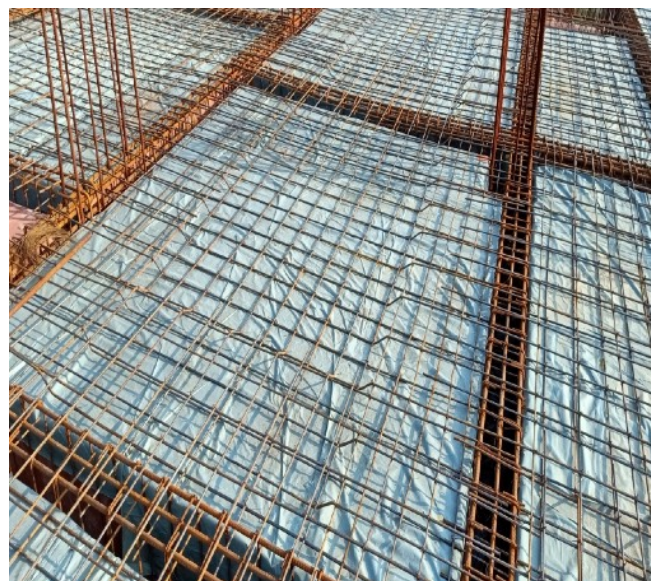

L - Block	July 2021 to September 2021
02/07/2021 To 04/08/2021	3 rd floor brick work is completed
15/07/2021 To ongoing	4 th floor brick work in progress
07/07/2021 To 25/08/2021	8 th slab shuttering work and materials making work
08/08/2021 To 12/08/2021	8 th slab beam and slab reinforcement work is completed
15/08/2021 To 19/08/2021	8 th slab casting work is completed



M Block	July 2021 to September 2021
10/07/2021 To ongoing	Foundation reinforcement work in progress
15/07/2021 To ongoing	Foundation casting work in progress



N Block	July 2021 to September 2021
25/07/2021 To ongoing	Soil filling and levelling work in progress



Thanks and Regards.

Yours Faithfully,
For Sri Anuanand Construction Pvt. Ltd.
