



SRI ANUANAND CONSTRUCTION PRIVATE LIMITED

CIN: U45203BR2009PTC014563

Corp. Office: 102, Kumar Tower, 1st Floor, Boring Road Crossing, Patna

SAI ENCLAVE

VIJAY SINGH YADAV PATH, Patna

RERA No. BRERAP00393-4/286/R-278/2018

Quarterly Reports for the Quarter Ended – 01.10.2021 to 31.12.2021

(1) Quarterly up to date status of the Project (Physical and Financial)			
	Status of the Project , -		SAI ENCLAVE
	A	Status of Construction of each building with photographs	ATTACHED
	B	Status of Construction of each floor with photographs	ATTACHED
	C	Status of Construction of Internal Infrastructure and common area with photographs	ATTACHED
(2) Quarterly up-to date the list of number and types of apartments or plots, as case may be booked			
	A	List of Number and types of Apartments	Total 14 towers

Following works completed at Site –

B Block	October 2021 to December 2021
25/11/2021 To 05/12/2021	Ramp area shading work in progress basement



E – Block	October 2021 to December 2021
04/10/2021 To 25/11/2021	9 th floor electrical conduiting work is completed
09/10/2021 To 05/11/2021	9 th floor chipping work is completed
15/10/2021 To 15/12/2021	9 th floor plaster work is completed
28/12/2021 To Ongoing	10 th floor plaster work
25/12/2021 To Ongoing	stair plaster work in progress
20/10/2021 To Ongoing	Down slab waterproofing work in progress
16/11/2021 To Ongoing	cpvc plumbing & testing work in progress
11/12/2021 To Ongoing	SWR plumbing work in progress
13/11/2021 To Ongoing	balcony line fitting work in progress
09/12/2021 To Ongoing	putty work in progress
12/11/2021 To Ongoing	outer plaster in progress




F - Block	October 2021 to December 2021
5/10/2021 To Ongoing	8 th floor electrical conduiting work in progress
26/11/2021 To 25/12/2021	Top parapet wall plaster work is completed
21/12/2021 To Ongoing	Flat no 206 electrical wire laying work in progress
18/11/2021 To Ongoing	Balcony railing fitting work in progress



G - Block	October 2021 to December 2021
03/10/2021 To Ongoing	7 th floor chipping work in progress
10/11/2021 To 26/07/2021	9 th floor brick work is completed
20/12/2021 To Ongoing	7 th floor door frame fitting work in progress
29/11/2021 To 30/12/2021	Parapet wall brick work is completed
25/11/2021 To 31/12/2021	Parapet column casting work in progress
01/11/2021 To 13/12/2021	1 st floor brick is completed
15/12/2021 To Ongoing	3 rd floor marble fitting work in progress
01/10/2021 To Ongoing	Door frame making work in progress



H – Block	October 2021 to December 2021
05/12/2021 To Ongoing	8 th floor brick work in progress
29/12/2021 To Ongoing	10 th last slab shuttering work in progress
20/10/2021 To 23/12/2021	5 th floor plaster work is completed
15/10/2021 To 20/12/2021	5 th floor electrical conduiting work is completed
10/10/2021 To 30/11/2021	5 th floor chipping work is completed
28/12/2021 To Ongoing	6 th floor plaster work in progress
18/12/2021 To Ongoing	Flat no 505 tiles work in progress
28/12/2021 To Ongoing	Flat no 505 CPVC pipe line work in progress

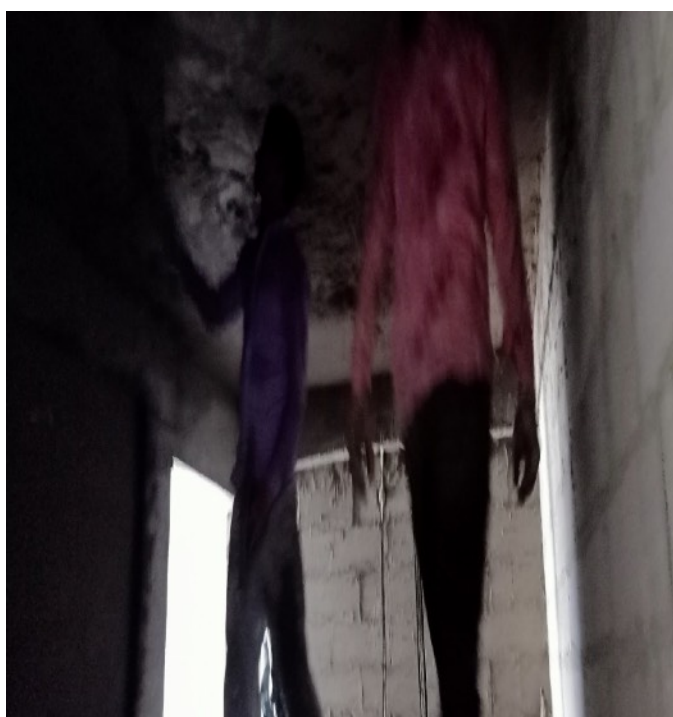

I Block	October 2021 to December 2021
30/11/2021 To Ongoing	Brick unloading for 5 th floor brick in progress



J Block	October 2021 to December 2021
13/12/2021 To Ongoing	Brick shifting for 4 th floor brick work in progress



K - Block	October 2021 to December 2021
23/12/2021 To Ongoing	1 st floor brick work in progress
12/12/2021 To Ongoing	Ground floor plaster work in progress
25/12/2021 To Ongoing	7 th slab column reinforcement in progress
05/12/2021 To Ongoing	Ground floor electrical conduiting work in progress



Thanks and Regards.

Yours Faithfully,
For Sri Anuanand Construction Pvt. Ltd.
