

LETTER REF. NO: SE/RERA/01/2020

To,
The Respected Authority,
RERA- Bihar

Dated – 27/08/2020

Subject – Submission of Work Progress and Financial Report

Dear Sir/Madam,

Please find attached with Progress Update and Financial Status for the period January 2020 to August 2020 for our Project “SAI ENCLAVE” Vijay Singh Path Marg, Danapur, Patna

For the periods –
January to August 2020 (April to May work suspended due to covid 19)

Following works completed at Site –

E :- BLOCK (January to August 2020)

- 2nd floor putty work
- 1,2,3,4,5,6th floor marble fitting passage area
- 9th floor brick work
- 10th floor deshuttering work
- 4,5th floor balcony railing work
- 1,2,3rd metal box fitting work
- 1,2,3rd plumbing pipe fitting work



F:- BLOCK

- 1,2,3rd floor marble fitting work(passage area).
- 2nd and 3rd floor skirting repairing work.
- 1st, 2nd and 3rd floor metal box fitting work.
- 10th floor deshuttering work
- 9th floor brick work
- Balcony railing fitting work



A:- BLOCK


- Parking dressing ,soling work
- Parking casting work



G :- BLOCK

- 2,3rd floor putty work
- 9,10th slab shuttering ,steel making and binding work

- 9, 10th slab casting work
- 11th slab shetting and steel making and binding work
- 2,3rd Door frame fitting work
- 2,3rd metal box fitting
- 2,3,4th plaster work & putty work

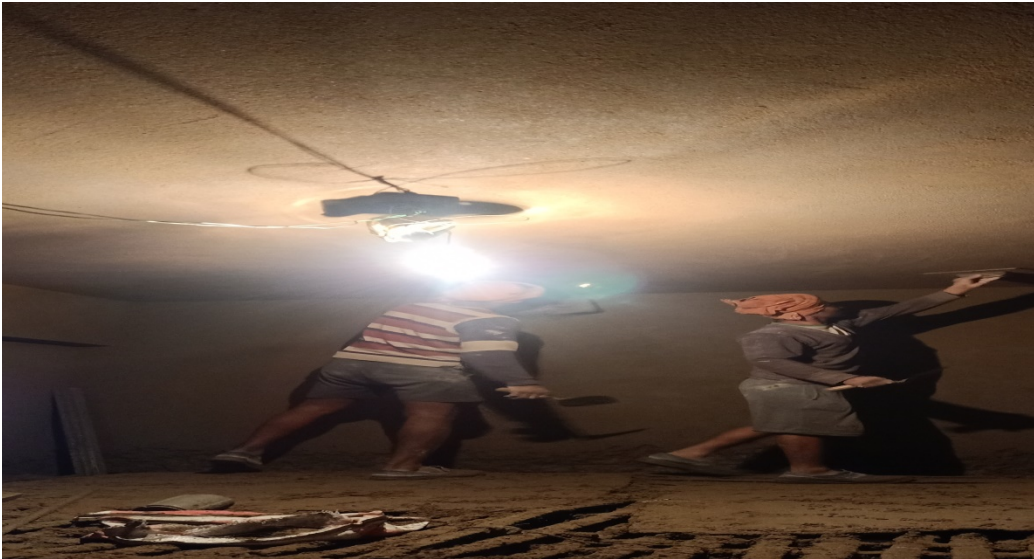

I BLOCK

- No work

J BLOCK

- No work

H:- BLOCK

- 7th slab shuttering work
- 7th slab reinforcement work
- 7th slab casting work

➤ 7th slab curing work



L:- BLOCK

- 6th slab shuttering work
- 6th Beam & slab reinforcement work
- 6th slab casting work



M:- BLOCK

- Dewatering work
- Layout work
- Soling work of cap
- Steel making and binding work
- Shuttering work
- Casting work



Thanks and Regards.

Yours Faithfully,

For Sri Anuanand Construction Pvt. Ltd.
