

QUARTERLY PROGRESS REPORT FOR RERA BIHAR

Oct – Dec, 2020

ABSTRACT

This report documents and describes the updates on project work progress, with updates on status of financials, bookings in the project along with status of the approvals for the quarter.

PROJECT NAME

KUNTI ENCLAVE

PROMOTER NAME

INDRALOK CONSTRUCTIONS

RERA REGISTRATION NO.

BRERAP00506-1/396/R-198/2018

PROJECT QUARTERLY PROGRESS STATUS

Quarter: Oct – Dec, 2020

Project Description: *A Residential project consisting of B+G+6 Floors and 30 premium 3 BHK Flats.*


Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Excavation	Yes	100%	Overall excavation works complete.
2	Foundation Works	Yes	100%	Overall foundation works complete.
3	Basement	Yes	57%	Soling and PCC works yet to start and finishing works yet to start. Waterproofing works complete.
4	Slabs of structure	Yes	94%	Slab casting upto 6 th floor completed and for terrace floor Reinforcement fixing and shuttering work complete.
5	Walls	Yes	81%	Brickwork complete till 5 th floor.
6	Internal Plaster & Putty	Yes	33%	Plastering works complete till 4 th floor.
7	Flooring inside units and common areas	Yes	0%	
8	Doors and Window to each of unit and common areas	Yes	11%	Door frame installation started complete upto 4 th floor.
9	Sanitary fittings within the unit including water proofing and plumbing	Yes	26%	CPVC works started. Installation complete till 4 th floor
10	Electrical fitting within the unit	Yes	22%	Electrical conduiting works started and complete till 4 th floor.
11	Staircase, lift walls and lobbies at each floor	Yes	32%	Structure of staircase upto 6 th floor is completed and lift wall complete on first 4 th floors, finishing work under

Progress Update of each Block/Wing separately

S. No.	Task/Activity	Applicable (Yes/No)	Percentage of Work Done	Remarks
				progress in full swing.
12	Water tank	Yes	0%	
13	External Plumbing works and completion of terrace with waterproofing of the building if specified.	Yes	0%	
14	External Plaster	Yes	0%	
15	External Paint	Yes	0%	
16	Installation of lifts water pumps, firefighting fittings as NOC, Electricals fittings to the common areas, electro mechanic equipment, finishing to the entrance lobby, plinth protection, paving of areas, compound walls and other requirements as may be required to obtain completion/occupancy certificate. (Misc. Works)	Yes	11%	Submersible Pump is installed.

PROGRESS CHART

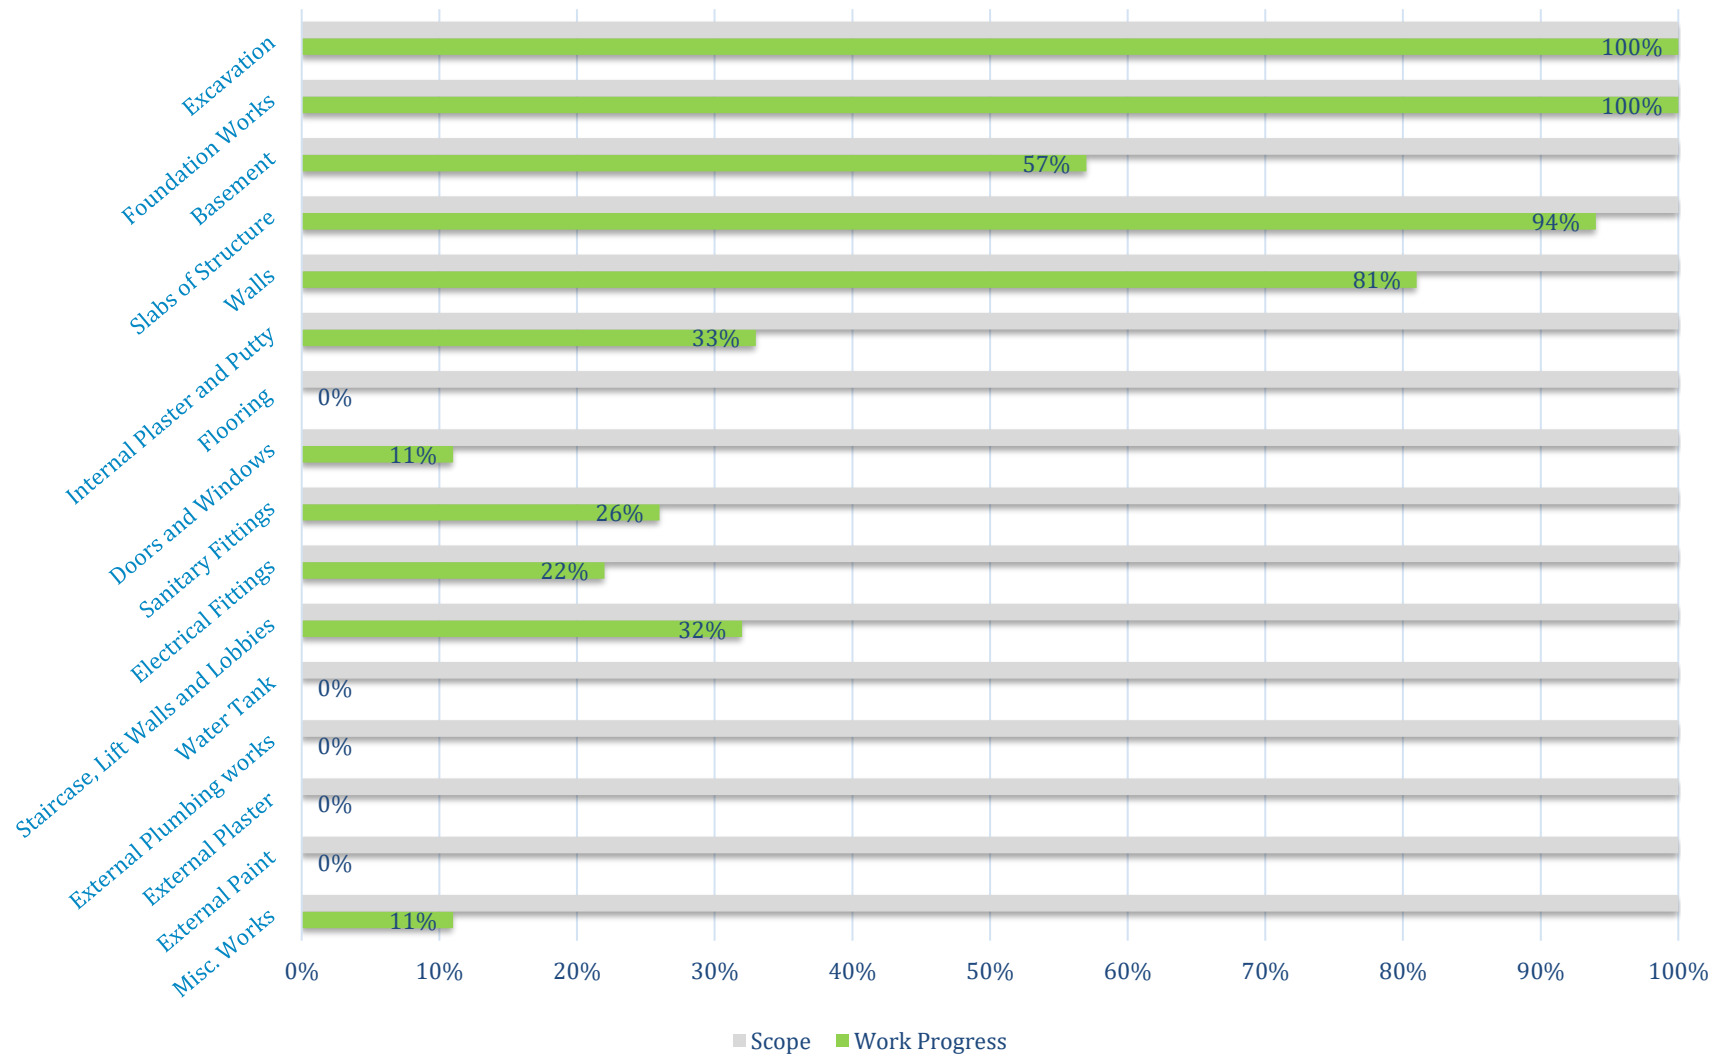

Progress Update for Common Areas, Facilities and Amenities in the Project

S. No.	Description	Applicable (Yes/No)	Percentage of Work Done	Remarks
1	Compound Walls	Yes	50%	Compound wall brickwork almost complete and finishing works yet to start.
2	Water supply	Yes	100%	Boring works complete.

Update on number and types of flats booked during the quarter

S.No	Unit Type	Total No. of Units in builder's Share	No. of Flats Booked				No. of Garages/ Covered Parking Booked			
			Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance	Opening Balance	Booked in the quarter	Cancelled in the quarter	Closing Balance
1	3 BHK	16	5	0	0	5	5	0	0	5

Status of financials in the project up to 31st December, 2020

S.No.	Description	Amount (in Rs.)
1	Amounts received from allottees against booking of units(for builder's share) (incl. GST)	1,62,40,552.00/-
2	Expenditure done towards completion of project	3,00,77,928.06/-

Status of Approvals

A. Approval Received

S. No.	Description	Date of Receipt
1	Provisional Fire Clearance	22.04.16
2	Sanctioning of Building Plan	29.05.18
3	RERA Registration	01.10.18

B. Approval Applied

S. No.	Description	Expected Date
NA	NA	NA

C. Approvals to be applied

S. No.	Description	Expected Date of application
NA	NA	NA

D. Modifications amendments or revisions, if any, issued by competent authority with regard to any sanctioned plans, layout plans, specifications, license, permit or approval for the project - NA

Project Site Photographs



