

SHREE OM SAI STRUCTURES And COLONISERS PVT.LTD.

ANNEXURE-A

Date: 11.07.2023

Quarterly Progress Report for quarter ending June of 2023.

I. PARTICULARS OF PROJECT

Project Registration Number	BRERAP63830-1/795/R-672/2019	Name of Project/Phase of Registered Project	SAI SHIVNANDAN PALACE
Name of Promoter	SHREE OM SAI STRUCTURES AND COLONISERS PVT. LTD.	Project Address	BEUR HASANPURA ROAD, NEAR KUSHWAHA CHOWK, ANISHABAD, PATNA.
Name of Co-promoter			
Project Registration is valid up to	31.12.2024		
Starting date of Project or Phase of the Project	31.10.2019		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 Years		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments - 56 NOS. Builder Share - 28 NOS. Landowner Share - 28 NOS.
1	1. 2 BHK - 24 NOS. 2. 3 BHK - 32 NOS.	650.00 950.00	56 NOS.	1. Booked/Allotted- 27 NOS. 2. Sold - 12

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF GARAGES

Building/Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
1	56	1. Booked/Allotted -	27 NOS.
		2. Sold -	12

Shree Om Sai Structures and Colonisers Pvt. Ltd.

[Signature]
Director

[Signature]
AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/39/25514



[Signature]

Corp. Office : Sai R.J.Kutir, R.K. Puram , Saguna More Danapur Road, Patna -801503
Call : 8051000888/999 . Web : www.shreeomsaigroup.in



IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport				
5.	Other Approval (s), if any, required for the Project.				

V. Construction Progress of the Project

1. Plan Case No. P/Beur-PRN-G+4/310/2018 (To beaded for each Building/Wing)

S. No. (1)	Tasks / Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	N/A
3.	Podiums (if any)	100%
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	100%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale.	100%
	Any other activities.	

Shree Om Sai Structures and Colonisers Pvt. Ltd.

[Signature]
Director

[Signature]
AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/300501



[Signature]

VI. Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	NO	N/A	
2.	Water Supply	NO	N/A	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	Septic tank & Plumbing
4.	Storm Water Drains	YES	100%	Plumbing
5.	Landscaping & Tree Planting	NO	N/A	N/A
6.	Street Lighting	YES	100%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	NO	N/A	
10.	Water Conservation/Rain Water Harvesting	YES	100%	
11.	Energy Management	NO	N/A	
12.	Fire Protection and Fire Safety Requirements	YES	100%	Fire Safety Tank
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT.

(A)	S. No.	Particulars
	1.	Front Elevation.
	2.	Rear Elevation
	3.	Side Elevation
(B)		Photograph of each floor

Shree Om Sai Structures and Colonisers Pvt. Ltd


Director

AMIT KUMAR
 B. ARCH
 C.O.A., DELHI, Reg. No. GA/96/25614


VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	0781102000009003
2.	Estimated Cost of the Project including land cost at the start of the Project.	1260.00 (IN LAKH)
3.	Amount received during the Quarter	92,81,108.68
4.	Actual Cost Incurred during the Quarter	83,41,136.01
5.	Net amount at end of the Quarter	7,44,669.41
6.	Total expenditure on Project till date	9,74,97,908.82
7.	Cumulative fund collected till the end of Quarter in question	11,84,98,588.52
8.	Cumulative expenditure done till the end of Quarter in question	9,74,97,908.82

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED	

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	04
2.	Agreement for Sale	00

Shree Om Sai Structures and Colonisers Pvt. Ltd


[Signature]
Director

[Signature]
AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/99/25514

[Signature]


XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

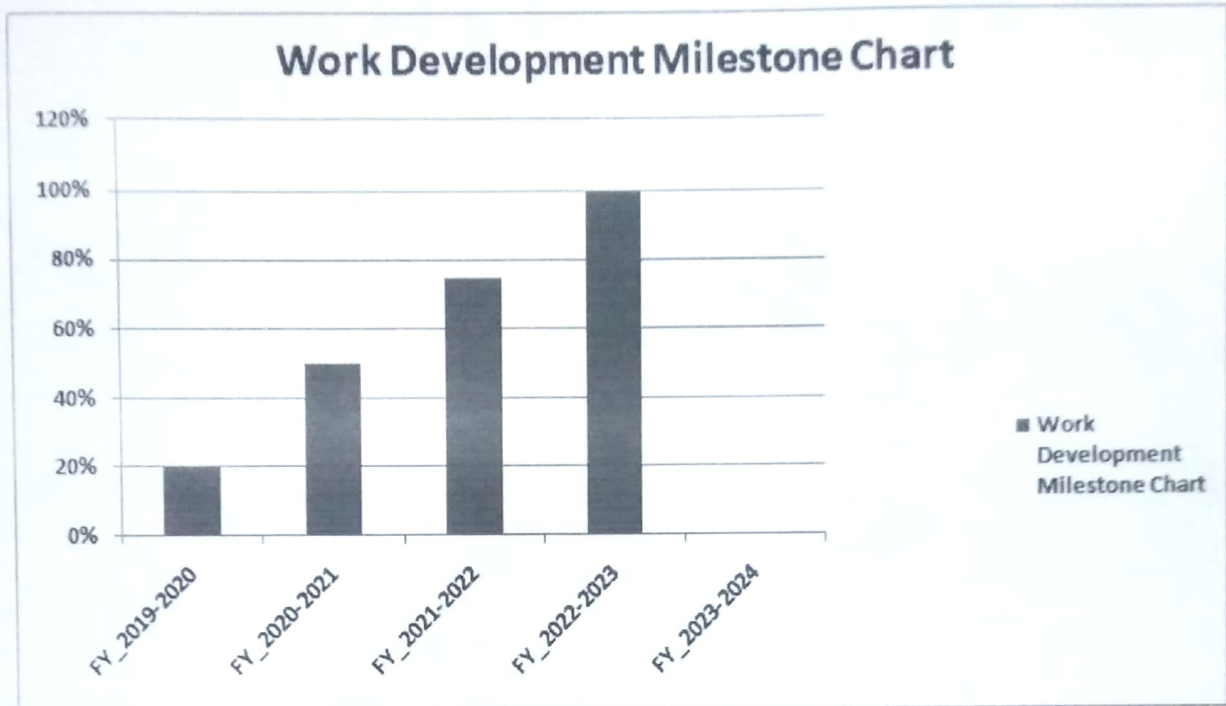

Project is in progress ahead as per time schedule.

The registration is valid for a period of 05 years 6 month commencing from 19.06.2019 and ending with 31.12.2024.

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Shree Om Sai Structures and Colonisers Pvt. Ltd.

[Signature]
Director

[Signature]
AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/99/25514

[Signature]



Signature of Promoter

Name : *Amitesh Arun*

Date : *11.07.2023*



Patna Division, Bihar, India
H38X+V88, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098319°
Lat 25.567161°
04/7/2023 05:43 PM




Patna Division, Bihar, India
H38X+Q8P, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098344°
Lat 25.566957°
04/7/2023 05:44 PM




Patna Division, Bihar, India
H38X+Q8P, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098344°
Lat 25.566957°
04/7/2023 03:19 PM



Patna Division, Bihar, India
H38X+V88, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098319°
Lat 25.567161°
04/7/2023 03:20 PM

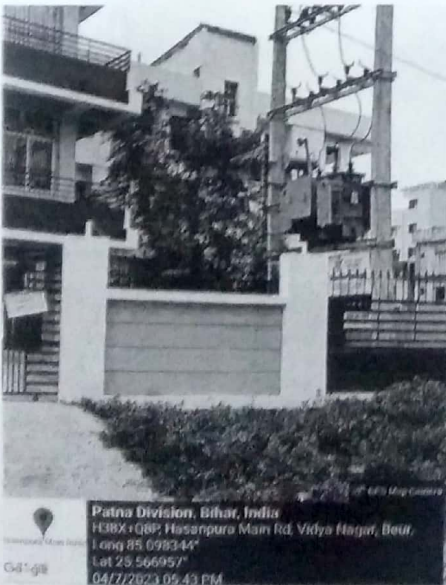

Patna Division, Bihar, India
H38X+Q8P, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098344°
Lat 25.566957°
04/7/2023 05:43 PM

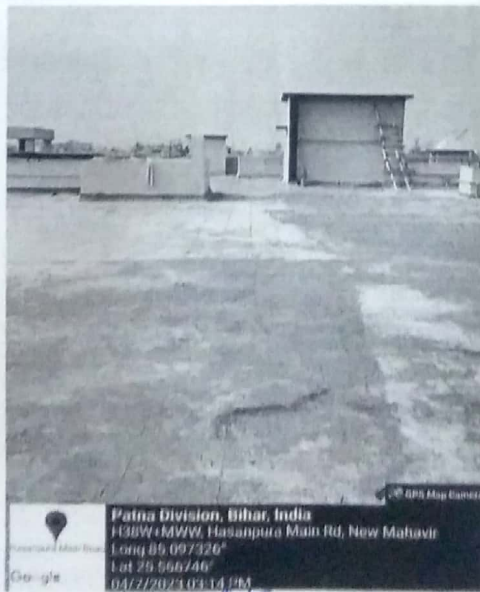

Patna Division, Bihar, India
H38W+MWW, Hasanpura Main Rd, New Mahavir,
Long 85.097326°
Lat 25.566746°
04/7/2023 03:14 PM



Patna Division, Bihar, India
H38X+Q8P, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098344°
Lat 25.566957°
04/7/2023 03:21 PM

Shree Om Sai Structures and Colonisers Pvt. Ltd.

[Signature]
Director

AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/99/2551

[Signature]



Scanned with OKEN Scanner




GPS Map Camera
Patna Division, Bihar, India
H38X+V88, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098319°
Lat 25.567161°
04/7/2023 04:27 PM



GPS Map Camera
Patna Division, Bihar, India
H38X+W6F, Hasanpura Main Rd, New Mahavir Colony,
Long 85.098050°
Lat 25.567341°
04/7/2023 04:28 PM




GPS Map Camera
Patna Division, Bihar, India
9546093777, New Patna Colony, North Sri Krishna Puri,
Long 85.098269°
Lat 25.567927°
04/7/2023 03:17 PM

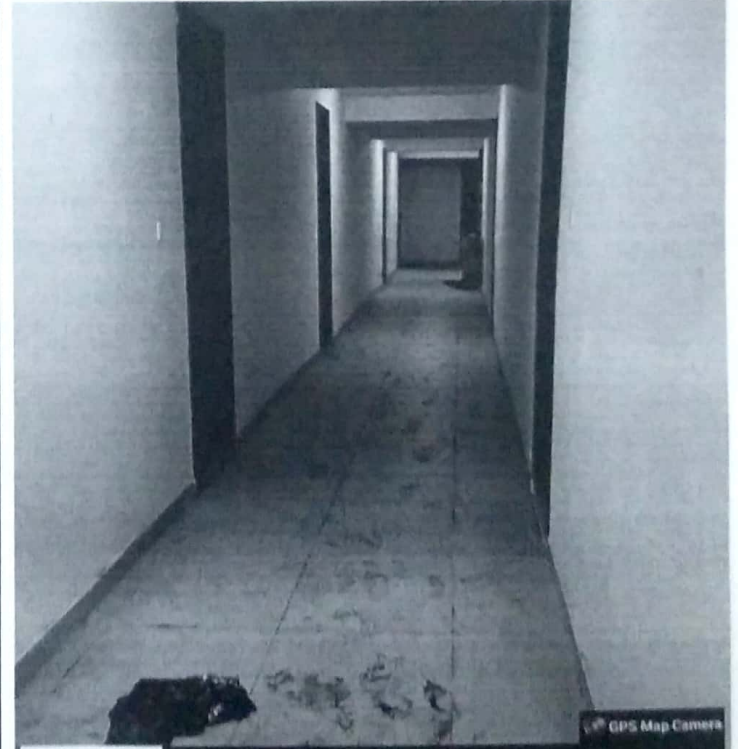


GPS Map Camera
Patna Division, Bihar, India
H38X+Q8P, Hasanpura Main Rd, Vidya Nagar, Beur,
Long 85.098344°
Lat 25.566957°
04/7/2023 04:27 PM

Shree Om Sai Structures and Colonisers Pvt. Ltd.


Director


AMIT KUMAR
B. ARCH
C.O.A., DELHI, Reg. No. CA/99/25514





FORM NO. 1
[See Regulation 3]

ARCHITECT'S CERTIFICATE
(To be submitted at the time of Registration of Ongoing Project and for withdrawal of
Money from Designated Account)

Date: 11.07.2023

To,
The M/s Shree Om Sai Structures And Colonisers Pvt. Ltd.
R. J. Sai Kurir, R. K. Puram, Khagaul-Danapur Road,
Saguna More, Patna-801503.

Subject: Certificate of Percentage of Work executed in the project

Having project, Sai Shivnandan Palace, No. of Building(s) 1 Wing(s) of the Phase-1, bearing the Bihar RERA registration No. BRERAP63830-1/795/R-672/2019 and being developed on the plot bearing CS No. ____ Khata No.- 44, 86 Survey Plot No. – 2062, 2064 demarcated by its boundaries (latitude and longitude of the end points) of the land 25.34021 & 25.34036 situated in New Patna Colony, Village- Beur, Block- Phulwari Sharif, Division- Beur, District- Patna, PIN - 801503. Admeasuring - 1966.73 sq.mts. area being developed by the promoter Shree Om Sai Structures And Coloniser Pvt. Ltd.

Sir,

I, We Ar. Amit Kumar have undertaken assignment as Architect / Licensed Surveyor of certifying Percentage of execution of Work of the Project, Sai Shivnandan Palace Building(s) 1 Wing(s) of the 1 Phase of the Project, Situated on the plot bearing C.S. No./Survey Plot No. 2062, 2064 of Village- Beur, Block – Phulwari Sharif, Division- Phulwari Sharif, District- Patna, PIN- 801503 admeasuring 1966.73 sq.mts. area being developed by the promoter Shree Om Sai Structures And Colonisers Pvt. Ltd.

1. Following technical professionals are appointed by Owner / Promoter :-

- (i) M/s /Shri/Smt. Amit Kumar as L.S. / Architect;
- (ii) M/s /Shri/Smt Brajesh Kumar as Structural Consultant
- (iii) M/s /Shri/Smt. Amit Kumar as Mechanical/Electrical/PlumbingConsultant (MEP)
- (iv) M/s /Shri/Smt. Er. Santosh Kumar as Site Supervisor

Based on site Inspection, with respect to reach of the Building/ Wing of the aforesaid Real Estate Project, I certify that as on the date of this certificate, the Percentage of Work done for each of the building/Wing of the Real Estate Project as registered vide number BRERAP63830-1/795/R-672/2019 Under Bihar RERA is as per table A herein below. The percentage of the work executed with respect to each of the activity of the entire phase is detailed in Table B.


CO.A, DELHI, Reg. No. CA/09/25514
B. ARCH
AMIT KUMAR



Table A

Building / Wing Number 1 (to be prepared separately for each Building/Wing of the Project)

1. Construction Progress of the Project		
1. Plan Case No. P/Beur-PRN-G+4/310/2018 (To beaded for each Building/Wing)		
S. No. (1)	Tasks / Activity(2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	N/A
3.	Podiums (if any)	100%
4.	Plinth	100%
5.	Stilt Floor	100%
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats/Premises.	100%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	100%


AMIT KUMAR
 B. ARCH
 C.O.A., DELHI, Reg. No. CN/31/25511

TABLE-B

Internal and External Development Work in respect of the entire Registered Phase.

2. Amenities and Common Area and External Infrastructure Development Works)				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	NO	N/A	
2.	Water Supply	NO	N/A	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	100%	Septic tank & Plumbing
4.	Storm Water Drains	YES	100%	Plumbing
5.	Landscaping & Tree Planting	NO	N/A	N/A
6.	Street Lighting	YES	100%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	NO	N/A	
10.	Water Conservation/Rain Water Harvesting	YES	100%	
11.	Energy Management	NO	N/A	
12.	Fire Protection and Fire Safety Requirements	YES	100%	Fire Safety Tank
13.	Closed Parking	YES	100%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	100%	
16.	Others (Option to Add More)			

Yours Faithfully,


AMIT KUMAR
 B. ARCH
 C.O.A., DELHI, Reg. No. CA/09/25514

Signature & Name (IN BLOCK LETTERS) of L.S./Architect

(Registration No./license No)
