


PROJECT NAME – KALAKRITI'S LALBAGH

PROMOTER NAME – KALAKRITI CONSTRUCTION

RERA REGISTRATION NO. BRERAP00359-1/371/R-175/2018

QUARTERLY PROGRESS REPORT FOR RERA, BIHAR

Period – JULY TO SEP. 2023



FORM-7

[REGULATION-9]

Quarterly Progress Report for quarter ending September of 2023

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP00359-1/371/R-175/2018	Name of Project/Phase of Registered Project	KALAKRITI'S LALBAGH
Name of Promoter	KALAKRITI CONSTRUCTION	Project Address	MAHULI TOLA, HARNICHAK, ANISABAD, PATNA-2
Name of Co-promoter	N/A		
Project Registration is valid up to	03/07/2021		
Starting date of Project or Phase of the Project	19/09/2018		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	3 YEARS		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments -
	1. 1 BHK	-			1. Booked/ Allotted - 13
	2. 2 BHK,	- 22			2. Sold -NIL
	3. 3 BHK	- 16		38	
	4. Shop	-			
	5. Bungalow	-			
	6. Plot etc.	-			

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- 13
	39	2. Sold	- NIL


For Kalakriti Construction
Partner

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of Further filing)

S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project

1. Building / Wing / Layout Number _____ (To beaded for each Building / Wing)

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	
		BLOCK-A	BLOCK-B
1.	Excavation (if any)	100%	100%
2.	Basements (if any)	100%	100%
3.	Podiums (if any)		
4.	Plinth	100%	100%
5.	Stilt Floor	100%	100%
6.	Slabs of Super Structure	100%	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	90%	90%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%	100%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	40%	45%

For Kalakriti Construction



Partner

10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	50%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%	0%

VI. Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)		Details
(1)	(2)	(3)	(4)		(5)
			BLOCK-A	BLOCK-B	
1.	Internal Roads & Footpaths	YES	20%	20%	
2.	Water Supply	YES	10%	10%	Deep Boring
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	0%	
4.	Storm Water Drains	NO			
5.	Landscaping & Tree Planting	YES	0%	0%	
6.	Street Lighting	YES	0%	0%	
7.	Community Buildings	NO			
8.	Treatment and Disposal of Sewage and Sullage Water	NO			

For Kalakriti Construction

Super

Partner

9.	Solid Waste Management & Disposal	YES	0%	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	0%	
11.	Energy Management	NO			
12.	Fire Protection and Fire Safety Requirements	YES	0%	0%	
13.	Closed Parking	YES	40%	40%	
14.	Open Parking	NO			
15.	Electrical Meter Room, Sub-Station, Receiving Station	NO			
16.	Others (Option to Add More)	NO			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			
8.	Water conservation/ Rain Water Harvesting			
9.	Energy Management			

For Kalakriti Construction

Partner

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	

VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	32219487385
2.	Estimated Cost of the Project including land cost at the start of the Project	5,98,04,000=00
3.	Amount received during the Quarter	4,20,000=00
4.	Actual Cost Incurred during the Quarter	4,82,302=00
5.	Net amount at end of the Quarter	1,36,499=46
6.	Total expenditure on Project till date	3,60,75,657=65
7.	Cumulative fund Collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	

IX. Details of Mortgage or Charge if any created	

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO


For Kalakriti Construction

 Partner

B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NO
2.	Agreement for Sale	
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

Undertaking:

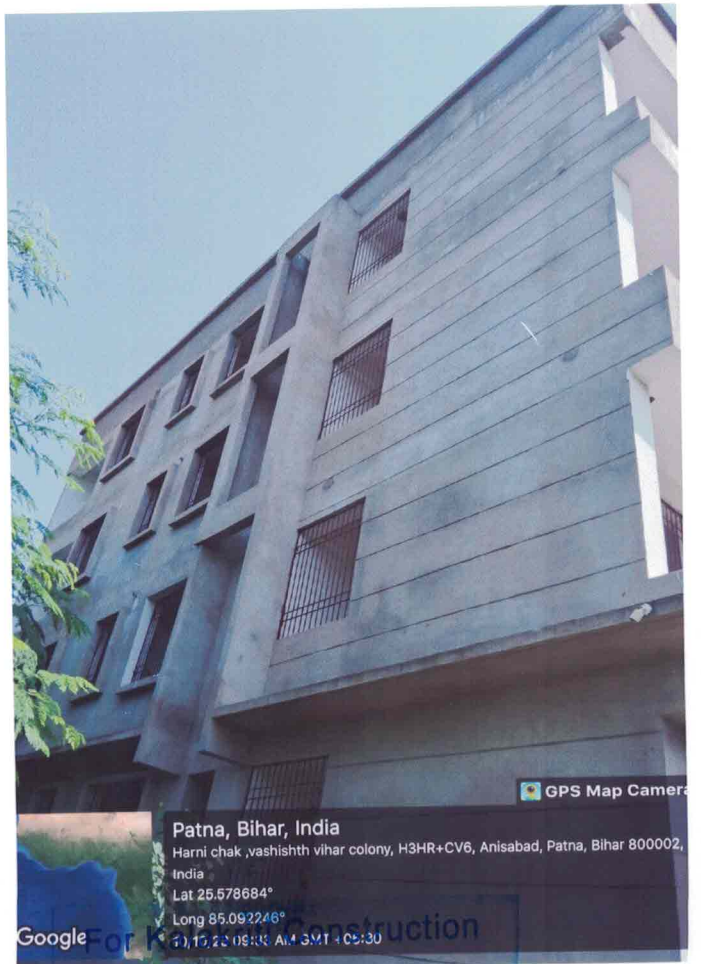
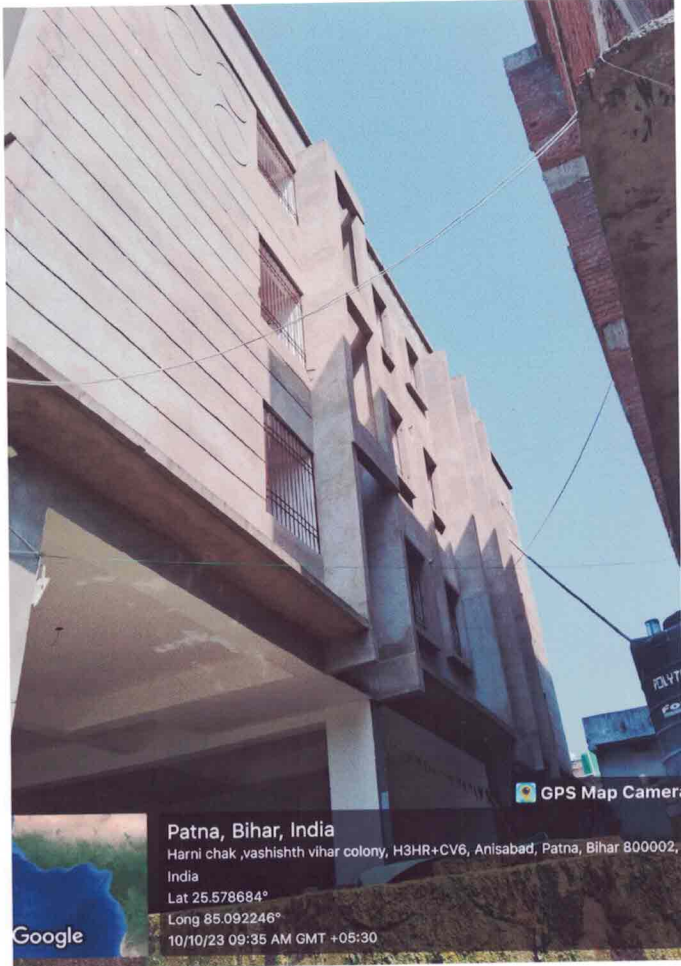
I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

For Kalakriti Construction

Partner
Signature of Promoter

Name:

Date:

Kalakriti's Lalsagh



Shyam Partner
