

FORM-7
[REGULATION-9]

Quarterly progress report for quarter ending March/June/sept/December of 2023
(year)

I. PARTICULARS OF PROJECT

Project Registration Number	BRERAP-23027-1/225/R-1520/2023	Name of Project/Phase of Registered Project	WINSOME P. R. RESIDENCY
Name of Promoter	SUDHIR KUMAR	Project Address	P. NO.-1003, KHATA -166, THA -37, MAUZA -NAGLA, PATNA C
Name of Co-promoter	PREMCHAND KUMAR NIRMAL		
Project Registration is valid up to	31-12-2028		
Starting date of Project or Phase of the Project			
Type of Project or Phase of the Project	1. Residential 2. Commercial 3. Residential-cum-Commercial 4. Plotted project	3. Residential-cum-Commercial	
Period of validity of map by the Competent Authority	From - 22-09-2022 to + 5 years		

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments 8 Shops & 42 Apartments
	1. 1 BHK - 2. 2 BHK, - 3. 3 BHK - 4. Shop - 5. Bungalow - 6. Plot etc. -		8 Shops & 42 Apartments	1. Booked/Allotted - 0 apartment 2. Sold -

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	0
1	42	2. Sold	

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director

3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. NAGLA (To be added for each Building / Wing)
PMAA/PCRN/MALSALAMI /G+07/43/2021

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	Site office and Godown work done
2.	Basements (if any)	
3.	Podiums (if any)	
4.	Plinth	
5.	Stilt Floor	
6.	Slabs of Super Structure	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats / Premises.	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other	

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director

requirements as may be required to complete project as per Specifications in Agreement of Sale.	
Any other activities.	

VI. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage (Chamber, Line, Septic Tank, STP)			
4.	Storm Water Drains			
5.	Landscaping & Tree Planting			
6.	Street Lighting			
7.	Community Buildings			
8.	Treatment and Disposal of Sewage and Sullage Water			
9.	Solid Waste Management & Disposal			
10.	Water Conservation / Rain Water Harvesting			
11.	Energy Management			
12.	Fire Protection and Fire Safety Requirements			
13.	Closed Parking			

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director

14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station			
16.	Others (Option to Add More)			

VI A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENTAGE OF ACTUALWORK DONE (As on date of certificate)	Details
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		
	1.	Front Elevation	Work not started till date, land photo Attached
	2.	Rear Elevation	Work not started till date, land photo Attached

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director

	3.	Side Elevation	Work not started till date, land photo Attached
(B)		Photograph of each floor	

VIII. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	37240200000397
2.	Estimated Cost of the Project including land cost at the start of the Project	1,457.50 lakhs
3.	Amount received during the Quarter	00 .00
4.	Actual Cost Incurred during the Quarter	00 .00
5.	Net amount at end of the Quarter	00 .00
6.	Total expenditure on Project till date	
7.	Cumulative fund collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED	

X. MISCELLANEOUS	
A	List of Legal Cases (if any)
1.	Case No.
2.	Name of Parties
B	Sale/Agreement for Sale during the Quarter
1.	Sale Deed
2.	Agreement for Sale

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART
Weather the project in progress is as per time schedule or lagging behind?

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.



Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar


Signature of Promoter **Director**

Name:

Date:

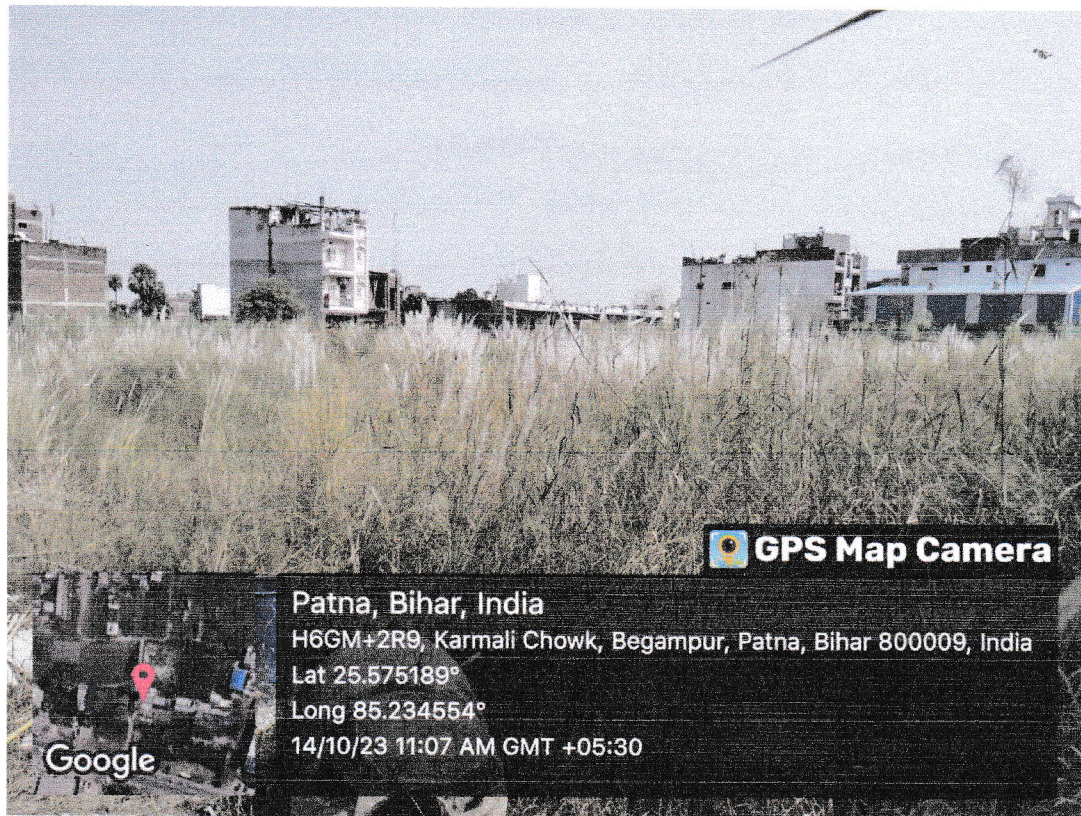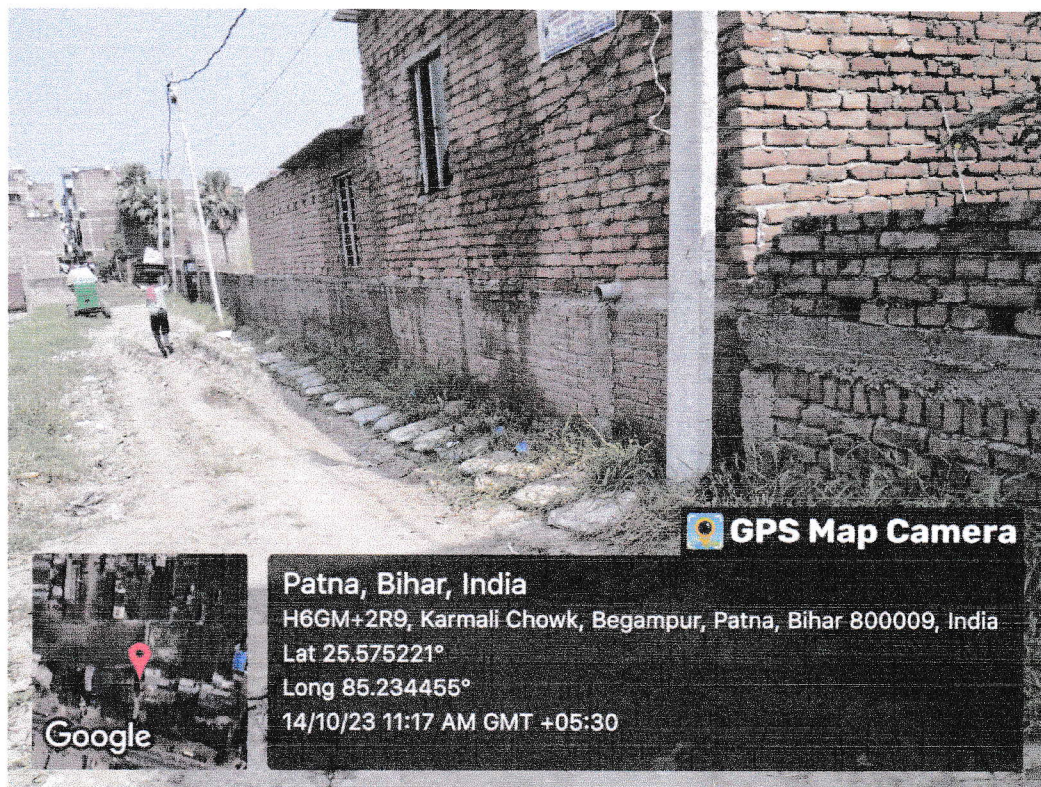

Winsome Builder & Developers Pvt. Ltd
Sydhir Kumar
Director

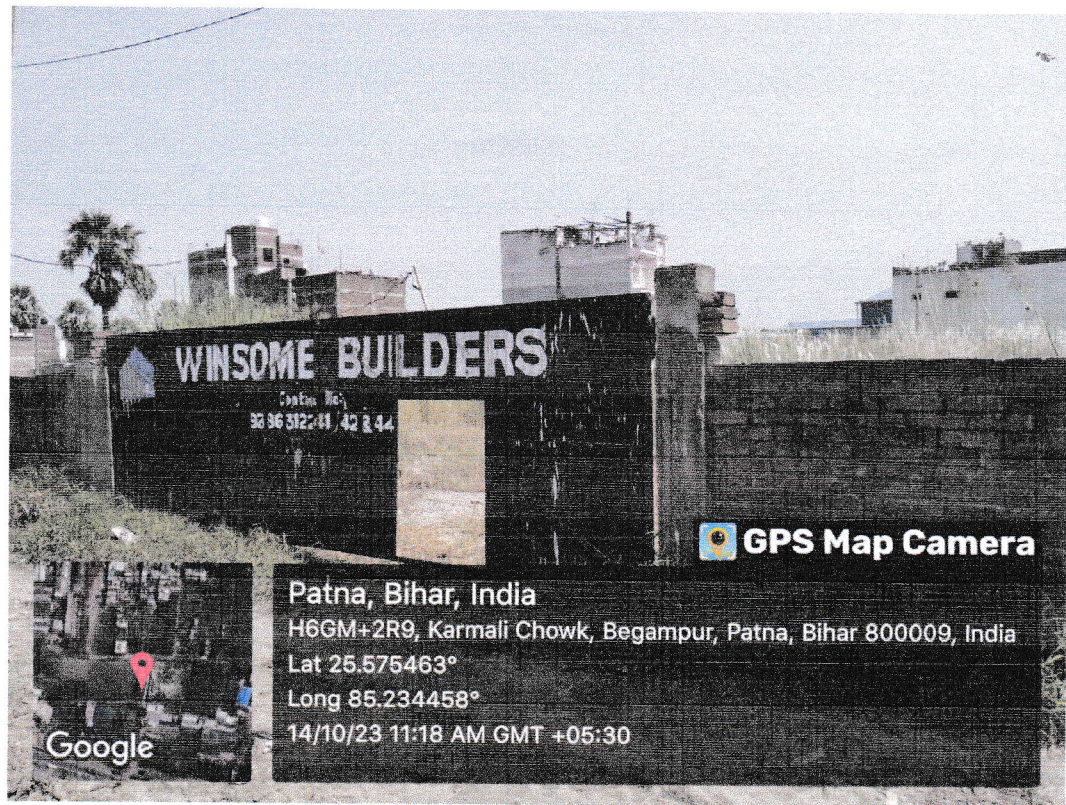

Winsome Builder & Developers Pvt. Ltd

Sudhir Kumar

Director
