

FORM-7**[REGULATION-9]****Quarterly Progress Report for quarter ending Oct-Dec of 2023 (Year)****I. PARTICULARS OF PROJECT**

Project Registration Number	BRERAP00071-4/1156/R-911/2020
Name of Project/Phase of Registered Project	SHREE SAVITRI LOK
Name of Promoter	SHREE VASI HOMES PVT. LTD.
Project Address	PLOT NO.- 05, MAUZA- KUMHRAR, THANA- AGAMKUAN, THANA NO.- 12, KHATA NO.- 159, TAUZI NO.- 26, DIST.- PATNA, BIHAR
Name of Co-promoter	NA
Project Registration is valid up to	30/01/2024
Starting date of Project or Phase of the Project	02/02/2020
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Shree Savitri Lok	3 BHK	1013.00	5	1. Booked-- 00 2. Sold--08
Shree Savitri Lok	3 BHK	1052.00	5	
Shree Savitri Lok	3 BHK	1138.00	5	
Shree Savitri Lok	2 BHK	785.00	1	In Quarter Oct-Dec 2023 1. Booked-- 00 2. Sold--00
Shree Savitri Lok	2 BHK	768.00	5	
Shree Savitri Lok	2 BHK	844.00	5	

For Shree Vasi Homes Private Limited

Ran- Kausi Pratap Singh
Managing Director

Page 1 of 8

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Shree Savitri Lok	No Garages available	1. Booked/Allotted - 2. Sold -	

IV. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project**1. Plan Case No.-P-Kumhrar-PRN-B+G+5/75/2019 Shree Savitri Lok (To be added for each Building / Wing)**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	NA
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%

For Shree Vasi Homes Private Limited

Ran. Kauri Prady
Managing Director

Page 2 of 8

9.	Staircases, Lifts Walls and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	100%

VI. (Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	Yes	100%	
6.	Street Lighting	Yes	100%	
7.	Community Buildings	Yes	100%	

For Shree Vasi Homes Private Limited
Page 3 of 8

Ran. Kaushal Pratap Singh
Managing Director

8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	Yes	100%	
13.	Closed Parking	Yes	100%	
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	Yes	100%	
16.	Others (Option to AddMore)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor

VIII. Financial Progress of the Project


S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	38986470360
2	Estimated Cost of the Project including land cost at the start of the Quarter (In Lakh)	717.52/-
3	Amount received during the Quarter	0.00/-
4	Actual Cost Incurred during the Quarter	33,88,798.00/-
5	Net amount at end of the Quarter	54,847.96/-
6	Total expenditure on Project till date	7,42,59,110.00/-
7	Cumulative fund collected till the end of Quarter in question	5,48,62,510.00/-
8	Cumulative expenditure done till the end of Quarter in question	7,42,59,110.00/-

For Shree Vasi Homes Private Limited

Ram. Kausi Prady Singh
Page 4 of 8
Managing Director

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED**13097112.40/-****X. MISCELLANEOUS**

A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	08
2.	Agreement for Sale	

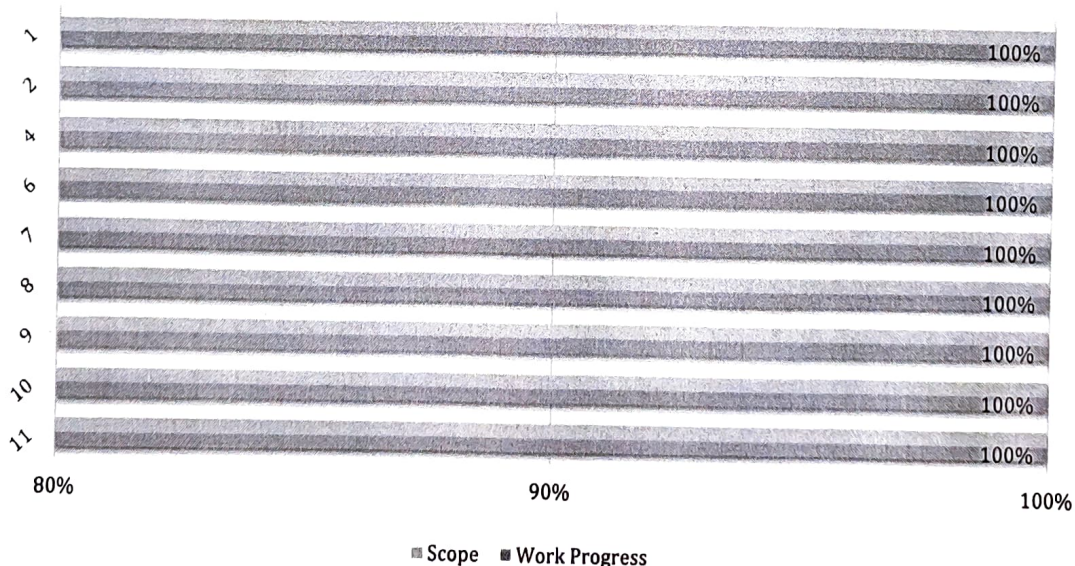XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART**Weather the project in progress is as per time schedule or lagging behind?****PROGRESS CHART**

For Shree Vasi Homes Private Limited

Ran- Kaur Singh
Page 5 of 8
Managing Director

Project Site Photographs

Front Elevation




For Shree Vasi Homes Private Limited

Ram. Kauri Pratap Singh

Managing Director

Page 6 of 8



Patna, Bihar, India

J62H+3CC, Daud Bigha, Mahatma Gandhi Nagar, Chitragupta Nagar, Patna, Bihar
800020, India

Lat 25.599998°

Long 85.178438°

05/01/24 03:51 PM GMT +05:30


OPS Map Camera

For Shree Vasi Homes Private Limited

Ravi Kauri Pratyap Singh

Managing Director

Page 7 of 8

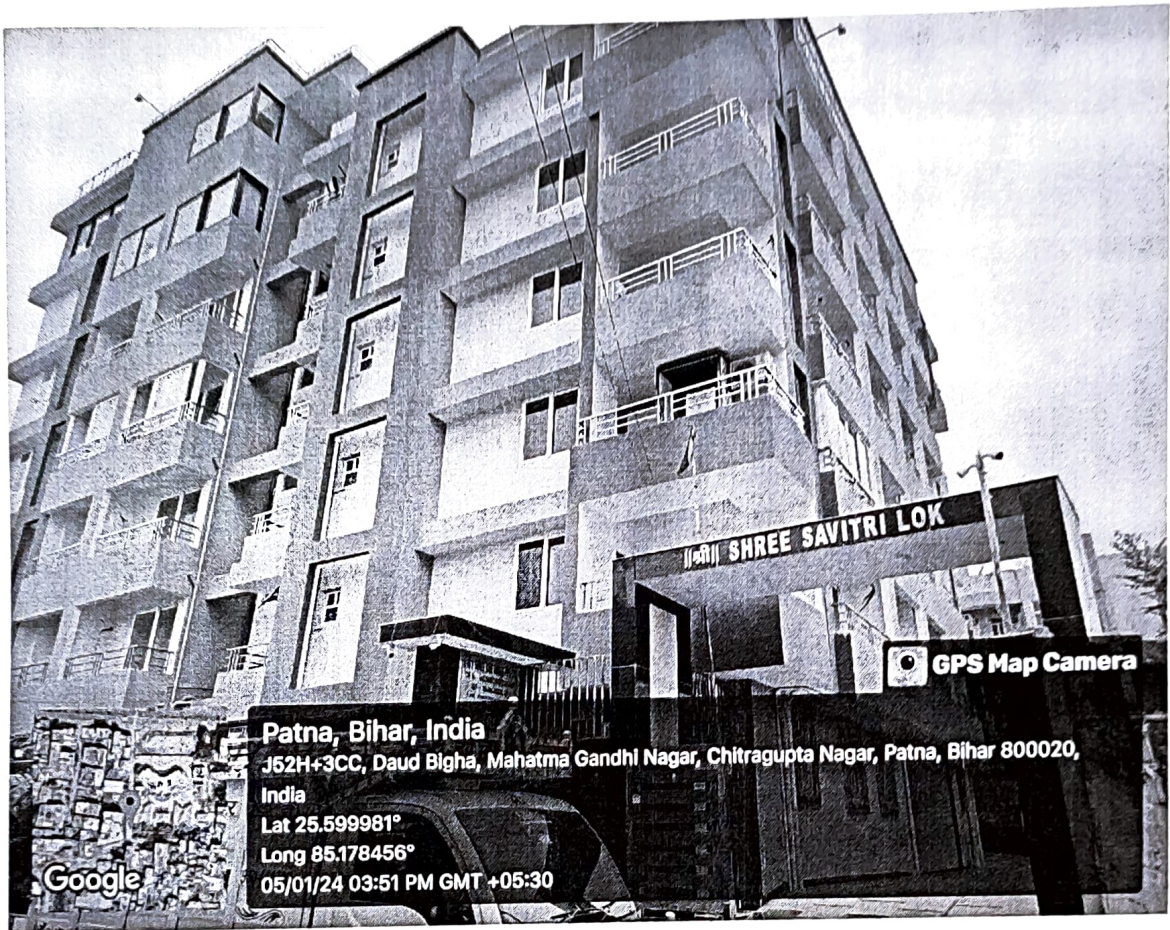

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter
Shree Vasi Homes Pvt. Ltd.

For Shree Vasi Homes Private Limited
Ran - Kausar Pratap Singh
Managing Director

Director

Date :
