


FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending Jan-Mar of 2024 (Year)

I. PARTICULARS OF PROJECT	
Project Registration Number	BRERAP00071-4/1156/R-911/2020
Name of Project/Phase of Registered Project	SHREE SAVITRI LOK
Name of Promoter	SHREE VASI HOMES PVT. LTD.
Project Address	PLOT NO.- 05, MAUZA- KUMHRAR, THANA- AGAMKUAN, THANA NO.- 12, KHATA NO.- 159, TAUZI NO.- 26, DIST.- PATNA, BIHAR
Name of Co-promoter	NA
Project Registration is valid up to	30/01/2024
Starting date of Project or Phase of the Project	02/02/2020
Type of Project or Phase of the Project	Residential/Group Housing
Period of validity of map by the Competent Authority	Three Years from the date of passing of MAP

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS				
Building/Block Number	Apartment Type	Carpet Area (In Sqft)	Total Number of sanctioned apartments	Total Number of Apartment
Shree Savitri Lok	3 BHK	1013.00	5	1. Booked-- 00 2. Sold--09
Shree Savitri Lok	3 BHK	1052.00	5	
Shree Savitri Lok	3 BHK	1138.00	5	
Shree Savitri Lok	2 BHK	785.00	1	In Quarter Jan-Mar 2024 1. Booked-- 00 2. Sold--01
Shree Savitri Lok	2 BHK	768.00	5	
Shree Savitri Lok	2 BHK	844.00	5	

For Shree Vasi Homes Private Limited


Director

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
Shree Savitri Lok	No Garages available	1. Booked/Allotted - 2. Sold -	

IV. DETAILS OF BUILDING APPROVALS


(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

V. Construction Progress of the Project**1. Plan Case No.-P-Kumhrar-PRN-B+G+5/75/2019 Shree Savitri Lok (To be added for each Building / Wing)**

S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	100%
3.	Podiums (if any)	NA
4.	Plinth	100%
5.	Stilt Floor	NA
6.	Slabs of Super Structure	100%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	100%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	100%

For Shree Vasi Homes Private Limited


Director

Page 2 of 8

9.	Staircases, Lifts Walls and Lobbies at each Floor level, Overhead and Underground Water Tanks.	100%
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	100%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	100%

VI. (Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	No		
2.	Water Supply	Yes	100%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	Yes	100%	
4.	Storm Water Drains	No		
5.	Landscaping & Tree Planting	No		
6.	Street Lighting	No		
7.	Community Buildings	No		

For Shree Vasi Homes Private Limited

Satish Singh
Director

7.	Community Buildings	No		
8.	Treatment and Disposal of Sewage and Sullage Water	No		
9.	Solid Waste Management & Disposal	No		
10.	Water Conservation / RainWater Harvesting	No		
11.	Energy Management	No		
12.	Fire Protection and FireSafety Requirements	No		
13.	Closed Parking	Yes	100%	
14.	Open Parking	No		
15.	Electrical Meter Room, Sub-Station, Receiving Station	No		
16.	Others (Option to AddMore)	No		

VII. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	S. No.	Particulars
	1.	Front Elevation.- Attached Below
	2.	Rear Elevation.- Attached Below
	3.	Side Elevation.- Attached Below
(B)		Photograph of each floor

VIII. Financial Progress of the Project

S.No.	Particulars	Amount (in Rs.)
1	Project Account No.	38986470360
2	Estimated Cost of the Project including land cost at the start of the Quarter (In Lakh)	717.52/-
3	Amount received during the Quarter Without GST	60,00,000.00/-
4	Actual Cost Incurred during the Quarter	23,84,496.00/-
5	Net amount at end of the Quarter	44,151.76/-
6	Total expenditure on Project till date	7,66,43,606.00/-
7	Cumulative fund collected till the end of Quarter in question	5,82,00,000.00/-
8	Cumulative expenditure done till the end of Quarter in question	7,66,43,606.00/-

For Shree Vasi Homes Private Limited

Saloni Singh
Director

IX. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

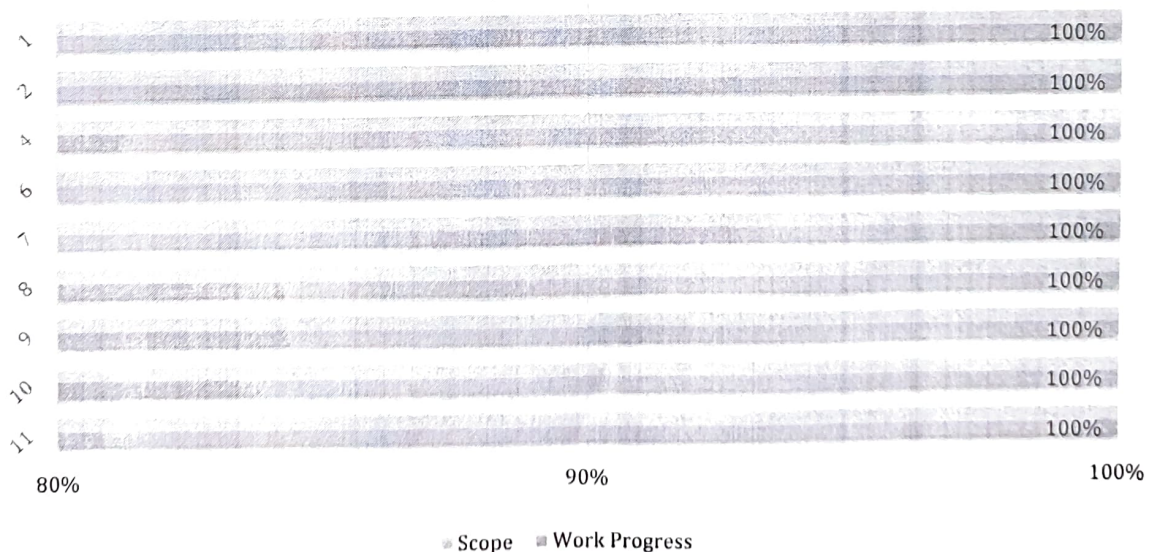
9312154.40/-

X. MISCELLANEOUS

A	List of Legal Cases (if any)	
1.	Case No.	NA
2.	Name of Parties	NA
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	09
2.	Agreement for Sale	

XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

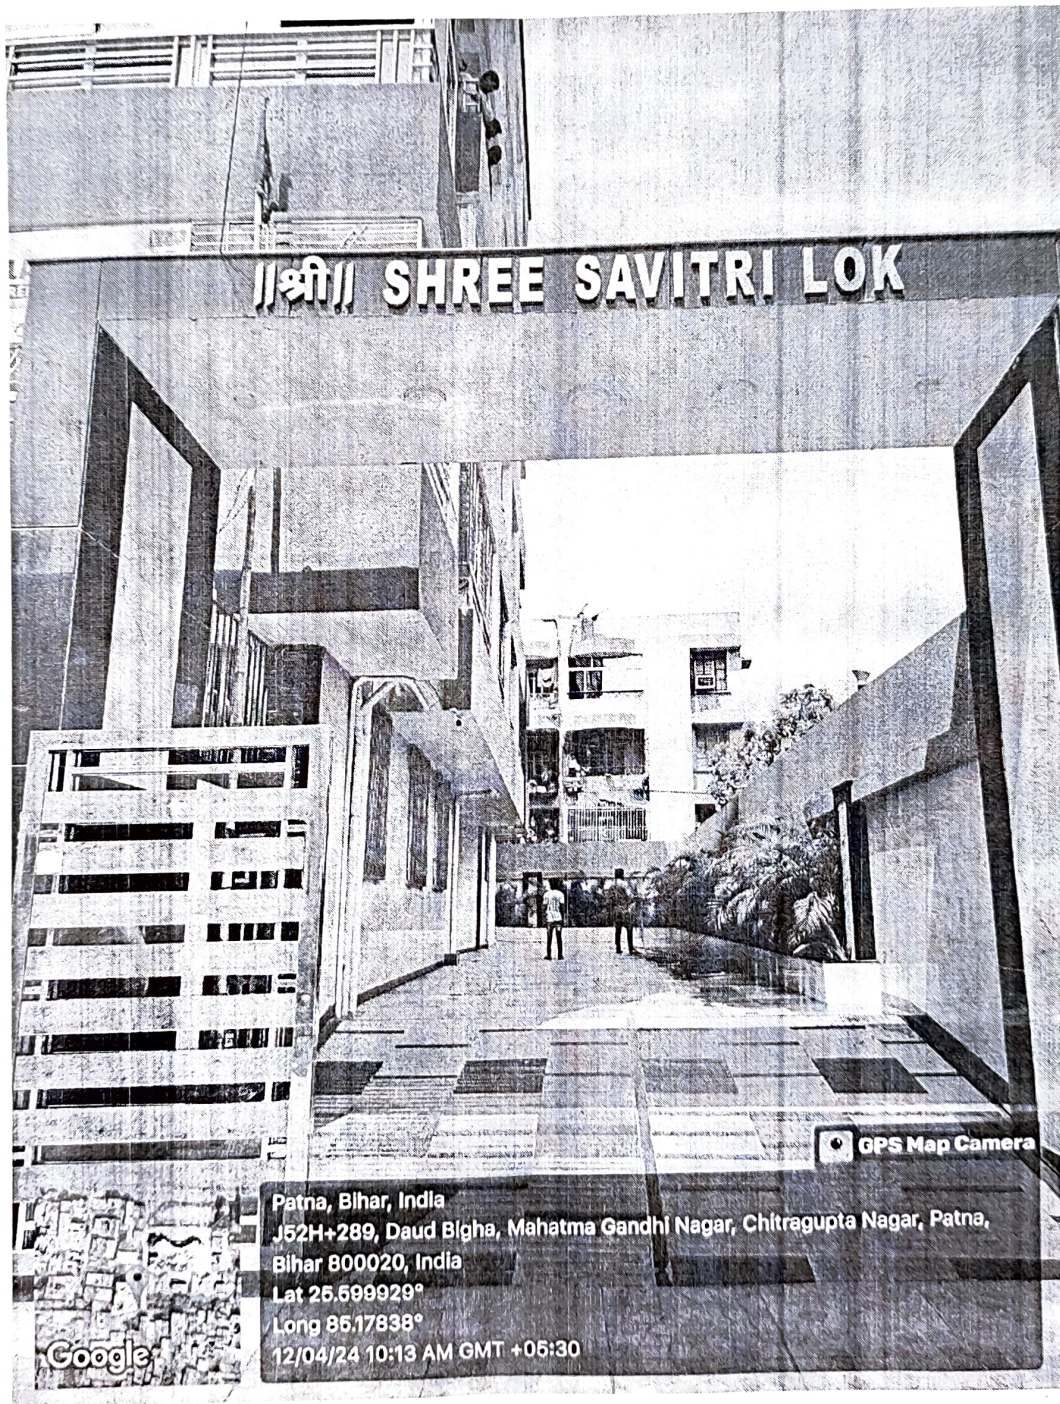
PROGRESS CHART

For Shree Vasi Homes Private Limited

Salvinder Singh
Director

Project Site Photographs

Front Elevation



For Shree Vasi Homes Private Limited

Saloni Singh
Director



Patna, Bihar, India
J52H+2B9, Daud Bigha, Mahatma Gandhi Nagar, Chitragupta Nagar, Patna,
Bihar 800020, India
Lat 25.599975°
Long 85.178429°
12/04/24 10:13 AM GMT +05:30

For Shree Vasi Homes Private Limited

Rajendra Singh

Director



Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

Signature of Promoter
Shree Vasi Homes Pvt. Ltd.

For Shree Vasi Homes Private Limited

Saloni Singh
Director

Director
Date :
