

FORM-7
[REGULATION-9]

Quarterly Progress Report for quarter ending March of 2024

I. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP92310-1/221/R-1515/2023	Name of Project/Phase of Registered Project	AARTI KUNJ
Name of Promoter	NANDISH DEVELOPERS AND CONSTRUCTION PVT.LTD	Project Address	DHANAWAN, NEAR TRIRAJ COLD STORAGE, BODH GAYA, GAYA
Name of Co-promoter	N/A		
Project Registration is valid up to	15/09/2027		
Starting date of Project or Phase of the Project	12/01/2023		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority			

II. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS					
Building/Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments -
	1. 1 BHK	-		16	1. Booked/ Allotted - NIL 2. Sold - NIL
	2. 2 BHK,	- 4			
	3. 3 BHK	- 12			
	4. Shop	-			
	5. Bungalow	-			
	6. Plot etc.	-			

III. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	- NIL
	16	2. Sold	- NIL

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.

Rahul Kumar

DIRECTOR

IV. DETAILS OF BUILDING APPROVALS (If already filed along with Registration Application, then there is no need of Further filing)					
S.NO.	Name of the Approval / N.O.C. / Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval (S), if any, required for the Project				

V. Construction Progress of the Project		
1. Building / Wing / Layout Number _____ (To beaded for each Building / Wing)		
S. No. (1)	Tasks / Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)
1.	Excavation (if any)	100%
2.	Basements (if any)	
3.	Podiums (if any)	0%
4.	Plinth	100%
5.	Stilt Floor	0%
6.	Slabs of Super Structure	0%
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.

Rahul Kumar
DIRECTOR

10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as may be required to complete project as per specifications in Agreement of Sale. Any other activities.	0%

VI. Amenities and Common Area and External Infrastructure Development Works)

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	0%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	NO		
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO		
8.	Treatment and Disposal of Sewage and Sullage Water	NO		
9.	Solid Waste Management & Disposal	YES	0%	

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.

Rahul Kumar
DIRECTOR

10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking			
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VI. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Details
1.	Internal Roads & Footpaths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Landscaping and Tree Planning			
6.	Street Lighting			
7.	Disposal of sewage & Sullage Water			
8.	Water conservation/ Rain Water Harvesting			
9.	Energy Management			

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.


Rahul Kumar
DIRECTOR

VII. GEO TAGGED AND DATE PHOTOGRAPH OF (EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation.	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	




NANDISH DEVELOPERS
 & CONSTRUCTIONS PVT. LTD.

Rahul Kumar
 DIRECTOR

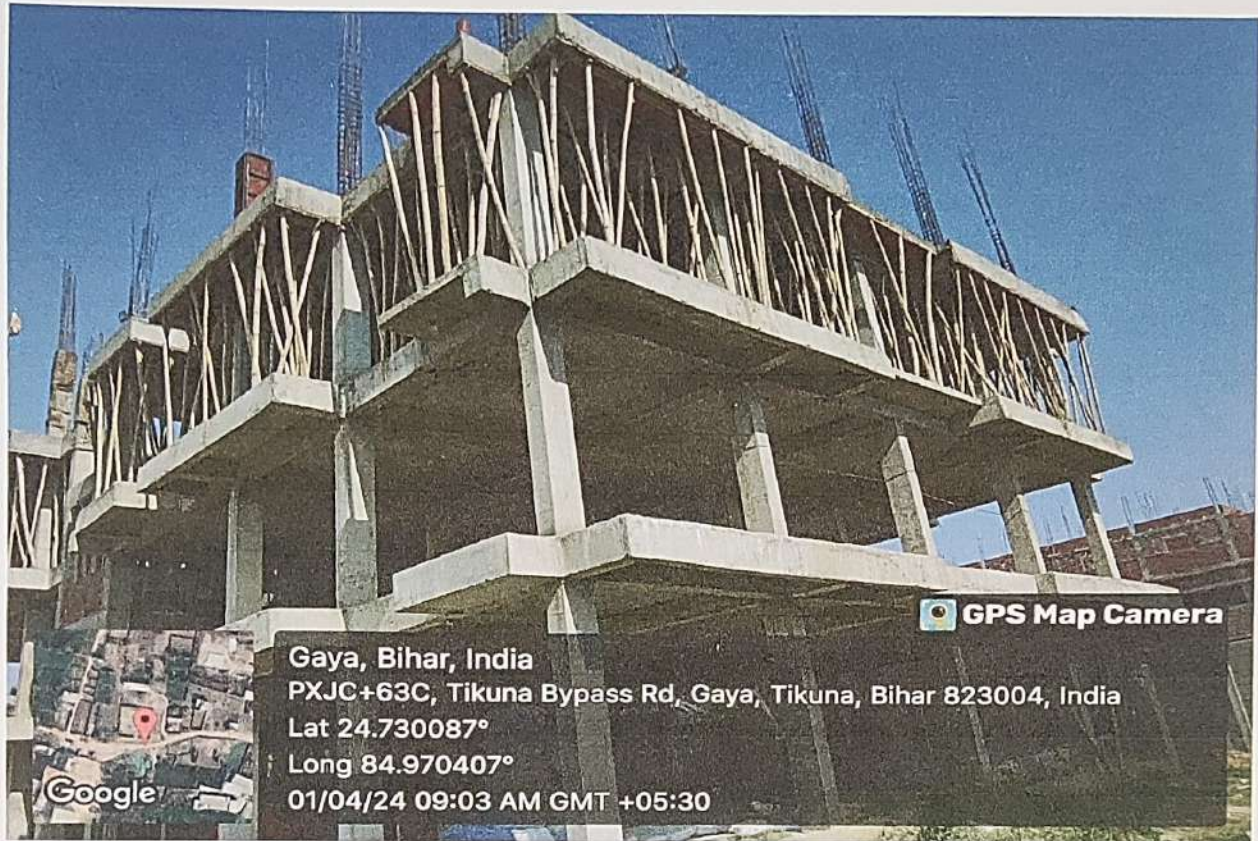

Gaya, Bihar, India
PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India
Lat 24.730087°
Long 84.970407°
01/04/24 09:03 AM GMT +05:30

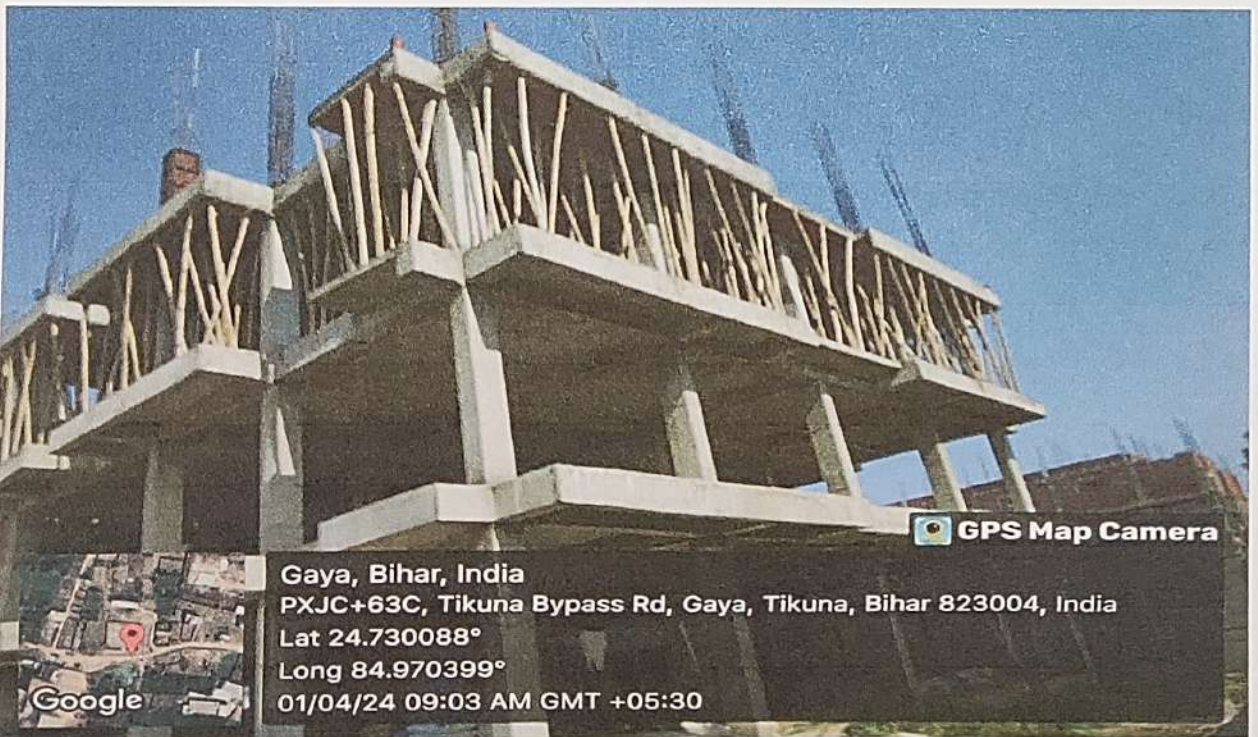

Gaya, Bihar, India
PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India
Lat 24.730088°
Long 84.970399°
01/04/24 09:03 AM GMT +05:30

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.

Rahul Kumar
DIRECTOR

VIII. Financial Progress of the Project		
S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	5251676779
2.	Estimated Cost of the Project including land cost at the start of the Project	2,57,00,000=00
3.	Amount received during the Quarter	11,11,111=00
4.	Actual Cost Incurred during the Quarter (Company Account)	11,19,041=00
5.	Net amount at end of the Quarter	1,37,640=16
6.	Total expenditure on Project till date	38,30,858=00
7.	Cumulative fund Collected till the end of Quarter in question	
8.	Cumulative expenditure done till the end of Quarter in question	

IX. Details of Mortgage or Charge if any created	

X. MISCELLANEOUS		
A	List of Legal Cases (if any)	
1.	Case No.	NO
2.	Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
XI. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.

Rahul Kumar
DIRECTOR

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my/our knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

NANDISH DEVELOPERS
& CONSTRUCTIONS PVT. LTD.


Rahul Kumar
DIRECTOR

Signature of Promoter

Name:

Date:



 **GPS Map Camera**



Gaya, Bihar, India


PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India


Lat 24.729973°

Long 84.970302°

01/04/24 09:02 AM GMT +05:30



 **GPS Map Camera**

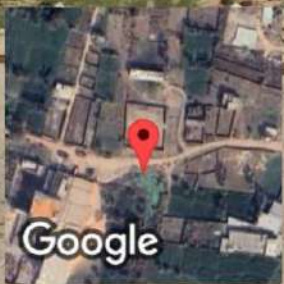

Gaya, Bihar, India

PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India

Lat 24.729988°

Long 84.970284°

01/04/24 09:02 AM GMT +05:30



 **GPS Map Camera**

Gaya, Bihar, India

PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India


Lat 24.730087°

Long 84.970407°

01/04/24 09:03 AM GMT +05:30

Google



 **GPS Map Camera**

Gaya, Bihar, India

PXJC+63C, Tikuna Bypass Rd, Gaya, Tikuna, Bihar 823004, India

Lat 24.730088°

Long 84.970399°

01/04/24 09:03 AM GMT +05:30

Google
