

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending June of 2024 (year)

I. PARTICULARS OF PROMOTERS

Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U51909BR2012PTC018934	Name of Firm	CHAURASIA IRON AND STEEL PRIVATE LIMITED
Firm Address :	BLOCK-B, 306, GANDHI NAGAR, KANTI FACTORY ROAD, KANKARBAGH, PATNA-800020		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	3 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	00	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT

Project Registration Number	BRERAP51727-1/169/R-1334/2022	Name of Project/Phase of Registered Project	JAGAT PRASAD ENCLAVE
Name of Promoter	CHAURASIA IRON AND STEEL PRIVATE LIMITED	Project Address	70 FEET ROAD ANJANPUR COLONY, DASRATHA, SIPARA, PATNA-800002
Name of Co-promoter	N/A		
Project Registration is valid up to	01/12/2026		
Starting date of Project or Phase of the Project	01/04/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	30-10-2024		

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERARanchandran K. Chourasia
Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments 40-FLATS	Total Number of Apartments in Promoter's share - FLAT-19	Total Number of Apartments in Landowner's share - FLAT-21
BLOCK-A	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	40			1. Booked / Allotted -02	3. Booked/ Allotted-NIL
	2. Sold-NIL				Sold -NIL	
				Percentage of booking 10.5%	Percentage of booking 0%	
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments 25-FLATS	Total Number of Apartments in Promoter's share - FLAT-25	Total Number of Apartments in Landowner's share -
BLOCK-B	1. 1 BHK 2. 2 BHK, - 3. 3 BHK 4. Shop 5. Bungalow 6. Plot etc.	05 20			1. Booked / Allotted -NIL	3. Booked/ Allotted-N/A
	2. Sold-NIL	Sold -N/A				
				Percentage of booking 0%	Percentage of booking N/A	

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-A	40	1. Booked/Allotted	02
		2. Sold	NIL
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-B	25	1. Booked/Allotted	NIL
		2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Rajendra Kr Chaurasia
Director

3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/CHITKOHRA-PRN-1B+G+5/219/2020

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) (BLOCK-A)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	83.33%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Chaurasia
Director

11.	<p>Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.</p> <p>Any other activities</p>	5%	
-----	--	----	--

1. Plan Case No. P/CHITKOHRA-PRN-1B+G+5/219/2020

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) (BLOCK-B)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	0%	
2.	Basements (if any)	0%	
3.	Podiums (if any)	N/A	
4.	Plinth	0%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	0%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Rajendra K. Chaurasia
Director

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	5%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Chaurasia
Director

5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4	Drains			

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Chaurasia
Director

5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT

(A)	Sr. No.		BLOCK-A	BLOCK-B
	1.	Front Elevation	Attach	
	2.	Rear Elevation	Attach	
	3.	Side Elevation	Attach	
(B)		Photograph of each floor		

X. FINANCIAL PROGRESS OF THE PROJECT

S. No.	Particulars	Amount (In Rs.)
(1)	(2)	(3)
1.	Project Account No.	27630200000799
2.	Estimated Cost of the Project including land cost at the start of the Project	19,67,90,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	12,32,90,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	25,00,000=00
5.	Amount received during the Quarter	29,50,000=00
6.	Actual Cost Incurred during the Quarter	81,38,742=00

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramcharan K. Chaurasia
Director

7.	Net amount at end of the Quarter	-51,38,742=00
8.	Total expenditure on Project till date	4,09,88,189=00
9.	Cumulative fund collected till the end of Quarter in question	29,50,000=00
10.	Cumulative expenditure done till the end of Quarter in question	4,09,88,189=00

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	NIL
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Rajmehar Singh K. Choudhary
Director

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.


CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Chaurasia
Director

Signature of Promoter

Name:

Date: *14/08/2024*

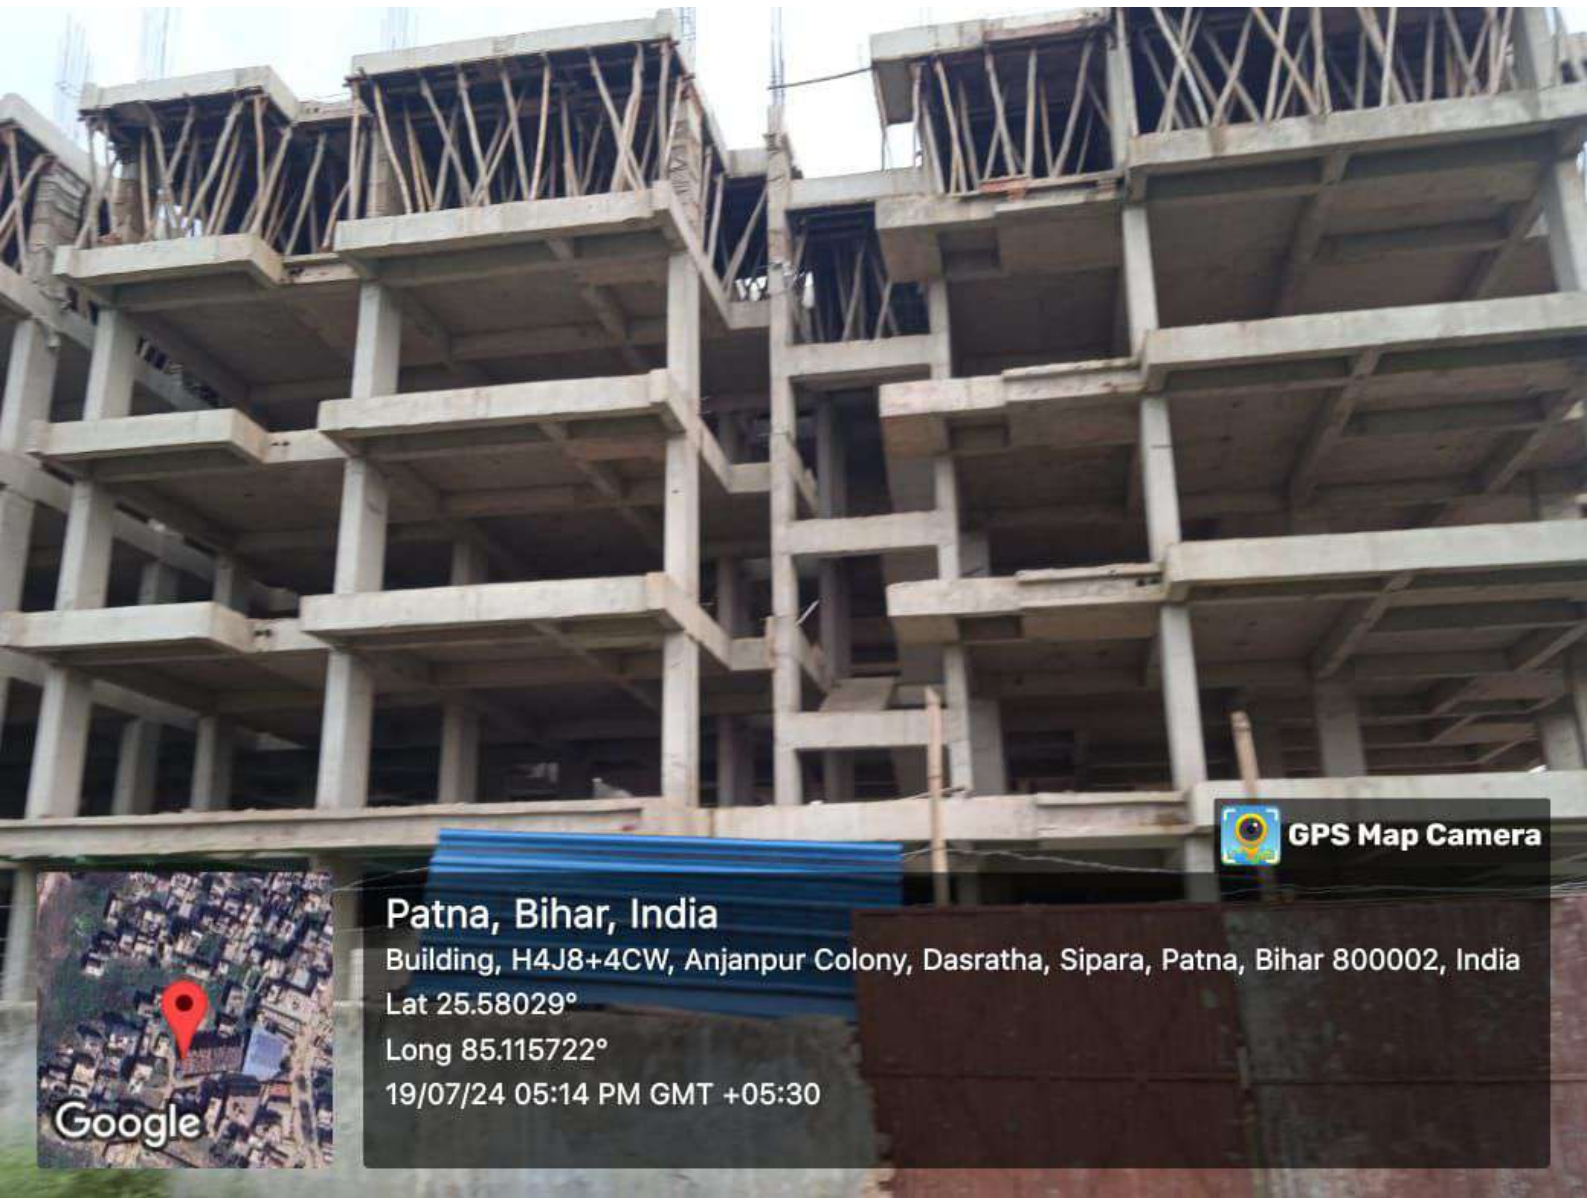

GPS Map Camera

Patna, Bihar, India


Building, H4J8+4CW, Anjanpur Colony, Dasratha, Sipara, Patna, Bihar 800002, India

Lat 25.58029°

Long 85.115722°

19/07/24 05:14 PM GMT +05:30

Google

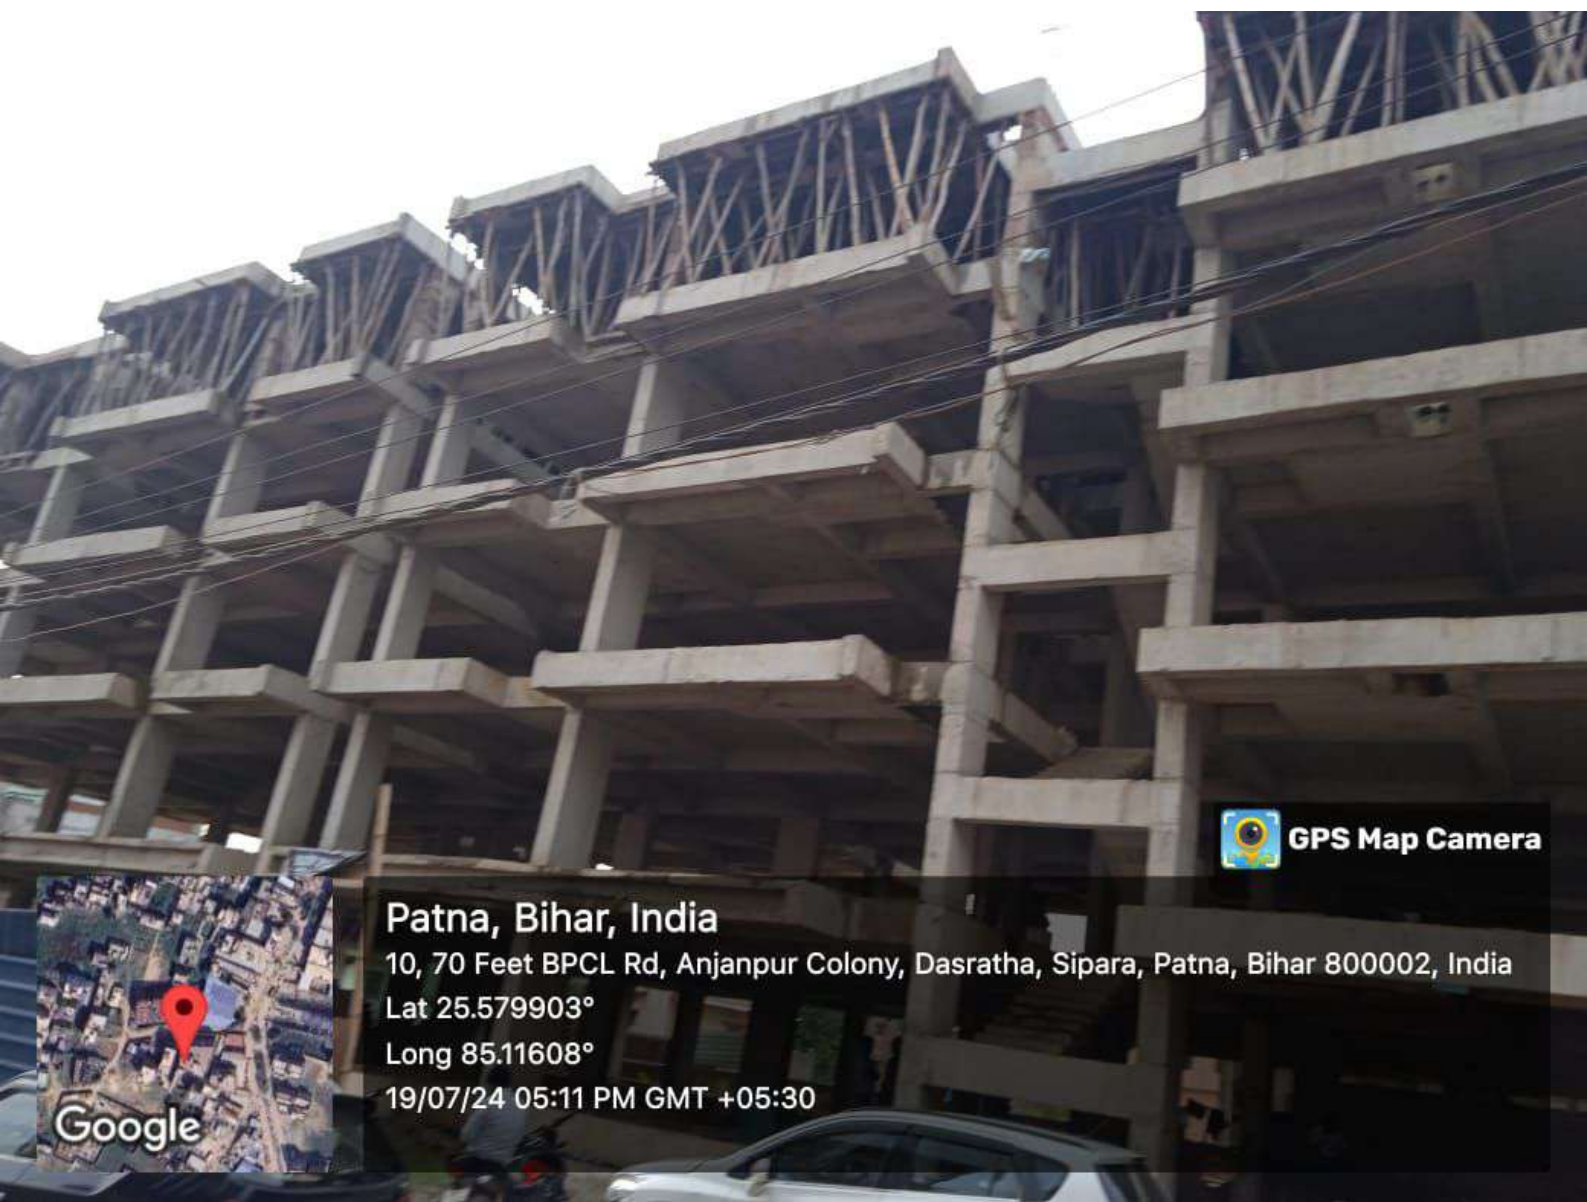

GPS Map Camera

Patna, Bihar, India

10, 70 Feet BPCL Rd, Anjanpur Colony, Dasratha, Sipara, Patna, Bihar 800002, India

Lat 25.579903°

Long 85.11608°

19/07/24 05:11 PM GMT +05:30





GPS Map Camera


Patna, Bihar, India

Building, H4J8+4CW, Anjanpur Colony, Dasratha, Sipara, Patna, Bihar
800002, India

Lat 25.580048°

Long 85.11553°

19/07/24 05:13 PM GMT +05:30

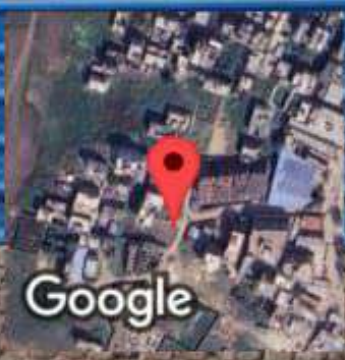

Google
