

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U51909BR2012PTC018934	Name of Firm	CHAURASIA IRON AND STEEL PRIVATE LIMITED
Firm Address :	BLOCK-B, 306, GANDHI NAGAR, KANTI FACTORY ROAD, KANKARBAGH, PATNA-800020		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	3 YEARS		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project	00	
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP51727-1/169/R-1334/2022	Name of Project/Phase of Registered Project	JAGAT PRASAD ENCLAVE
Name of Promoter	CHAURASIA IRON AND STEEL PRIVATE LIMITED	Project Address	70 FEET ROAD ANJANPUR COLONY, DASRATHA, SIPARA, PATNA-800002
Name of Co-promoter	N/A		
Project Registration is valid up to	01/12/2026		
Starting date of Project or Phase of the Project	01/04/2022		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	30-10-2024		

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Choudhary
Director

III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS						
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-19	Total Number of Apartments in Landowner's share - FLAT-21
BLOCK-A	1. 1 BHK	40		40-FLATS	1. Booked / Allotted -04	3. Booked/ Allotted-NIL
	2. Sold-NIL				Sold -NIL	
	2. 2 BHK, -				Percentage of booking 21.5%	Percentage of booking 0%
	3. 3 BHK					
	4. Shop					
	5. Bungalow					
	6. Plot etc.					
Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - FLAT-25	Total Number of Apartments in Landowner's share -
BLOCK-B	1. 1 BHK	05		25-FLATS	1. Booked / Allotted -NIL	3. Booked/ Allotted-N/A
	2. Sold-NIL				Sold -N/A	
	2. 2 BHK, -	20			Percentage of booking 0%	Percentage of booking N/A
	3. 3 BHK					
	4. Shop					
	5. Bungalow					
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.			
Association of allottees name			
Details of allottees - Name, Address, Email id (if any), contact number.			
These details may not be available to common people			
Name	Address	contact number	Email id (If any)

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES			
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-A	40	1. Booked/Allotted -	04
		2. Sold -	NIL
Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
BLOCK-B	25	1. Booked/Allotted -	NIL
		2. Sold -	NIL

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA
Ramkanta K. Chaurasia
Director

V. DETAILS OF BUILDING APPROVALS					
(If already filed along with Registration Application, then there is no need of further filing)					
S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment				
2.	Fire N.O.C.				
3.	Water Supply Permission				
4.	NOC from Airport Authority of India				
5.	Other Approval(s), if any, required for the Project.				

VI. CONSTRUCTION PROGRESS OF THE PROJECT			
1. Plan Case No. P/CHITKOHRA-PRN-1B+G+5/219/2020			
S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) (BLOCK-A)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	90%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	

CHAURASIA IRON
(JAGAT PRASAD ENCLAVE) KEN

Ram Lal Singh Kr Chaurasia
Director

9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0% 100%	

1. Plan Case No. P/CHITKOHRA-PRN-1B+G+5/219/2020

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3) (BLOCK-B)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	0%	
2.	Basements (if any)	0%	
3.	Podiums (if any)	N/A	
4.	Plinth	0%	
5.	Stilt Floor	N/A	

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Rg mehan/29 Mr Chaurasia
Director

6.	Slabs of Super Structure	0%	
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0%	
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0%	
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0%	
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0%	
11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale. Any other activities	0%	

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS

S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA

Ramchandra Kr Chaurasia
Director

1.	Internal Roads & Footpaths	YES	0%	
2.	Water Supply	YES	5%	
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	
4.	Storm Water Drains	YES	0%	
5.	Landscaping & Tree Planting	YES	0%	
6.	Street Lighting	YES	0%	
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	
9.	Solid Waste Management & Disposal	YES	0%	
10.	Water Conservation / Rain Water Harvesting	YES	0%	
11.	Energy Management	YES	0%	
12.	Fire Protection and Fire Safety Requirements	YES	0%	
13.	Closed Parking	YES	0%	
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)			

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			

CHAURASIA IRON AND STEEL PVT. LTD.
(JAGAT PRASAD ENCLAVE) RERA



Ramchandra Kr Chaurasia
Director

2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			
9.	Energy Management			

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT				
(A)	Sr. No.		BLOCK-A	BLOCK-B
	1.	Front Elevation	Attach	
	2.	Rear Elevation	Attach	
	3.	Side Elevation	Attach	
(B)		Photograph of each floor		

CHAURASIA IRONWALL STREET
(JAGAT PRASAD ENCLAVE)

Ramchandra Kr Chaurasia
Director

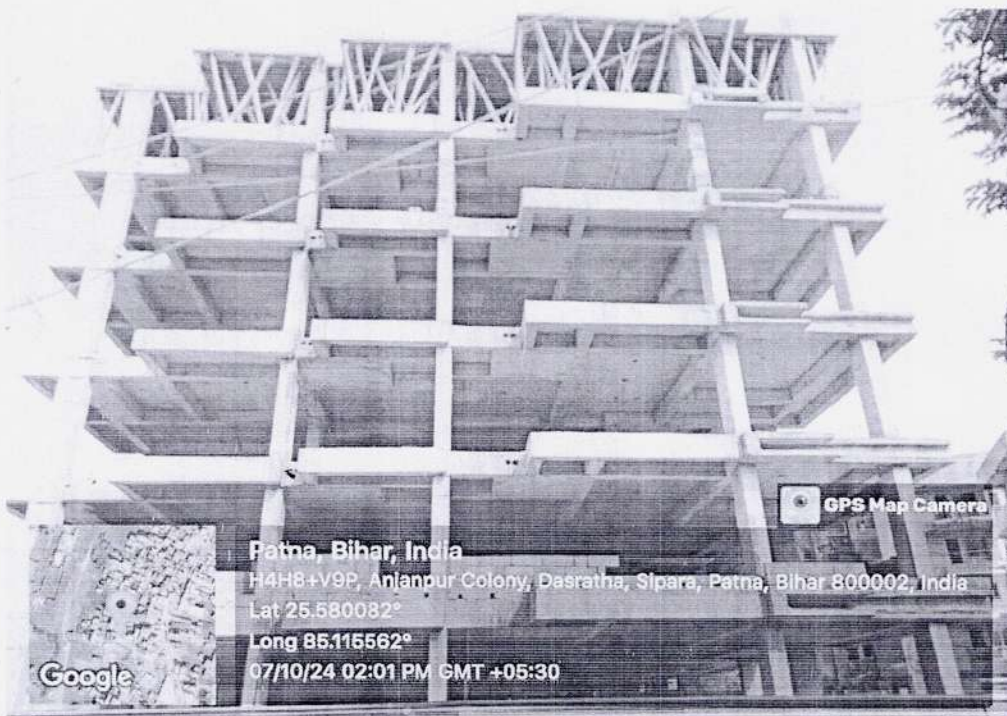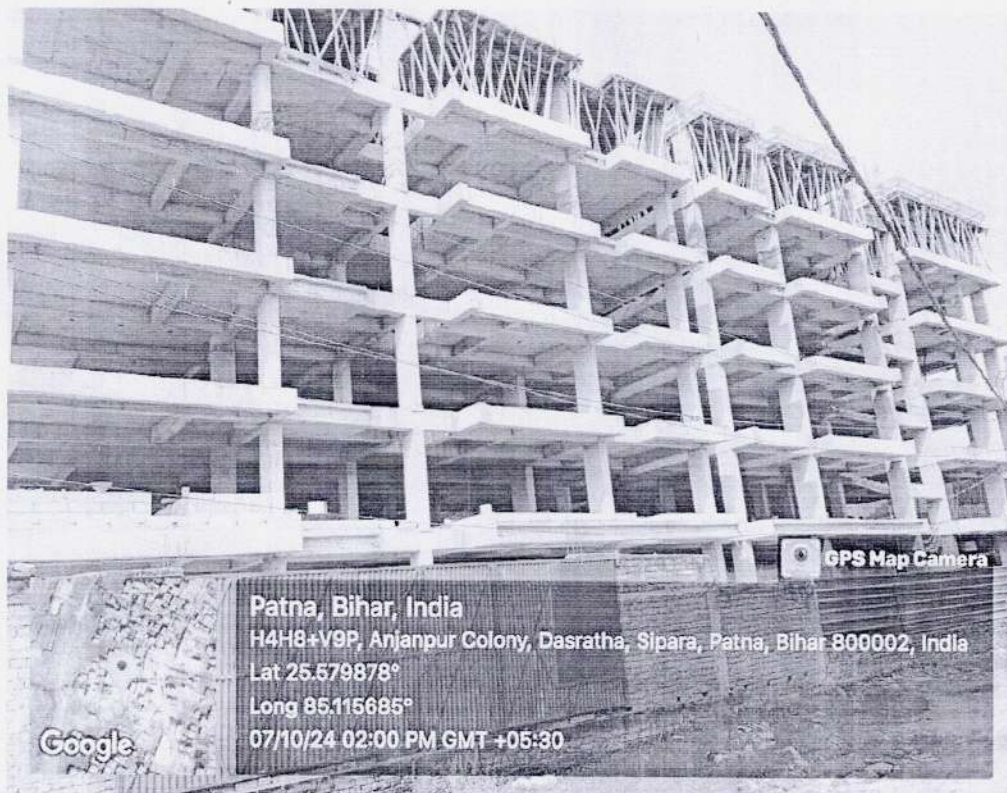

CHAURASIA IRON AND STEEL PVT. LTD.
 (GASAT PRASAD ENCLAVE) RERA

Ramchandra per choyra
 Director



X. FINANCIAL PROGRESS OF THE PROJECT

S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	27630200000799
2.	Estimated Cost of the Project including land cost at the start of the Project	19,67,90,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	12,32,90,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	25,00,000=00
5.	Amount received during the Quarter	24,83,250=00
6.	Actual Cost Incurred during the Quarter	19,87,138=00
7.	Net amount at end of the Quarter	
8.	Total expenditure on Project till date	4,29,75,327=00
9.	Cumulative fund collected till the end of Quarter in question	64,97,500=00
10.	Cumulative expenditure done till the end of Quarter in question	4,29,75,327=00

CHANDRASIA IRON AND STEEL PVT. LTD.
 (JAGAT PRASAD ENCLAVE) REH.

Ramchandra K. Chandrasia
 Director

XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED

XII. MISCELLANEOUS		
A	List of Legal Cases (if any) – On Project / Promoter	
1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO
B	Sale/Agreement for Sale during the Quarter	
1.	Sale Deed	NIL
2.	Agreement for Sale	02
3.	No. of possessions given to allottees	NIL
XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART		
Weather the project in progress is as per time schedule or lagging behind?		

XIV UNITS ALLOCATION DETAILS		
Total Number of sanctioned apartments 1 BHK- 2 BHK -05 3 BHK-60 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc
XV. BROCHURE /Prospectus		

CHAURASIA IRON AND STEEL PVT. LTD.
 (JAGAT PRASAD ENCLAVE) RERA
Rajendra Singh Chaurasia
 Director

XVI Grievance Redressal Officer

Name : RAMCHANDRA KUMAR CHOURASIA

Contact No : 7004537742

Email id : goyaltaxconsultant@yahoo.com

Address : block-b, 306, gandhi nagar ,kanti factory road,kankarbagh

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

CHANDRA IRON AND STEEL PVT LTD
(GATE NO. 10 ENCLAVE) RERA

Ramchandra K. Chourasia

Director

Signature of Promoter

Name:

Date: 14/10/2024
