

FORM-7 [REGULATION-9]

Quarterly progress report for quarter ending September of 2024 (year)

I. PARTICULARS OF PROMOTERS			
Promoter's Registration Number/CIN No/Partnership deed no/LLP Details/Any other registration with MSME Or Govt. Bodies	CIN NO. U45209BR2020PTC047284	Name of Firm	ACCOCCA DEVELOPERS PRIVATE LIMITED
Firm Address :	C/O- AJAY KUMAR SINGH, MANGAL MARKET, RAJA BAZAR, PATNA		
Total Experience of promoter in Real Estate sector			
Total Experience in Real Estate after Implementation of RERA	07 Years		
No of Project done Before Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		
No of Project done After Implementation of RERA	1. Residential 2. Commercial 3. Residential- cum Commercial 4. Plotted project		

II. PARTICULARS OF PROJECT			
Project Registration Number	BRERAP12502-001/13/R-1679/2024	Name of Project/Phase of Registered Project	GEETA PALACE
Name of Promoter	ACCOCCA DEVELOPERS PRIVATE LIMITED	Project Address	NEAR DIGITAL ITI, BATAURA, BEUR, PATNA
Name of Co-promoter	N/A		
Project Registration is valid up to	20-06-2028		
Starting date of Project or Phase of the Project	24-04-2024		
Type of Project or Phase of the Project	Residential		
Period of validity of map by the Competent Authority	20-06-2028		

ACCOCCA DEVELOPERS PVT. LTD.

[Signature]
Director



III. DISCLOSURE OF SOLD/BOOKED INVENTORY OF APARTMENTS

Building /Block Number	Apartment Type		Carpet Area	Total Number of sanctioned apartments	Total Number of Apartments in Promoter's share - Flat-8.5	Total Number of Apartments in Landowner's share - Flat-7.5
	1. 1 BHK	04		Flat-16	1. Booked / Allotted -01	3. Booked/ Allotted-NIL
	2. 2 BHK, -	12			2. Sold-NIL	Sold -NIL
	3. 3 BHK					
	4. Shop				Percentage of booking 11.76%	Percentage of booking 0%
	5. Bungalow					
	6. Plot etc.					

If the booking percentage exceeds 50% of the total booking then Information about formation of association of allottees.

Association of allottees name

Details of allottees - Name, Address, Email id (if any), contact number.

These details may not be available to common people

Name	Address	contact number	Email id (If any)
------	---------	----------------	--------------------

IV. DISCLOSURE OF SOLD / BOOKED INVENTORY OF GARAGES

Building / Block Number	Total Number of Sanctioned Garages	Total Number of Garages:	
		1. Booked/Allotted	01
	16	2. Sold	NIL

V. DETAILS OF BUILDING APPROVALS

(If already filed along with Registration Application, then there is no need of further filing)

S. No.	Name of the Approval / N.O.C./ Permission / Certificate	Issuing Authority	Applied Date	Issuance Date	Enclosed as Annexure No.
1.	NOC for Environment	N/A			
2.	Fire N.O.C.	DIRECTOR-CUM-STATE FIRE OFFICER		21-06-2022	
3.	Water Supply Permission	N/A			
4.	NOC from Airport Authority of India	N/A			
5.	Other Approval(s), if any, required for the Project.	N/A			

ACCOCCA DEVELOPERS PVT. LTD.

Signature
Director



VI. CONSTRUCTION PROGRESS OF THE PROJECT

1. Plan Case No. P/BEUR/PRN/G+4/358/2021

S. No. (1)	Tasks/Activity (2)	Percentage of Actual Work Done (As on date of the Certificate) (3)	Expected Completion date in (dd/mm/yyyy) Format
1.	Excavation (if any)	100%	15/04/2024
2.	Basements (if any)	N/A	
3.	Podiums (if any)	N/A	
4.	Plinth	100%	10/5/2024
5.	Stilt Floor	N/A	
6.	Slabs of Super Structure	20%	15/12/2024
7.	Internal walls, Internal Plaster, Floorings, Doors and Windows within Flats /Premises.	0% 0% 0% 0%	15/10/2025 15/10/2025 15/10/2025 15/10/2025
8.	Sanitary Fittings within the Flat/Premises, Electrical Fittings within the Flat/Premises	0% 0%	10/03/2027 10/03/2027
9.	Staircases, Lifts Wells and Lobbies at each Floor level, Overhead and Underground Water Tanks.	0% 0% 0%	15/06/2027 15/06/2027 15/06/2027
10.	External plumbing and external plaster, elevation, completion of terraces with waterproofing of the Building/Wing.	0% 0% 0% 0%	30/06/2027 30/06/2027 30/06/2027 30/06/2027

ACCOCOA DEVELOPERS PVT. LTD.

[Signature]
Director



11.	Installation of Lifts, water pumps, Fire Fighting Fittings and Equipment as per CFO NOC, Electrical fittings, Mechanical Equipment, compliance to conditions of environment/CRZ NOC, Finishing to entrance lobby/s, plinth protection, paving of areas appurtenant to Building/Wing, Compound Wall and all other requirements as me be required to complete project as per Specifications in Agreement of Sale.	0%	10/08/2027
		0%	10/08/2027
		0%	10/08/2027
		0%	10/08/2027
	Any other activities	0%	10/08/2027

VII. AMENITIES AND COMMON AREA AND EXTERNAL INFRASTRUCTURE DEVELOPMENT WORKS				
S. No.	Common Areas and Facilities	Proposed (Yes/No)	Percentage of actual Work Done (As on date of the Certificate)	Expected Completion date in (dd/mm/yy y) Format
(1)	(2)	(3)	(4)	(5)
1.	Internal Roads & Footpaths	YES	0%	10/04/2028
2.	Water Supply	YES	0%	15/06/2027
3.	Sewerage (Chamber, Line, Septic Tank, STP)	YES	0%	10/03/2027
4.	Storm Water Drains	YES	0%	15/04/2027
5.	Landscaping & Tree Planting	YES	0%	30/06/2027
6.	Street Lighting	YES	0%	15/04/2027
7.	Community Buildings	NO	N/A	
8.	Treatment and Disposal of Sewage and Sullage Water	NO	N/A	

ACCOCOA DEVELOPERS PVT. LTD.


 Director



9.	Solid Waste Management & Disposal	YES	0%	10/04/2028
10.	Water Conservation / Rain Water Harvesting	YES	0%	20/04/2026
11.	Energy Management	YES	0%	15/06/2027
12.	Fire Protection and Fire Safety Requirements	YES	0%	20/04/2028
13.	Closed Parking	YES	0%	15/04/2027
14.	Open Parking	NO	N/A	
15.	Electrical Meter Room, Sub-Station, Receiving Station	YES	0%	
16.	Others (Option to Add More)	NO	N/A	

VIII. A EXTERNAL AND INTERNAL DEVELOPMENT WORKS IN CASE OF PLOTTED DEVELOPMENT

		PROPOSED YES/NO.	PERCENT AGE OF ACTUAL WORK DONE (As on date of certificate)	Expected Completion date in (dd/mm/yy) Format
1.	Internal Roads and foot paths			
2.	Water Supply			
3.	Sewerage Chambers Septic Tank			
4.	Drains			
5.	Parks, Land Scaping and Tree Planting			
6.	Street Lighting			
7.	Disposal of sewage & sullage water			
8.	Water conservation/Rain Water Harvesting			

ACCOCOA DEVELOPERS PVT. LTD.

 Director


9.	Energy Management			
----	-------------------	--	--	--

IX. GEO TAGGED AND DATE PHOTOGRAPH OF(EACH BLOCK) OF THE PROJECT			
(A)	Sr. No.		
	1.	Front Elevation	Attach
	2.	Rear Elevation	Attach
	3.	Side Elevation	Attach
(B)		Photograph of each floor	



ACCOSCA DEVELOPERS PVT. LTD.
Signature
 Director



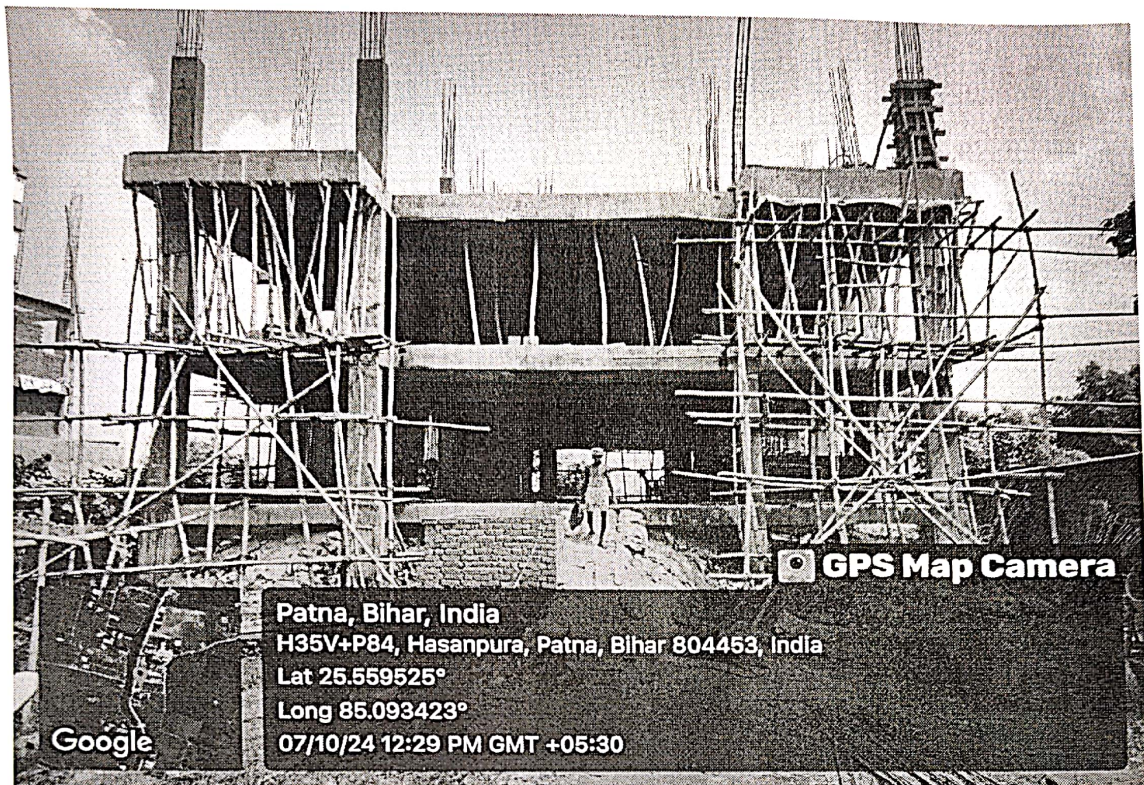

ACCOCCA DEVELOPERS PVT. LTD.

[Signature]
Director



Scanned with OKEN Scanner



X. FINANCIAL PROGRESS OF THE PROJECT		
S. No. (1)	Particulars (2)	Amount (In Rs.) (3)
1.	Project Account No.	922020025299936
2.	Estimated Cost of the Project including land cost at the start of the Project	4,65,05,000=00
3.	Estimated Development Cost of the Project at the start of the Project.(Excluding Land Cost)	2,41,00,000=00
4.	Any Variation in Development Cost which is declared at the start of the Project.	N/A
5.	Amount received during the Quarter	20,00,000=00
6.	Actual Cost Incurred during the Quarter	27,20,000=00
7.	Net amount at end of the Quarter	NIL
8.	Total expenditure on Project till date	27,20,000=00
9.	Cumulative fund collected till the end of Quarter in question	20,00,000=00
10.	Cumulative expenditure done till the end of Quarter in question	NIL

ACCOCOA DEVELOPERS PVT. LTD.

S. Jais
Director



XI. DETAILS OF MORTGAGE OR CHARGE IF ANY CREATED**XII. MISCELLANEOUS****A List of Legal Cases (if any) – On Project / Promoter**

1.	Case No.	NO
2.	Name of Parties	NO
3.	No of Execution Cases against this project Case No. Name of Parties	NO
4.	No of Suo - Moto cases against this project Case No. Name of Parties	NO
5.	No of Certificate cases /PDR cases against this project Case No. Name of Parties	NO

B Sale/Agreement for Sale during the Quarter

1.	Sale Deed	NIL
2.	Agreement for Sale	01
3.	No. of possessions given to allottees	NIL

XIII. PERCENTAGE OF WORK ALONG WITH MILESTONE CHART

Weather the project in progress is as per time schedule or lagging behind?

XIV UNITS ALLOCATION DETAILS

Total Number of sanctioned apartments 1 BHK- 2 BHK -04 3 BHK-12 4 BHK- Shop- Bungalow - Plot etc	Details of allotment made so far with Flat number/ Bungalow - Plot etc	Cancellation of flat allotment, If any with Flat number/ Bungalow - Plot etc

XV. BROCHURE /Prospectus

ACCOCCA DEVELOPERS PVT. LTD.
Sethu
Director



XVI Grievance Redressal Officer

Name : SATYAM JAMAIYAR

Contact No : 8873035496

Email id : accoccadevelopers@gmail.com

Address : AJAY KUMAR SINGH, MANGAL MARKET, RAJA BAZAR, PATNA

Undertaking:

I/we solemnly affirm, declare and undertake that all the details stated above are true to the best of my knowledge and nothing material has been concealed here from. I am/we are executing this undertaking to attest to the truth of all the foregoing and to apprise the Authority of such facts as mentioned as well as for whatever other legal purposes this undertaking may serve.

ACCOCCA DEVELOPERS PVT. LTD.

Satyam
Director

Signature of Promoter

Name: SATYAM JAMAIYAR

Date: 14/10/2024

